




TRACKING PROGRESS & ASSESSING PERFORMANCE

# ANNUAL REPORT 2022-23



**EMBRACING AUTOMATION**



**MONITORING & EVALUATION CELL  
PLANNING & DEVELOPMENT DEPARTMENT  
GOVT OF SINDH**

[WWW.MECSINDH.GOV.PK](http://WWW.MECSINDH.GOV.PK)

+92 21 99211418





# ANNUAL REPORT

## 2022-23





## MEC ANNUAL REPORT 2022-23 (CONTRIBUTORS)

### APPROVING AUTHORITY

**Chairman - P&D Board**  
Syed Hassan Naqvi

### REVIEWER

**Director General - MEC**  
Ghulam Sarwar Chachar

### EDITORIAL

**Director (A&A) - MEC**  
Ghulam Hassan Bughio

**Assistant Director (MIS) - MEC**  
Sarfraz Ahmed Khan

**Assistant Director (CM) - MEC**  
Tufail Ahmed Shaikh

## DISCLAIMER (MEC ANNUAL REPORT 2022-23)

Every effort has been made to cross-check and verify the authenticity of the data. All data and statistics used are correct as of FY 2022-23. The status of monitored schemes has been updated for the corresponding financial year and may be changed after the defined period.

Please note that the level of analysis for this report is centered on units monitored during FY 2022-23. In other words, development schemes that are implemented in different geographical locations are counted as separate units while monitoring. Hence, the term 'scheme' is used synonymously as units even where one scheme has multiple units. Monitoring reports that were published have been included in the corresponding financial year. There might be some monitoring reports that were visited in preceding years but have been included in the subsequent financial year(s) as per the date of being published. Data exported from online system on 05-July-2023.

This report does not contain references to third parties, neither does the report endorse any such third parties or their product/services nor is the report sponsored, endorsed or associated with such third parties.

For any queries or feedback regarding this report, please contact MEC official Platform:



info@mecsindh.gov.pk



www.mecsindh.gov.pk



+ 0092 (21) 99211927  
+ 0092 (21) 99211418 (Ext-DG)



3rd Floor, Office of the Director  
General – Monitoring &  
Evaluation Cell, Tughluq House,  
Sindh Secretariat, Karachi.

# FOREWORD



## CHAIRMAN, P&D BOARD

The Planning & Development Board facilitates Administrative Departments in policy and procedure guidelines while making Annual Development Plans (ADP) and coordinates in progress-reporting and amelioration of the ADP schemes. The Monitoring & Evaluation Cell was established under the P&DD to ensure the envisaged execution of financial and physical progress of the development schemes and provide timely course-corrections, if needed, for the schemes that deviate from the planned parameters.

It is heartening to see that Monitoring & Evaluation Cell (MEC) is evolving as an unconventional and unorthodox monitoring body to strive to attain the optimum value for the public sector development portfolio in the province. The primary responsibility of the MEC is proactively monitoring the development portfolio with real-time reporting in a paperless environment on key performance indicators of the schemes for timely rectification measures.

This report provides a corpus of consolidated information on the overall monitoring activities undertaken by the MEC during the FY 2022-23 which demonstrates out and out commitment of the P&D

Department to ensure that the development funds are effectively and efficiently utilized to quantifiably uplift the living standards & lives of people of the province. The MEC Officials possess adequate technical expertise which is a prerequisite for a dynamic assessment and the analysis of the financial and physical progress of a diverse portfolio of projects.

It is promising that the MEC through its continuous and consistent monitoring efforts and adaptation of updated Information Communication Technology (ICT) systems has augmented its vigilance and reporting mechanism. This is evident by the digitization of ADP Budget Book Volume-v through which all stakeholders including the general public of the province can review the progress & quality status of each project through a single click. Moreover, the MEC team is always responsive to any special time limit assignments to provide mid-year or annual reviews on Federal PSDP portfolios progression to assist the highest forum in decision making. It is pleasing to express that the endeavor of the MEC team is being appreciated by the honorable Chief Minister, Sindh on the floor of the Sindh Assembly.

I wish, this vital organ of P&D Board continues on the path of steady progress by harnessing modern monitoring & evaluation mechanisms and leveraging technological solutions. I would like to see the MEC as a proactive organic organization that contributes conspicuously to enhance public service delivery leading towards improved outcomes and better services for the general public.

**SYED HASSAN NAQVI**

# PREFACE



## DIRECTOR GENERAL (MEC)

Since its inception, the Monitoring & Evaluation Cell (MEC) has been committed to becoming a dynamic organization equipped with robust monitoring and evaluation systems. Its primary objective is to oversee the progress of ongoing development schemes. Over the years, the MEC has made continuous efforts to enhance the effectiveness of its monitoring initiatives. The ultimate goal is to ensure the efficient utilization of public sector funds, resulting in improved service delivery.

As the Director General of the Monitoring & Evaluation Cell, I take great pleasure in presenting the Annual Report of the MEC for the fiscal year 2022-23. With an unwavering dedication to upholding excellence, this report showcases the collective efforts and achievements of the M&E Cell. It highlights our proactive approach to monitoring and evaluating a substantial portion of the Government of Sindh's development portfolio, including ongoing schemes in remote and inaccessible regions.

The MEC has significantly strengthened its Monitoring and Evaluation system by leveraging technological solutions. The introduction of real-time reporting through smartphones, automation of ADP Budget Book Volume - V, and the implementation of an

end-to-end process with a centralized progress monitoring dashboard, have played a pivotal role in this transformation. The establishment of fully-functional regional offices in Karachi, Hyderabad, Sukkur, and Larkana has enhanced MEC's capacity and capability to monitor the progress of numerous provincial and district ADP schemes. Besides, in order to augment the performance and reporting standards of the monitoring team, highly technical monitoring equipment was procured in F.Y. 2022-23.

In the fiscal year 2022-23, along with its regular tasks, the MEC accomplished the additional/special monitoring targets, which included monitoring of 817 ADP Schemes across Sindh Province within one-week's timeframe, monitoring of 08 federal PSDP Umbrella Schemes, and monitoring of 07 Mega Schemes in Karachi.

I would like to extend my sincere appreciation and acknowledgment to all the regional field monitoring offices of the MEC, the MIS Directorate, and other associated officers for their unwavering dedication and rejuvenated efforts. Their commitment has played a vital role in accomplishing the intended objectives and targets of the organization. Their hard work and contributions are invaluable in ensuring the successful implementation of monitoring and evaluation activities.

This publication serves as a comprehensive compilation of insightful observations, analysis, and valuable information regarding a significant portfolio of the Sindh Annual Development Plan for the fiscal year 2022-23. It provides a holistic view of the progress, challenges, and achievements of development schemes, offering valuable insights for stakeholders and decision-makers.

**GHULAM SARWAR CHACHAR**

# CREDITS

## MEC ANNUAL REPORT 2022-2023

### Director General (MEC)

Ghulam Sarwar Chachar

### Director (A&A) - MEC

Ghulam Hassan Bughio

### Assistant Director (MIS) - MEC

Sarfraz Ahmed Khan

### Assistant Director (CM) - MEC

Tufail Ahmed Shaikh



Planning &  
Development  
Department



Monitoring &  
Evaluation  
Cell

# ACRONYM

<b>ACS</b>	Additional Chief Secretary
<b>AD</b>	Administrative Department
<b>ADB</b>	Asian Development Bank
<b>ADP</b>	Annual Development Plan
<b>AEN</b>	Assistant Engineer
<b>CD/CDA</b>	Coastal Development Authority
<b>CDWP</b>	Central Development Working Party
<b>CM</b>	Chief Minister
<b>CMS</b>	Content Management System
<b>DC</b>	Deputy Commissioner
<b>DDWP</b>	District Development Working Party
<b>DEV</b>	Development
<b>DG</b>	Director General
<b>DS</b>	Deputy Secretary
<b>EA</b>	Executing Agency
<b>FD</b>	Finance Department
<b>FILMS</b>	File Management System
<b>FY</b>	Fiscal Year
<b>GIS</b>	Geographic Information System
<b>GoS</b>	Government of Sindh
<b>GPS</b>	Global Positioning System
<b>HR</b>	Human Resource
<b>IMP</b>	Implementation
<b>KDA</b>	Karachi Development Authority
<b>KMC</b>	Karachi Metropolitan Corporation
<b>KW&amp;SB</b>	Karachi Water & Sewerage Board
<b>MDA</b>	Malir Development Authority
<b>M&amp;E</b>	Monitoring and Evaluation
<b>MEC</b>	Monitoring and Evaluation Cell
<b>MEO/MO</b>	Monitoring and Evaluation Officer
<b>MIS</b>	Management Information System
<b>MPR</b>	Monthly Progress Report
<b>P&amp;D</b>	Planning and Development
<b>PD</b>	Project Director
<b>PDWP</b>	Provincial Development Working Party
<b>PHED</b>	Public Health Engineering Department
<b>PM</b>	Prime Minister
<b>PS</b>	Personal Secretary
<b>QR</b>	Quick Response
<b>RMEO/RMO</b>	Regional Monitoring and Evaluation Officer
<b>SBI</b>	Sindh Board of Investment
<b>SGACD</b>	Services General Administration and Coordination
<b>SGRRP</b>	Sindh Growth and Rural Rehabilitation Program
<b>SMEO/SMO</b>	Sector Monitoring and Evaluation Officer
<b>SMES</b>	Schemes Management & Evaluation System
<b>SMS</b>	Short Messaging Service
<b>SPPRA</b>	Sindh Public Procurement Regulatory Authority
<b>SSWMB</b>	Sindh Solid Waste Management Board
<b>TPM</b>	Third Party Monitoring
<b>WB</b>	World Bank
<b>XEN</b>	Executive Engineer

# EXECUTIVE SUMMARY

---

The annual report provides an overview of the activities and achievements of the Monitoring & Evaluation Cell (MEC), Planning & Development Department, Government of Sindh, for the fiscal year 2022-23. The MEC is responsible for monitoring and evaluating the progress and quality of the development schemes under the Provincial Annual Development Plan (ADP) of Sindh. The main objectives of this report are:

- To highlight the MEC's functions, features, and systems for effective monitoring and evaluation of the development schemes and projects
- To summarize the field monitoring observations and status of the development schemes under the Provincial ADP of Sindh for the financial year 2022-23
- To identify the issues and challenges faced by the MEC, Administrative Departments (ADs) and Executing Agencies (EAs) in implementing and completing the development schemes
- To make recommendations for quality improvement and performance enhancement of the development schemes and projects

The MEC has introduced new technological features to digitize the ADP Budget Book Volume-V, which allows all stakeholders, including the general public, to review the progress and monitoring status of the projects with a single click of a smartphone. Besides, the MEC has adopted a paper-less work environment through File Management System (FILMS), where MEC reporting, communication, and decision making are processed on the dashboard. The MEC has also been continuously improving and strengthening its Monitoring & Evaluation systems by procuring latest monitoring equipment and adopting constant improvement in its reporting tablets. The MEC team ensures an active feedback loop with the ADs and EAs, aiming to communicate, address, and rectify issues identified during monitoring to strengthen their work environment. These course-correction measures are destined to achieve the envisaged results of the development schemes vis a vis the financial progress of the schemes.

In the fiscal year 2022-23, the Provincial ADP of Sindh consisted of a total of 4,158 development schemes, with 2,506 being ongoing and 1,652 new schemes. During the year, due to floods, monitoring visits were halted for three months.

The MEC published 542 monitoring reports only, out of which 344 (i.e., 63%) reports were satisfactory, while 198 (i.e., 37%) reports were unsatisfactory. The ADs responded to 91 (i.e. 46%) unsatisfactory schemes with compliance reports to address the identified issues. Additionally, in a special monitoring assignment, 817 ADP schemes and eight umbrella schemes of Federal Government development projects were visited and reported.

The overall observation of the MEC is that most of the schemes were satisfactory and in accordance with the planned scope of the schemes. However, some of the common reasons for unsatisfactory schemes were:

- Negligence on feasibility study (PC-II) which resulted in incomplete planning (PC-I) by ignoring the services of other departments on site
- Deviation from scope due to premature planning which ended in revised PC-Is with escalated costs
- Shortcomings in execution due to improper planning timelines and in coordination with other departments
- Unnecessary delays in permissions and responses from other departments especially Pakistan Railways and KE, respectively
- Compromise in quality
- Change of scheme locations
- Poor workmanship and supervision
- Non-existence of annual performance report (PC-V) to learn the lessons for the future

In recommendations it is proposed that in order to maintain proper quality and achieve desired results on time, all parameters of quality management designed by PMI (Project Management Institute) should be adopted especially affecting feasibility reports (PC-II) before detailed planning (PC-I) including the coordination with other departments and implementation of PC-V. These are necessary requirements to achieve desired results, decline in number of unsatisfactory reports and revision of the schemes.



# SALIENT FEATURES



# Table of Contents

## Organizational Overview 01

Vision, Mission, Values and Functions

ADP Progress Monitoring Dashboard

Integration

MEC Monitoring Plan

## Development Overview 15

Prioritized Department-Wise Release Position

Key Monitoring Indicators for Prioritized Departments

## 09 ADP Portfolio

5-Year Trend Analysis of Provincial ADP Allocations

Department-Wise ADP Allocations

## 27 Key Performance Indicators

Overall Status of Monitoring Visits and Schemes

Department-Wise Monitoring Visits

Department-Wise Status of Schemes Monitored

Regional Monitoring Visits

5-Year Trend Analysis of Monitoring Visits

Special Assignment

## Key Result Indicators **39**

Department-Wise Compliance Status of Monitored Schemes

5-Year Trend Analysis of the Status of Monitored Schemes

Monitoring Revisits Outcomes

Summary of Completed Schemes

## Way Forward **65**

MEC's Monitoring Plan for FY 2022-23

## **51** Findings & Recommendations

Agriculture Department

Culture & Tourism Department

Education Department

Health Department

Irrigation Department

Local Government

Public Health Engineering Department

Sports & Youth Affair Department

Works & Services Department

## **69** Annexures

Annexure (A)

Department Wise Schemes Monitored in FY 2022-23

Annexure (B)

List of Re-Visited Schemes in FY 2022-23

Annexure (C)

List of Completed Schemes in FY 2022-23

Annexure (D)

List of Special Assignment Schemes in FY 2022-23

Annexure (E)

Progress Summary of PSDP 2022-23 Schemes

Executed by Government of Sindh

Annexure (F)

MEC Offices & Team Members

Annexure (G)

MEC Officers Pictures



# OVERVIEW



# ORGANIZATIONAL



## **Improve Public Sector Development Service Delivery Outcomes for Amplified Societal Impact**



### **Ensuring rigorous monitoring and evaluation of public sector development schemes for improved service delivery with the following objectives**

1. *To ensure that the Standards of Quality are maintained in development projects*
2. *To keep a regular track of the progress of schemes*
3. *To enable timely & informed decisions through efficient reporting*
4. *To promote and enhance institutional learning and knowledge through the instant availability of chronological indicators*
5. *To coordinate with various authorities for smooth and unhindered implementation*
6. *To Review and Evaluate the output & outcome of schemes.*

# CORE VALUES



## QUALITY

Robust monitoring and evaluation benchmark



## INNOVATION

Adopt advanced techniques and modern technological solutions for effective and efficient end-to-end systems



## INTEGRITY

Adhere to the utmost level of transparency in every part of the conduct



## COMMITMENT


Endeavor to improve service delivery for enhanced societal impact



# FUNCTIONS



# MONITORING DASHBOARD (WORKFLOW)

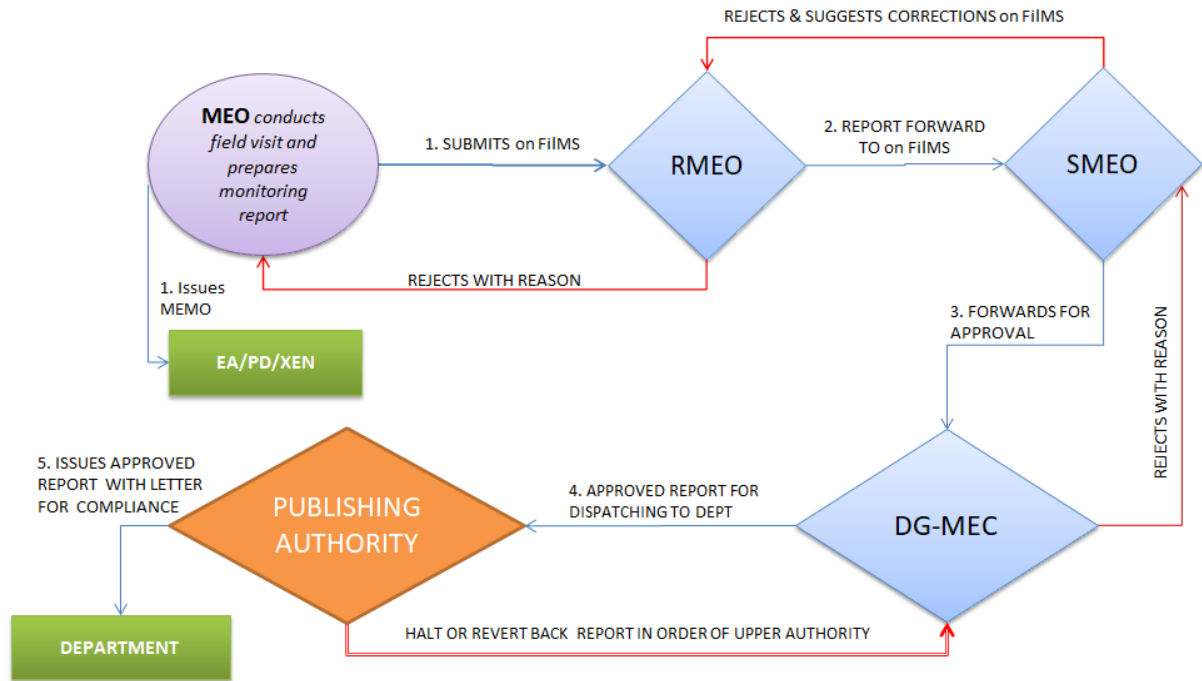

MEC has several quality filters to ensure that the automated and paperless monitoring system is transparent. File Management System (FILMS) is an indigenously-built bespoke system that ensures efficient monitoring, reporting, and evaluation of development schemes.

The monitoring & Evaluation Officer (MEO) submits the report after the monitoring visit to the Regional Monitoring & Evaluation Officer (RMEO) who ensures that all the technical requirements pertaining to the monitoring visit are addressed. RMEO intimates the relevant Sector Monitoring & Evaluation Officer (SMEO) for validation of the report for the requisite compliance standards. SMEO then submits the validated reports and submitted to the Director-General for approval and after the approval SMEO issue letter to the relevant Line Department for compliance vis-à-vis the monitoring report findings.


# AUTOMATION OVERVIEW

PC-I Automation system (PCFMS) and ADP Information Management System (AiMS) Dashboard are electronic systems for holistic monitoring of the Provincial ADP and its portfolio with integration of financial and physical progress of the ongoing development schemes with relevant disaggregated indicators and an overlay of geo-spatial mapping.

## OBJECTIVE (PCFMS)

To provide an online holistic view of the ADP portfolio by presenting information on:

1. GIS Maps with pin-pointed location of the development schemes
2. Financial progress as reported by FD/FABS
3. Physical progress reporting from the field by the line department and MEC
4. Monthly Progress and Issuance of UID
5. Conducting TCM and PDWP meetings
6. Analytical and Summarized Reports

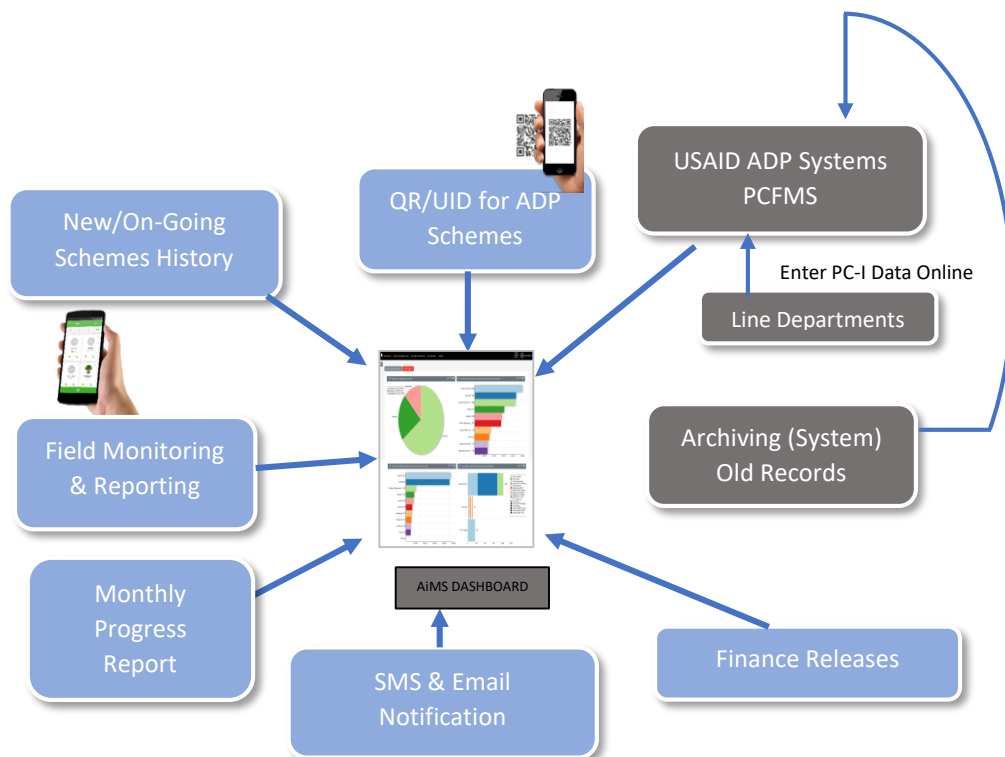

## UNIFIED REPORTING

The dashboard integrates and consolidates data from various sources.

1. Integration with existing paperless workflow automation system of MEC (FiMS) with quality detailed reports
2. Weekly fetching of data from Finance Department
3. Weekly reports of approved and unapproved ADP schemes analysis & Reporting
4. QR support to adopt new technology and schedule TCM/PDWP meetings
5. Every scheme will have a unique ID to enable tracking throughout the life of the project

## ANALYSIS AND VISUALIZATION


1. Data visualization in Grids/Charts with filters on multiple fields;
2. One click + real time access to information on the web through a simple log in;
3. Data input from Android smartphones from field is reflected in real-time in on-screen visual and tabular analytical reports
4. Department wise and District/Division wise reporting
5. Comparative Analysis of financial, physical and location-based data.

## SMARTPHONE APPLICATION


Previously, the key information required on frequent basis from MEC field monitors was submitted through an online web-based system called FiMS that included information on financial outlays, key issues faced and status of projects (satisfactory/unsatisfactory) acquired through field visits.

Now, the mobile App of the ADP Monitoring Dashboard allows MEC monitoring officers to submit this key information on a real time basis through their Smartphone from the field with their geo-tagged location with pictures to report physical progress and inform of any issues/obstacles along with other details.


# MEC MONITORING PLAN



Routine Visits

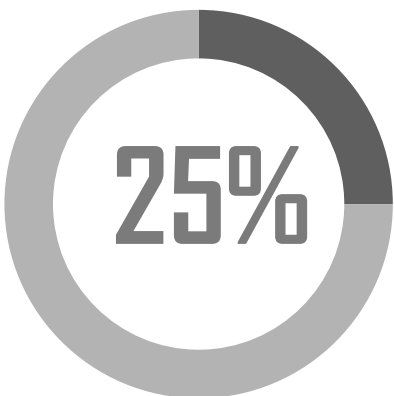

LTBC/SI Visits

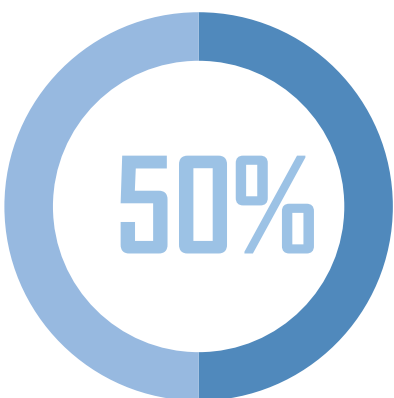

Compliance Visits

MEC is responsible for active monitoring and rigorous evaluation of ADP schemes executed by various departments working for the Government of Sindh. MEC's robust monitoring mechanism is manifested through its overall visit plan that comprises 25% routine visits, 25% visits to ADP schemes that are Likely to be Completed (LTBC)/Special Initiatives in the corresponding financial year, and 50% compliance visits to the schemes with previously unsatisfactory status.

The three main categories of monitoring visits include First Visits, Revisits, and Visits for Compliance. In simple terms, the MEC team visits a cohort of schemes every financial year out of which a subset of schemes is revisited.

It is worth mentioning that revisits are also done for schemes that are termed 'satisfactory' to ascertain if the satisfactory status of those schemes is maintained over time. For schemes that are termed 'unsatisfactory', the MEC team issues compliance notices to make sure that the issues are promptly rectified.

Once the Department submits para-wise replies to indicate compliance with the issues raised by the MEC team, the 'compliance' monitoring visit is conducted to ensure that the submitted replies have been implemented on the ground too. These quality filters ensure that the Departments guarantee timely compliance to improve the financial and physical progress of the ongoing ADP schemes



ADP

PORTFOLIO




# FINANCIAL TREND ANALYSIS OF PROVINCIAL ADP

In the post-devolution context, Government of Sindh has been progressively increasing the size of its development portfolio to undertake a series of initiatives for the province. The focus of these initiatives has been to achieve a balanced growth of infrastructure, production and social sectors for equitable development.

Rs. million

ADP	ON-GOING SCHEMES	NEW SCHEMES	TOTAL SCHEMES	THROW-FORWARD	ALLOCATION	RELEASES	EXPENDITURE	UTILIZATION %
2018-19	2,226	25	2,251	507,712	223,000	123,229	87,435	70
2019-20	1,853	852	2,705	606,227	208,000	117,350	81,516	69
2020-21	2,069	177	2,246	607,570	155,000	96,214	82,877	86
2021-22	1,645	1,670	3,315	740,771	222,500	171,208	152,824	89
2022-23	2,506	1652	4,158	893,054	332,165	219,912	208,135	95

The last 5-year period of Provincial ADP shows that quantum of total development schemes has increased from 2251 in FY 2018-19 to 4158 schemes in FY 2022-23. The size of Provincial ADP Portfolio has increased in terms of allocations from Rs. 223 billion in FY 2018-19 to about Rs. 332 billion in FY 2022-23. Throw-Forward as of June, 2018 was Rs. 507 billion; making the ratio of throw-forward to total allocation in FY 2018-19 equal to 2.3:1. Throw-Forward as of June, 2022 was Rs. 893 billion; making the ratio of throw-forward to total allocation in FY 2022-23 equal to 2.7:1.

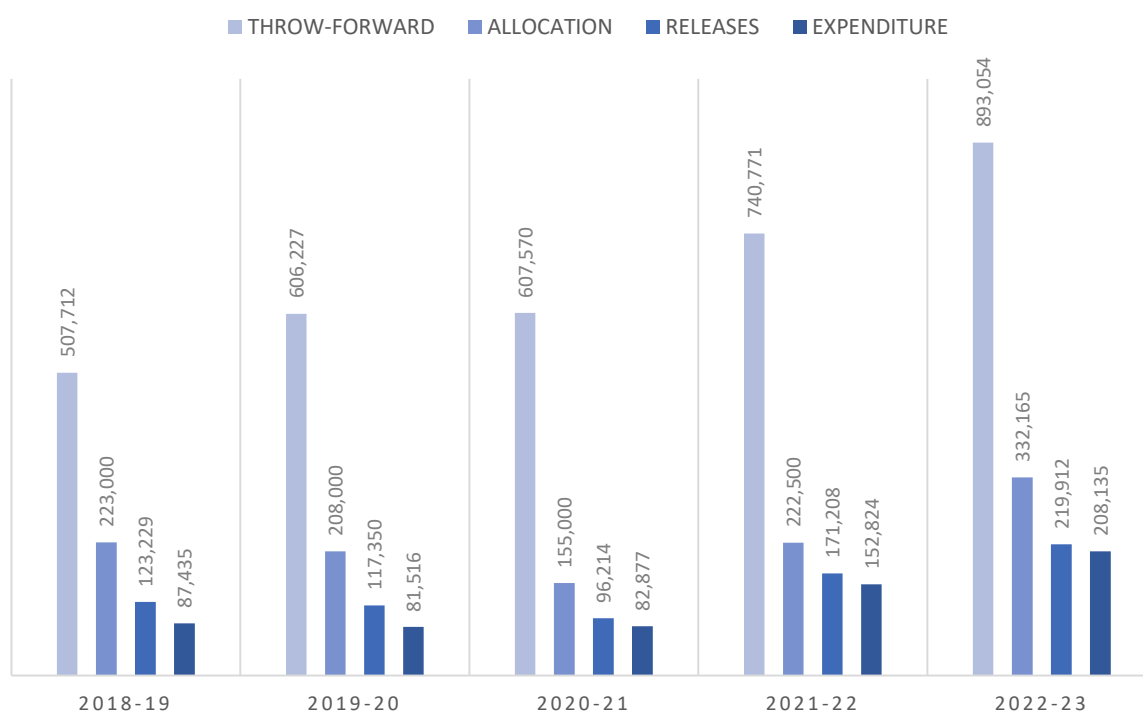

# DEPARTMENT-WISE ADP BUDGET ALLOCATION IN FY 2022-23

Department	Allocation (Rs. Mil)
AGRICULTURE, SUPPLY & PRICES	7450
AUQAF, ZAKAT, USHR & R.A.	500
BOARD OF REVENUE	201
COOPERATIVE	17
CULTURE, TOUR:, ANTIQ: & ARCH	2001
EDUCATION SECTOR	34218
ENERGY	2550
ENVIRONMENT, C. C. & C.D.	1200
EXCISE & TAXATION	144
FINANCE	1325
FOOD	345
FOREST & WILDLIFE	1501
GOVERNOR'S SECRETARIAT	69
HEALTH	23335
HOME	9202
HUMAN RIGHTS	115
HUMAN SETTLEMENT, SD&SH	58
INDUSTRIES & COMMERCE	2033
INFORMATION	205
INFORMATION, SCI. & TECH	855
INVESTMENT	287
IRRIGATION	22525
LABOUR & HUMAN RES:	115
LAW P.A, & PROSECUTION	1760
LINING OF MAIN CANALS	10000
LIVESTOCK & FISHERIES	1716
LOCAL GOVERNMENT & HTP	62080
MATCHING ALLOCATION	1570
MEGA PROJECTS FOR KARACHI CITY	10820
MINES & MINERAL DEV:	85
MINORITIES AFFAIRS	1001
PLANNING & DEVELOPMENT	7986
POPULATION WELFARE	350
PROVINCIAL ASSEMBLY	345
PROVINCIAL OMBUDSMAN	58
PUBLIC HEALTH ENGG: & RD	23476
REHABILITATION (PDMA)	1000
SGA&C	3502
SINDH REVENUE BOARD	10
SOCIAL PROTECTION & PRP	1150
SOCIAL WELFARE	800
SPORTS & YOUTH AFFAIRS	2801
THAR COAL INFRASTR. DEV:	425
TRANSPORT & MASS TRANSIT	8204
WOMEN DEVELOPMENT	300
WORKS & SERVICES	82476

The size of Provincial ADP for FY 2022-23 was about Rs. 332 billion. The ADP portfolio comprised of 4158 Schemes (2506 Ongoing and 1652 New Schemes). The overall development portfolio also included allocations of Rs. 30 billion for District ADP, Federal Grants of Rs. 6.025 Billion and Foreign Project Assistance of Rs. 91.5 billion. The total development outlay for FY 2022-23 amounted upto the tune of Rs. Rs. 460 billion.


In terms of ADP allocations, the priority departments are Works & Services, Local Government, Education, Public Health Engineering, Health, and Irrigation.

The Works & Services department has received the highest allocation in FY 2022-23 and was recorded at Rs. 82.4 billion out of the total ADP portfolio of Rs. 332 billion. This accounts for about 25% of the Total Provincial ADP outlay.

The prioritization of Local Government & HTP sector is also reflected in the Provincial ADP of FY 2022-23 with allocations of about Rs. 62.0 billion. This adds up to Rs. 144.4 billion which is almost 44% of the Provincial ADP portfolio. Earmarking significant allocations for priority sectors reflects the resolve and commitment of the provincial government towards balanced growth and equitable development of the province.

(RS. MILLION)

## ADP ALLOCATION IN FY 2022-23

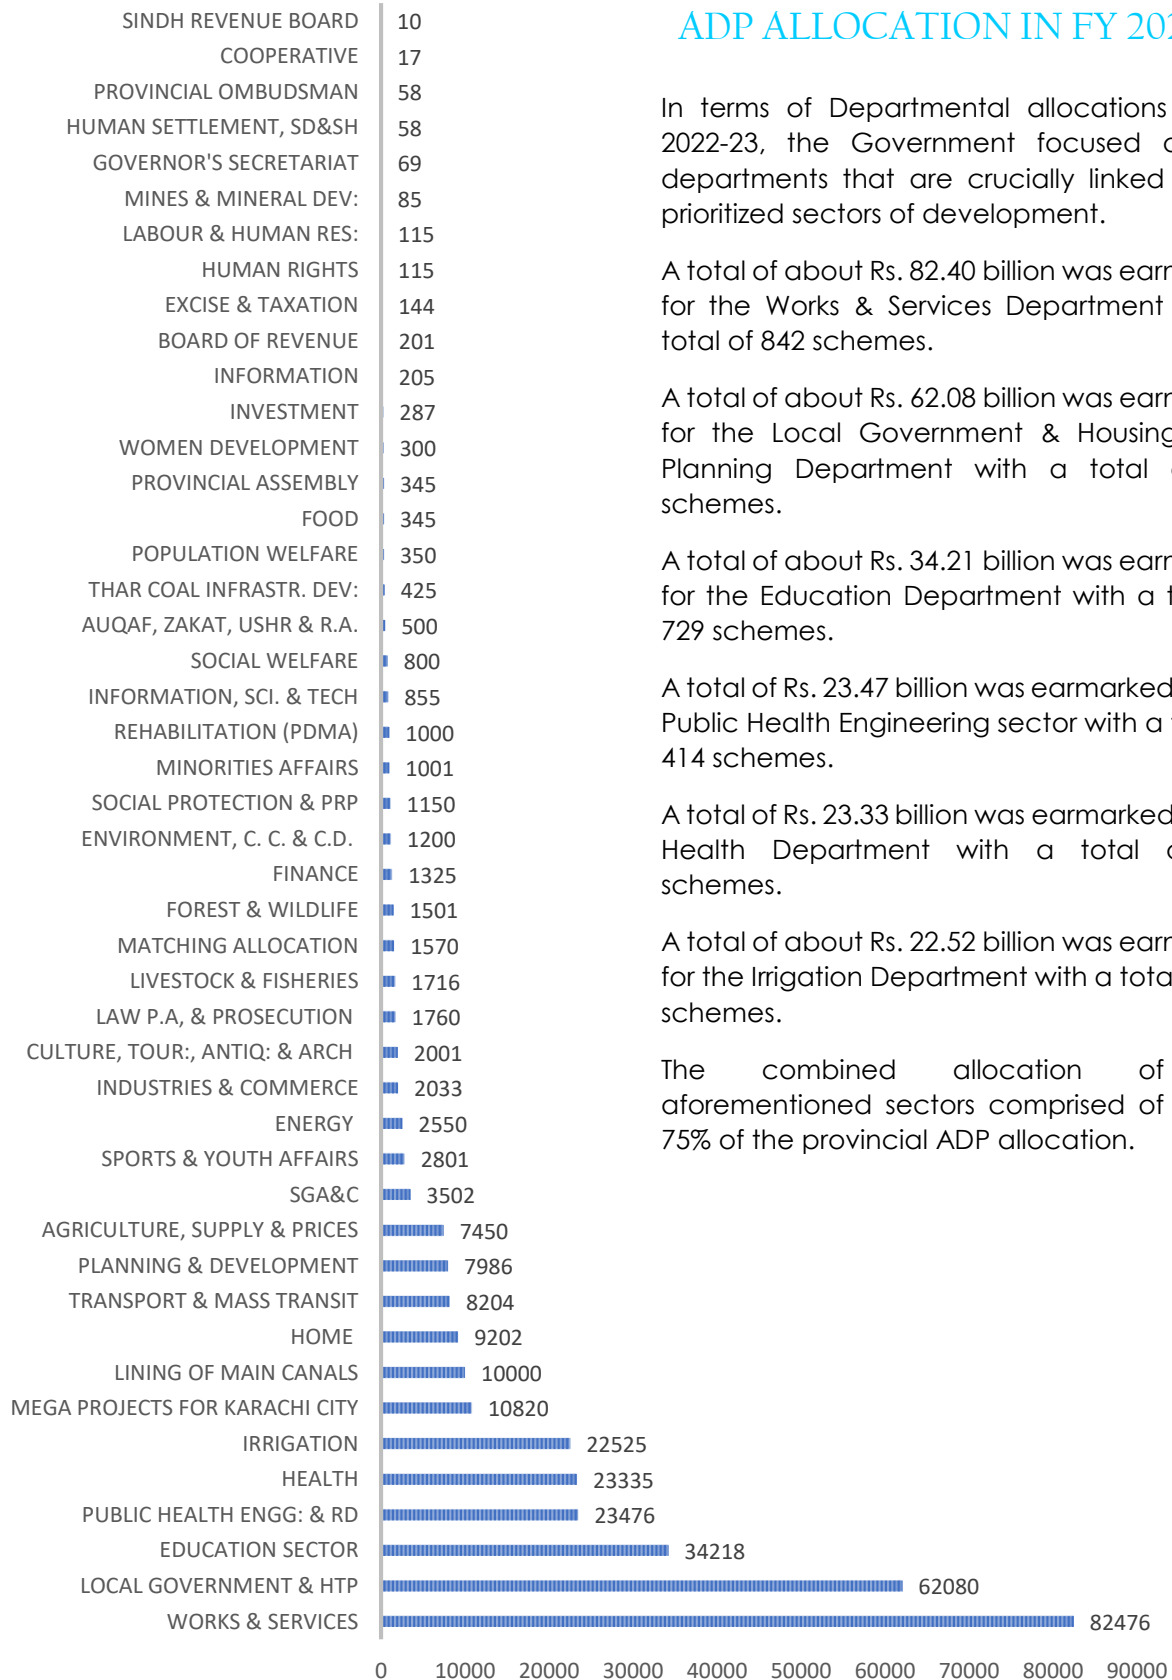

In terms of Departmental allocations for FY 2022-23, the Government focused on key departments that are crucially linked to the prioritized sectors of development.

A total of about Rs. 82.40 billion was earmarked for the Works & Services Department with a total of 842 schemes.

A total of about Rs. 62.08 billion was earmarked for the Local Government & Housing Town Planning Department with a total of 768 schemes.


A total of about Rs. 34.21 billion was earmarked for the Education Department with a total of 729 schemes.

A total of Rs. 23.47 billion was earmarked for the Public Health Engineering sector with a total of 414 schemes.

A total of Rs. 23.33 billion was earmarked for the Health Department with a total of 219 schemes.

A total of about Rs. 22.52 billion was earmarked for the Irrigation Department with a total of 198 schemes.

The combined allocation of the aforementioned sectors comprised of almost 75% of the provincial ADP allocation.

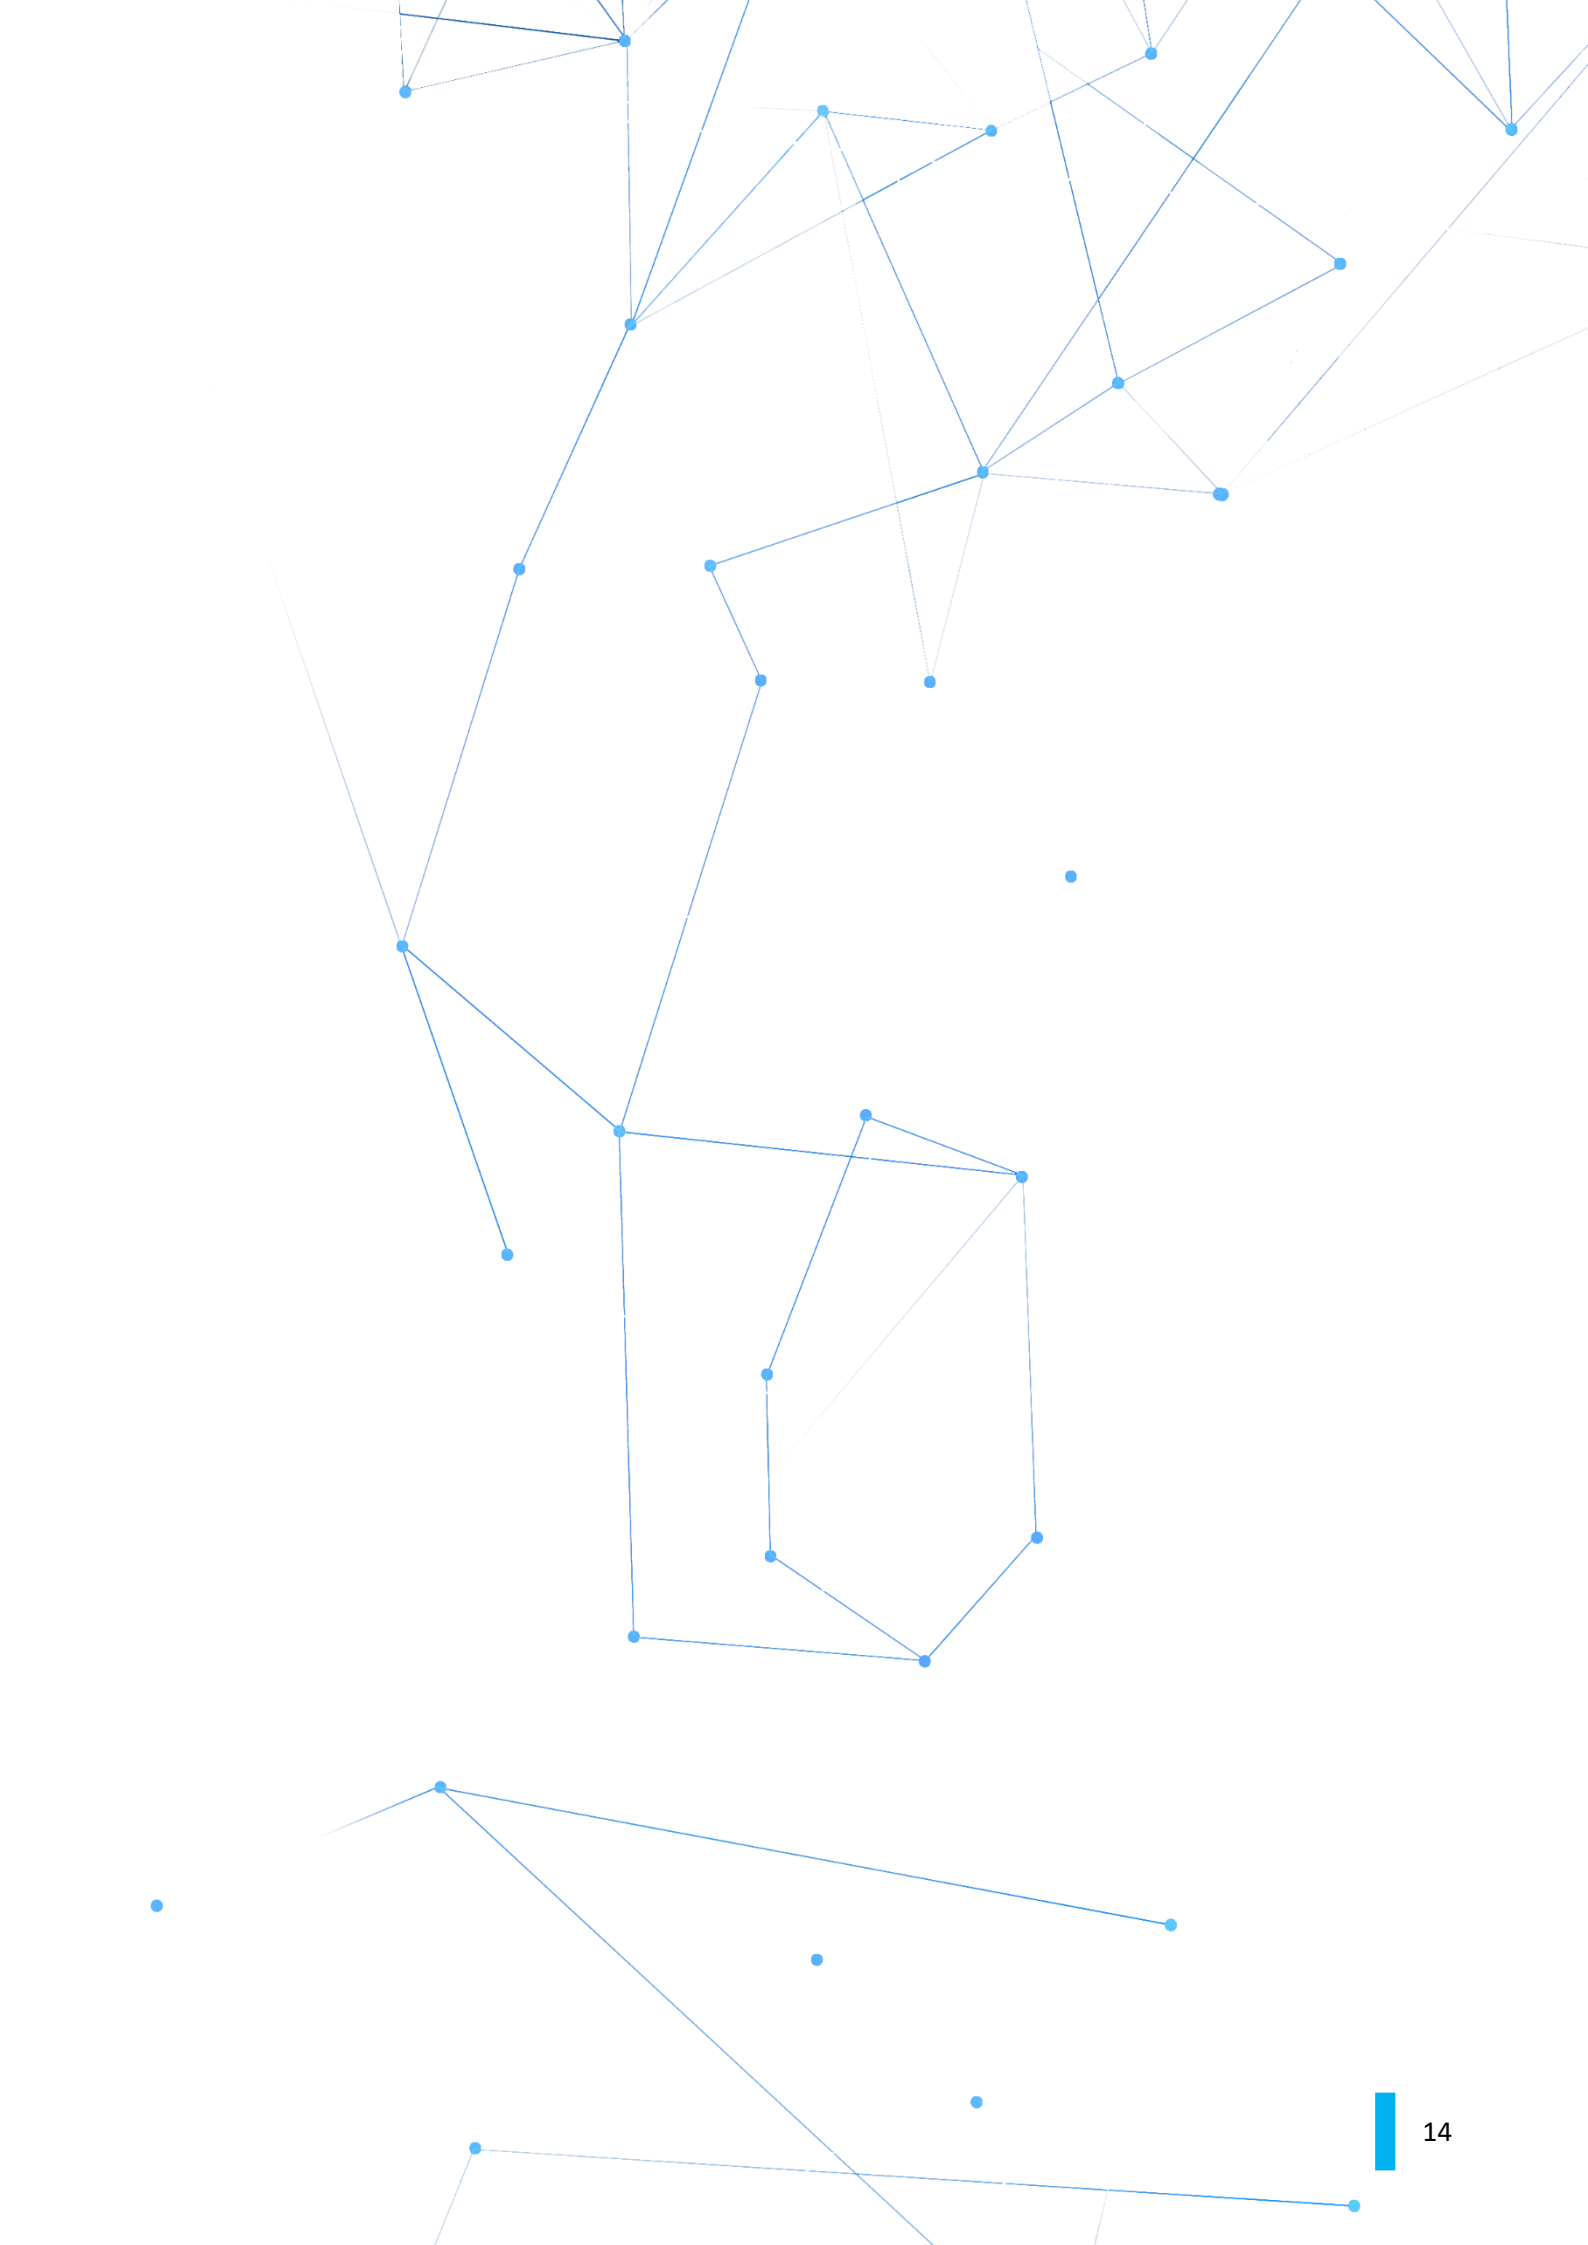




# OVERVIEW



DEVELOPMENT

# AGRICULTURE

Agriculture is the backbone of the economy of Pakistan and Sindh contributes due share in agriculture sector of the country. The primary domain of the Agriculture, Supply & Prices Department of GoS is to transform Sindh's agriculture sector into a competitive, productive and sustainable segment of the economy with modern agricultural practices and technology. Throw-Forward for the department as of June, 2022 was Rs. 20,984 million with Rs. 7,450 million allocated FY 2022-23. This translates into a throw-forward to allocation ratio of 2.8:1 The Financial releases were Rs. 5,540 million of which Rs.5,245 million were utilized to complete the developmental schemes for the year. 08 schemes were monitored for the Agriculture Department with 10 monitoring visits.

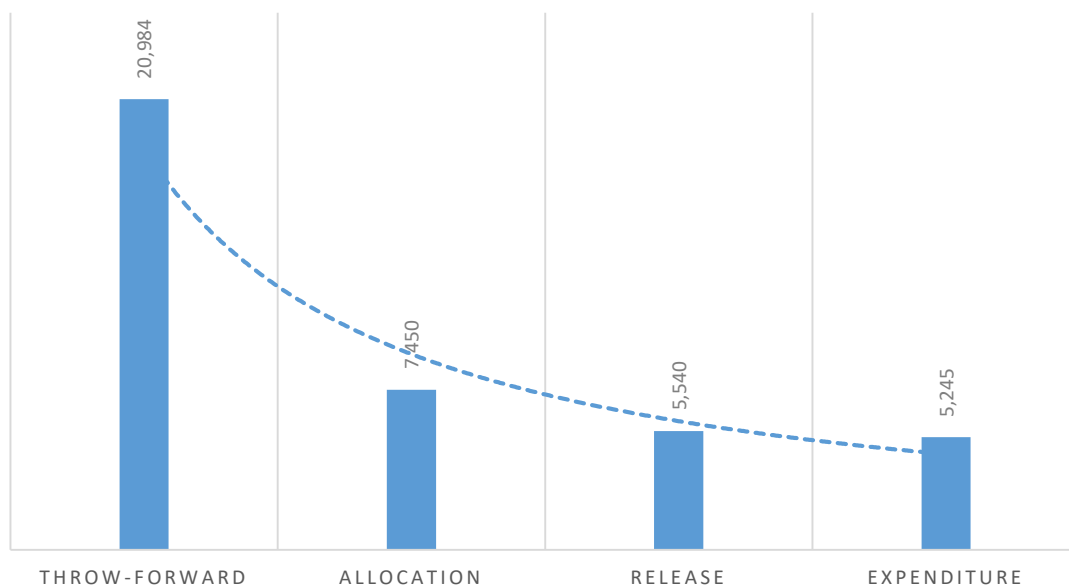


## Monitoring Status



# EDUCATION

Education is one of the priority sectors of the Government of Sindh comprising of 5 Administrative Departments i.e., School Education & literacy Department, College Education Department, Universities and Boards Department, Department of Empowerment of Persons with Disabilities (DEPD), and Sindh Technical Education & Vocational Training Authority (STEVTa). Throw-Forward for the department as of June, 2022 was Rs. 102,900 million with Rs. 34,218 million allocated for FY 2022-23. This translates into a throw-forward to allocation ratio of 3.0:1. The releases amounted to Rs. 14,956 million out of which an expenditure of Rs.13,976 million was incurred. 56 schemes of the Education Sector were monitored with 65 monitoring visits.

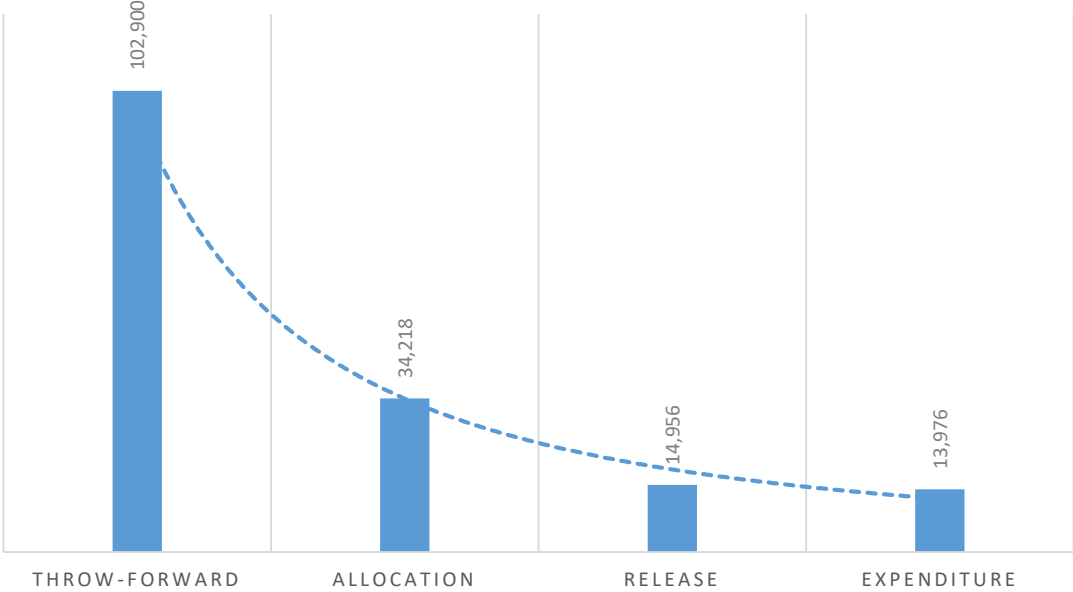


## Monitoring Status



# HEALTH

The Provincial Health department of GoS is responsible for ensuring quality healthcare services for the province with functions including administration, execution, legislation and regulation of the healthcare institutions. Throw-Forward for the department as of June, 2022 was Rs. 61,684 million with Rs. 23,335 million allocated for FY 2022-23. This translates into a throw-forward to allocation ratio of 2.6:1. The releases were Rs. 5,930 million of which the department was able to utilize Rs. 4,661 million in FY 2022-23. 31 schemes of the Health Department were monitored with 40 visits.

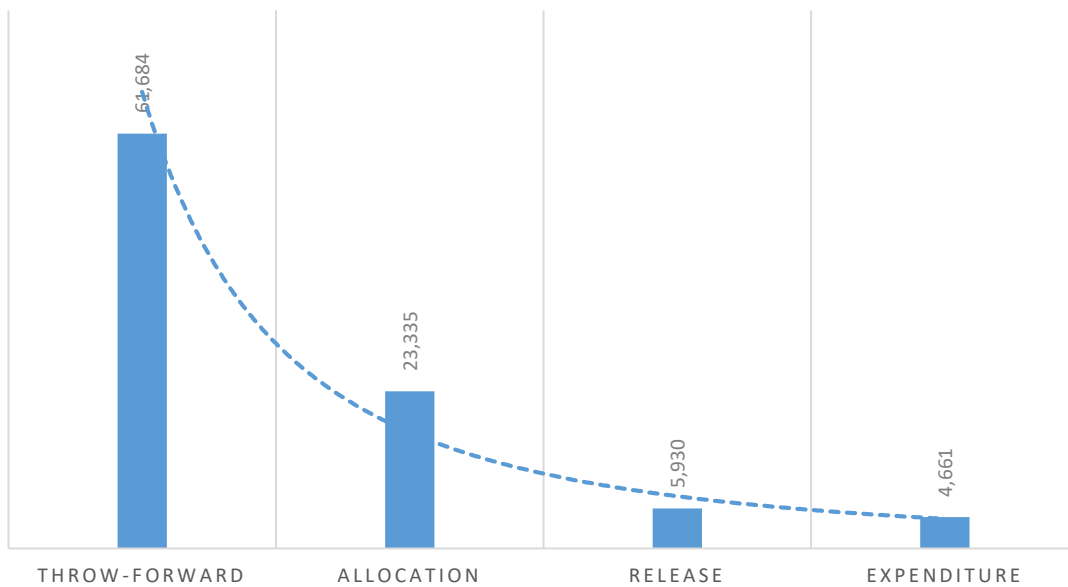


## Monitoring Status



# HOME

Home Department plays a pivotal role in maintenance of law & order and internal security. In addition, there is long list of traditional functions performed by the Department. The aforementioned role requires constant support from various attached departments which include Police Department, Inspectorate General of Prisons and Directorate of Civil Defense and Directorate of Reclamation & Probation. Throw-Forward for the department as of June, 2022 was Rs. 24,210 million with Rs. 9,202 million allocated for FY 2022-23. This translates into a throw-forward to allocation ratio of 2.6:1. The releases amounted to Rs. 2,849 million. The expenditures incurred were Rs. 2,655 million. 07 schemes of Home Department were monitored with 10 monitoring visits.

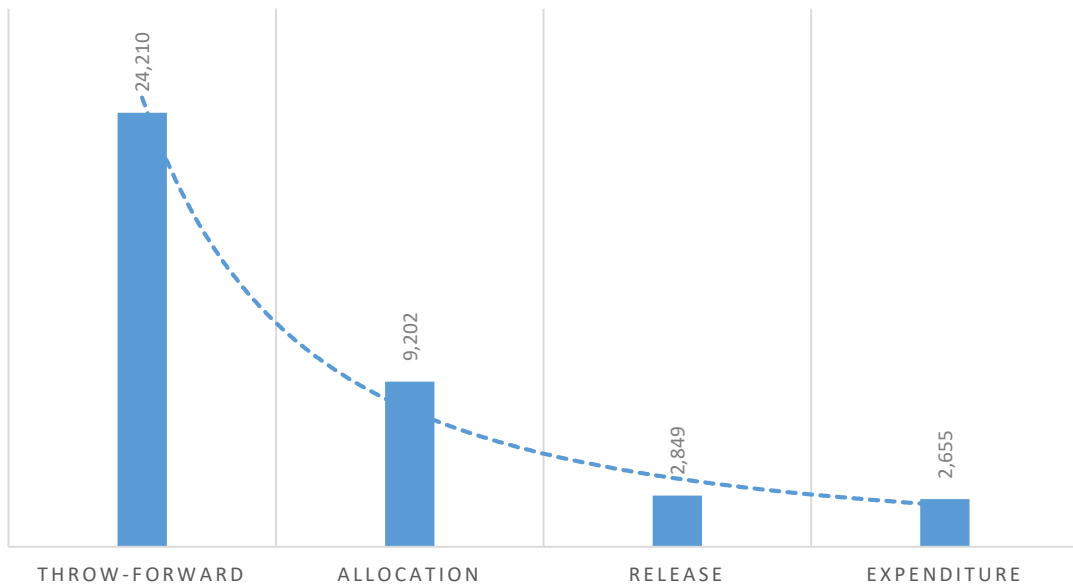

## Monitoring Status




ADP Allocations  
in billion Rupees

Schemes Monitored

Monitoring Visits

# IRRIGATION

Irrigation Department is responsible for operations, maintenance, development & management of irrigation network, surface drainage system and tube-wells in addition to flood control and rain water harvesting. Throw-Forward for the department as of June, 2022 was Rs. 111,673 million with Rs. 22,525 million allocated for FY 2022-23. This translates into a throw-forward to allocation ratio of 5.0:1. The releases against which were Rs. 23,315 million. The department was able to utilize Rs.22,640 million during the year. 18 schemes of the Irrigation Department were monitored with 18 monitoring visits.

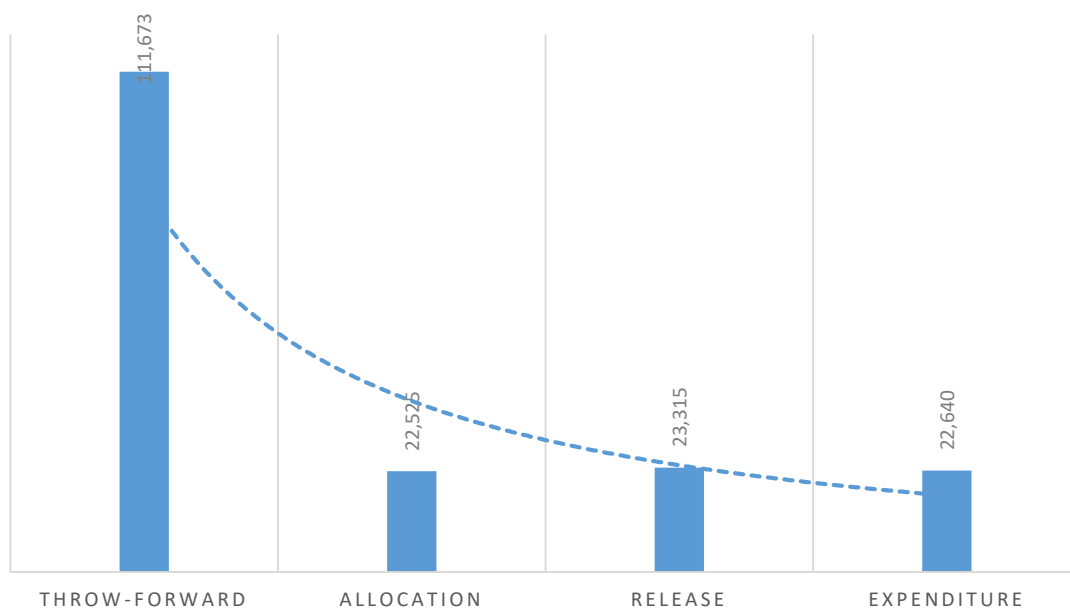

## Monitoring Status




ADP Allocations  
in billion Rupees

Schemes Monitored

Monitoring Visits

# LAW, P.A. & PROSECUTION

The Law, Parliamentary Affairs & Criminal Prosecution department deals with legal matters pertaining to government business. Throw-Forward for the department as of June, 2022 was Rs. 5,388 million with Rs. 1,760 million allocated for FY 2022-23. This translates into a throw-forward to allocation ratio of 3.0:1. The releases amounted to Rs. 1,539 million out of which around Rs. 1,357 million were utilized. 03 schemes of Law, P.A. & Prosecution Department were monitored with 04 monitoring visits.

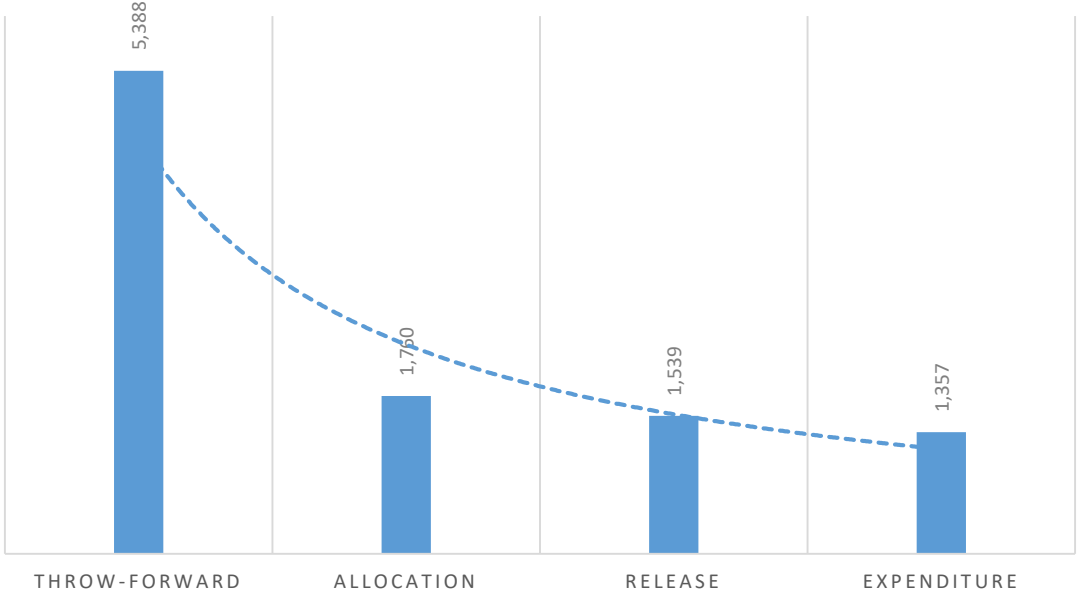


## Monitoring Status



# LIVESTOCK AND FISHERIES

Livestock & Fisheries Department caters to the requirements of livestock sector in the province. Livestock is increasingly becoming a very important sector of national economy, contributing even more than all the other agricultural crops combined. Throw-Forward for the department as of June, 2022 was Rs. 7,616 million with Rs. 1,716 million allocated for FY 2022-23. This translates into a throw-forward to allocation ratio of 4.4:1. The releases were Rs. 1,207 million. The expenditures incurred were Rs. 1,083 million. 02 schemes of Livestock & Fisheries Department were monitored with 05 monitoring visits.

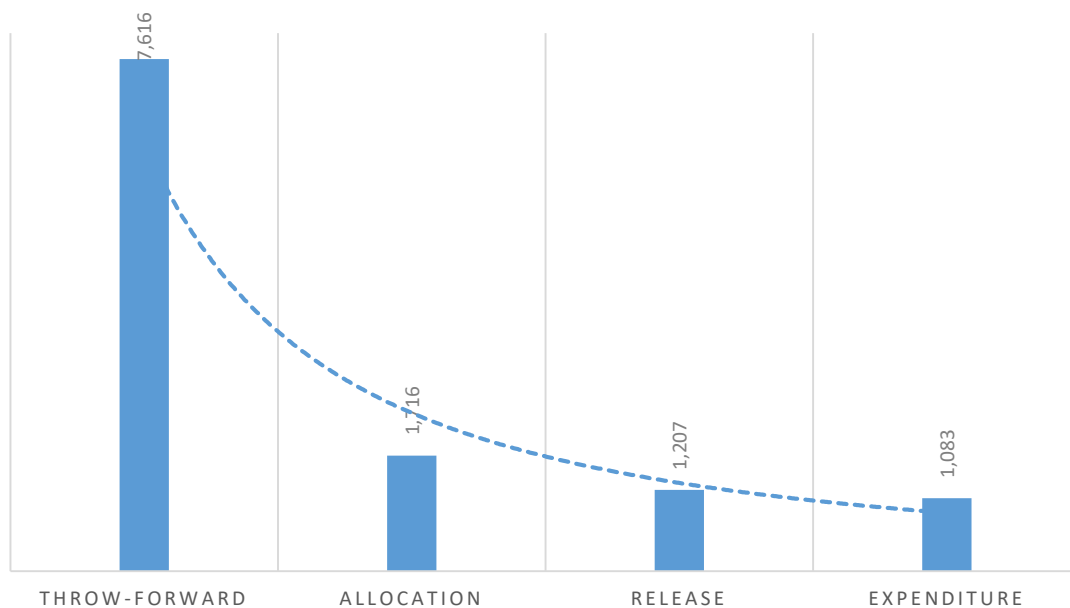


## Monitoring Status



# LOCAL GOVERNMENT

The Local Government department of GoS is responsible to promote good governance, effective delivery of services and transparent decision-making through institutionalized participation of the people at local level. Throw-Forward for the department as of June, 2022 was Rs. 157,226 million with Rs. 62,080 million allocated for FY 2022-23. This translates into a throw-forward to allocation ratio of 2.5:1. The releases were recorded at Rs.38,641 million out of which Rs. 36,681 million were utilized. 62 schemes of the Local Government Department were monitored with 76 monitoring visits.

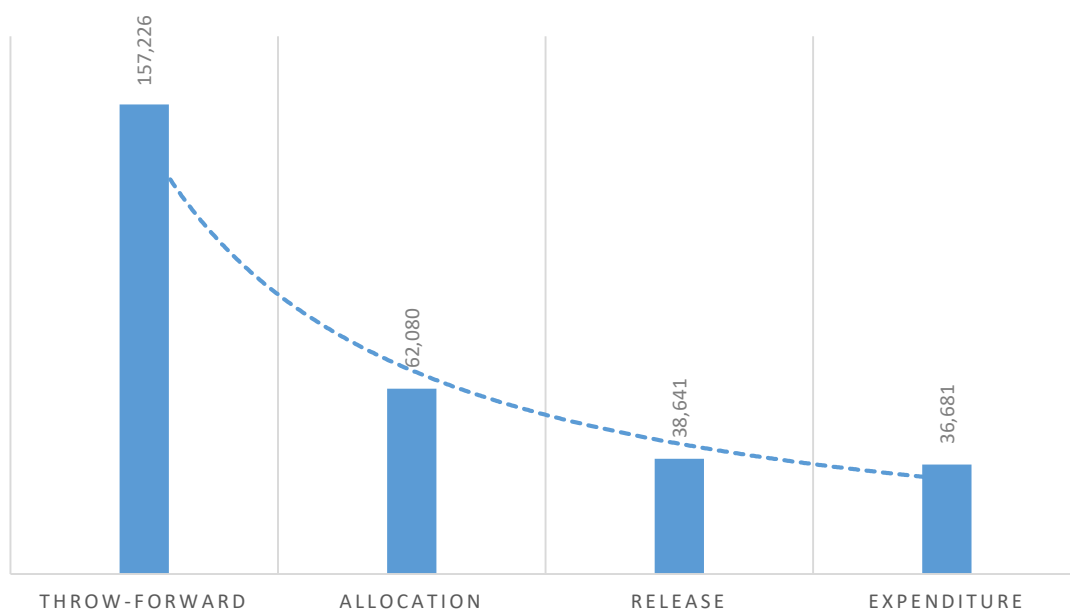


## Monitoring Status



# PUBLIC HEALTH ENGINEERING & RURAL DEVELOPMENT

The Public Health Engineering & Rural Development Department works on designing, planning and executing water supply and drainage schemes in urban and rural areas of Sindh. Throw-Forward for the department as of June, 2022 was Rs. 52,109 million with Rs. 23,476 million allocated for FY 2022-23. This translates into a throw-forward to allocation ratio of 2.2:1. The releases were recorded at Rs.14,086 million out of which Rs. 12,552 million were utilized. 60 schemes of PHE & RD Department were monitored with 68 monitoring visits.

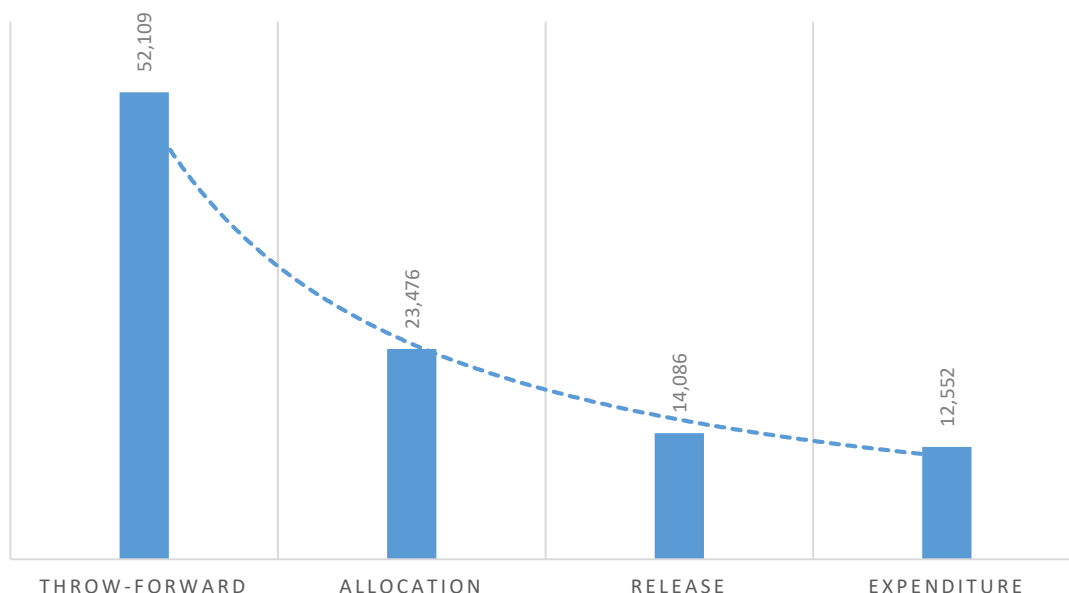


## Monitoring Status



# WORKS & SERVICES

Works & Services department is directly responsible for development initiatives that are concerned with development works such as roads, bridges and other related infrastructural initiatives of the province. Throw-Forward for the department as of June, 2022 was Rs. 135,219 million with Rs. 82,476 million allocated for FY 2022-23. This translates into a throw-forward to allocation ratio of 1.6:1. The financial releases were Rs. 76,718 million out of which the expenditures incurred were 75,430 million. 92 schemes of Works & Services Department were monitored with 97 monitoring visits.

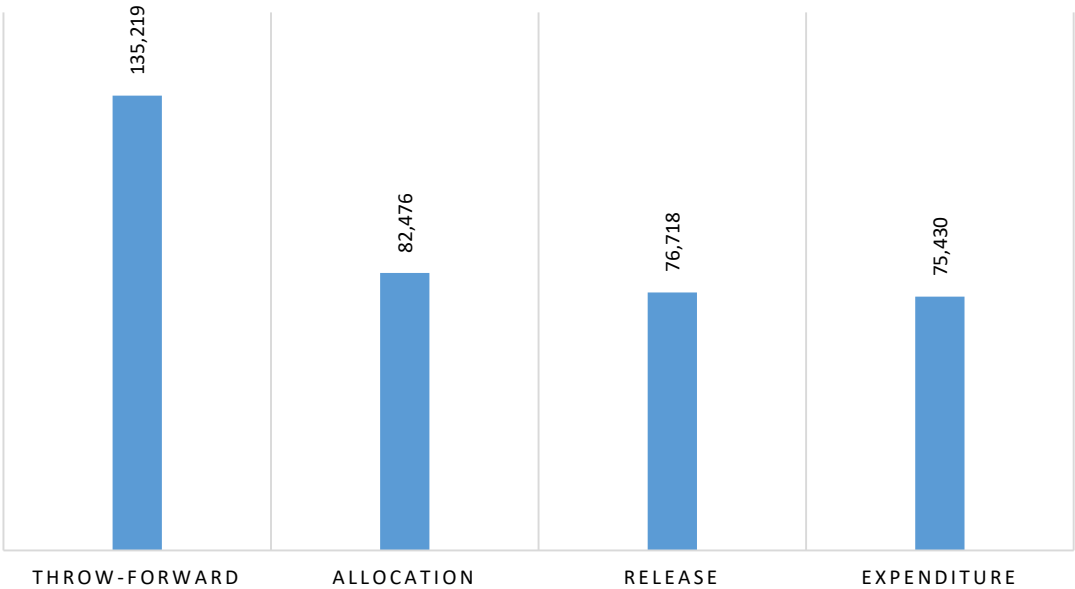

## Monitoring Status





**KEY**




**PERFORMANCE  
INDICATOR**

# MONITORING PROGRESS

MEC made a total of 542 field monitoring visits to the 465 schemes during FY 2022-23. This essentially meant revisiting several schemes to track monitoring during the execution phase, ensure compliance of unsatisfactory observations and improvement in the progress indicators. Out of the 542 visits, 344 visits were found satisfactory (63%) and 198 visits were found unsatisfactory (37%). Number of compliances received was 91 (46% of unsatisfactory visits).


## Monitoring Visits Status

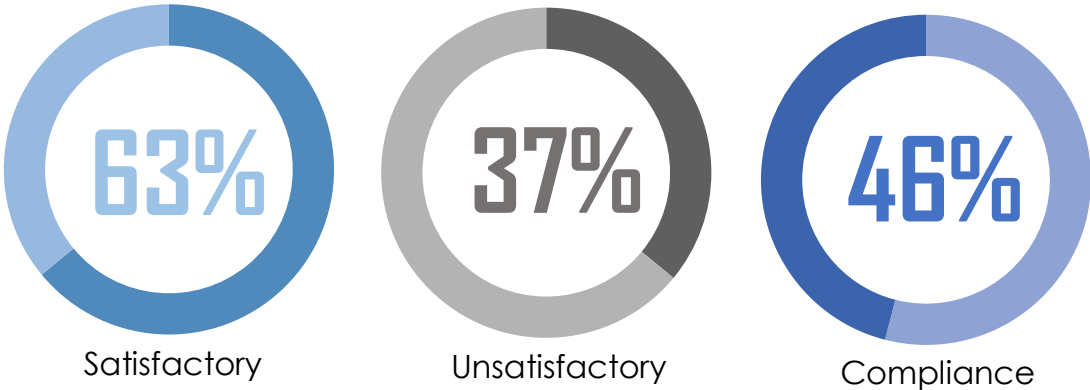

# STATUS OF SCHEMES MONITORED

## FY 2022-23

MEC Team monitored 465 schemes during FY 2022-23, out of which 342 schemes (74%) were found satisfactory and 123 schemes (26%) were found unsatisfactory.

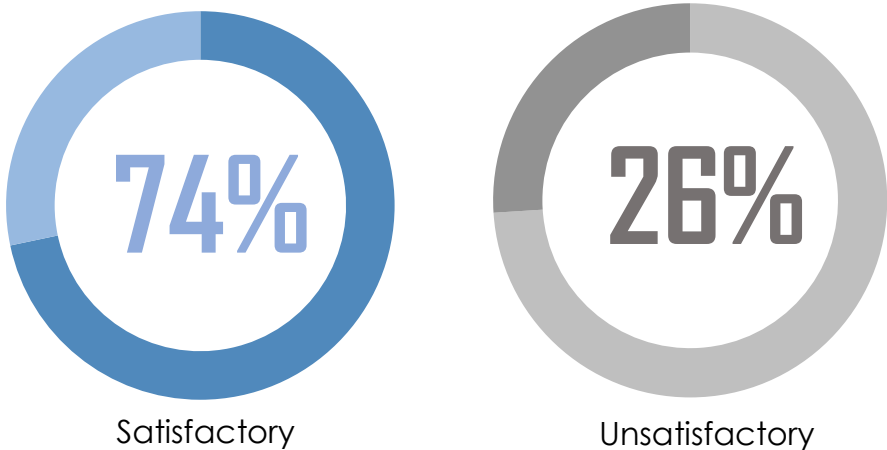

# DEPARTMENT-WISE MONITORING VISITS IN FY 2022-23

S.#.	Departments / Sectors	Number of Visits	Satisfactory	Percentage	Un-Satisfactory	Percentage	Compliance Received	Percentage
1	Agriculture, GOS	10	7	70	3	30	2	67
2	Auqaf, GOS	8	5	63	3	38	3	100
3	Cooperative, GOS	1	0	0	1	100	0	0
4	Culture, GOS	14	9	64	5	36	3	60
5	Education and Literacy, GOS	65	46	71	19	29	10	53
6	Energy, GOS	4	3	75	1	25	0	0
7	Excise & Taxation, GOS	3	1	33	2	67	0	0
8	Food, GOS	15	1	7	14	93	4	29
9	Forest, Wildlife & CDA, GOS	14	11	79	3	21	1	33
10	Health, GOS	40	18	45	22	55	8	36
11	Home, GOS	10	2	20	8	80	6	75
12	Human Settlement, Spatial Development & Social Housing	1	0	0	1	100	0	0
13	Industrial & Commerce, GOS	2	1	50	1	50	0	0
14	Information & Archives, GOS	2	0	0	2	100	0	0
15	Information, Science & Technology, GOS	1	1	100	0	0	0	0
16	Irrigation (Water & Drainage), GOS	18	14	78	4	22	0	0
17	Karachi Metropolitan Corporation, KWSB	3	2	67	1	33	0	0
18	Law P.A. & Prosecution	4	3	75	1	25	1	100
19	Lining of Main Canals	7	5	71	2	29	2	100
20	Livestock and Fisheries, GOS	5	3	60	2	40	2	100
21	Local Government, GOS	76	44	58	32	42	19	59
22	Mega Schemes for Karachi City	6	5	83	1	17	1	100
23	Minorities & Affairs, GOS	12	9	75	3	25	0	0
24	Physical Planning & Housing (Buildings), GOS	4	2	50	2	50	1	50
25	Planning & Development, GoS	2	1	50	1	50	0	0
26	Population Welfare, GOS	6	5	83	1	17	1	100
27	Public Health Engineering, GOS	68	48	71	20	29	11	55

S.#.	Departments / Sectors	Number of Visits	Satisfactory	Percentage	Un-Satisfactory	Percentage	Compliance Received	Percentage
28	Rehabilitation (PDMA), GOS	3	2	67	1	33	0	0
29	Rural Development, GOS	11	9	82	2	18	0	0
30	S.G.A.and Coordination, GOS	3	2	67	1	33	0	0
31	Sports & Youth Affairs, GOS	15	10	67	5	33	4	80
32	STEVTA, GOS	2	2	100	0	0	0	0
33	Universities and Boards	6	5	83	1	17	1	100
34	Women Development, GOS	4	2	50	2	50	1	50
35	Work and Service, GOS	97	66	68	31	32	10	32
<b>TOTAL</b>		<b>542</b>	<b>344</b>	<b>63</b>	<b>198</b>	<b>37</b>	<b>91</b>	<b>46</b>

In terms of the Line Departments with respect to monitoring, MEC focused on ten prioritized Departments which accounted for 74% (342 out of 465 schemes) of total schemes monitored and 73% (397 out of 542 visits) of the total monitoring visits (including fresh visits, re-visits and compliance visits)

The prioritized departments included Agriculture Department which is comprised of 08 schemes of Agriculture during FY 2022-23 with 10 total monitoring visits. Out of 08 schemes, 07 (88%) were found to be satisfactory while 01 schemes (12%) were found unsatisfactory. Out of the 10 monitoring visits, 07 visits were satisfactory (70%) and 03 were unsatisfactory (30%).

MEC team monitored the schemes of Education Department comprised of 56 schemes monitored during FY 2022-23 with 65 total monitoring visits. Out of 56 schemes, 46 (82%) were found to be satisfactory and 10 schemes (18%) were found to be unsatisfactory. Out of the 65 monitoring visits, 46 visits were satisfactory (71%) and 19 were unsatisfactory (29%).

MEC monitored 11 schemes of Forest, Wildlife & CDA Department during FY 2022-23 with 14 total monitoring visits. Out of 11 schemes, 11 (100%) were found to be satisfactory and none schemes found to be unsatisfactory. Out of the 14 monitoring visits, 11 visit were satisfactory (79%) and 03 were unsatisfactory (21%).

MEC visited 31 development schemes of Health Department during FY 2022-23 with 40 total monitoring visits. Out of 31 schemes, 18 (58%) were found to be satisfactory and 13 schemes (42%) were found to be unsatisfactory. Out of the 40 monitoring visits, 18 visits were satisfactory (45%) and 22 were unsatisfactory (55%).

Visits to Irrigation Department comprised of 18 monitored schemes during FY 2022-23 with 18 total monitoring visits. Out of 18 schemes, 14 (78%) were found to be satisfactory and 04 schemes (22%) were found to be unsatisfactory. Out of the 18 monitoring visits, 14 visits were satisfactory (78%) and 04 were unsatisfactory (22%).

In case of Law, Parliamentary Affairs and Criminal Prosecution Department visits comprised of 03 schemes monitored during FY 2022-23 with 04 total monitoring visits. Out of 03 schemes, 03 (100%) were found to be satisfactory and none schemes were found to be unsatisfactory. Out of the 04 monitoring visits, 03 visits were satisfactory (75%) and 01 were unsatisfactory (25%).

Monitoring of schemes of Livestock & Fisheries Department comprised of 02 monitored schemes during FY 2022-23 with 05 total monitoring visits. Out of 02 schemes, 02 (100%) were found to be satisfactory and none schemes were found to be unsatisfactory. Out of the 05 monitoring visits, 03 visits were satisfactory (60%) and 02 were unsatisfactory (40%).

MEC team's visit to the schemes of Local Government Department comprised of 62 schemes during FY 2022-23 with 76 total monitoring visits. Out of 62 schemes, 43 (69%) were found to be satisfactory and 19 schemes (31%) were found to be unsatisfactory. Out of the 76 monitoring visits, 44 visits were satisfactory (58%) and 32 were unsatisfactory (42%).

Monitoring visits to Public Health Engineering Department comprised of 60 monitored schemes during FY 2022-23 with 68 total monitoring visits. Out of 60 schemes, 48 (80%) were found to be satisfactory and 12 schemes (20%) were found to be unsatisfactory. Out of the 68 monitoring visits, 48 visits were satisfactory (71%) and 20 were unsatisfactory (29%).

Visits to Works & Services Department comprised of 92 monitored schemes during FY 2022-23 with 97 total monitoring visits. Out of 92 schemes, 66 (72%) were found to be satisfactory and 26 schemes (28%) were found to be unsatisfactory. Out of the 97 monitoring visits, 66 visits were satisfactory (68%) and 31 were unsatisfactory (32%).

## NUMBER OF SCHEMES MONITORED IN FY 2022-23

S.#.	Departments / Sectors	Number of Schemes Visited	Satisfactory	Percentage	Un-Satisfactory	Percentage
1	Agriculture, GOS	8	7	88	1	13
2	Auqaf, GOS	6	5	83	1	17
3	Cooperative, GOS	1	0	0	1	100
4	Culture, GOS	11	9	82	2	18
5	Education and Literacy, GOS	56	46	82	10	18
6	Energy, GOS	4	3	75	1	25
7	Excise & Taxation, GOS	3	1	33	2	67
8	Food, GOS	11	1	9	10	91
9	Forest, Wildlife & CDA, GOS	11	11	100	0	0
10	Health, GOS	31	18	58	13	42
11	Home, GOS	7	2	29	5	71
12	Human Settlement, Spatial Development & Social Housing	1	0	0	1	100
13	Industrial & Commerce, GOS	2	1	50	1	50
14	Information & Archives, GOS	2	0	0	2	100
15	Information, Science & Technology, GOS	1	1	100	0	0
16	Irrigation (Water & Drainage), GOS	18	14	78	4	22
17	Karachi Metropolitan Corporation, KWSB	3	2	67	1	33


S.#.	Departments / Sectors	Number of Schemes Visited	Satisfactory	Percentage	Un-Satisfactory	Percentage
18	Law P.A. & Prosecution	3	3	100	0	0
19	Lining of Main Canals	5	5	100	0	0
20	Livestock and Fisheries, GOS	2	2	100	0	0
21	Local Government, GOS	62	43	69	19	31
22	Mega Schemes for Karachi City	5	5	100	0	0
23	Minorities & Affairs, GOS	12	9	75	3	25
24	Physical Planning & Housing (Buildings), GOS	3	2	67	1	33
25	Planning & Development, GoS	2	1	50	1	50
26	Population Welfare, GOS	5	5	100	0	0
27	Public Health Engineering, GOS	60	48	80	12	20
28	Rehabilitation (PDMA), GOS	3	2	67	1	33
29	Rural Development, GOS	11	9	82	2	18
30	S.G.A.and Coordination, GOS	3	2	67	1	33
31	Sports & Youth Affairs, GOS	11	10	91	1	9
32	STEVA, GOS	2	2	100	0	0
33	Universities and Boards	5	5	100	0	0
34	Women Development, GOS	3	2	67	1	33
35	Work and Service, GOS	92	66	72	26	28
<b>TOTAL</b>		<b>465</b>	<b>342</b>	<b>74</b>	<b>123</b>	<b>26</b>

## DEPARTMENTAL PERFORMANCE

MEC team made 542 monitoring visits to 465 ongoing schemes in FY 2022-23 to determine whether the scheme has been satisfactory or unsatisfactory in terms of financial and physical progress. Overall, 342 schemes (74%) were termed satisfactory and 123 schemes (26%) were found unsatisfactory. The M&E Cell working under P&DD schedule the visit plan on monthly basis which is approved a week before the following month. MEC team starts collecting data from the executing agencies and prepare the plan accordingly, liaison with the concerned engineers and project directors. With the use of experienced team and modern equipment, MEC strive hard to achieve their objective to provide factual position of development schemes helping heads of administrative departments and other government agencies to take corrective measures to improve the public sector delivery.

The following graph illustrates the performance of the Line Departments in terms of the relative proportion of schemes termed satisfactory and unsatisfactory.

# Departmental Performance Pyramid (%)

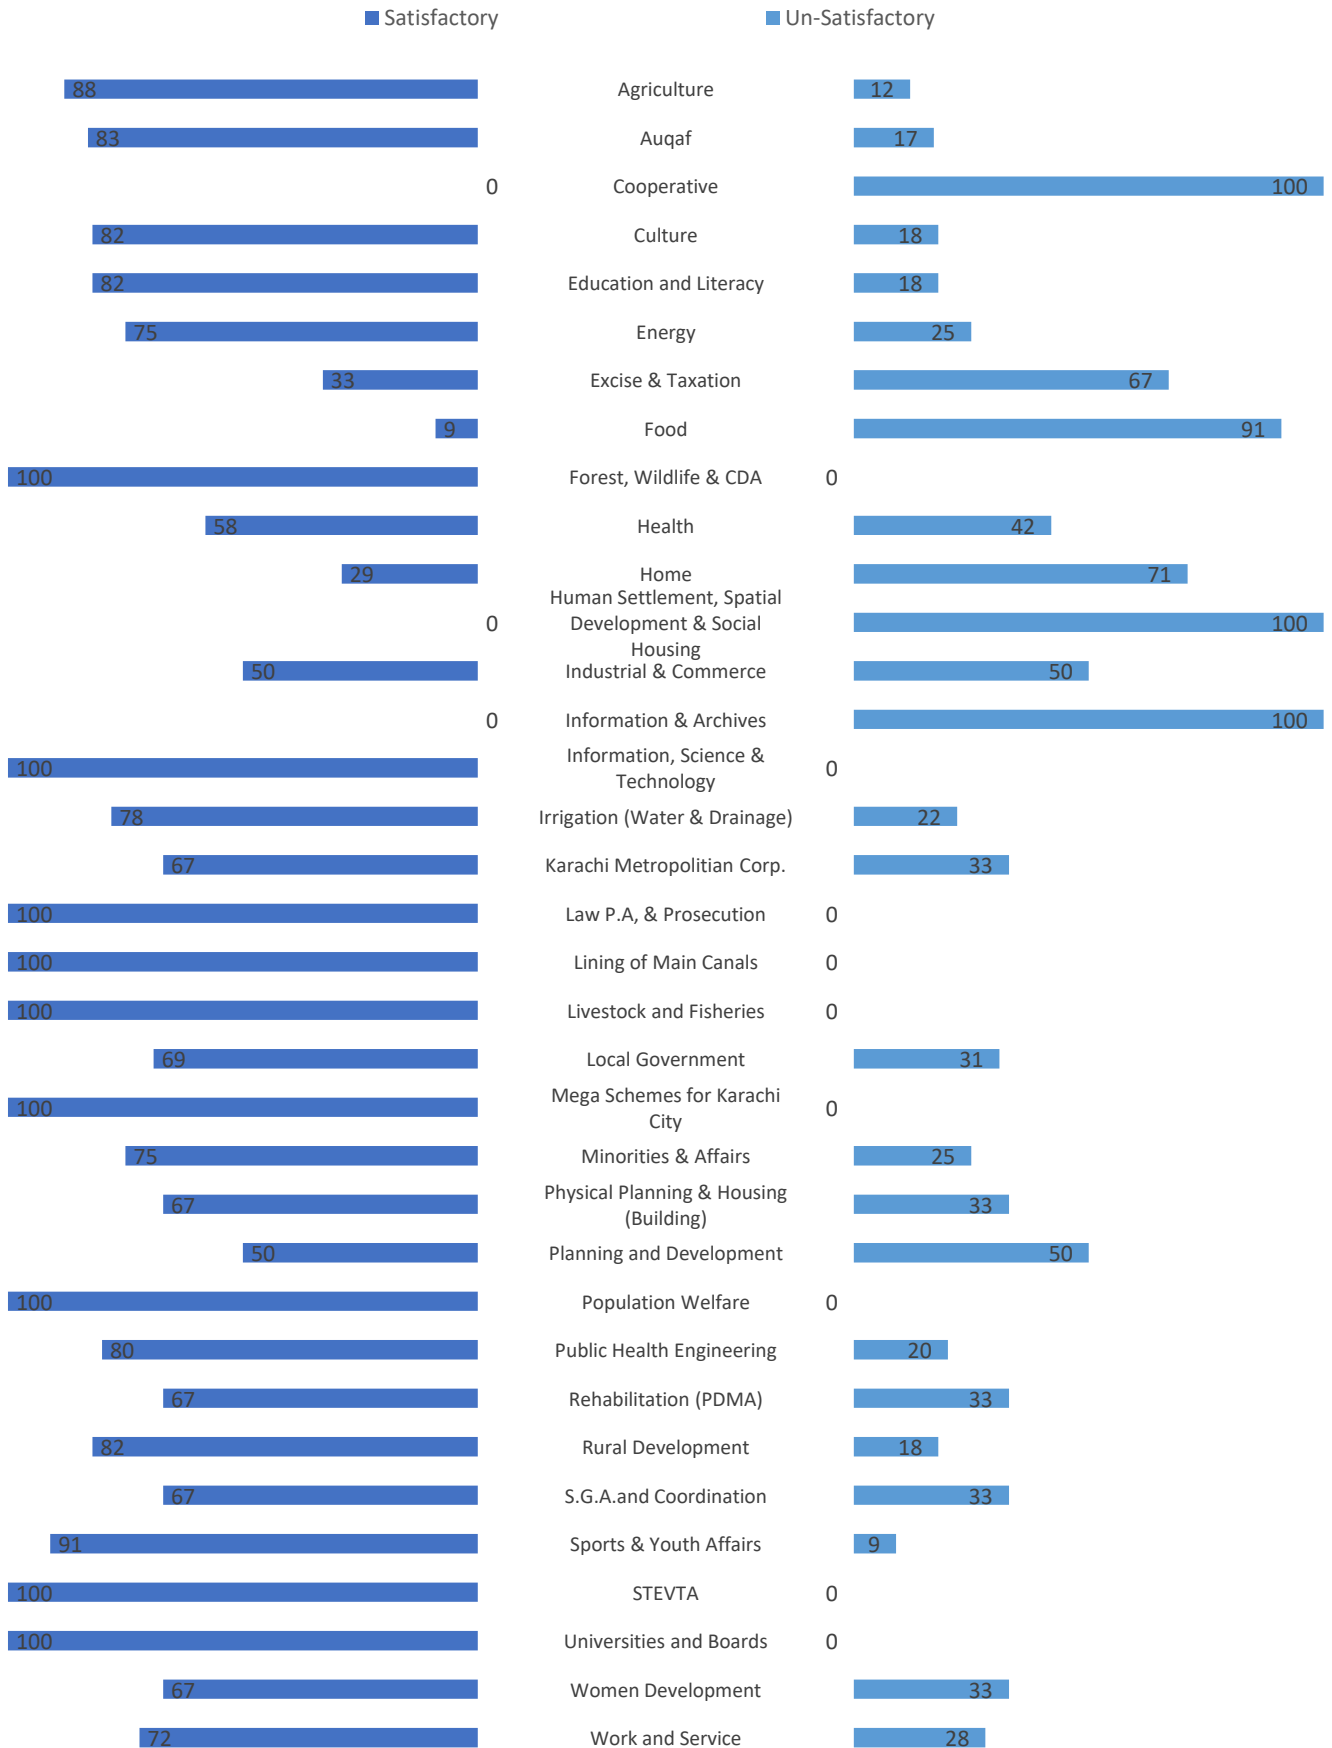

# MONITORING BY REGIONAL OFFICES

Disaggregating the monitoring visits and schemes monitored by region illustrates interesting findings about the regional progress of development schemes.

In Karachi Region, MEC Team monitored 93 schemes with 115 monitoring visits. Out of the 93 schemes monitored, 67 were found to be satisfactory (72%) and 26 schemes were found unsatisfactory (28%). Out of the 115 monitoring visits, 68 visits were found satisfactory (59%) and 47 visits were unsatisfactory (41%).

## Monitoring Summary of Region-Wise Schemes in FY 2022-23

Region	Schemes	Satisfactory	Unsatisfactory
Hyderabad	147	109	38
Sukkur	80	62	18
Karachi	93	67	26
Larkana	145	104	41
<b>Total</b>	<b>465</b>	<b>342</b>	<b>123</b>

In Hyderabad Region, MEC Team monitored 147 schemes with 171 monitoring visits. Out of the 147 schemes monitored, 109 were found to be satisfactory (74%) and 38 schemes were found unsatisfactory (26%). Out of the 171 monitoring visits, 110 visits were found satisfactory (64%) and 61 visits were unsatisfactory (36%).


In Larkana Region, MEC Team monitored 145 schemes with 165 monitoring visits. Out of the 145 schemes monitored, 104 were found to be satisfactory (72%) and 41 schemes were found unsatisfactory (28%). Out of the 165 monitoring visits, 104 visits were found satisfactory (63%) and 61 visits were unsatisfactory (37%).

In Sukkur Region, MEC Team monitored 80 schemes with 91 monitoring visits. Out of the 80 schemes monitored, 62 were found to be satisfactory (78%) and 18 schemes were found unsatisfactory (22%). Out of the 91 monitoring visits, 62 visits were found satisfactory (68%) and 29 visits were unsatisfactory (32%).

## Regional Monitoring Visits in FY 2022-23


Region	Schemes	Satisfactory	Unsatisfactory
Hyderabad	171	110	61
Sukkur	91	62	29
Karachi	115	68	47
Larkana	165	104	61
<b>Total</b>	<b>542</b>	<b>344</b>	<b>198</b>

## REGIONAL MONITORING VISITS

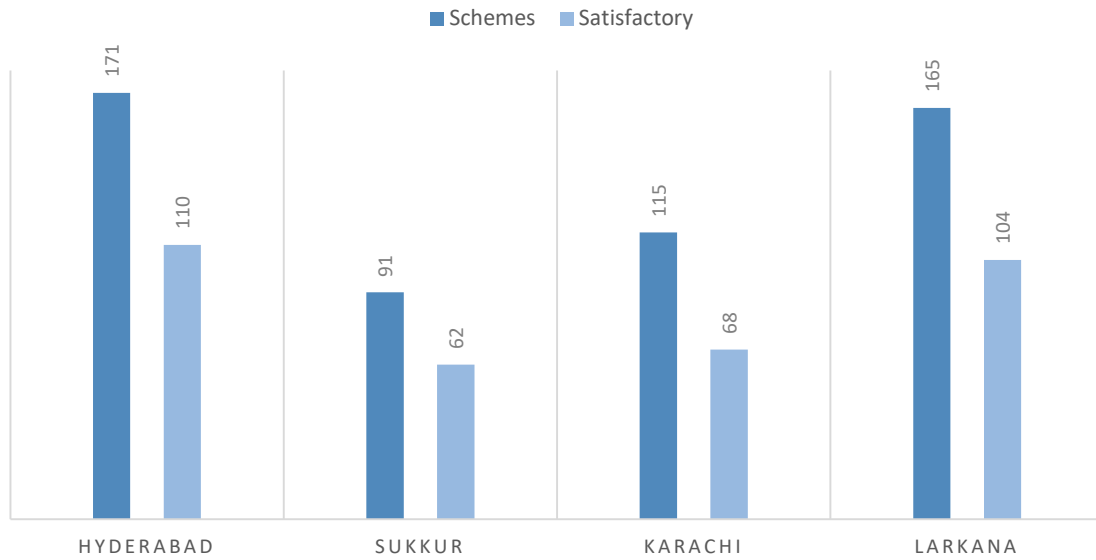

## FIELD MONITORING OVER THE YEARS

MEC Team visited a total of 465 schemes during FY 2022-23 with several re-visits for a number of schemes. The total number of monitoring visits accumulated to 542. The total ADP portfolio for FY 2022-23 comprised of 4158 schemes with 2506 ongoing and 1652 new schemes. The graph below illustrates the field monitoring trend over the years in relation to the total ADP portfolio for the corresponding year.

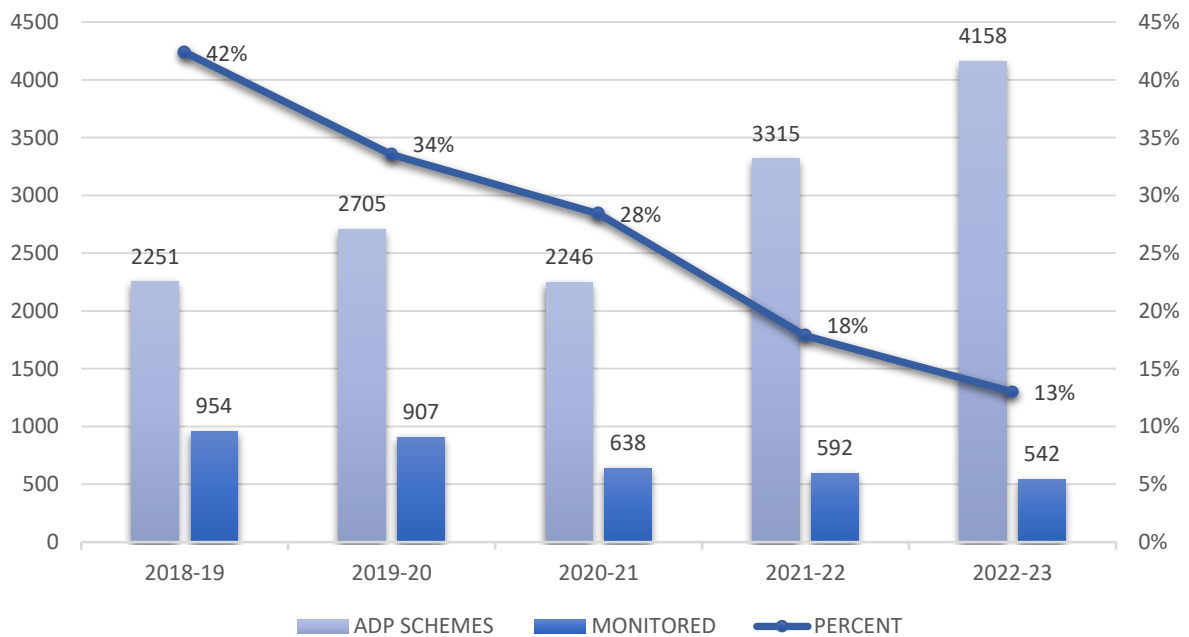


# SPECIAL ASSIGNMENT

Worthy Chairman, P&D Board, assigned following special visits/assignments as time limit case:

S.NO	Task	Time-Line
1.	To visit <b>*817 ADP Schemes</b> in throughout Sindh	Within One-Week of time
2.	To visit <b>03 SIDCL PSDP schemes</b> (Manghopir, Nishtar Road, RO Plant)	Within One-Day of Time
3.	To visit <b>05 umbrella PSDP Schemes</b> (Bridge Over Indus Larkana, Water & Sewerage System in District Korangi-Karachi, 65 Development Scheme in Tharparkar, SITE industrial Estate Karachi, Prime Minister Program in Sindh)	Within Two-Days of Time

*\*Detail of Schemes is given in Annexure D*







# KEY RESULT INDICATORS

# RESPONSES RECEIVED FROM LINE DEPARTMENTS

MEC Team proactively pursued monitoring of 465 schemes along various Line Departments with a total of 542 monitoring visits. This reflected the commitment to ensure quality control for development schemes, especially those termed unsatisfactory.

Top 10 Departmental Response Against Compliance	Percentage
Auqaf, GOS	100
Law P.A, & Prosecution	100
Lining of Main Canals	100
Livestock and Fisheries, GOS	100
Mega Schemes for Karachi City	100
Population Welfare, GOS	100
Universities and Boards	100
Sports & Youth Affairs, GOS	80
Home, GOS	75
Agriculture, GOS	67

In terms of response received from the corresponding department against the compliance sent for unsatisfactory status, almost 20 of total 33 departments complied and rectified the issues in the time prescribed.


However, 13 departments failed to comply against the feedbacks generated by MEC for unsatisfactory performance.

While 10 Departments performed fairly (i.e. partial compliance) against the feedbacks generated by the MEC for unsatisfactory performance of the respective schemes.

# TREND ANALYSIS OF OBSERVATION TYPE

With a total of 542 monitoring visits for 465 development schemes for FY 2022-23, MEC has ensured that repeated monitoring visits translate into improved financial and physical progress indicators over time. It is evident that repeated visits over the same schemes have considerably improved their quality. This is reflected in the fact that out of 542 monitoring visits, 344 visits were found to be satisfactory (63%) and 198 visits were found to be unsatisfactory (37%). However, the ultimate status of the 465 monitored schemes demonstrate that 342 schemes were termed satisfactory (74%) and 123 schemes remained unsatisfactory (26%). This essentially means that continuous monitoring and repeated visits helped improve the quality of schemes considerably.

Status	2018-19	2019-20	2020-21	2021-22	2022-23
Satisfactory	56%	69%	57%	65%	63%
Unsatisfactory	44%	31%	43%	35%	37%

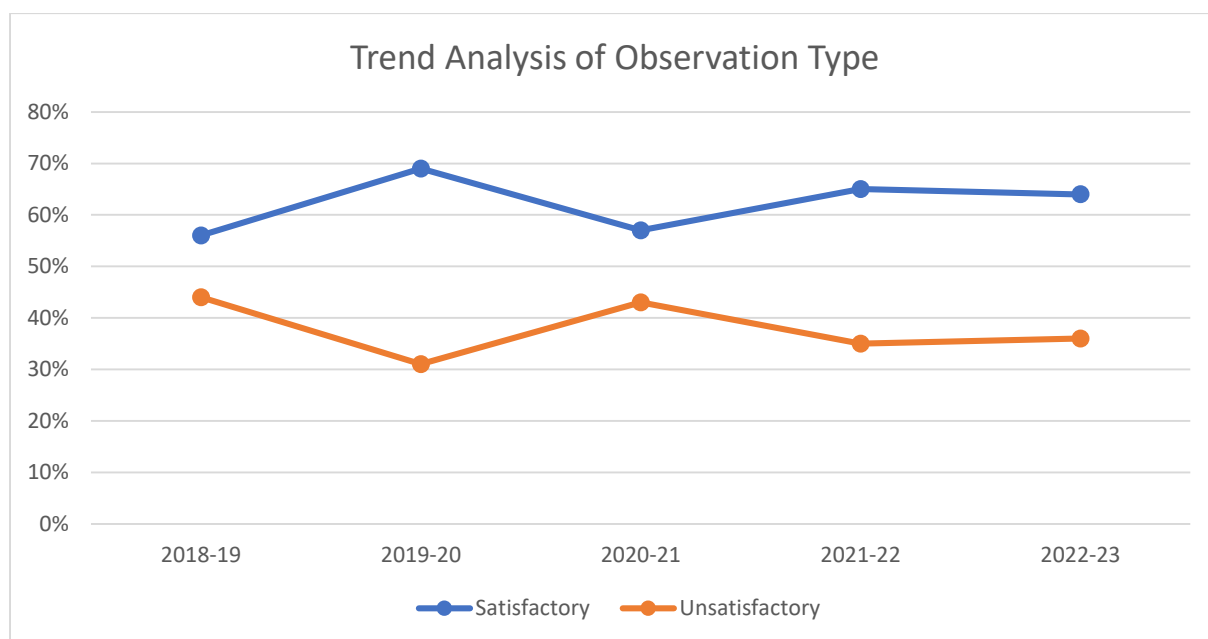

*Note: Before FY 2018-19, the categories of observation type included Average, Satisfactory and Unsatisfactory status. However, FY 2018-19 onwards, the "average" observation type is now considered unsatisfactory. Hence, now the observation type only includes two broad categories of satisfactory and unsatisfactory status.*

# UNSATISFACTORY SCHEMES 4 YEAR ANALYSIS

Departments	Percent % Of Unsatisfactory Schemes						
	2019-20	2020-21	2021-22	3-Year Average	2022-23	Increase/Decrease	Index
Agriculture, Supply & Prices	38.0	36.0	20.0	<b>31.3</b>	30.0	-1.3	↓
Auqaf, Zakat, Ushr & R.A.	42.0	36.4	57.0	<b>45.1</b>	38.0	-7.1	↓
Board of Revenue	17.0	88.9	0.0	<b>35.3</b>	0.0	-35.3	↓
Culture, Tour & Antique	55.0	27.3	53.0	<b>45.1</b>	36.0	-9.1	↓
Education Sector	25.0	37.5	31.0	<b>31.2</b>	29.0	-2.2	↓
Environment & Coastal Development	67.0	0.0	0.0	<b>22.3</b>	0.0	-22.3	↓
Forest & Wildlife	20.0	45.5	8.0	<b>24.5</b>	21.0	-3.5	↓
Health	31.0	34.1	51.0	<b>38.7</b>	53.0	14.3	↑
Home	20.0	50.0	38.0	<b>36.0</b>	80.0	44.0	↑
Industries & Commerce	50.0	50.0	75.0	<b>58.3</b>	50.0	-8.3	↓
Irrigation	25.0	40.0	35.0	<b>33.3</b>	22.0	-11.3	↓
Livestock & Fisheries	38.0	51.7	50.0	<b>46.6</b>	40.0	-6.6	↓
Local Government & HTP	35.0	37.7	28.0	<b>33.6</b>	42.0	8.4	↑
Minorities Affairs	43.0	50.0	38.0	<b>43.7</b>	25.0	-18.7	↓
Planning & Development	25.0	33.3	0.0	<b>19.4</b>	50.0	30.6	↑
Public Health Engineering	33.0	49.2	27.0	<b>36.4</b>	29.0	-7.4	↓
Rural Development	100.0	95.8	100.0	<b>98.6</b>	18.0	-80.6	↓
SGA & C	47.0	36.4	40.0	<b>41.1</b>	33.0	-8.1	↓
Sports & Youth Affairs	17.0	20.0	16.0	<b>17.7</b>	33.0	15.3	↑
Thar Coal Infrastructure Development	50.0	100.0	67.0	<b>72.3</b>	0.0	-72.3	↓
Women Development	100.0	75.0	0.0	<b>58.3</b>	50.0	-8.3	↓
Works & Services	29.0	34.9	35.0	<b>33.0</b>	32.0	-1.0	↓
<b>Average</b>	<b>41.2</b>	<b>46.8</b>	<b>35.0</b>	<b>41.0</b>	<b>32.3</b>		
<b>No. of Departments where the % of Unsatisfactory Schemes Decreased</b>						↓	<b>17</b>
<b>No. of Departments where the % of Unsatisfactory Schemes Increased</b>						↑	<b>5</b>


# MONITORING OUTCOMES

## Compliance Outcomes in FY 2022-23

S. No.	Department	1st Visit Compliances Received	Revisit(s) Compliances Received	Total Compliances Received	% Contribution of Revisits in Compliance
1	Agriculture, GOS	2	0	2	0
2	Auqaf, GOS	2	1	3	33.33
3	Cooperative, GOS	0	0	0	n/a
4	Culture, GOS	2	1	3	33.33
5	Education and Literacy, GOS	9	1	10	10.00
6	Energy, GOS	0	0	0	n/a
7	Excise & Taxation, GOS	0	0	0	n/a
8	Food, GOS	2	2	4	50
9	Forest, Wildlife & CDA, GOS	1	0	1	0
10	Health, GOS	3	6	9	66.67
11	Home, GOS	3	3	6	n/a
12	Human Settlement, Spatial Development & Social Housing	0	0	0	n/a
13	Industrial & Commerce, GOS	0	0	0	n/a
14	Information & Archives, GOS	0	0	0	n/a
15	Information, Science & Technology, GOS	0	0	0	n/a
16	Irrigation (Water & Drainage), GOS	0	0	0	n/a
17	Karachi Metropolitan Corporation, KWSB	0	0	0	n/a
18	Law P.A. & Prosecution	1	0	1	0
19	Lining of Main Canals	2	0	2	n/a
20	Livestock and Fisheries, GOS	3	0	3	0
21	Local Government, GOS	19	0	19	0
22	Mega Schemes for Karachi City	1	0	1	n/a
23	Minorities & Affairs, GOS	1	0	1	0.00
24	Physical Planning & Housing (Buildings), GOS	1	0	1	0.00

S. No.	Department	1st Visit Compliances Received	Revisit(s) Compliances Received	Total Compliances Received	% Contribution of Revisits in Compliance
25	Planning & Development, GoS	0	0	0	n/a
26	Population Welfare, GOS	1	0	1	n/a
27	Public Health Engineering, GOS	9	2	11	n/a
28	Rehabilitation (PDMA), GOS	0	0	0	n/a
29	Rural Development, GOS	0	0	0	n/a
30	S.G.A.and Coordination, GOS	0	0	0	n/a
31	Sports & Youth Affairs, GOS	4	0	4	0.00
32	STEVTA, GOS	0	0	0	n/a
33	Universities and Boards	1	0	1	n/a
34	Women Development, GOS	1	0	1	n/a
35	Work and Service, GOS	11	0	11	n/a
<b>Total</b>		<b>79</b>	<b>16</b>	<b>95</b>	<b>16.84</b>

### IMPROVEMENT IN COMPLIANCES RECEIVED DUE TO REVISITS

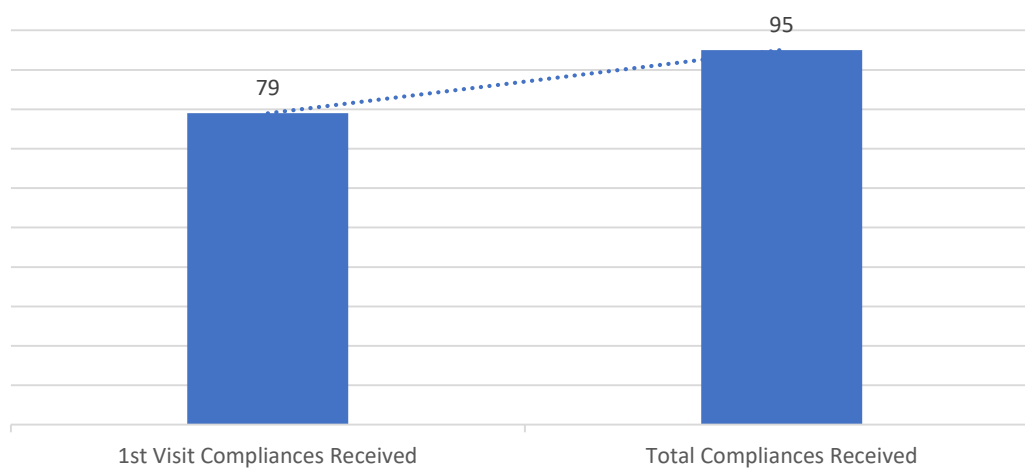


# UNSATISFACTORY STATUS

S. No.	Department	Unsatisfactory Status (FY 2021-22)	Unsatisfactory Status (FY 2022-23)
1	Agriculture, GOS	2	1
2	Auqaf, GOS	1	1
3	Cooperative, GOS	1	1
4	Culture, GOS	3	2
5	Education and Literacy, GOS	12	10
6	Energy, GOS	1	1
7	Excise & Taxation, GOS	3	2
8	Food, GOS	0	10
9	Forest, Wildlife & CDA, GOS	1	0
10	Health, GOS	11	13
11	Home, GOS	3	5
12	Human Settlement, GOS	0	1
13	Industrial & Commerce, GOS	3	1
14	Information & Archives, GOS	0	2
15	Irrigation (Water & Drainage), GOS	6	4
16	Karachi Metropolitan Corporation, KWSB	0	1
17	Law P.A. & Prosecution, GOS	3	0
18	Lining of Main Canals, GOS	3	0
19	Livestock and Fisheries, GOS	5	0
20	Local Government, GOS	7	19
21	Minorities & Affairs, GOS	1	3
22	Physical Planning & Housing (Buildings), GOS	0	1
23	Planning & Development, GoS	0	1

S. No.	Department	Unsatisfactory Status (FY 2021-22)	Unsatisfactory Status (FY 2022-23)
24	Population Welfare, GOS	0	0
25	Public Health Engineering, GOS	13	12
26	Rehabilitation (PDMA), GOS	0	1
27	Rural Development, GOS	2	2
28	S.G.A.and Coordination, GOS	3	1
29	Sports & Youth Affairs, GOS	0	1
30	Thar Coal Infrastructure Development, GOS	2	0
31	Transport & Comm. (Roads), GOS	2	0
32	Women Development, GOS	0	1
33	Work and Service, GOS	28	26
	<b>Total</b>	<b>116</b>	<b>123</b>


### UNSATISFACTORY VISITS

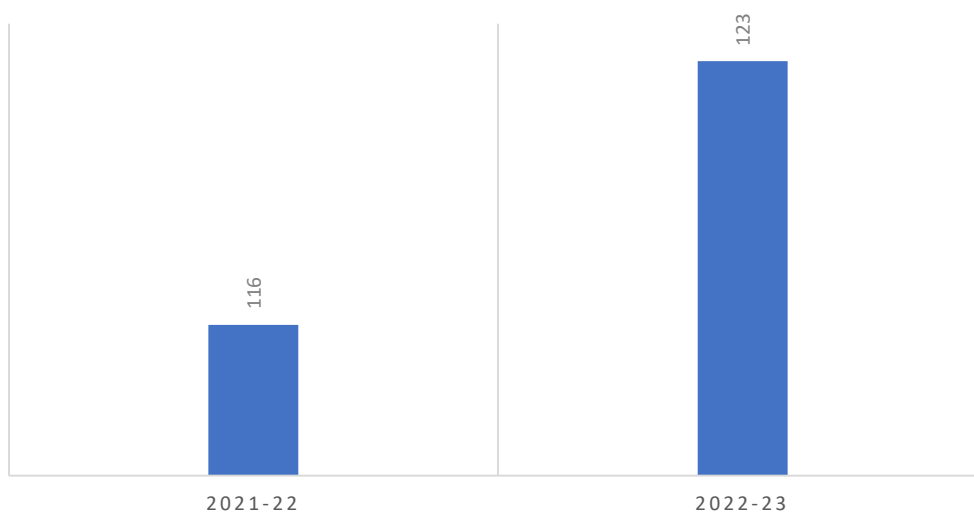

# SUMMARY OF COMPLETED SCHEMES IN FY 2022-23

Department	No of Schemes	Estimated Cost	Allocation
Agriculture, Supply & Prices	13	2355.342	1382.002
Auqaf, Zakat, Ushr & R.A.	17	180.378	229.075
Cooperative	1	118.421	11.000
Culture, Tourism, Antiquities & Archives	12	787.042	337.404
Education (School)	44	11118.588	2170.861
Education (College)	2	2329.649	1130.234
Education (Emp)	1	45.000	40.050
Education (U&B)	3	596.385	287.557
Energy	3	1637.447	883.412
Finance	1	79.753	64.903
Forest & Wildlife	1	708.000	248.666
Governor's Secretariat	1	25.362	9.734
Health	7	3777.029	416.154
Home	7	243.765	70.719
Human Settlement	4	105.210	38.288
Industries & Commerce	3	1436.823	100.681
Irrigation	17	3767.295	1526.869
Law, P.A & Prosecution	4	1149.437	72.112
Livestock & Fisheries	1	100.000	87.500
Local Govt. (Water Supply)	145	25778.653	14475.554
Local Govt. (Buildings)	3	182.000	142.854
Local Govt. (Roads)	87	14680.142	7816.225
Local Govt. (Health)	2	82.361	0.002

<b>Department</b>	<b>No of Schemes</b>	<b>Estimated Cost</b>	<b>Allocation</b>
Local Govt. (Community Services)	11	1031.522	867.087
Mega Projects for Karachi	5	2088.656	1382.533
Minorities Affairs	6	567.249	187.181
Population Welfare	3	74.583	36.630
Public Health Engineering	99	9002.767	5089.569
Rural Development	19	334.000	192.000
SGA&CD	1	25.374	13.149
Sports & Youth Affairs	3	70.000	46.250
Thar Coal Infrastructure	2	2284.446	116.808
Works & Services	240	50966.453	28277.505
<b>TOTAL</b>	<b>768</b>	<b>137,729.132</b>	<b>67,750.568</b>

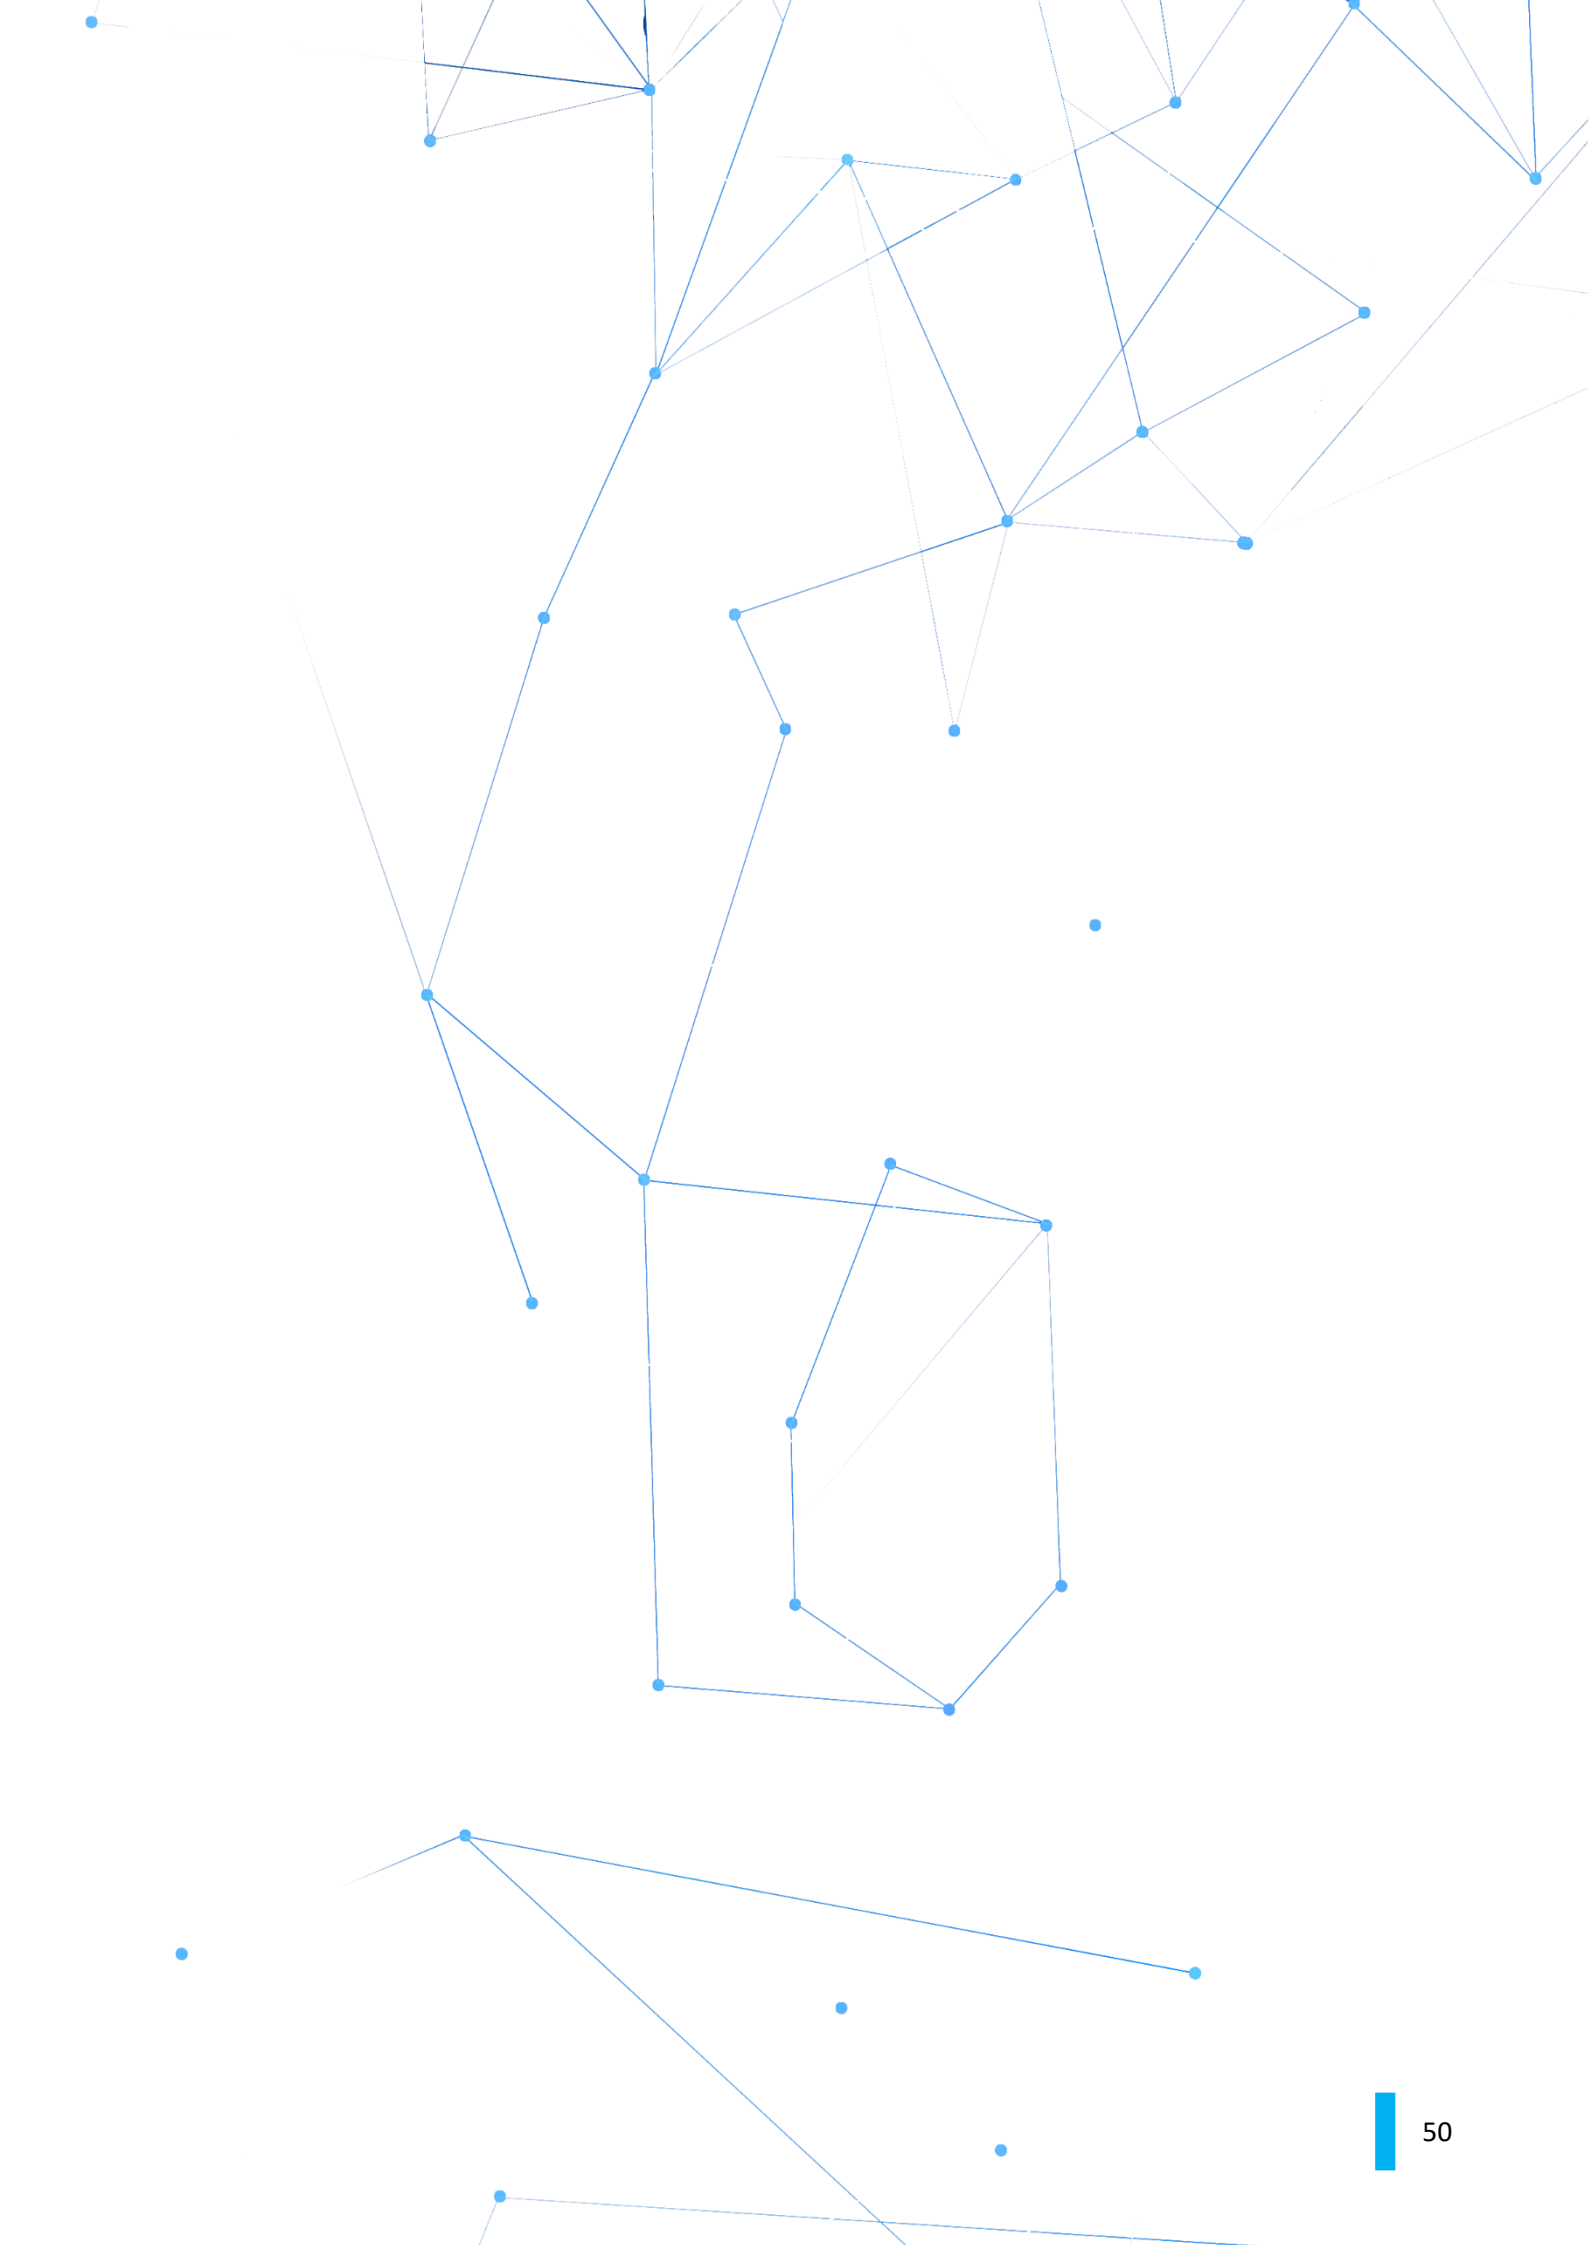



# FINDINGS &

# RECOMMENDATIONS



# AGRICULTURE, SUPPLY & PRICE

## GENERAL FINDINGS

MEC conducted 10 visits of Agriculture, Supply & Price Department and found 07 schemes satisfactory while 03 schemes were unsatisfactory.

- It was generally observed that the department could not get funds released in time resultantly it failed to provide planned machinery, equipment and implement to the growers before the growing season
- On some schemes the pace of work was found lagging behind the financial progress
- In some old on-going schemes, the execution remained unnecessarily slow which otherwise should have been priority of the department to conclude
- On several occasions project documentation is not provided or provided very late which create hindrances in preparing monitoring reports
- The scheme of solar tube wells not executed in this year
- Mostly all schemes are executed by the DG offices which are located in Hyderabad, so the people face many difficulties

## RECOMMENDATIONS

- The Administrative Department should have execution plan to expedite the release utilization of funds in time to reach out to the growers in need
- Procurement of required machinery and items should be made according to SPPRA rules and within stipulated time frame
- The department should ensure that experienced work force is deputed and good quality material should be procured as per mentioned standards
- The pace of work should be expedited as per financial progress
- The Solarization of Tube well scheme which are not executed in this year should be executed as per the plan period of the scheme
- Project documentation should be provided timely so that MEC team verify the physical and financial progress of the scheme
- The On-Going old schemes should be given priority to be completed as per the plan period
- The devolution of the authority should be made at divisional level so as to facilitate the farmers to seek required help and guidance accordingly
- Administrative Department must submit the PC-IV of the completed schemes so as maintain the infrastructure and get the desired results
- Monthly Progress Report (MPR) of schemes must be submitted by Administrative Department before 10th of every month



Integrated Water Resource  
Management Jamshoro &  
TM Khan



Integrated Water Resource  
Management in SindhDistt.  
Shaheed Benazir Abad



Lining of Water Course  
Matliari

# CULTURE TOURISM AND ANTIQUITIES

## GENERAL FINDINGS

During FY 2022-23, total 14 schemes were visited by the MEC, 09 schemes were declared satisfactory, whereas 05 schemes were declared unsatisfactory due to poor quality of work

- The deviation of scope was observed in some schemes due to poor planning and non-execution of PC-II & Land Survey
- In most of the schemes found that non-scheduled items rate has been quoted by E/A in place of available scheduled rates. In case of non-scheduled items rate should be rationalized
- It is observed that the department is habitual of delaying the scheme which resulted in unnecessary cost escalation and revision of the scheme which should be discourage
- It is observed specially in execution work of the scheme of Umerkot and Narunkot fort preservation was not done as per standards set for restoration and conservation
- During the visits of heritage site it was generally observed that many historic items specially vehicles were left unattended to deteriorate in first place and later on department usually come up with the restoration scheme of huge cost to conserve / preserve the same
- During visit, it was observed that the department had got published thousands of books under various schemes for preservation & compilation of different authors but those books were found dump without any planning & mechanism to distribute the same

## RECOMMENDATIONS

- In all restoration and conservation work, it must be ensured that the originality of the old structure should be preserved that otherwise is found compromised in most the scheme
- The Land scape around heritage properties was found neglected while maintaining its historical values
- Restoration and conservation work will be done with special care to avoid any sort of damage to old structure and without disturbing the originality of the archeological sites
- In the light of study / survey, priority should be given to those areas/components, which are vulnerable, and needs immediate attention
- Keeping in view the social & cultural importance of the schemes, department Should have to expedite its vigilance to monitor the scheme on regular basis so that the designed objects would be achieved within the required time frame
- E/A should hire the technical/ project staff as per PC-I because it was observed that due to non-hiring of project staff quality of work at some sites were being compromised
- Administrative Department must submit the PC-IV of the completed schemes so as maintain the infrastructure and get the desired results
- It was observed that although restroom/washroom are available in PC-I at various museum sites such as Chahunjo Daro at Nawabshah, Kot Dijji, Miskeen Shah at Mitthi and Makli at Thatta yet they are not physically available or functional at location. It is therefore advised that administrative department may intervene and address this short coming
- Monthly Progress Report (MPR) of schemes must be submitted by Administrative Department before 10th of every month



Dargah Jaral Shah  
Larkana



Sindh Institute for Music &  
Performing Arts Jamshoro



Culture Centre Kotri

# EDUCATION

## GENERAL FINDINGS

Education sector is categorized into three different departments i.e., School Education, College Education, Universities/Boards & Technical Education. MEC, P&D Department, Govt of Sindh visited 65 schemes of education sector during FY 2022-23. Out of 65 Schemes, 46 Schemes were found satisfactory, whereas 19 Schemes were declared unsatisfactory.

Education Department executed various schemes in FY 2022-23 generally aimed at improving educational activities and to prepare much needed infrastructure for basic education.

The major issues observed during the monitoring of these schemes were:

- Non-availability of revenue component details i.e., Tender documents, Invoices & Delivery Challans etc.
- Workmanship issues exists that causing honey combing and other deficiencies in structural work
- Lack of planning in execution of various schemes which causes unnecessary delays in completion of scheme
- Delay in release of funds in some schemes was observed
- Partial/late/no delivery of documents from E/A to MEC which leads to delay in submission of Monitoring Reports.

## RECOMMENDATIONS

- A framework must be developed for the proper utilization of Revenue Component by the Education Department
- E/A should provide all the necessary documents as indicated in the official visit letter by the MEC team
- The Education Department Should expedite vigilance to monitor the scheme on regular basis so that the designed project objectives could be achieved within the required time frame
- E/A should improve the quality of workmanship specially for concrete work at site to avoid honeycombing
- E/A should pay attention to the specific observations and recommendations raised by the visiting team to achieve the project objectives timely
- Verification of quantities must be performed by the XEN and AEN concerned before the payment is made to the contractor
- Smooth funding as per the allocation from the source is necessary and should be released as per the allocation
- Proper maintenance of completed buildings must be carried out by the E/A
- Administrative Department must submit the PC-IV of the completed schemes so as maintain the infrastructure and get the desired results
- Monthly Progress Report (MPR) of schemes must be submitted by Administrative Department before 10th of every month



Public School & College  
Shikapur



GBDC - GGDC Naudero  
District Larkano



SBBU of Veterinary and  
Animal Sciences Sakrand

# HEALTH

## GENERAL FINDINGS

MEC conducted 40 visits of Health Department and found 18 schemes satisfactory i.e 45% while 22 schemes were unsatisfactory i.e 55%

Health Department included various schemes in FY 2022-23 generally aimed at improving basic and advanced health facilities.

The major issues observed during the monitoring of the schemes were: -

- The Department was reluctant to provide the details of Revenue component such as Tender documents, Invoices & Delivery Challans etc. to visiting team
- Overall delay in procurement of revenue component items was observed
- Quality of work was highly compromised and farm work along with poor workmanship
- The department was unable to get funds released & utilize in time resultantly most of the scheme were delayed from the plan period
- Partial/late/no provision of documents from E/A to MEC.

## RECOMMENDATIONS

- Keeping in view the significance of Health schemes, department should expedite vigilance to monitor the scheme on regular basis so that the objectives of the scheme could be achieved within time frame
- It is imperative that a framework must be developed by the Health Department for the proper and effective utilization of Revenue component of the scheme
- The E/A must make sure that MEC Team should be provided with all the scheme related documents before visit
- Overall construction quality needs to be improved by the E/A
- Payments should be associated with work done at site after due verification of quantities by the concerned AEN/XEN
- Smooth funding as per the allocation from the source is necessary and should be released as per the allocation
- Administrative Department must submit the PC-IV of the completed schemes so as maintain the infrastructure and get the desired results
- Monthly Progress Report (MPR) of schemes must be submitted by Administrative Department before 10th of every month



Cardio thoracic  
Surgery Department at  
LUMHS, Hyderabad



DHQ Hospital  
Shikarpur




Government Hospital  
Saudabad, Karachi

# IRRIGATION

## GENERAL FINDINGS

MEC conducted 18 visits of Schemes of Irrigation Department and found 14 schemes satisfactory i.e 78% while 04 schemes were unsatisfactory i.e 22%

- In Unsatisfactory schemes, MEC team observed poor quality of executed work due to poor workmanship and lack of supervision by E/A
- The earth work carried out at some locations was of average quality especially in embankment work. The suitable material without weeds, dressing, leveling, desired compaction & maintenance of slope, etc. were not observed properly
- At some locations schemes could not be completed timely due to slow pace of work & revisions of the schemes were also observed due to incomplete scope of work
- The complete scheme related data /documents were difficult to obtain on time particularly the M.B & T.S resulting facing difficulty in verifying the quantities recorded for payment
- In most of the cases the relevant Tests are not performed to ensure the suitability of the material & ensure quality parameters
- At some locations the pumping machinery found non-functional due to non-availability of electricity & back-up generators
- Stone pitching found disturbed in most of locations due to improper interlocking etc.
- Filler materials were not provided in the stone pitching as gaps/voids were observed which could lead to seepage and settlement issues
- The Profile, alignment and slope of stone pitching was not maintained properly at some locations
- Cracks observed in the concrete panels of lined canals at some locations
- The thickness of concrete work of lined canals was lesser at some locations

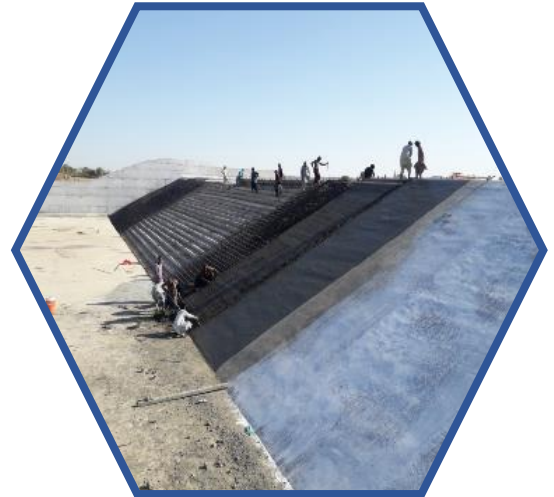

Sindh Resilience  
Project Nagarparkar  
Tharparkar



C.C. Lining of  
Wagherji Distry




Haibat Bund Begari  
Division Kashmir.

# IRRIGATION

## RECOMMENDATIONS

- The earth work may be carried out as per standard procedures & specifications
- The E/A may take adequate efforts for proper planning, execution and supervision of schemes to achieve targets as per PC-I
- The quality tests must be practiced at site to ensure quality execution
- In stone pitching work the proper profiling, alignment & slopes be maintained to ensure the work as per specification. The filler material at sides may be used properly to avoid seepages
- The thickness of concrete work in lining work may be executed as per drawing & design
- The pumping machinery at pumping stations & tube well sites may be provided as per site requirement & backup of generators be provided in case of electricity failures
- The thickness/gauge of steel plates used in regulator work may be ensured as per specifications
- The required dia of steel reinforcement may be used in Reinforced concrete work along with proper spacing as per design
- Administrative Department must submit the PC-IV of the completed schemes so as to maintain the infrastructure and get the desired results
- Monthly Progress Report (MPR) of schemes must be submitted by Administrative Department before 10th of every month

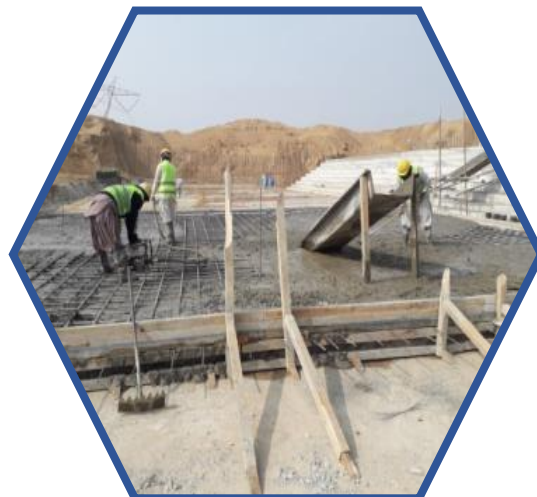

Sindh Resilience Project  
GADAP Karachi



Sindh Resilience Project,  
Small Dam Sehwan



Surface Drainage  
Scheme

# LOCAL GOVERNMENT

## GENERAL FINDINGS

- Local Government Department comprises of following autonomous bodies to execute development works in Karachi i) KMC ii) DMCs iii) KW&SB iv) KDA v) MDA vi) LDA vii) SSWMB viii) Karachi Mega Projects ix) M.D. Click and Donor agencies' projects (i.e. WB, ADB). However, in rest of the Sindh following autonomous bodies contribute in execution of development works i) HMC ii) HDA iii) WASA iv) SMC v) LMC vi) Sehwan Development Authority vii) Larkana Development Authority, other Project Directors and Local Councils across the province of Sindh. In certain circumstances Works & Services department also provide execution support in development work under portfolio of Local Government Department
- The schemes executed by the Local Government Department include mainly the rehabilitation and up-gradation of basic infrastructure facilities for public use. Facilities include construction/rehabilitation/ up-gradation of Roads, Building, Infrastructure i.e. Water Supply & Sewerage and Health Facilities
- In the financial year 2022-23, a total of 76 schemes were visited by MEC Department. Out of 76 Schemes the work on 44 Schemes i.e. 58% were declared satisfactory, while the work on the remaining 32 schemes i.e. 42% were declared unsatisfactory. Out of 44 Un-Satisfactory schemes, compliance of 19 schemes were received from department after rectification. However, compliance of 25 scheme was pending
- The major issues encountered during the monitoring of schemes were lack of planning in design and execution of roads and drainage schemes that proper infrastructure was not provided to accommodate the sewerage and storm water separately. Lack of proper layout and connectivity of infrastructure, as per approved in PC-I. Layout of utilities i.e., PTCL, water & sewerage services, electricity services were not as per standard practices. Most of the time sewerage and storm water flows either in sewerage or drainage network resulting in choking or overflow of system during peak discharge or rainy reason. Improper drainage water planning causes stagnation of water which deteriorates and failure of roads infrastructure
- The other main issues are inadequate allocation and releases of funds by the department which take years to complete the scheme and by the time scheme gets to completion, initial work get deteriorated and there is no proper SOPs for the repair and maintenance. Majority of the schemes were revised due to unrealistic estimates by department at the time of preparation of PC-I. Lack of supervision by field staff during the execution phase, frequent transfer and posting of project directors. The NHA/PWD/SHERE specifications not being followed properly in execution and testing of material (i.e. soil classification & gradation, bitumen quality test, field density test, compaction test, Pressure testing of pipe, strength test of concrete & steel)
- The KW&SB within Local Government Department does not cooperate with the MEC Team neither they provide any scheme related documents nor accompany/facilitate the MEC Team for the field visit



Paver Block Work in UC-17, 27 & 28 at Karachi



Carpeting of Road in different areas of UC3 Karachi



Nala along with Supreme Court Karachi

# LOCAL GOVERNMENT

On various ADP schemes the Executing Agency (Local Government Department) had not provided complete documents to the M&E Cell. In a few schemes, it was observed while reviewing the measurement book that Overpayments and Advance Payments were made to the contractor.

## RECOMMENDATIONS

- The E/A should ensure proper sewerage and drainage network flow alongside the road. Sewerage and drainage networks must be separately planned, designed and executed
- The E/A should improve the quality of work, workmanship to meet the prescribed specification and standard and ensure that material should be procured from vendor and quarry
- The E/A should conduct and provide M&E Cell with detailed Material Testing Reports
- The E/A should avoid making advanced payment to contractor
- The department should ensure the timely flow of funds so that the work does not suffer and ensure that procurement of required items should be made according to SPPRA rules and within the timeframe
- The department should ensure that an experienced workforce is deputed, and good quality material should be procured to ensure quality as per mentioned standards
- On many schemes the pace of work found lagging behind the financial progress. The E/A ensured that the physical progress shall be at par with Financial Progress
- It is observed that most of the Project Directors of Local Government department specially KMC, Mega Projects, CLICK and others are reluctant to provide pre-requisite documents to the MEC team as per visit schedule. So much so that many letters (07 Letters to M.D. Click, 08 Letters to P.D. Mega Projects) have been written to these Project Directors to come up with the documents on the desk monitoring but even then, they are reluctant to provide the project information that is PC-I, Measurement Book, Technical Survey, Detail of Running bills and etc. Beside the Project Directors failed to provide Technical Sanctions of the estimates / Tender Documents in above given projects. Therefore, it is strongly recommended that the Project Directors of these projects should be directed by the concern higher authorities to be vigilant and responsive to the request of MEC team of scheduled visit plans, desk meetings & required documents so as the work of MEC may be performed smoothly
- Besides it is noteworthy to mentioned that there are multiple executive agencies in Local Government therefore it has been observed that overlapping of development works is a frequent practice which causes loss of public money and difficulty in monitoring to the MEC and retrieving record of the schemes. The MEC team found it hard to identify and trace the exact executing agency for fixing the responsibility of deficiency within department of Local Government
- Administrative Department must submit the PC-IV of the completed schemes so as maintain the infrastructure and get the desired results
- Monthly Progress Report (MPR) of schemes must be submitted by Administrative Department before 10th of every month



Paver Block @ UC-31  
Sohrab Goth Karachi



Sewerage Line, Paver Block  
and Carpeting Road UC-3  
Karachi



Paver work in various roads at  
Jacobabad

# PUBLIC HEALTH ENG. & RURAL DEV.

## GENERAL FINDINGS

In financial year 2022-23, total of 68 schemes of Public Health Engineering department were visited by MEC. Out of 68 Schemes, the work on 48 Schemes i.e. 71% was found satisfactory, while on 20 schemes i.e. 29% was unsatisfactory

The major issues observed during the monitoring of the schemes were:

- Executing agency mainly focuses on minor works like CC block, paver blocks & CC drains instead of achieving the core objectives of the scheme like proper drainage disposal & provision of potable/treated water
- The sewerage almost directly disposed of in natural streams without proper treatment. In urban areas the direct disposal of drainage schemes has been resolved to a greater extent while in towns & rural areas' schemes the issue is constant
- Lack of ownership of completed development schemes by end user i.e. Public & Local Govt Department especially in urban areas in terms of poor operation & maintenance
- Poor operation and maintenance by local government department i.e. Concerned Municipal Committee/ Town Committee. The Committees do not carry out the O&M work specially in pumping machinery, Diesel engine sets, suction & delivery pipes etc. after transferring of schemes from PHED to Local govt department
- Insufficient deployment of staff at disposal works & Treatment works
- Massive leakages in distribution networks of water supply schemes were observed due to quality of pipes and non-provision of domestic connection by department

## RECOMMENDATIONS

- The department may be directed to reset the priorities and try to execute the items which benefit the community and local people in place of utilization of funds on less prioritized items like Paver & CC block. They should Always prioritize the construction of drainage scheme with all components then paver block and CC blocks
- Land acquisition matters for construction of treatment works & disposal works should be finalized before start of civil works as in 90% treatment works land was not yet acquired due to land disputes & slow process of revenue department
- The department may be directed to stop direct disposal of sewerage into natural streams/water bodies
- PE pipes should be used in all water supply & drainage schemes
- It is observed that Rural Development Department is short of qualified and experience human resource to conceive and execute better schemes so as to improve the overall foot-print of the department especially Solar Light Schemes, Asphalt Metaled Roads and etc.
- EA should provide domestic connection to public and provision in PC-1 must be ensured
- Administrative Department must submit the PC-IV of the completed schemes so as maintain the infrastructure and get the desired results
- Monthly Progress Report (MPR) of schemes must be submitted by Administrative Department before 10th of every month



Paver Blocks for Muhallas of Shahdadkot City



Elimination of Urban Sewerage Phase -I at Badin



Pipe Line Water Supply Kunri Distt. Tharparkar

# SPORTS & YOUTH AFFAIRS

## GENERAL FINDINGS

Sports & Youth Affairs Department executed various schemes in FY 2022-23, generally aimed at Promoting sports/healthy activities and to prepare much needed infrastructure of sports facilities for public in their neighborhood. It is the need of the hour that the public of the province be given the sports facility on permanent basis in their cities / areas. Moreover, the Department aimed to provide the young generation with the facilities of indoor and outdoor games at their educational institute and to facilitate the communities by providing gymnasium in the vicinity to improve sports facilities at National and International levels.

A total of number of 15 schemes were visited by MEC in FY 2022-23. Out of 15 Schemes the quality of work on 10 Schemes were satisfactory, whereas 05 Schemes were unsatisfactory. Moreover, compliance was received for 04 out of 05 schemes, which were then marked as satisfactory as rectification were done in light of observations raised by the MEC Team.

The major issues observed during the monitoring of schemes were, deviation from the scope of PC-I, Inferior quality of form work and average quality of concrete work, Delay in release of funds in some schemes & Partial/late/no delivery of project documents from Executive Agency to MEC Team prior to visit.

## RECOMMENDATIONS

- Keeping in view the social & cultural importance of the schemes, department should have to expedite vigilance of the schemes on a regular basis so that the intended objectives would be achieved within the required time frame.
- The department should initiate more projects to facilitate the community and development of accessible sports facilities.
- E/A should improve the quality of workmanship and concrete work at site to avoid honeycombing and deterioration of infrastructure during completion phase. Moreover, the quality of formwork should be enhanced with the use of plywood.
- In the light of study / survey, priority should be given to those areas/components, which are deprived of sports facilities while selection of ADP portfolio.
- Payments may be made as per work done at site after due verification of quantities by the concerned XEN.
- E/A should provide all necessary documents as indicated in the official visit letter by the MEC team.
- E/A should ensure proper maintenance of completed buildings and make them functional for the consumption of public.
- Administrative Department must submit the PC-IV of the completed schemes so as maintain the infrastructure and get the desired results
- Monthly Progress Report (MPR) of schemes must be submitted by Administrative Department before 10th of every month



Players Hostel at Ghotki



Hockey Stadium NIPA  
Karachi



Sports Ground at Thul

# WORKS & SERVICES

## GENERAL FINDINGS

In the financial year 2022-23, a total of 97 schemes were visited by the MEC Department. Out of 97 Schemes the work on 66 Schemes i.e., 68% were declared satisfactory, while the work on the remaining 31 schemes i.e., 32% were declared unsatisfactory. Out of 31 Un-Satisfactory schemes, compliance of 10 schemes were received from department after rectification while compliance of 21 scheme was pending. Following are the major issues during the visit of MEC Team:

### **BUILDINGS**

- Honey combing and bleeding in structure work at specific locations due to non-availability of vibrator
- Unevenness in plaster work
- non-provision of clear cover in RCC work
- Unevenness in tile / marble flooring work
- Improper grouting in tile work
- Alignment issues in beams, columns & slabs
- Inferior quality of electric wiring fitting and fixtures, water supply and sanitary fixtures
- Deviation in scope of PC-I
- The shuttering work at most of the works was observed to be of inferior quality & needs to be improved, if possible, the steel/ply shuttering may be used

### **ROADS**

- The major issues encountered during the monitoring that there is lack of planning in design and execution of roads and drainage schemes that proper infrastructures were not provided to accommodate the sewerage and storm water separately. Most of the time sewerage and storm water flows either in sewerage or drainage network resulting in choking or overflow of system during peak discharge or rainy reason
- Furthermore, appropriate slope was not maintained in execution of road to smoothly drain the water. Due to improper drainage water remains stagnant which results in deterioration and complete failure of roads
- The other main issues are inadequate allocation and releases of funds by the department which take years to complete the scheme and by the time scheme gets to completion, initial work gets deteriorated and there is no proper SOPs for the repair and maintenance
- Majority of the schemes were revised due to unrealistic estimates by department at the time of preparation of PC-I, Lack of supervision by field staff during the execution phase, frequent transfer and posting of project managers i.e., Project Director or Executive Engineer
- Administrative Department should submit Google Earth/ Google Map drawing/video to show actual ground position of the Road before revision/approval of the scheme in order to avoid any duplication



Road Network from  
Badin to Wango Mior



Link road from National  
Highway Thatta City



W/R of road from Saddiq  
Memon to Hafiz Sandhano  
road to Tando Allahyar

# WORKS & SERVICES

- The NHA/PWD/SHERE specifications not being followed properly in execution and testing of material (i.e., soil classification & gradation, bitumen quality test, field density test, compaction test, Pressure testing of pipe, strength test of concrete & steel).

## RECOMMENDATIONS

- The in-depth monitoring of execution of construction work is required from AEN & XEN concerned to extract quality work
- The use of quality materials must be maintained. The contractors may be directed to obtain quality material from reputed suppliers
- The E/A may improve the quality of work as per specification & T.S approved
- The workmanship of the Contractor needs to be improved to meet the prescribed specification and standards
- The Material Testing must be carried out frequently to ensure quality execution
- The overpayments/advance payments to contractors may be discouraged & payments be made as per quantity executed at site
- The SPPRA rules must be followed in the tendering & procurement process
- The shuttering work needs to be improved at most of the places
- The use of vibrator may be used in Concreting work to avoid honey combing & attain desired strength
- The quality of D.Bs, switches, buttons & cables used in electric work may be ensured as per specification & T.S.
- Under-gauge steel reinforcement bars may be avoided in execution of works
- Administrative Department must submit the PC-IV of the completed schemes so as maintain the infrastructure and get the desired results
- Monthly Progress Report (MPR) of schemes must be submitted by Administrative Department before 10th of every month



W/R of road from Ghulamullah to Pirpatho



W/R of Mithi to Diplo road



Road from Old Indus Highways City Oorifion Larkano




WAY

FORWARD



# WAY FORWARD

- Overall MEC with the existing human resource was able to monitor 15% to 17% of the ADP scheme every year which need to be enhanced and improved for quality assurance therefore it is envisaged to establish regional offices of the MEC at Divisional level
- Pursuant to enhance MEC's outreach to maximum number of the scheme hiring of Monitoring Supervisors is planned
- Moreover, Third Party Monitoring mechanism is also planned and processed not only to monitor the mega projects but also to compare and introspect the work ethics and processes of the MEC monitoring team
- To develop & implement a Digitized Monthly Progress Report (MPR) System with Quick Response (QR) Code integration with Administrative Departments to enhance the timely submission of scheme progress updates
- Creating a Centralized Dashboard for Foreign Aided / World Bank Projects, aimed at providing regular updates and facilitating monitoring of the progress of foreign-funded projects through a specialized and dedicated platform
- Provide comprehensive training and development programs to all employees and equip them with cutting-edge technology which enables them to adopt modern techniques and monitoring methodologies that adhere to international standards.
- Construction of Regional Offices of M&E Cell at Karachi, Sukkur & Larkana regions through new ADP schemes
- Maximize the Evaluation of Completed Development Schemes

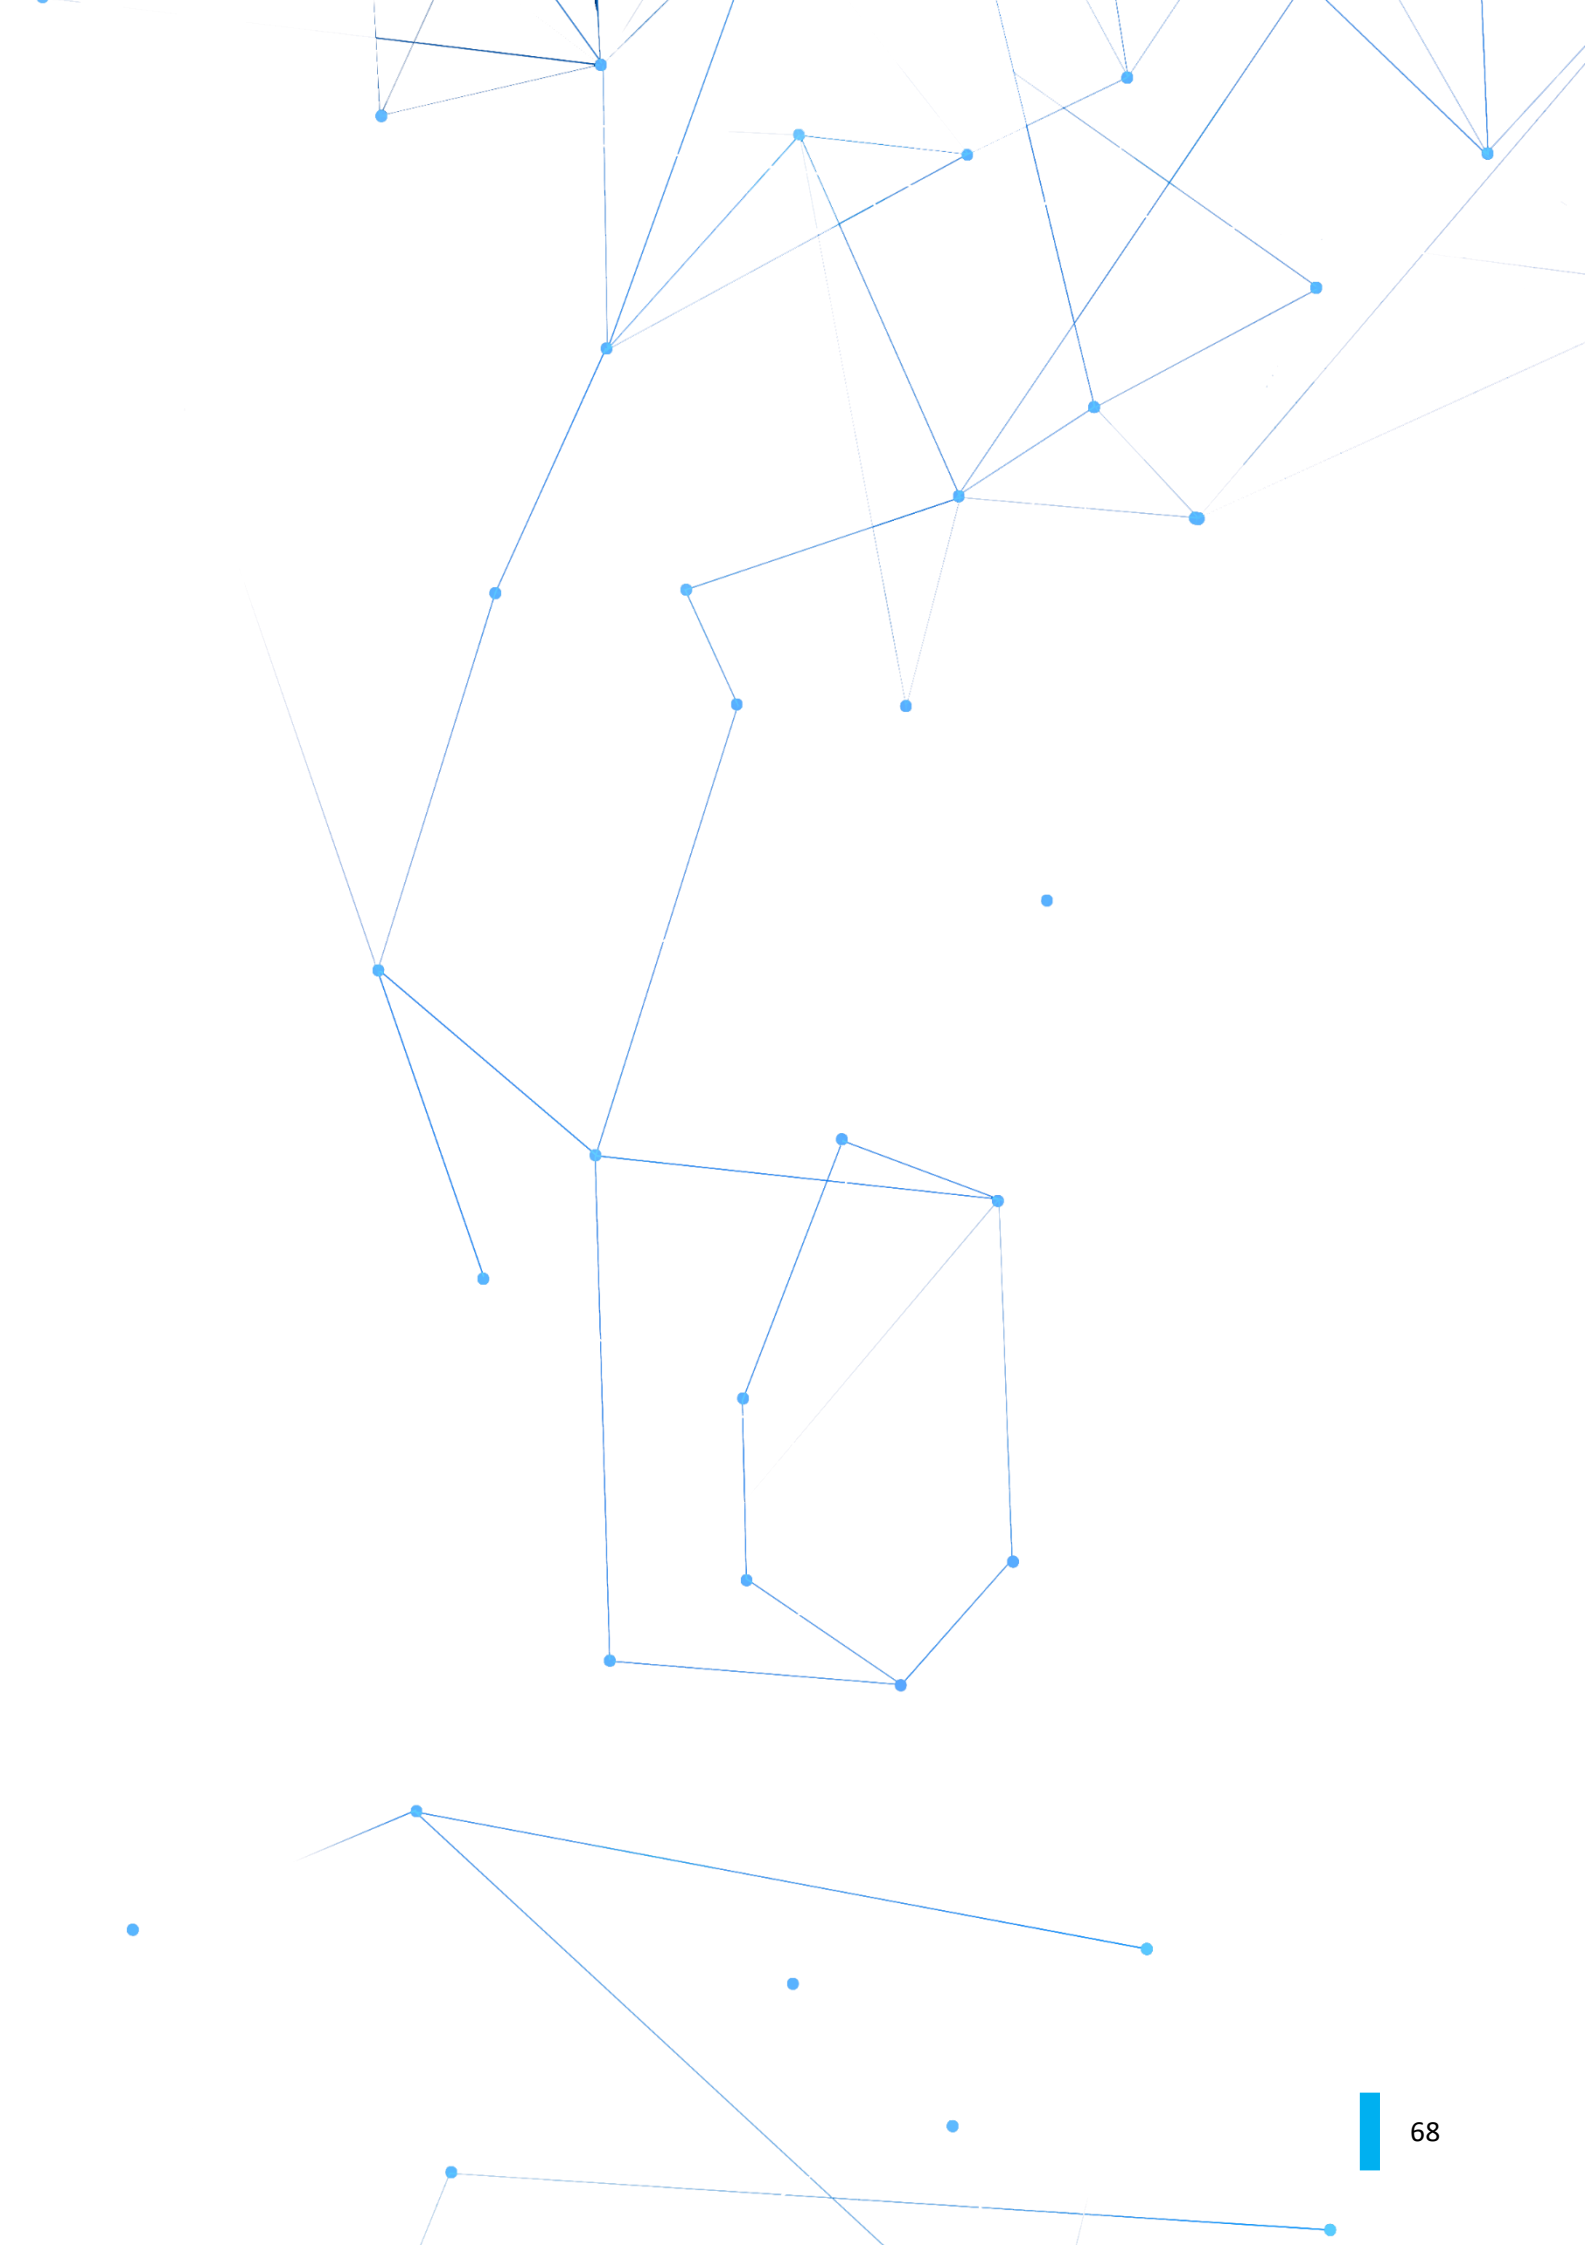



# ANNEXURES



# Annexure (A)

## DEPARTMENT WISE SCHEMES MONITORED IN FY 2022-23

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 37	Construction of Office Building for On-Farm Water Management staff (Badin, Mirpurkhas, Sanghar, SBA, Sukkur, Khairpur, Shikarpur, Dadu, Ghotki, Kashmore & Jamshoro ).	Un-Satisfactory	10-10-2022	Agriculture, GOS	12-01-2023	Badin	96.389
2022-23 40	Additional Lining of Watercourses in Sindh. (Total Cost Rs.5664.404 M, GOS Share 4659.847 M & Farmer Share Rs.1004.530 M).	Satisfactory	02-02-2023	Agriculture, GOS	01-03-2023	Matiari	4659.87
2022-23 40	Additional Lining of Watercourses in Sindh. (Total Cost Rs.5664.404 M, GOS Share 4659.847 M & Farmer Share Rs.1004.530 M)	Un-Satisfactory	08-08-2022	Agriculture, GOS	21-11-2022	Matiari	4659.87
2021-22 12	Construction / Rehabilitation of Agriculture Extension Office in Sindh.	Satisfactory	06-07-2022	Agriculture, GOS	02-08-2022	Qambar Shahdadkot	439.149
2021-22 27	Provision of Agricultural Land Development Machinery & Equipments (On Subsidized Rate)	Satisfactory	09-03-2023	Agriculture, GOS	12-05-2023	Sukkur	759
2021-22 27	Provision of Agricultural Land Development Machinery & Equipments (On Subsidized Rate)	Un-Satisfactory	19-04-2022	Agriculture, GOS	03-10-2022	Sukkur	759
2021-22 27	Provision of Agricultural Land Development Machinery & Equipments (On Subsidized Rate)	Satisfactory	18-11-2021	Agriculture, GOS	04-07-2022	Hyderabad	759
2021-22 3	Construction of Compound wall to ARI Campus Tando Jam including Experimental Field, Pavement of Approach Road and Rehabilitation of Residential Colony	Satisfactory	11-04-2022	Agriculture, GOS	19-08-2022	Hyderabad	148.864
2021-22 36	Integrated Water Resource Management in Sindh (Total Cost Rs.2393.495 M, GOS Share Rs.1932.447 M and Farmer Share Rs.400.00 M).	Satisfactory	21-02-2022	Agriculture, GOS	16-08-2022	Tando Muhammad Khan, Jamshoro	1932.45
2021-22 36	Integrated Water Resource Management in Sindh (Total Cost Rs.2393.495 M, GOS Share Rs.1932.447 M and Farmer Share Rs.400.00 M).	Satisfactory	21-12-2021	Agriculture, GOS	16-01-2023	Shaheed Benazirabad	1932.45
2022-23 47	Construction / Reconstruction / Rehabilitation & Allied Facilities of Dargahs in Sindh (6 Nos.), T.M Khan (01), Thatta (02), Khairpur (01), Hyderabad (01) and Larkano (01).	Satisfactory	06-03-2023	Auqaf, GOS	17-03-2023	Thatta	150.599
2022-23 47	Construction / Reconstruction / Rehabilitation & Allied Facilities of Dargahs in Sindh (6 Nos.), T.M Khan (01), Thatta (02), Khairpur (01), Hyderabad (01) and Larkano (01)	Un-Satisfactory	24-10-2022	Auqaf, GOS	11-01-2023	Thatta	150.599
2021-22 50	Reconstruction of Musafirkhana / Construction of main Entrance Gate / Water Tank at Dargah Shah Abdul Latif Bhattai at Bhitshah	Satisfactory	20-06-2022	Auqaf, GOS	16-08-2022	Matiari	19.257
2021-22 51	Construction of Dargah Makhdoom Nooh Hala District Matiari	Satisfactory	02-08-2022	Auqaf, GOS	15-11-2022	Matiari	17.327
2021-22 53	Reconstruction of Shrine, Construction of Musafirkhana and other Allied Units at Dargah Syed Ubhan Shah Taluka Kot Diji District Khairpur Mirs	Un-Satisfactory	09-02-2022	Auqaf, GOS	10-11-2022	Khairpur	10.047
2021-22 64	Provision of Fiber Glass Shade, Installation of RO plants and Establishment of Museum at Dargah Qalander Lal Shahbaz Sehwan Sharif District Jamshoro	Satisfactory	28-07-2022	Auqaf, GOS	01-09-2022	Jamshoro	22.238
2021-22 65	Provision of Fiber Glass Shade and Improvement of Water Supply at Dargah Abdullah Shah Ashabi	Satisfactory	10-03-2023	Auqaf, GOS	14-03-2023	Thatta	18.3

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2021-22 65	Provision of Fiber Glass Shade and Improvement of Water Supply at Dargah Abdullah Shah Ashabi	Un-Satisfactory	22-03-2022	Auqaf, GOS	19-08-2022	Thatta	18.3
2021-22 101	Construction of Sindh Government Cooperative College Hyderabad.	Un-Satisfactory	16-03-2023	Cooperative, GOS	11-04-2023	Hyderabad	118
2022-23 104	Auditorium Hall Rest House And Main Entrance Gate at Dargah Hazrat Sardar Ahmed Shah Lakyari Taluka Saeedabad District Matiari (Revised on 18.01.22) (C:86.833+R:12.768)	Satisfactory	26-09-2022	Culture, GOS	11-01-2023	Matiari	99.601
2022-23 111	Provision of Missing Allied Facilities in Library at Sujawal. (Revised on 24.12.20) (C:39.909+R:26.905)	Satisfactory	25-10-2022	Culture, GOS	11-01-2023	Sujawal	66.814
2022-23 115	Provision of Additional Allied Facilities & External Development at Sindh Institute for Music & Performing Arts & DR. N.A Balouch Institute at Jamshoro. (C:60.277+R:8.683)	Satisfactory	24-10-2022	Culture, GOS	11-01-2023	Jamshoro	68.96
2022-23 117	Establishment of Muhammad Ibrahim Jyo Translation Bureau at Jamshoro. (C:6.730+R:32.102)	Satisfactory	04-08-2022	Culture, GOS	15-11-2022	Jamshoro	38.832
2022-23 121	Establishment of Auditorium at Badin. (C:37.424+R:12.163)	Un-Satisfactory	08-08-2022	Culture, GOS	26-10-2022	Badin	49.587
2022-23 124	Provision of Allied Facilities at Cultural Complex Thatta. (C:64.564+R:14.941)	Un-Satisfactory	24-10-2022	Culture, GOS	19-01-2023	Thatta	79.505
2022-23 142	Establishment of Digitization & Conservation Laboratory for Providing Physical Treatments, Testing, Cleaning and Protecting of Decaying Artifacts, i.e. Stones, Coins, Manuscripts etc. (C:21.978+R:75.100)	Satisfactory	06-01-2023	Culture, GOS	18-01-2023	Karachi	97.078
2022-23 144	Provision of Additional Allied Facilities & External Development of Sub-office of Antiquities & Archaeological Museum Sukkur. (Revised on 24.12.20) (C:74.034+R:15.604)	Satisfactory	15-08-2022	Culture, GOS	07-03-2023	Sukkur	89.638
2021-22 111	Provision of Missing Allied Facilities in Library at Sujawal. (Revised) (C:39.909+R:26.905)	Un-Satisfactory	16-06-2022	Culture, GOS	16-08-2022	Sujawal	66.814
2021-22 114	Provision of Missing Allied Facilities & Construction of Auditorium Hall and Waiting area at Dargah Jaral Shah, Taluka Larkano District Larkano (Revised) (C:66.116+R:6.177)	Satisfactory	06-06-2022	Culture, GOS	23-11-2022	Larkana	72.293
2021-22 116	Provision of Additional Allied Facilities & External Development of Culture Department offices Near Rumi Graveyard at Northern Bypass, Karachi	Satisfactory	05-01-2023	Culture, GOS	18-01-2023	Karachi	80
2021-22 116	Provision of Additional Allied Facilities & External Development of Culture Department offices Near Rumi Graveyard at Northern Bypass, Karachi (C:59.468+R:20.532)	Un-Satisfactory	18-04-2022	Culture, GOS	16-08-2022	Karachi	80
2021-22 121	Establishment of Auditorium at Dadu. (C:42.208+R:24.830) (Revised) (ADP NO.83 of 2019-20)	Satisfactory	05-10-2022	Culture, GOS	01-12-2022	Dadu	67.038
2021-22 121	Establishment of Auditorium at Dadu. (C:42.208+R:24.830) (Revised) (ADP NO.83 of 2019-20)	Un-Satisfactory	17-05-2022	Culture, GOS	04-07-2022	Dadu	67.038
2022-23 1900056	Repair, Renovation & rehabilitation work of GBPS Long Dalpota Taluka Jhando Mari District Tando Allah Yar	Satisfactory	10-03-2023	Education and Literacy, GOS	03-04-2023	Tando Allahyar	5.136
2022-23 341	Miscellaneous Immediate Works of Public School Hyderabad (C:554.871+R:51.189) (SDG#4)	Un-Satisfactory	28-09-2022	Education and Literacy, GOS	02-01-2023	Hyderabad	606.06
2022-23 350	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 40.000 + R: 3.395) (SDG#4)	Un-Satisfactory	09-12-2022	Education and Literacy, GOS	17-01-2023	Sujawal	43.395

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 431	Construction / Reconstruction of Govt. Boys High School Jhuddo (SDG#4)	Satisfactory	21-10-2022	Education and Literacy, GOS	15-03-2023	Mirpurkhas	43.241
2022-23 576	Construction of (Govt. Boys / Girls Secondary Schools) in Shirin Jinnah Colony Karachi (02 Units) (C:45.199+R:2.00) (SDG#4)	Satisfactory	15-03-2023	Education and Literacy, GOS	20-03-2023	Karachi South	47.199
2022-23 576	Construction of (Govt. Boys / Girls Secondary Schools) in Shirin Jinnah Colony Karachi (02 Units) (C:45.199 + R:2.00) (SDG#4)	Un-Satisfactory	12-08-2022	Education and Literacy, GOS	04-01-2023	Karachi South	47.199
2022-23 589	Establishment of Government Secondary School (Boys & Girls) in Chuhar Jamali Sujawal District (RGC) (Pertains to RGC Project under PRS assisted by European Union)	Satisfactory	22-11-2022	Education and Literacy, GOS	06-02-2023	Sujawal	205.5
2022-23 664	Improvement / Renovation of Govt.Boys\ Degree College Gulzar-e-Hijri East Karachi (SDG#4)	Satisfactory	27-04-2023	Education and Literacy, GOS	09-06-2023	Karachi East	99.349
2022-23 708	Re-Construction of Building Govt. Boys Degree College Miro Khan District Kamber-Shahdadkot	Satisfactory	08-11-2022	Education and Literacy, GOS	17-03-2023	Qambar Shahdadkot	70.62
2022-23 709	Rehabilitation & Provision of Missing Facilities in Existing GBDC / GGDC Naudero District Larkano (SDG#4)	Satisfactory	09-11-2022	Education and Literacy, GOS	17-03-2023	Larkana	62.784
2022-23 739	Establishment of Cadet College Khairpur (C:1141.114 + R:379.225) (Revised on 26.04.16) (SDG#4)	Satisfactory	23-11-2022	Education and Literacy, GOS	20-01-2023	Khairpur	1520.34
2022-23 743	Establishment of Cadet College, Badin (C:701.840 + R:127.194) (SDG#4)	Satisfactory	29-09-2022	Education and Literacy, GOS	06-02-2023	Badin	829.034
2022-23 746	Provision of Additional Facilities and Boundary Wall of Boys Cadet College Larkana (SDG#4)	Satisfactory	10-11-2022	Education and Literacy, GOS	15-03-2023	Larkana	99.808
2022-23 796	Construction of B-Tech Department at Government College of Technology (GCT) Hyderabad	Un-Satisfactory	20-09-2022	Education and Literacy, GOS	11-10-2022	Hyderabad	140.569
2022-23 805	Establishment of Syed Qutab Ali Shah Government Polytechnic Institute at Shujabad (C:57.313 + R:42.687) (SDG # 1,4,9).	Satisfactory	08-03-2023	Education and Literacy, GOS	11-04-2023	Mirpurkhas	100
2022-23 805	Establishment of Syed Qutab Ali Shah Government Polytechnic Institute at Shujabad (C:57.313 + R:42.687) (SDG # 1,4,9)	Un-Satisfactory	13-10-2022	Education and Literacy, GOS	27-01-2023	Mirpurkhas	100
2022-23 835	Establishment of Shaheed Benazir Bhutto University of Veterinary and Animal Sciences Sakrand (C:852.257 + R:326.615)	Satisfactory	14-11-2022	Education and Literacy, GOS	02-02-2023	Shaheed Benazirabad	1178.87
2022-23 839	Immediate Needs of QUEST at Nawabshah (C:176.182 + R:17.880) (SDG#4)	Un-Satisfactory	25-11-2022	Education and Literacy, GOS	27-01-2023	Shaheed Benazirabad	194.062
2022-23 842	Development of Remaining Essential Facilities Required for Establishment of Mehran University College of Engineering and Technology at Khairpur Mir's (C:717.236 + R:130.492) (SDG#4)	Un-Satisfactory	20-09-2022	Education and Literacy, GOS	13-12-2022	Khairpur	847.728
2022-23 844	Establishment of Shaheed Mohtarma Benazir Bhutto Chair & Convention Centre at Karachi University (C:345.005 + R:97.036) (SDG#4)	Satisfactory	17-05-2023	Education and Literacy, GOS	29-05-2023	Karachi	442.041
Non-ADP	Ingrated / Rehabilitation of Primary/Middle/ Elementary Schools Taluka Larkano (11 units) (2016-17 programme)	Un-Satisfactory	26-09-2022	Education and Literacy, GOS	11-01-2023	Larkana	19.5
Non-ADP	Re-habilitation Govt. Boys High School Mir Nabi Bux Town Taluka City	Satisfactory	19-07-2022	Education and Literacy, GOS	21-11-2022	Hyderabad	9
Non-ADP	Construction/ Reconstruction of Existing GGHSS Kotri, (Old Black) Taluka Kotri, District Jamshoro.	Satisfactory	21-07-2022	Education and Literacy, GOS	08-02-2023	Jamshoro	10
2021-22 187	Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Primary / Elementary	Satisfactory	20-01-2022	Education and Literacy, GOS	07-07-2022	Shikarpur	1270.04

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Schools) (155 Units) (C:1101.709+R:168.328) (SDG#4)						
Non-ADP	Construction of Shelterless Government Primary School Gul Mir Mari Taluka Jhando Mari District Tando Allahyar (01 Unit)	Satisfactory	22-08-2022	Education and Literacy, GOS	21-11-2022	Tando Allahyar	2.401
Non-ADP	Repair/ Renovation and rehabilitation work of GBPS Long Dalpota Taluka Jhando Mari District Tando Allahyar	Un-Satisfactory	23-08-2022	Education and Literacy, GOS	07-11-2022	Tando Allahyar	3.337
2021-22 191	Construction of Six Room Buildings for Shelterless Primary Schools (01 Unit) (C: 12.154 + R: 1.210) (SDG#4)	Satisfactory	15-11-2021	Education and Literacy, GOS	19-08-2022	Tando Allahyar	13.364
2021-22 200	Rehabilitation of High Enrollment Dangerous Primary Schools with Additional Class Rooms and Provision of Missing Facilities (05 Units) (SDG#4)	Satisfactory	29-06-2022	Education and Literacy, GOS	31-08-2022	Matiari	24.327
2021-22 291	Sindh Basic Education Program (SBEP) (Approved Cost: Rs.14355 M USAID Grant: Rs.13485 M & G.O.S. Share: Rs.870 M) (C: 651.147 + R: 218.853) (SDG#4)	Satisfactory	28-09-2021	Education and Literacy, GOS	15-08-2022	Karachi	870
2021-22 296	Construction / Re-construction of Building in Existing Secondary Schools PAF Base Shahbaz Jacobabad (C: 54.000 + R: 2.397)	Satisfactory	22-11-2021	Education and Literacy, GOS	04-07-2022	Jacobabad	56.397
2021-22 300	Purchase of Security Equipment and Construction of Boundary Wall & Other Remaining Work at Public School Shikarpur (C:78.534+R:14.292) (SDG#4)	Satisfactory	19-05-2022	Education and Literacy, GOS	01-09-2022	Shikarpur	92.826
2021-22 307	Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Secondary Schools) (7 Units) (C:93.023+R:51.420) (SDG#4)	Un-Satisfactory	27-09-2021	Education and Literacy, GOS	22-07-2022	Qambar Shahdadkot	144.443
2021-22 312	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 40.000 + R: 5.000) (SDG#4)	Satisfactory	08-12-2021	Education and Literacy, GOS	22-07-2022	Dadu	45
2021-22 313	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 39.782 + R: 3.134) (SDG#4)	Un-Satisfactory	28-06-2022	Education and Literacy, GOS	31-10-2022	Matiari	42.916
2021-22 314	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 39.712 + R: 4.295) (SDG#4)	Satisfactory	26-05-2022	Education and Literacy, GOS	16-08-2022	Tando Muhammad Khan	44.007
2021-22 315	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 40.000 + R: 4.214) (SDG#4)	Satisfactory	19-04-2022	Education and Literacy, GOS	06-07-2022	Tando Allahyar	44.214
2021-22 318	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 40.000 + R: 2.923) (SDG#4)	Satisfactory	22-02-2022	Education and Literacy, GOS	01-09-2022	Tharparkar	42.923
2021-22 326	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (02 Units) (C: Rs. 89.724 + R: 6.816) (SDG#4)	Satisfactory	21-01-2022	Education and Literacy, GOS	22-08-2022	Larkana	96.54
2021-22 328	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5	Un-Satisfactory	26-05-2022	Education and Literacy, GOS	16-08-2022	Shikarpur	49.262

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	K.M Radius (01 Unit) (C: Rs. 45.450 + R: 3.812) (SDG#4)						
2021-22 329	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 45.450 + R: 2.767) (SDG#4)	Un-Satisfactory	11-05-2022	Education and Literacy, GOS	16-08-2022	Kashmore	48.217
2021-22 330	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 45.819 + R: 3.681) (SDG#4)	Satisfactory	24-05-2022	Education and Literacy, GOS	01-12-2022	Jacobabad	49.5
2021-22 331	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 39.685 + R: 1.940) (SDG#4)	Un-Satisfactory	13-04-2022	Education and Literacy, GOS	19-08-2022	Karachi East	41.625
2021-22 478	Establishment of Degree College at Garhi Khairo District Jacobabad (C:89.089 + R:7.963) (SDG#4)	Satisfactory	16-12-2021	Education and Literacy, GOS	22-08-2022	Jacobabad	97.052
2021-22 481	Establishment of Degree College in existing Nasarpur Higher Secondary School Tando Allah Yar (C:25.000 + R:2.500) (SDG#4)	Satisfactory	20-04-2022	Education and Literacy, GOS	06-07-2022	Tando Allahyar	27.5
2021-22 485	Establishment of Degree College in existing Warha Higher Secondary School District Kamber Shahdad Kot (C:25.905 + R:1.851) (SDG#4)	Satisfactory	21-12-2021	Education and Literacy, GOS	22-07-2022	Qambar Shahdadkot	27.756
2021-22 491	Rehabilitation & Provision of Missing Facilities in C&S Govt. Boys College Shikarpur (C:49.963 + R:5.000) (SDG#4)	Satisfactory	17-03-2022	Education and Literacy, GOS	27-07-2022	Shikarpur	50.963
2021-22 494	Improvement / Repair of D.J. Science College South Karachi (SDG#4)	Satisfactory	13-12-2021	Education and Literacy, GOS	07-07-2022	Karachi South	39.228
2021-22 495	Rehabilitation / Addition of Missing Facilities Govt. for Women College Shahr-e-Liaquat Saddar Karachi (SDG#4)	Un-Satisfactory	19-04-2022	Education and Literacy, GOS	19-08-2022	Karachi	39.608
2021-22 496	Improvement / Renovation of Govt.Boys Degree College Gulzar-e-Hijri East Karachi (SDG#4)	Worst	20-04-2022	Education and Literacy, GOS	21-10-2022	Karachi East	19.999
2021-22 497	Remaining Work of Law College Halla District Matiari (SDG#4)	Satisfactory	27-06-2022	Education and Literacy, GOS	02-09-2022	Matiari	20
2021-22 562	Establishment of Shaheed Benazir Bhutto Girls Cadet College Larkano (C:2039.382 + R:190.457) (Revised) (SDG#4)	Satisfactory	10-05-2022	Education and Literacy, GOS	22-07-2022	Larkana	2229.84
2021-22 563	Establishment of Cadet College Khairpur (C:1141.114 + R:379.225) (Revised) (SDG#4)	Un-Satisfactory	31-05-2022	Education and Literacy, GOS	01-09-2022	Khairpur	1520.34
2021-22 592	Modernization of Government College of Technology, SITE Karachi & Mirpurkhas (Phase-I) (C:87.057 + R:10.904) (SDG # 1,4,9) (Planned as per request of Universities & Boards Deptt.)	Satisfactory	15-09-2021	Education and Literacy, GOS	06-07-2022	Karachi	97.961
2021-22 593	Establishment of Government Vocational Centres for Girls (09 Units) in Sindh (Larkano, Khairpur, & N.Feroze (2 Unit each), Mirpurkhas, Umerkot & Tharparkar (1 Unit each) (C: 218.696 + R: 35.075) (SDG # 1,4,9)	Satisfactory	14-06-2022	Education and Literacy, GOS	05-08-2022	Umerkot	253.771
Non-ADP	Repair/ Renovation and Rehabilitation work of Government Girls Community Model School Sultan Abad District Tando Allahyar	Satisfactory	19-10-2022	Education and Literacy, GOS	30-11-2022	Tando Allahyar	7.888
2020-21 114	Early Childhood Education (ECE) Intervention Larkana Division (C:16.980 + R:30.979) (SDG#4)	Satisfactory	24-11-2021	Education and Literacy, GOS	29-08-2022	Kashmore	47.959
2020-21 114	Early Childhood Education (ECE) Intervention Larkana Division (C:16.980 + R:30.979) (SDG#4)	Satisfactory	05-11-2021	Education and Literacy, GOS	29-08-2022	Jacobabad	47.959

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2020-21 146	Up-gradation of Primary Schools to Middle Schools, District Thatta. (05 Units).(C:47.391 + R:7.500 ) (SDG#4).	Satisfactory	22-03-2023	Education and Literacy, GOS	30-03-2023	Thatta	54.891
2020-21 249	Establishment of Comprehensive Schools in Sindh ( 25 Units ) (C: 3550.998 + R: 191.550)	Satisfactory	24-08-2022	Education and Literacy, GOS	21-10-2022	Dadu	3742.55
2020-21 294	Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Secondary Schools) (16 Units) (C:71.438+R:30.406) (SDG#4)	Satisfactory	27-08-2021	Education and Literacy, GOS	01-07-2022	Larkana	101.844
2019-20 267	Rehabilitation of Existing High Schools & Higher Secondary Schools District Thatta (AASP)(C: 47.240 + R: 11.230) (SDG#4).	Satisfactory	20-03-2023	Education and Literacy, GOS	30-03-2023	Thatta	58.47
2018-19 194	Immediate Needs for Public School Gadap Town, Karachi (C:231.328 + R:59.364) (SDG # 4)	Un-Satisfactory	08-02-2022	Education and Literacy, GOS	20-07-2022	Karachi	290.692
2018-19 211	Rehabilitation of Government Primary School / Government Girls Secondary School Khatoon- E-Pakistan Stadium Road Karachi (Phase-II) (AASP) (SDG # 4)..	Satisfactory	11-01-2022	Education and Literacy, GOS	01-09-2022	Karachi	43.018
2018-19 294	Establishment of Boys / Girls Degree Colleges in Sindh (23 Units) ( Revised) (C:2093.709 + R: 200.100) (SDG # 4).	Satisfactory	21-03-2023	Education and Literacy, GOS	30-03-2023	Thatta	2864.59
2015-16 185	Up-gradation of Secondary Schools to Higher Secondary Schools in Sindh (2005-06 Programme) (Compliance)	Un-Satisfactory	24-03-2023	Education and Literacy, GOS	06-04-2023	Jamshoro	23.7
2022-23 885	Village Electrification Programme in Sindh (Phase-VIII)	Un-Satisfactory	16-08-2022	Energy, GOS	27-10-2022	Thatta	987.46
2020-21 516	Electrification of Primary Health Facilities Through Solar PV Technology (Revised) (SBA., Ghotki, Larkana, Badin, Dadu, Jamshoro, Khairpur, Shikarpur, Matiari, Sanghar, Mirpurkhas, T.A.Yar & N.Feroze)	Satisfactory	20-10-2022	Energy, GOS	27-01-2023	Shaheed Benazirabad	505.662
2020-21 516	Electrification of Primary Health Facilities Through Solar PV Technology (Revised) (SBA, Ghotki, Larkana, Badin, Dadu, Jamshoro, Khairpur, Shikarpur, Matiari, Sanghar, Mirpurkhas,, T.A.Yar & N.Feroze)	Satisfactory	29-07-2022	Energy, GOS	11-10-2022	Ghotki	505.662
2020-21 516	Electrification of Primary Health Facilities Through Solar PV Technology (Revised) (SBA, Ghotki,, Larkana, Badin, Dadu, Jamshoro, Khairpur, Shikarpur, Matiari, Sanghar, Mirpurkhas, T.A.Yar & N.Feroze)	Satisfactory	26-07-2022	Energy, GOS	11-10-2022	Sanghar	505.662
2022-23 937	Renovation of Excise and Taxation Office Thatta (SDG # 9)	Un-Satisfactory	19-08-2022	Excise & Taxation, GOS	07-12-2022	Thatta	26.417
2022-23 939	Renovation of Excise and Taxation Office Dadu (SDG # 9)	Satisfactory	15-11-2022	Excise & Taxation, GOS	26-01-2023	Dadu	23.786
2021-22 710	Integration / upgradation of Tax Database and Online Tax Collection (SDG # 9).(LTBC)	Un-Satisfactory	21-07-2022	Excise & Taxation, GOS	17-11-2022	Karachi	120
2022-23 954	Construction of Open Platforms/ Plinth for Grain Storage in Sindh	Satisfactory	20-03-2023	Food, GOS	18-04-2023	Kashmore	634.843
2022-23 954	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	06-03-2023	Food, GOS	10-04-2023	Badin	634.843
2022-23 954	Construction of Open Platforms/ Plinth for Grain Storage in Sindh	Un-Satisfactory	15-09-2022	Food, GOS	10-11-2022	Badin	634.843
2022-23 955	Construction of District Food Controller (DFC) Offices, Residences and construction of Security Towers & Compound Walls at various locations of Hyderabad and Mirpurkhas Division (SDG # 2)	Un-Satisfactory	23-11-2022	Food, GOS	20-12-2022	Matiari	417.808
2022-23 955	Construction of District Food Controller (DFC) Offices, Residences and construction of Security Towers & Compound Walls at various	Un-Satisfactory	22-11-2022	Food, GOS	20-12-2022	Tando Muhammad Khan	417.808

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	locations of Hyderabad and Mirpurkhas Division (SDG # 2)						
2022-23 955	Construction of District Food Controller (DFC) Offices, Residences and construction of Security Towers & Compound Walls at various locations of Hyderabad and Mirpurkhas Division (SDG # 2)	Un-Satisfactory	21-11-2022	Food, GOS	13-12-2022	Badin	417.808
2021-22 720	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	14-07-2022	Food, GOS	21-10-2022	Mirpurkhas	634.843
2021-22 720	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	23-06-2022	Food, GOS	03-08-2022	Badin	634.843
2021-22 720	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	07-04-2022	Food, GOS	11-10-2022	Gambar Shahdaddockt	634.843
2021-22 720	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	18-03-2022	Food, GOS	03-08-2022	Matiari	634.843
2021-22 720	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	09-03-2022	Food, GOS	04-08-2022	Jacobabad	634.843
2021-22 721	Construction of District Food Controller (DFC) Offices, Residences and construction of Security Towers & Compound Walls at various locations of Hyderabad and Mirpurkhas Division (SDG # 2)	Un-Satisfactory	20-07-2022	Food, GOS	19-08-2022	Matiari	417.808
2021-22 721	Construction of District Food Controller (DFC) Offices, Residences and construction of Security Towers & Compound Walls at various locations of Hyderabad and Mirpurkhas Division (SDG # 2)	Un-Satisfactory	04-07-2022	Food, GOS	19-08-2022	Hyderabad	417.808
2020-21 542	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	21-06-2021	Food, GOS	05-09-2022	Kashmore	634.843
2020-21 542	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	10-06-2021	Food, GOS	05-09-2022	Larkana	634.843
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m	Satisfactory	07-12-2022	Forest, Wildlife & CDA, GOS	18-01-2023	Tando Muhammad Khan	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m	Satisfactory	06-12-2022	Forest, Wildlife & CDA, GOS	01-03-2023	Mirpurkhas	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m	Satisfactory	05-12-2022	Forest, Wildlife & CDA, GOS	10-01-2023	Badin	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m	Un-Satisfactory	28-09-2022	Forest, Wildlife & CDA, GOS	08-11-2022	Tando Muhammad Khan	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m	Un-Satisfactory	27-09-2022	Forest, Wildlife & CDA, GOS	08-11-2022	Mirpurkhas	3016.35

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m						
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m	Un-Satisfactory	26-09-2022	Forest, Wildlife & CDA, GOS	17-11-2022	Badin	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m	Satisfactory	19-08-2022	Forest, Wildlife & CDA, GOS	26-01-2023	Shikarpur	3016.35
2021-22 723	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m	Satisfactory	28-07-2022	Forest, Wildlife & CDA, GOS	10-01-2023	Tando Allahyar, Matiari, Hyderabad	3016.35
2021-22 724	Possible Role of Mangroves in Curbing Sea Intrusion in Indus Delta (SDG # 15)	Satisfactory	16-05-2022	Forest, Wildlife & CDA, GOS	15-08-2022	Sujawal	698.11
2021-22 725	Enhancing Tree Cover on State Forest Lands in Sindh (Revised) (Jamshoro, Dadu, Matiari, SBA, Sanghar, Shikarpur, Kashmore, Sukkur, Khairpur, Ghotki, N.Feroze, T.M. Khan, Umerkot, Thar, Badin, T.A.Yar, Kamber, Larkano & Jacobabad) (SDG # 15)	Satisfactory	14-06-2022	Forest, Wildlife & CDA, GOS	29-08-2022	Matiari, Jamshoro	708
2021-22 726	Sarsabz Sindh Making Sindh Green and Environment Friendly (SDG # 15)	Satisfactory	12-07-2022	Forest, Wildlife & CDA, GOS	23-11-2022	Larkana	599.944
2021-22 726	Sarsabz Sindh Making Sindh Green and Environment Friendly (SDG # 15)	Satisfactory	06-07-2022	Forest, Wildlife & CDA, GOS	14-12-2022	Kashmore, Jacobabad	599.944
2021-22 726	Sarsabz Sindh Making Sindh Green and Environment Friendly (SDG # 15)	Satisfactory	14-06-2022	Forest, Wildlife & CDA, GOS	14-12-2022	Shikarpur, Qambar Shahdadkot	599.944
2021-22 728	Completion of leftover/remaining targets of Bahman Nature Park Larkano (C: 44.802+R:15.198) (SDG # 15)	Satisfactory	06-09-2021	Forest, Wildlife & CDA, GOS	27-07-2022	Larkana	60
2022-23 1029	Construction of RHC in Village Dau Jahanpur, Taluka Garhi Khairo, District Jacobabad.(C:45.081+R:19.958)(SDG #3)	Satisfactory	15-12-2022	Health, GOS	14-02-2023	Jacobabad	65.039
2022-23 1030	Expansion of Radiology and IPD Services at JIMS, Jacobabad (C:125.080+R:291.424) (SDG #3, 9)	Satisfactory	17-11-2022	Health, GOS	09-02-2023	Jacobabad	416.504
2022-23 1072	Up gradation of BHU to RHC Shadipalli, Taluka Pithoro (Revised on 07.04.21) (C:60.493+R:30.414)(SDG#3)	Un-Satisfactory	19-09-2022	Health, GOS	26-10-2022	Umerkot, Mirpurkhas	90.907
2022-23 1086	Up gradation of THQ Hospitals to the level of DHQ Hospitals (03 Nos) at Matiari, Kamber & Umerkot (Revised on 22.01.16). (C: 1875.856+R: 608.005) (SDG #3)	Un-Satisfactory	21-11-2022	Health, GOS	30-11-2022	Umerkot	2483.86
2022-23 1087	Up gradation of THQ Hospital to the level of DHQ Hospital in newly created district Sindh at Kashmore at Kandhkot (Revised on 13.01.16). (C: 545.542+R: 217.685) (SDG #3)	Satisfactory	13-09-2022	Health, GOS	15-03-2023	Kashmore	763.227
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in	Un-Satisfactory	23-03-2023	Health, GOS	06-04-2023	Matiari	3334.16

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	THQ Hospitals (41 Nos.). (C: 1415.876 + R: 1918.285) (SDG #3) (Bhit Shah & Hala)						
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876 + R: 1918.285) (SDG #3) (Sujawal, Mirpur Bathoro & Jati)	Un-Satisfactory	22-03-2023	Health, GOS	06-04-2023	Sujawal	3334.16
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876 + R: 1918.285) (SDG #3) (Matli, Tando Bago & Golarchi)	Un-Satisfactory	21-03-2023	Health, GOS	06-04-2023	Badin	3334.16
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876 + R: 1918.285) (SDG #3) (Digri & Kot Ghulam Mohammed)	Un-Satisfactory	20-03-2023	Health, GOS	06-04-2023	Mirpurkhas	3334.16
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876 + R: 1918.285) (SDG #3) (Tando Jam)	Un-Satisfactory	17-03-2023	Health, GOS	06-04-2023	Hyderabad	3334.16
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876 + R: 1918.285) (SDG #3) (Nangar & Diplo)	Un-Satisfactory	15-03-2023	Health, GOS	10-04-2023	Tharparkar	3334.16
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876 + R: 1918.285) (SDG #3)	Un-Satisfactory	06-03-2023	Health, GOS	27-06-2023	Larkana	3334.16
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3)	Un-Satisfactory	03-03-2023	Health, GOS	27-06-2023	Dadu	3334.16
2022-23 1179	Neonatal screening for Congenital Hypothyroidism (CH) in Sindh at NICH, Karachi (Revised on 04.06.21) (C:16.448+R:132.465 + PIU 61.373)(SDG#3)	Satisfactory	03-11-2022	Health, GOS	02-01-2023	Karachi	210.286
2022-23 995	Establishment of Psychiatry and Accident / Emergency Unit at Sindh Government Hospital Saudabad, Karachi. (Revised on 18.07.19) (C:177.536+R: 193.215) (SDG #3.4, 3.6)	Satisfactory	09-03-2023	Health, GOS	03-04-2023	Karachi	370.751
2022-23 995	Establishment of Psychiatry and Accident / Emergency Unit at Sindh Government Hospital Saudabad, Karachi. (Revised on 18.07.19) (C: 177.536+R: 193.215) (SDG #3.4, 3.6)	Un-Satisfactory	29-09-2022	Health, GOS	19-01-2023	Karachi	370.751
2021-22 777	Upgradation of Provincial Health Development Centre (PHDC) to the level of Sindh Health Institute of Training & Research. (C:130.193+R:56.670)(SDG#3)	Un-Satisfactory	07-12-2021	Health, GOS	13-10-2022	Jamshoro	186.863
2021-22 782	Construction of Divisional Warehouse at Shaheed Benazirabad. (C:88.930 +R:5.312)(SDG#3)	Satisfactory	25-05-2022	Health, GOS	16-08-2022	Shaheed Benazirabad	94.242
2021-22 783	Upgradation of RHC Daur to the level of Taluka Hospital Daur (Revised) (C: 35.534+R: 56.457)	Satisfactory	25-11-2021	Health, GOS	21-10-2022	Shaheed Benazirabad	91.991
2021-22 787	Upgradation of existing Rural Health Centre to Taluka Headquarter Hospital at Garhi Khairo, District Jacobabad.(C: 170.178 + R:25.000) (SDG #3)	Satisfactory	12-04-2022	Health, GOS	04-07-2022	Jacobabad	195.178

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2021-22 793	Renovation and Rehabilitation of Paramedical Institute, Larkano. (C: 47.948+R: 19.785) (SDG #3)	Un-Satisfactory	20-06-2022	Health, GOS	25-11-2022	Larkana	67.733
2021-22 794	Construction of Divisional Warehouse at Larkano. (C:88.930+R:5.312)(SDG#3)	Satisfactory	11-03-2022	Health, GOS	14-11-2022	Larkana	94.242
2021-22 795	Establishment of Thalassemia Day Care Centre at Dargah Jaral Shah, Larkano. (C:13.224+R:8.762)	Satisfactory	12-11-2021	Health, GOS	27-07-2022	Larkana	21.986
2021-22 796	Upgradation of RHC to 50 bedded hospital at Garhi Khuda Bakhsh Bhutto (C:44.429+R:15.098)(SDG #3)	Satisfactory	25-05-2022	Health, GOS	18-11-2022	Larkana	59.527
2021-22 809	Upgradation of BHU to RHC at Wahi Pandhi, Taluka Johi.(C:44.972+R:19.958)(SDG#3)	Un-Satisfactory	20-09-2021	Health, GOS	11-10-2022	Dadu	64.93
2021-22 810	Upgradation of BHU to RHC Village Bhawalpur, Taluka Johi. (C:44.972+R:19.958)(SDG#3)	Un-Satisfactory	21-09-2021	Health, GOS	30-09-2022	Dadu	64.93
2021-22 820	Upgradation of BHU to RHC Sher Muhammad Bijarani, UC Saifal, Taluka Tangwani. (C:41.989+R:19.958)(SDG# 3)	Un-Satisfactory	15-12-2021	Health, GOS	04-08-2022	Kashmore	61.947
2021-22 821	Upgradation of Health facility at Village Ber Sharif, Taluka Kamber.(C:10.679+R:2.816)(SDG #3)	Un-Satisfactory	08-04-2022	Health, GOS	28-07-2022	Qambar Shahdadkot	13.495
2021-22 829	Upgradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3) at Sujawal, Mirpur Bathoro & Jati.	Worst	23-02-2022	Health, GOS	31-10-2022	Sujawal	3334.16
2021-22 829	Upgradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals @ Ratodero & Dokri (41 Nos.). (C: 1415.876+ R: 1918.285)	Un-Satisfactory	22-02-2022	Health, GOS	18-11-2022	Larkana	3334.16
2021-22 829	Upgradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3) at Bhit Shah & Halla.	Un-Satisfactory	22-02-2022	Health, GOS	05-10-2022	Matiari	3334.16
2021-22 898	Neonatal screening for Congenital Hypothyroidism (CH) in Sindh at NICH, Karachi. (C:5.162+R:157.839)(SDG#3)	Un-Satisfactory	30-07-2021	Health, GOS	03-10-2022	Karachi	163.001
2020-21 559	Establishment of 25 bedded Trauma Centre at Sindh Government Lyari General Hospital, Karachi. (C: 275.969+R: 521.168) (SDG #3)	Satisfactory	26-01-2021	Health, GOS	06-07-2022	Karachi	797.137
2020-21 563	Establishment of Cardio thoracic Surgery Department at Liaquat University Hospital, Hyderabad (Revised). (C: 23.594+R: 353.073) (SDG #3)	Satisfactory	10-08-2021	Health, GOS	26-07-2022	Hyderabad	376.667
2020-21 670	Upgradation of BHU to RHC at Village Kantio, Taluka Chachro. (C:47.781+ R:15.046)(SDG#3)	Satisfactory	07-12-2020	Health, GOS	21-10-2022	Tharparkar	62.827
2020-21 679	Upgradation of BHU to RHC Gulzar Khalil, Taluka Samaro. (C:43.209+R:19.958)(SDG#3)	Satisfactory	13-01-2021	Health, GOS	21-10-2022	Umerkot	63.167
2019-20 705	Upgradation of BHU to RHC Talhi City, Taluka Kunri. (C:43.209+R:19.958)(SDG#3)	Satisfactory	10-03-2020	Health, GOS	21-10-2022	Umerkot	63.167
2019-20 746	Sindh Immunization support program (SIP). (GoS:7648.920+ GoP:400.000 =8048.920) (SDG #3)	Un-Satisfactory	19-05-2022	Health, GOS	30-12-2022	Larkana, Dadu	7648.92
2018-19 525	Up gradation of BHU to RHC Phull. (C:43.874+R:19.958)(SDG# 3)GS	Satisfactory	14-10-2022	Health, GOS	26-01-2023	Naushero Feroz	63.832
2017-18 734	Expansion & Improvement of DHQ Hospitals (03 Nos) at (1) Khairpur (2) Badin & (3) Shikarpur (Revised) (C: 2516.747+R: 923.828) (SDG #3)	Satisfactory	12-10-2022	Health, GOS	14-02-2023	Shikarpur	3440.58
2022-23 1188	Construction of Buildings for Sindh Police at various locations under Police Package (Karachi, Hyderabad, Sujawal, Dadu, Thatta,	Un-Satisfactory	15-11-2022	Home, GOS	04-01-2023	Hyderabad	642.101

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Matiari, Shaheed Benazir Abad, Kamber & Sukkur)(Revised)						
2022-23 1189	Raising / Construction of Watch Tower & Boundary Wall at RRF Base Al-Falah, Naval Colony Base & Police Head Quarter District South Garden Road, Karachi (SDG # 16)..	Un-Satisfactory	23-09-2022	Home, GOS	17-01-2023	Karachi	805.239
2022-23 1202	Construction of Police Station at Phulji	Satisfactory	18-05-2023	Home, GOS	08-06-2023	Dadu	44.998
2022-23 1208	Construction of Police Station (Category-C) & Bachelor Barracks (Ground + 1) at Nindo District Badin (859 of 2017-18) (Remaining work)	Un-Satisfactory	13-09-2022	Home, GOS	21-11-2022	Badin	37.198
2022-23 1209	Construction of Police Station (Category-C) at Dando Taluka Tando Ghulam Hyder District Tando Muhammad Khan. (613 of 2018-19) (Remaining work).	Satisfactory	14-03-2023	Home, GOS	06-04-2023	Badin	29.528
2022-23 1209	Construction of Police Station (Category-C) at Dando Taluka Tando Ghulam Hyder District Tando Muhammad Khan. (613 of 2018-19) (Remaining work)	Un-Satisfactory	14-09-2022	Home, GOS	24-11-2022	Badin	29.528
2021-22 909	Improvement / Strengthening of Security to SCTC Sakrand (Compound Wall with Watch Towers) (SDG # 16)	Un-Satisfactory	27-01-2022	Home, GOS	07-07-2022	Shaheed Benazirabad	48.629
2021-22 917	Construction of Police Station Building at PS Dehi (SDG # 16)	Un-Satisfactory	06-07-2022	Home, GOS	30-08-2022	Badin	34.136
2021-22 925	Construction of Police Station at Phulji	Un-Satisfactory	24-01-2022	Home, GOS	18-11-2022	Dadu	44.998
2021-22 950	Construction of boundary wall around Jail & Residential Colony i/c strengthening of existing main wall, rehabilitation of Watch Towers (4 Nos) & improvement of drainage at Central Prison Larkano.	Un-Satisfactory	26-05-2022	Home, GOS	05-01-2023	Larkana	76.983
2021-22 962	Provision of basic facilities of Sewerage / CC Drain / CC topping in different Katchi Abadis in Sindh..	Worst	14-02-2022	Human Settlement, Spatial Development & Social Housing	04-01-2023	Karachi	40
2022-23 1289	Improvement of Basic Infrastructure at Small Industrial Estate, Industrial Park, Shershah Karachi (4.68 acre land)	Un-Satisfactory	17-11-2022	Industrial & Commerce, GOS	04-01-2023	Karachi	49.11
2021-22 982	Construction of RCC Drain, Allied Works and Road Culverts Along Karachi Circular Railway (KCR) at various locations of Site Area Karachi.	Satisfactory	18-01-2022	Industrial & Commerce, GOS	29-08-2022	Karachi	343.842
2021-22 990	Construction of District Information office at Badin (C: 11.073+R: 01.762)	Un-Satisfactory	06-06-2022	Information & Archives, GOS	19-08-2022	Badin	12.835
2021-22 996	Construction of District Information office at Sujawal (C: 11.138+R: 01.762)	Un-Satisfactory	07-06-2022	Information & Archives, GOS	31-10-2022	Sujawal	12.9
2021-22 1002	Upgradation of Video Conferencing System in Sindh (Revised)(LTBC)	Satisfactory	10-06-2022	Information, Science & Technology, GOS	24-11-2022	Karachi	189.15
2022-23 1435	Rehabilitation of Employees Residence Quarters including Construction of Compound Wall of Irrigation Colonies in Irrigation Department. (Revised on 06.06.22)	Satisfactory	23-09-2022	Irrigation (Water & Drainage), GOS	27-03-2023	Sukkur	767.044
2022-23 1442	Renovation, Reconstruction and Improvement of Executive Engineer Offices and Sub-Divisional Office Complexes in Sindh (Phase -I).	Satisfactory	29-08-2022	Irrigation (Water & Drainage), GOS	20-01-2023	Shaheed Benazirabad	169.521
2022-23 1444	Renovation, Reconstruction and Improvement of Landhi's on all Canal System of Sindh (Phase-I).	Satisfactory	19-08-2022	Irrigation (Water & Drainage), GOS	20-02-2023	Naushero Feroz	194.23

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 1454	Remedial Works to improve Feeding of Manchar Lake from existing Irrigation System.	Satisfactory	05-10-2022	Irrigation (Water & Drainage), GOS	15-11-2022	Jamshoro	207.489
2022-23 1472	Re-sectioning and Sand Coring of Gharaghat Bund mile 0/0 to 2/4 and Haibat Bund mile 0/0 to 5/0 in Begari Division Kashmore.	Satisfactory	22-11-2022	Irrigation (Water & Drainage), GOS	06-03-2023	Kashmore	879.985
2021-22 1047	Surface Drainage Scheme near Village Alam Khan Odho (left over pocket) (Revised) (SDG # 6 & 15)	Satisfactory	16-06-2022	Irrigation (Water & Drainage), GOS	10-11-2022	Jacobabad	399.872
2021-22 1097	Rehabilitation / Resectioning of Johi Branch from Head to Tail (RD-0.0 to 238.560) in Southern Dadu Division & Lining of Pahore and Kharoo Minor (SDG # 6)	Un-Satisfactory	15-03-2022	Irrigation (Water & Drainage), GOS	01-09-2022	Dadu	299.837
2021-22 1123	Lining of Surhari, Brandi, Maldasi, Shahdadpur Minors and Ujjano, Lundo Disty (SDG # 6)	Un-Satisfactory	27-07-2022	Irrigation (Water & Drainage), GOS	23-11-2022	Sanghar	499.579
2021-22 1135	Construction of office Complex in Southern Dadu Division @ Dadu.	Satisfactory	16-03-2022	Irrigation (Water & Drainage), GOS	01-09-2022	Dadu	145.328
2021-22 1163	Removal of Encroachment from Irrigation Department s Property & Securing its possession including Schemes of Rehabilitation (Phase-I).	Satisfactory	14-04-2022	Irrigation (Water & Drainage), GOS	29-08-2022	Sukkur	150
2021-22 1205	Cement Concrete Lining of Ali Bahar Branch from RD-0+00 to RD-20+900	Satisfactory	28-03-2022	Irrigation (Water & Drainage), GOS	29-08-2022	Matiari	255.362
2021-22 1211	C.C. Lining of Wagherji Disty from RD-0+00 to 58+200	Satisfactory	23-03-2022	Irrigation (Water & Drainage), GOS	19-08-2022	Badin	479.415
2021-22 1232	Sindh Resilience Project (Irrigation Component) for Construction of Small Dams including System for Improving Resilience - Phase II (Through Additional Financing) - (Total Cost Rs. 24,493.841 Million (IDA Share Rs. 22,652.920 Million & GoS Share Rs. 1,840.9	Satisfactory	14-03-2022	Irrigation (Water & Drainage), GOS	31-10-2022	Tharparkar	1840.92
2021-22 1232	Sindh Resilience Project (Irrigation Component) for Construction of Small Dams including System for Improving Resilience - Phase II (Through Additional Financing) - (Total Cost Rs. 24,493.841 Million (IDA Share Rs. 22,652.920 Million & GoS Share Rs. 1,840.9	Satisfactory	14-02-2022	Irrigation (Water & Drainage), GOS	27-10-2022	Jamshoro	1840.92
2021-22 1232	Sindh Resilience Project (Irrigation Component) for Construction of Small Dams including System for Improving Resilience - Phase II (Through Additional Financing) - (Total Cost Rs. 24,493.841 Million (IDA Share Rs. 22,652.920 Million & GoS Share Rs. 1,840.9	Satisfactory	17-01-2022	Irrigation (Water & Drainage), GOS	27-10-2022	Tharparkar	2350.71
2021-22 1232	Sindh Resilience Project (Irrigation Component) for Construction of Small Dams including System for Improving Resilience - Phase II (Through Additional Financing) - (Total Cost Rs. 24,493.841 Million (IDA Share Rs. 22,652.920 Million & GoS Share Rs. 1,840.9	Satisfactory	30-12-2021	Irrigation (Water & Drainage), GOS	21-10-2022	Karachi Malir	2350.71
2019-20 904	Construction of Link Drain at RD 0.0 to 25 out-falling in Seerani Branch Drain at RD 40 IP side for Village Pir Buksho and ARO Pusio, U.C Seerani; (ii) Construction of Link Drain RD 0.0 to 14 out-falling in 6-R Tando Bago Sub-Drain at RD 22 IP side for Vi	Un-Satisfactory	22-02-2022	Irrigation (Water & Drainage), GOS	03-08-2022	Badin	119.278

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2018-19 789	Construction of Regulator at Dhoro Puran Intersection RD-261 of LBOD (SDG # 6)	Un-Satisfactory	10-03-2022	Irrigation (Water & Drainage), GOS	29-09-2022	Badin	84.843
Non-ADP	KQ15P00190- Construction of Zulfiqar Oil Tanker Parking Terminal , Zulfiqarabad Karachi, Phase-I (District ADP)	Un-Satisfactory	21-06-2022	Karachi Metropolitan Corporation, KWSB	07-11-2022	Karachi Malir	20
Non-ADP	KQ12P00195- Construction of Food Court in Safari Park Karachi (District ADP)	Satisfactory	17-06-2022	Karachi Metropolitan Corporation, KWSB	01-12-2022	Karachi East	20
Non-ADP	KQ16P00103- Renoation & Improvement outskirts of main lake at Safari Park Karachi (District ADP)	Satisfactory	17-06-2022	Karachi Metropolitan Corporation, KWSB	21-11-2022	Karachi East	19.9
2022-23 1590	Rehabilitation of Old Sessions Court Building / Re-Construction of Compound Wall and External Work at Judicial Complex District Badin (Revised)	Satisfactory	21-12-2022	Law P.A. & Prosecution	15-03-2023	Badin	72.95
2021-22 1283	Construction of Two (02) Courts at MiroKhan (SDG # 16)	Satisfactory	05-01-2022	Law P.A. & Prosecution	18-11-2022	Qambar Shahdaddock	48.833
2021-22 1291	Construction of Record Room alongwith Store Room & Provision of Elevator / Lift Facilities and Construction of Cafeteria at High Court Circuit, Larkano (C: 23.320+R: 1.680)	Un-Satisfactory	12-05-2022	Law P.A. & Prosecution	01-12-2022	Larkana	25
2020-21 1050	Construction of Courts (32 Nos.) at District Court Building, Korangi Karachi (Re-Revised) (Cap:1131.920+Rev:129.601) (SDG # 16)..	Satisfactory	28-02-2022	Law P.A. & Prosecution	11-01-2023	Karachi	1261.52
2022-23 1618	Cement Concrete Lining of Masoodi Distry RD-0.00 to Tail(SDG # 6)	Satisfactory	16-03-2023	Lining of Main Canals	30-03-2023	Thatta	391.171
2022-23 1618	Cement Concrete Lining of Masoodi Distry RD-0.00 to Tail (SDG # 6)	Un-Satisfactory	02-11-2022	Lining of Main Canals	04-01-2023	Thatta	391.171
2022-23 1621	Cement Concrete Lining of Inam & Abad Minor from RD-0.00 to 32 & 2 RDs(SDG # 6)	Satisfactory	17-03-2023	Lining of Main Canals	09-06-2023	Thatta	138.517
2022-23 1621	Cement Concrete Lining of Inam & Abad Minor from RD-0.00 to 32 & 2 RDs (SDG # 6)	Un-Satisfactory	29-11-2022	Lining of Main Canals	11-01-2023	Thatta	138.517
2022-23 1632	Cement Concrete Lining of Husri Distry from RD-18+500 to 37+000 (SDG # 6)	Satisfactory	17-10-2022	Lining of Main Canals	06-02-2023	Hyderabad	219.617
2021-22 1302	Cement Concrete Lining of Mari Minor from RD-0.00 to 48.500	Satisfactory	25-03-2022	Lining of Main Canals	04-07-2022	Sanghar	218.67
2021-22 1304	C.C Lining of Daulatpur Distry from RD-38 + 150 TO RD 100	Satisfactory	24-01-2022	Lining of Main Canals	01-07-2022	Shaheed Benazirabad	331.099
2022-23 1663	Fattening of Calves (R:222.110) (Jamshoro, SBA, Dadu, Sukkur, Khairpur, Ghotki, Larkano, Kamber at S.Kot, Kashmore at K.Kot, Shikarpur & Jacobabad (SDG #2)	Worst	25-11-2022	Livestock and Fisheries, GOS	06-01-2023	Jamshoro	222.11
2021-22 1325	Pilot Project on Establishment of Mobile Artificial Insemination & Extension Service Units in Sindh (Phase-I), (Sukkur, Shikarpur, Jacobabad, Sanghar, Dadu, Jamshoro & Sujawal)	Satisfactory	11-05-2022	Livestock and Fisheries, GOS	04-07-2022	Jamshoro	73.673
2021-22 1327	Installation of Liquid Nitrogen Gas Bouzers (Storage Tanks) for Cryogenic Storage and Transportation System at Rohri and Karachi (R:50.000) (SDG # 2)	Un-Satisfactory	11-11-2021	Livestock and Fisheries, GOS	01-07-2022	Sukkur	50
2021-22 1341	Establishment of Fish Bio Diversity Hatchery & Training and Extension Institute at Manchar Lake, District Jamshoro (C:157.748 + R: 39.950)	Satisfactory	18-11-2021	Livestock and Fisheries, GOS	07-07-2022	Jamshoro	197.698
2021-22 1342	Completion of Missing Schemes of Livestock & Fisheries Department (Hyd., M.Khas, Thatta, T.M. Khan, Sanghar & Jamshoro) (C:82.074 + R:2.000) (SDG #2)[Misssing scheme]	Satisfactory	23-03-2022	Livestock and Fisheries, GOS	16-08-2022	Thatta	84.074

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 1700	Revamping of Mehmoodabad nala from Malir Bund/KPT Fly over to Mehmoodabad	Satisfactory	14-10-2022	Local Government, GOS	02-01-2023	Karachi	271
2022-23 1729	Rehabilitation / Replacement / Improvement of Water Supply and Sewerage System including Pumping Stations in District Central, Karachi	Un-Satisfactory	31-10-2022	Local Government, GOS	02-01-2023	Karachi	149.978
2022-23 1730	Rehabilitation / Replacement / Improvement of Water Supply and Sewerage system including Pumping Stations in District South, Karachi	Un-Satisfactory	03-10-2022	Local Government, GOS	11-01-2023	Karachi	133.771
2022-23 1745	Construction & Rehabilitation of Main / Internal Roads. Providing Sewerage line of 12	Satisfactory	14-03-2023	Local Government, GOS	28-03-2023	Karachi East	95.418
Non-ADP	Construction & Rehabilitation of Main / Internal Roads. Providing Sewerage line of 12	Un-Satisfactory	29-12-2022	Local Government, GOS	24-01-2023	Karachi	95.418
2022-23 1747	Construction / Rehabilitation of Main / Internal Roads and installation of Paver Blocks / CC flooring & Street lights in Sachal Goth Block A to G, Ayub Goth, Christian Para and Shaheed Zulfiqar Ali Bhutto Goth (Seeta Nagar), Bilawal Shah Noorani Goth and	Satisfactory	08-11-2022	Local Government, GOS	01-03-2023	Karachi East	96.098
2022-23 1749	Construction / Rehabilitation of Main Roads / Internal Roads and installation of Paver Blocks / CC flooring & Street Lights in Junejo Town, Chutta Gabol Goth, Saindad Village, Noor Khan Goth, Ahmed Jamal Goth, Khuda Bux Goth and various areas of UC-31	Satisfactory	25-05-2023	Local Government, GOS	16-06-2023	Karachi East	98.023
2022-23 1749	Construction / Rehabilitation of Main Roads / Internal Roads and installation of Paver Blocks / CC flooring & Street Lights in Junejo Town, Chutta Gabol Goth, Saindad Village, Noor Khan Goth, Ahmed Jamal Goth, Khuda Bux Goth and various areas of UC-31	Un-Satisfactory	10-11-2022	Local Government, GOS	24-01-2023	Karachi East	98.023
2022-23 1753	Construction / Rehabilitation of Main / Internal Roads, Providing Sewerage line of 12	Satisfactory	31-05-2023	Local Government, GOS	16-06-2023	Karachi East	99.278
2022-23 1753	Construction / Rehabilitation of Main / Internal Roads, Providing Sewerage line of 12", 15", 18" RCC pipe 4" & 6" PE Water supply line in Rabia City Rabia Bungalows to Classic apartments, Service road from Rabia City via Johar square, Muneer brid	Un-Satisfactory	03-10-2022	Local Government, GOS	09-01-2023	Karachi East	99.278
2022-23 1756	Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line 12	Satisfactory	15-03-2023	Local Government, GOS	28-03-2023	Karachi East	95.126
2022-23 1756	Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line 12	Un-Satisfactory	14-11-2022	Local Government, GOS	11-01-2023	Karachi East	95.126
2022-23 1764	Road Carpeting, C.C Flooring Sewerage line, Manzoor Colony-II (UC-06)	Satisfactory	03-03-2023	Local Government, GOS	15-03-2023	Karachi East	84.749
2022-23 1764	Road Carpeting, C.C Flooring Sewerage line, Manzoor Colony-II (UC-06)	Un-Satisfactory	30-11-2022	Local Government, GOS	11-01-2023	Karachi East	84.749
2022-23 1764	Road Carpeting, C.C Flooring Sewerage line, Manzoor Colony-II (UC-06)	Un-Satisfactory	16-11-2022	Local Government, GOS	11-01-2023	Karachi East	84.749
2022-23 1771	Improvement of Storm Water Drain System alongwith Supreme Court and Rising & Wall of Nallah.	Satisfactory	30-11-2022	Local Government, GOS	16-06-2023	Karachi South	73
2022-23 1784	CC Flooring, Water Supply & Sewerage Line & Road Carpeting in UC-9, Islamia Colony.	Satisfactory	17-11-2022	Local Government, GOS	11-01-2023	Karachi West	66.827
2022-23 1787	Improvement of water supply line, Installation of sewerage line, paver	Un-Satisfactory	21-11-2022	Local Government, GOS	11-04-2023	Karachi West	117.577

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	block and road carpeting in UC-17, UC-27 & UC-28						
2022-23 1788	Improvement of Water Supply line, installation of Sewerage line, CC Flooring, Ground and Road Carpeting in UC-18, UC-24 & UC-26.	Un-Satisfactory	04-10-2022	Local Government, GOS	24-01-2023	Karachi West	95.704
2022-23 1813	Water Supply line, Sewerage line, Paver Block and Carpeting of Roads in different areas of UC-3.	Satisfactory	05-10-2022	Local Government, GOS	05-12-2022	Karachi West	96.463
2022-23 1826	Providing & Laying of Paver Block in Different Streets of UC-41, UC-42, UC-43, UC-44, UC-45 and UC-46 in DMC Keamari	Un-Satisfactory	05-10-2022	Local Government, GOS	26-01-2023	Karachi Keamari	95.99
2022-23 1831	Improvement of Water Supply and installtion of Sewerage line and Carpeting of Road in UC-3 Keamari Town.	Satisfactory	18-10-2022	Local Government, GOS	11-01-2023	Karachi Keamari	68.017
2022-23 1879	Laying of Paver Block at UC 16,17,18,19 and 20 Larkano City	Satisfactory	18-11-2022	Local Government, GOS	27-03-2023	Larkana	58.696
2022-23 1880	Providing & Laying of Paver Block in Taluka Dokri	Satisfactory	02-03-2023	Local Government, GOS	13-03-2023	Larkana	24.966
2022-23 1880	Providing & Laying of Paver Block in Taluka Dokri	Un-Satisfactory	25-10-2022	Local Government, GOS	14-11-2022	Larkana	24.966
2022-23 1882	Providing & Laying of C.C. Paver in various roads & streets of Jacobabad	Satisfactory	16-11-2022	Local Government, GOS	13-02-2023	Jacobabad	300
2022-23 1883	Providing & Laying of Paver Block at Various Streets of Mubarakpur City Taluka Thul	Satisfactory	07-11-2022	Local Government, GOS	27-01-2023	Jacobabad	41.998
2022-23 1887	Providing of Paver Block in Various Streets of Different Villages of Taluka Khanpur	Satisfactory	24-10-2022	Local Government, GOS	08-02-2023	Shikarpur	93.66
2022-23 1888	Providing of Paver Block in various streets in different Ward-I to Ward-30, City Shikarpur	Satisfactory	16-12-2022	Local Government, GOS	23-02-2023	Shikarpur	113.413
2022-23 1889	Providing of Paver Block in various streets of Different villages of Taluka Shikarpur	Satisfactory	01-12-2022	Local Government, GOS	08-02-2023	Shikarpur	95.356
2022-23 1890	Improvement of Various Sreets with Paver Blocks in (i) Rustam Town (ii) Jahan Khan (iii) Village Pyaro Khan Bhayo (iv) Channar Goth (v) Village Qasim Bhayo (vi) Kot Altaf Bhayo	Satisfactory	02-12-2022	Local Government, GOS	08-02-2023	Shikarpur	92.565
2022-23 2156	Construction/Installation of 10 (TEN) No. Pedestrin Bridges at Different Locatios of Karachi	Satisfactory	02-03-2023	Local Government, GOS	14-03-2023	Karachi	284.446
2022-23 2156	Construction/Installation of 10 (TEN) No. Pedestrin Bridges at Different Locatios of Karachi	Un-Satisfactory	11-10-2022	Local Government, GOS	01-12-2022	Karachi	284.446
2022-23 2181	Reconstruction / Rehabilitation of roads, Drain work and Paver Blocks C.C flooring at UC45 Gulshan e Sikandarabad District Keamari Karachi	Un-Satisfactory	14-10-2022	Local Government, GOS	20-12-2022	Karachi Keamari	99.493
2022-23 2236	Construction of Road alongwith drainage, Sewerage and Paver stones in UC Quaidabad and UC Cattle Colony Ward No. 1 District Malir Karachi	Satisfactory	20-10-2022	Local Government, GOS	11-01-2023	Karachi Malir	99.826
2022-23 2387	Construction of Government Dispensaries in Talukka Sakrand and Kazi Ahmed, District Shaheed Benazirabad (04 Nos.), 297+R: 2.888)	Satisfactory	21-12-2022	Local Government, GOS	17-05-2023	Shaheed Benazirabad	23.185
2022-23 2412	Construction of Park and Playground in UC - 30 & 31	Satisfactory	02-11-2022	Local Government, GOS	16-06-2023	Karachi South	100
2022-23 2448	Development of Township in Major Urban Centers (50,000 120 Square Yard Plots with All Civic Services	Satisfactory	18-10-2022	Local Government, GOS	18-01-2023	Karachi	9420.88
Non-ADP	KQ16P00095- Supply & Installation of Flood Lights Power System at Cricket Ground Nazeer Hussain Gulberg , Gym ,F.B Area, KMC Part-I (District ADP)	Satisfactory	24-06-2022	Local Government, GOS	30-11-2022	Karachi Central	20

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
Non-ADP	KQ16P00096- Supply & Installation of Flood Lights Power System at Cricket Ground Nazeer Hussain Gulberg , Gym ,F.B Area, KMC Part-II (District ADP)	Satisfactory	24-06-2022	Local Government, GOS	01-12-2022	Karachi Central	20
Non-ADP	KQ16P00073- Improvement/Repair of M.A Jinnah Road from Capri Cinema to Tower (South) (District ADP)	Un-Satisfactory	22-06-2022	Local Government, GOS	25-01-2023	Karachi South	20
Non-ADP	KQ16P00077- Patch Repair of Allama Rasheed Turabi Road from Rashid Minhas Road to Ziauddin Hospital, District Central Karachi (District ADP)	Un-Satisfactory	22-06-2022	Local Government, GOS	25-01-2023	Karachi Central	19.95
Non-ADP	KQ13P00042- Rehabilitation/Improvement of road from Old Clifton Bridge to PIDC bridge along Railway line District South Karachi (District ADP)	Un-Satisfactory	20-06-2022	Local Government, GOS	25-01-2023	Karachi South	20
2021-22 1375	Improvement of Sewerage System of Sachal Colony, Larkano City (SDG # 6)	Satisfactory	13-07-2022	Local Government, GOS	10-01-2023	Larkana	50
2021-22 1377	Providing Sewerage lines in PS-24 (SDG # 6)	Un-Satisfactory	31-03-2022	Local Government, GOS	13-07-2022	Shaheed Benazirabad	60.409
2021-22 1385	Construction of RCC Nallah including paver Block and replacement of P.E Pipe lines in the route of RCC Nallah for Sehwan Town, District Jamshoro	Satisfactory	07-03-2022	Local Government, GOS	06-02-2023	Jamshoro	189.562
2021-22 1390	Improvement of Drainage System of Sukkur City,	Satisfactory	06-04-2023	Local Government, GOS	10-04-2023	Sukkur	552.66
2021-22 1390	Improvement of Drainage System of Sukkur City	Un-Satisfactory	26-04-2022	Local Government, GOS	22-08-2022	Sukkur	552.66
2021-22 1417	Rehabilitation/Replacement/Improvement of Sewerage, System by replacement P/L 36" 1/2 dia, 24" 1/2 dia 18" 1/2 dia & 12" 1/2 dia Sewerage Line at Block No. 7, Clifton, District South, Karachi.	Worst	14-12-2021	Local Government, GOS	31-10-2022	Karachi	73.42
2021-22 1421	Rehabilitation/Replacement/Improvement of Water Supply System by P/L 12 (LTBC)	Un-Satisfactory	25-05-2022	Local Government, GOS	24-11-2022	Karachi	35.91
2021-22 1421	Replacement of P/F, 12 dia (315MM), 6" 1/2 dia (160MM) & 4" 1/2 dia (11MM) Polyethylene pipeline in Block No. 5 & Different Areas for the Improvement of Water Supply position in Clifton, District South, Karachi	Un-Satisfactory	17-12-2021	Local Government, GOS	26-10-2022	Karachi	35.91
2021-22 1423	Rehabilitation / Improvement and replacement of water and sewerage system in UC-29, 30 and 31 Saddar, DMC South (LTBC)	Un-Satisfactory	14-06-2022	Local Government, GOS	24-11-2022	Karachi	29.13
2021-22 1424	Construction of Underground Tank one lac gallon capacity at Ismail Shaheed Park, Shah Beg lane Pir Muhammad road Lyari, DMC South Karachi (LTBC)	Un-Satisfactory	26-05-2022	Local Government, GOS	11-10-2022	Karachi	27
2021-22 1426	Improvement / Rehabilitation of Strom water Drain along 8000 road and 5000 Road to Yousuf Goth Gadap Town Karachi (Revised) (TCM request)...	Satisfactory	27-04-2022	Local Government, GOS	05-07-2022	Karachi	488.7
2021-22 1427	Providing and Fixing CC paving block Dr. Ghulam Rasool to Baloch Chowk Resham Gali Aga Khan Hospital razzaq Kumbhar Chowk, Jamia Masjid old National Bank & Various Streets at Town Committee Mirpur Sakro District Thatta	Satisfactory	12-04-2022	Local Government, GOS	27-10-2022	Thatta	95
2021-22 1434	Construction of Cover Drain/Repair of exisitbg Drain Ward No.	Satisfactory	07-07-2022	Local Government, GOS	21-12-2022	Sukkur	82.797

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	1,2,3,4,5,6,7,8,9 & 10 MC Rohri District Sukkur(TCM)						
2021-22 1437	Construction of Staff Quarter for Sweeper M.C Rohri	Satisfactory	12-04-2022	Local Government, GOS	27-03-2023	Sukkur	47
2021-22 1443	Construction of Paving block CC Drain and Water Supply for various Streets and Villages of UC Arrore, District Sukkur	Satisfactory	06-01-2022	Local Government, GOS	01-07-2022	Sukkur	115.8
2021-22 1444	Construction of Paving blocks, CC Drains & Water Supply Scheme for Various Streets & Villages of UC Trimoonh, District Sukkur(TCM)	Satisfactory	06-07-2022	Local Government, GOS	22-08-2022	Sukkur	116.2
2021-22 1445	Construction of Paving Block CC Drains for Various Streets & Villages of UC Kotri, District Sukku (TCM)	Satisfactory	08-07-2022	Local Government, GOS	21-12-2022	Sukkur	87.8
2021-22 1661	Widening / Reconditioning of road from Haji Juma Jekhio Goth Dumlottee No.03 to Waja Ali Muhammad Goth (2.0 km) (SDG # 9).	Satisfactory	15-12-2021	Local Government, GOS	08-02-2023	Karachi	18.23
2021-22 1672	Construction / Reconditioning of Roads (02 Units) in Shahdadkot City, Taluka Shahdadkot (6 km) (SDG # 9)	Satisfactory	16-02-2022	Local Government, GOS	22-07-2022	Qambar Shahdadkot	70
2021-22 1677	Rehabilitation of roads of Different Streets of S.M.C.H.S Block-B Karachi (SDG # 9)...	Satisfactory	05-07-2022	Local Government, GOS	05-08-2022	Karachi	45.007
2021-22 1687	Construction of Road # 15 from Dalmia Road to K-Electric Grid Station via Jamia Masjid Zia-ul-Islam Including RCC Sewerage Line System and Providing and Fixing Street Lights Block-19 Gulshan-e-Iqbal District East Karachi (1.67 Km)	Satisfactory	13-03-2023	Local Government, GOS	03-04-2023	Karachi East	56.238
2021-22 1687	Construction of Road # 15 from Dalmia Road to K-Electric Grid Station via Jamia Masjid Zia-ul-Islam Including RCC Sewerage Line System and Providing and Fixing Street Lights Block-19 Gulshan-e-Iqbal District East Karachi (1.67 Km)	Un-Satisfactory	30-03-2022	Local Government, GOS	11-01-2023	Karachi	56.238
2021-22 1688	Construction of Access Road around Malir Campus of Sindh Madressat-ul-Islam University (SMIU), Education City in Gadap Town Karachi (2.44 km)	Satisfactory	20-03-2023	Local Government, GOS	12-06-2023	Karachi	44.774
2021-22 1688	Construction of Access Road around Malir Campus of Sindh Madressat-ul-Islam University (SMIU), Education City in Gadap Town Karachi (2.44 km)	Un-Satisfactory	31-03-2022	Local Government, GOS	19-08-2022	Karachi	44.774
2021-22 1693	Construction of Dumlottee Road from Dumlottee Well to M-9 & M-5 Link Road (12.3 km)	Un-Satisfactory	22-12-2021	Local Government, GOS	27-10-2022	Karachi	494.823
2021-22 1733	Construction/Rehabilitation of Roads , Sewerage and C.C, Flooring in Dumba Goth, District Malir, Karachi	Satisfactory	28-04-2022	Local Government, GOS	05-07-2022	Karachi	159.931
2021-22 1848	Up-gradation of Rural Health Centre Chuhar Jamali to the level of Taluka Hospital Shah Bander at Chuhar Jamali (24 Bedded and Musafirkhana) District Sujawal (C: 27.118+R: 20.551) (SDG #	Un-Satisfactory	11-01-2022	Local Government, GOS	05-08-2022	Sujawal	47.669
2021-22 1854	Rehabilitation / Renovation of Jaral Shah Dargah at Larkano (Re- Revised)	Un-Satisfactory	10-05-2022	Local Government, GOS	05-01-2023	Larkana	30
2021-22 1861	Construction of Parks at Landhi Kotal Chowrangi, Karachi	Satisfactory	09-02-2022	Local Government, GOS	07-07-2022	Karachi	40
2021-22 1867	Beautification of M.C Rohri District Sukkur	Un-Satisfactory	17-03-2022	Local Government, GOS	04-08-2022	Sukkur	51.953
Non-ADP	Renovation of Volly Ball Ground Hussainabad, Hyderabad	Un-Satisfactory	07-06-2022	Local Government, GOS	22-08-2022	Hyderabad	12.867

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
Non-ADP	Construction of Watch Towers, Guard Rooms, Vehicle Shades and Renovation of other Structures of Deputy Commissioner	Un-Satisfactory	22-06-2022	Local Government, GOS	27-09-2022	Hyderabad	40
2020-21 1163	Providing of 10 Nos. Suction Machines and 10 Nos. High Pressure Jetting Machines including Up-gradation of existing machines for improvement of Sewer work in different Districts of Karachi (SDG # 6)..	Satisfactory	18-07-2022	Local Government, GOS	31-10-2022	Karachi	899.92
2022-23 2471	Rehabilitation / Reconstruction of Shahrah-e-Noor Jehan from Abdullah College to Qalandaria Chowk	Satisfactory	12-10-2022	Mega Schemes for Karachi City	11-01-2023	Karachi	1303.83
2022-23 2473	Rehabilitation / Reconstruction of Road from Cafe piyala (near Gulberg Chowrangi) to Rashid Minhas road near UBL Sports complex	Satisfactory	06-10-2022	Mega Schemes for Karachi City	11-01-2023	Karachi	491.895
2022-23 2477	Re-Construction / rehabilitation of Chakiwara Road, Mehrab Khan Essa Road and Tenny Road, Lyari Town (District South) Including SWD System	Satisfactory	11-10-2022	Mega Schemes for Karachi City	11-01-2023	Karachi	933.928
2022-23 2478	Rehabilitation of Approach Roads of Lyari Expressway.	Satisfactory	01-03-2023	Mega Schemes for Karachi City	14-03-2023	Karachi	219.502
2022-23 2478	Rehabilitation of Approach Roads of Lyari Expressway.	Un-Satisfactory	10-10-2022	Mega Schemes for Karachi City	01-12-2022	Karachi	219.502
2020-21 1476	Rehabilitation and Improvement of Karachi Zoo (Re-Revised) (SDG # 9)(visit after expiry of grace period)	Satisfactory	18-03-2022	Mega Schemes for Karachi City	19-08-2022	Karachi	391.934
2022-23 2498	Implementation of various Development Schemes of Minorities in Sindh (Jamshoro, Ghotki, Karachi, Khairpur, Jacobabad, Larkano, Kashmore, Sukkur, N.Feroze, Dadu, SBA, Sanghar, Mirpurkhas, Umerkot, Tharparkar, Matiari, Jacobabad, Jamshoro, Thatta, Shikarp	Satisfactory	03-03-2023	Minorities & Affairs, GOS	02-05-2023	Jamshoro	704.565
2022-23 2498	Implementation of various Development Schemes of Minorities in Sindh (Jamshoro, Ghotki, Karachi, Khairpur, Jacobabad, Larkano, Kashmore, Sukkur, N.Feroze, Dadu, SBA, Sanghar, Mirpurkhas, Umerkot, Tharparkar, Matiari, Jacobabad, Jamshoro, Thatta, Shikarp	Satisfactory	13-10-2022	Minorities & Affairs, GOS	30-11-2022	Tando Allahyar	704.565
2022-23 2498	Implementation of various Development Schemes of Minorities in Sindh (Jamshoro, Ghotki, Karachi, Khairpur, Jacobabad, Larkano, Kashmore, Sukkur, N.Feroze, Dadu, SBA, Sanghar, Mirpurkhas, Umerkot, Tharparkar, Matiari, Jacobabad, Jamshoro, Thatta, Shikarp	Satisfactory	11-10-2022	Minorities & Affairs, GOS	15-11-2022	Matiari	704.565
2022-23 2498	Implementation of various Development Schemes of Minorities in Sindh (Jamshoro, Ghotki, Karachi, Khairpur, Jacobabad, Larkano, Kashmore, Sukkur, N.Feroze, Dadu, SBA, Sanghar, Mirpurkhas, Umerkot, Tharparkar, Matiari, Jacobabad, Jamshoro, Thatta, Shikarp	Satisfactory	05-10-2022	Minorities & Affairs, GOS	15-11-2022	Mirpurkhas	704.565
2022-23 2500	Repair / Renovation of various Mandirs in Hyderabad Division (Hyderabad, Tando Allahyar, T.M Khan, Matiari, Badin, Thatta, Jamshoro, Dadu & SBA)	Satisfactory	30-09-2022	Minorities & Affairs, GOS	21-11-2022	Badin	289.663
2022-23 2500	Repair / Renovation of various Mandirs in Hyderabad Division (Hyderabad, Tando Allahyar, T.M Khan, Matiari, Badin, Thatta, Jamshoro, Dadu & SBA)	Satisfactory	29-09-2022	Minorities & Affairs, GOS	15-11-2022	Matiari	289.663

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 2500	Repair / Renovation of various Mandirs in Hyderabad Division (Hyderabad, Tando Allahyar, T.M Khan, Matiari, Badin, Thatta, Jamshoro, Dadu & SBA)	Satisfactory	28-09-2022	Minorities & Affairs, GOS	01-12-2022	Tando Muhammad Khan	289.663
2022-23 2500	Repair / Renovation of various Mandirs in Hyderabad Division (Hyderabad, Tando Allahyar, T.M Khan, Matiari, Badin, Thatta, Jamshoro, Dadu & SBA)	Satisfactory	22-09-2022	Minorities & Affairs, GOS	24-11-2022	Tando Allahyar	289.663
2022-23 2500	Repair / Renovation of various Mandirs in Hyderabad Division (Hyderabad, Tando Allahyar, T.M Khan, Matiari, Badin, Thatta, Jamshoro, Dadu & SBA)	Satisfactory	20-09-2022	Minorities & Affairs, GOS	30-11-2022	Hyderabad	289.663
2021-22 1941	Repair / Renovation of various Mandirs in Sindh (Karachi, Dadu, Thatta, Tharparkar, Jamshoro, Hyderabad, Larkano, N.Feroze, Khairpur Mirs, Matiari & T.Allahyar) (Revised)	Un-Satisfactory	13-05-2022	Minorities & Affairs, GOS	11-10-2022	Larkana	75.829
2021-22 1942	Reconstruction / Uplift / Expansion of Minorities Places in Sindh (Karachi, Shikarpur, Jamshoro, Umerkot, Thatta & Hyderabad) (Revised)	Un-Satisfactory	16-05-2022	Minorities & Affairs, GOS	14-11-2022	Shikarpur	62.691
2021-22 1944	Implementation of various Development Schemes of Minorities in Sindh (Jamshoro, Ghotki, Karachi, Khairpur, Jacobabad, Larkano, Kashmore, Sukkur, N.Feroze, Dadu, SBA, Sanghar, Mirpurkhas, Umerkot, Tharparkar, Matiari, Jacobabad, Jamshoro, Thatta, Shikarpur)	Un-Satisfactory	29-09-2021	Minorities & Affairs, GOS	01-09-2022	Ghotki	704.565
Non-ADP	Additional facilities of and solar system of DC office Dadu	Satisfactory	22-07-2022	Physical Planning & Housing (Buildings), GOS	30-11-2022	Dadu	19.2
Non-ADP	Remaining work / Missing facilities in Gym Khana Dadu	Un-Satisfactory	15-06-2022	Physical Planning & Housing (Buildings), GOS	05-09-2022	Dadu	30
Non-ADP	Construction of Compound Wall Around Graveyard @ Dado Yaqoob Shah Near Karo Ghat Tulka Ghotki	Un-Satisfactory	30-06-2022	Physical Planning & Housing (Buildings), GOS	13-12-2022	Ghotki	6.3
Non-ADP	Construction of Surface Drains CC Topping & Brick Pavement Union Counsel Darbelo Taluka Kandiyaro	Satisfactory	20-06-2022	Physical Planning & Housing (Buildings), GOS	15-02-2023	Naushero Feroz	4.95
2022-23 2623	Construction/Reconstruction & Rehabilitation of Field Offices-Cum-Residences of Sindh Bureau of Statistics at Meher	Satisfactory	25-08-2022	Planning & Development, GoS	27-01-2023	Dadu	19.993
2021-22 2009	Reconstruction, Renovation & Rehabilitation of Divisional/ District & Sub-Divisional Offices-cum-Residences of Bureau of Statistics, Sindh. (C:165.065 m + R:17.370 m) (Hyderabad, Jamshoro, Dadu, SBA, Badin, T.M.Khan, Sukkur, Ghotki, Larkano, Jacobabad,	Un-Satisfactory	04-07-2022	Planning & Development, GoS	05-09-2022	Jacobabad	302.149
2022-23 2645	Remaining works of RHS-A Centre at Dokri (C:2.847) (SDG # 3, 5)	Un-Satisfactory	18-08-2022	Population Welfare, GOS	19-01-2023	Larkana	2.847
2021-22 2019	Costed Implementation Plan (Revised) (R:2157.837) (SDG # 3, 5)	Satisfactory	07-06-2022	Population Welfare, GOS	25-11-2022	Dadu	2157.84
2021-22 2019	Costed Implementation Plan (Revised) (R:2157.837) (SDG # 3, 5)	Satisfactory	19-01-2022	Population Welfare, GOS	16-08-2022	Ghotki	2157.84
2021-22 2019	Costed Implementation Plan (Revised) (R:2157.837) (SDG # 3, 5)	Satisfactory	18-01-2022	Population Welfare, GOS	12-10-2022	Sukkur	2157.84
2020-21 1533	Costed Implementation Plan (Revised) (R:2157.837) (SDG # 3, 5)	Satisfactory	11-02-2022	Population Welfare, GOS	24-11-2022	Thatta	2157.84
2020-21 1533	Costed Implementation Plan (Revised) (R:2157.837) (SDG # 3, 5)	Satisfactory	10-02-2022	Population Welfare, GOS	24-11-2022	Karachi East	2157.84

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 2676	Providing & Installation of 200 submersible pumps in various villages of district Tharparkar	Satisfactory	27-03-2023	Public Health Engineering, GOS	08-05-2023	Tharparkar	200
2022-23 2676	Providing and Installation of 200 Submersible Pumps in Various Villages of District Tharparkar (SDG # 6).	Un-Satisfactory	26-10-2022	Public Health Engineering, GOS	02-01-2023	Tharparkar	270.743
2022-23 2677	Improvement of Water Supply Scheme in Town Committee Chhachhro & Town Committee Kheme-jo-Par (SDG # 6).	Un-Satisfactory	06-10-2022	Public Health Engineering, GOS	27-01-2023	Tharparkar	65.833
2022-23 2678	Upgradation & Extension of Pipe Line Water Supply Scheme Kunri-Cheel Bund-Kantio-Chachro (WSL-3) (SDG # 6).	Satisfactory	13-10-2022	Public Health Engineering, GOS	06-02-2023	Tharparkar	137.495
2022-23 2714	Construction of Water Supply Scheme Deh Gulanpur, Deh Kathgarh, Deh Line Purani and Deh Keenjhar (SDG#6)	Satisfactory	10-10-2022	Public Health Engineering, GOS	14-02-2023	Kashmore	100
2022-23 2777	Drainage Scheme Misri Khan Jarwar alongwith Disposal Taluka Tando Allahyar.	Satisfactory	22-03-2023	Public Health Engineering, GOS	19-04-2023	Tando Allahyar	25
2022-23 2809	Drainage Scheme Kaloi Town	Satisfactory	19-10-2022	Public Health Engineering, GOS	19-04-2023	Tharparkar	60
2022-23 2828	Providing and Fixing Paving Blocks with Road Drainage in Various Streets of Khanpur Town and Various Villages of UC Mian Jo Goth (SDG # 6).	Satisfactory	14-11-2022	Public Health Engineering, GOS	16-03-2023	Shikarpur	68.651
2022-23 2829	Drainage Scheme Garhi Yaseen (SDG # 6).	Satisfactory	11-10-2022	Public Health Engineering, GOS	09-02-2023	Shikarpur	94.386
2022-23 2843	Drainage Scheme of Radhan Town (SDG # 6).	Satisfactory	21-03-2023	Public Health Engineering, GOS	03-05-2023	Dadu	99.533
2022-23 2843	Drainage Scheme of Radhan Town (SDG # 6).	Un-Satisfactory	27-10-2022	Public Health Engineering, GOS	05-01-2023	Dadu	99.533
2022-23 2847	Construction of Paver Blocks & C.C Drains in Various Muhalla's City Shahdadkot (SDG # 6).	Satisfactory	12-12-2022	Public Health Engineering, GOS	09-02-2023	Qambar Shahdadkot	164.857
2022-23 2849	Construction of C.C Drains and Paver Blocks for Muhallas of Shahdadkot City (SDG # 6).	Satisfactory	13-12-2022	Public Health Engineering, GOS	27-02-2023	Qambar Shahdadkot	100
2022-23 2861	Drainage System for left over areas of City Naudero (SDG#6).	Satisfactory	08-12-2022	Public Health Engineering, GOS	28-02-2023	Larkana	124.851
2022-23 2862	Construction of Paver Block And C.C Drain in Various Areas of City Ratodero (SDG # 6).	Satisfactory	09-12-2022	Public Health Engineering, GOS	28-02-2023	Larkana	123.786
2022-23 2864	Construction of Paver Block & CC Drain in Various locations of UC-01 to 05 Larkano City (SDG # 6).	Satisfactory	07-12-2022	Public Health Engineering, GOS	27-02-2023	Larkana	150
2022-23 2865	Construction of Paver Block and CC Drains of Various Locations of UC-06 to 10 City Larkano (SDG # 6).	Satisfactory	06-12-2022	Public Health Engineering, GOS	27-02-2023	Larkana	150
2022-23 2871	Construction of Drains & Paver Block in Various Streets of Ward No.1,II,III,V&VII of Naudero, Taluka Ratodero(SDG#6).	Satisfactory	10-11-2022	Public Health Engineering, GOS	16-03-2023	Larkana	49.411
2022-23 2873	Construction of Paver Block & CC Drain of Akil Circle ( UC's Akil, Aghani & Phull) (2.50 KMs), Taluka Larkano (SDG # 6).	Satisfactory	07-10-2022	Public Health Engineering, GOS	16-03-2023	Larkana	45.37
2022-23 2874	Construction of Paver/CC Block & CC Drain from Railway Station Badeh to Govt. Hospital Badeh, and Construction of CC Block Paver Block & CC Drain Channa Bridge Dokri to Dokri Bus Stand Via Village Babal Jarwar and various streets of City Badeh and City Do	Satisfactory	08-11-2022	Public Health Engineering, GOS	16-03-2023	Larkana	76.12
2022-23 2875	Construction of Paver/CC Block & CC Drain in different Villages of District Larkano (SDG # 6).	Satisfactory	09-11-2022	Public Health Engineering, GOS	28-02-2023	Larkana	94.616

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 2994	Elimination of Urban Sewerage Discharging in Irrigation Canals and lakes in Sindh Phase-I (Revised on 19.02.19) (SDG # 6)	Satisfactory	06-03-2023	Public Health Engineering, GOS	03-05-2023	Dadu	3764.65
2022-23 2994	Elimination of Urban Sewerage Discharging in Irrigation Canals and lakes in Sindh Phase-I (Revised on 19.02.19) (SDG # 6)	Satisfactory	22-12-2022	Public Health Engineering, GOS	19-04-2023	Badin	3764.65
Non-ADP	Rural Water Supply Scheme Ramzan Rajar, Taluka Kotri, District Jamshoro.	Satisfactory	22-07-2022	Public Health Engineering, GOS	08-02-2023	Jamshoro	3.5
Non-ADP	CONSTRUCTION OF DRAINS, CC BLOCK & PAVER @ VARIOUS EIGHT (8) LOCATIONS OF UC-8,10,11 & 13 OF LARKANA CITY.	Satisfactory	05-04-2022	Public Health Engineering, GOS	04-07-2022	Larkana	19
2021-22 2040	Water Supply Scheme Hub Dam to 42 Various Village Construction of Surface with Pump Room i/c Electricity System near Hub Dam River Deh Allah Phai. (As per TCM request)	Satisfactory	04-07-2022	Public Health Engineering, GOS	02-09-2022	Karachi	144.337
2021-22 2049	Water Supply Line from Dhaknio to Bachu Mahendro-Ji-Dhani and Dargah Mehar Ali Faqeer (SDG # 6).	Satisfactory	17-03-2022	Public Health Engineering, GOS	16-08-2022	Tharparkar	10.975
2021-22 2050	Water Supply Scheme Sokliyo to Veeranio Sokliyo to Behrao Via Rahirani (SDG # 6).	Satisfactory	18-03-2022	Public Health Engineering, GOS	16-08-2022	Tharparkar	36.9
2021-22 2053	Water Supply Scheme Soomar Village (SDG # 6).	Satisfactory	18-05-2022	Public Health Engineering, GOS	15-11-2022	Sujawal	20
2021-22 2054	Water Supply Scheme Raj Malik (SDG # 6).	Un-Satisfactory	16-06-2022	Public Health Engineering, GOS	05-10-2022	Sujawal	13.093
2021-22 2059	Water Supply Scheme Jumma Khan Gabol Deh Amri Taluka Manjhand (SDG # 6).	Satisfactory	15-06-2022	Public Health Engineering, GOS	19-08-2022	Jamshoro	29.978
2021-22 2062	Rehabilitation of Urban Water Supply Scheme Nindo City (SDG # 6).	Satisfactory	05-04-2022	Public Health Engineering, GOS	24-11-2022	Badin	25
2021-22 2071	Water Supply Scheme Mir Mushtaque Ahmed Bijarani UC Karampur Taluka Tangwani	Un-Satisfactory	08-03-2022	Public Health Engineering, GOS	29-08-2022	Kashmore	10
2021-22 2074	Rural Water Supply Scheme Boohar Mathyoon Taluka Kamber (SDG # 6).	Satisfactory	11-11-2021	Public Health Engineering, GOS	29-07-2022	Qambar Shahdadkot	20
2021-22 2076	Rural Water Supply Scheme Khair Muhammad Buriro Taluka Warah (SDG # 6).	Un-Satisfactory	06-04-2022	Public Health Engineering, GOS	28-07-2022	Qambar Shahdadkot	10
2021-22 2077	Water Supply Scheme Village Kot Ghulam Shah UC Rowanti Taluka Kamber (SDG # 6).	Un-Satisfactory	10-01-2022	Public Health Engineering, GOS	27-07-2022	Qambar Shahdadkot	15
2021-22 2081	Urban Water Supply Scheme Shahpur Chakkar Phase-II (SDG # 6).	Satisfactory	22-11-2021	Public Health Engineering, GOS	04-07-2022	Sanghar	306.405
2021-22 2085	Rural Water Supply Scheme Village Jaggan bhayo (Shifting of Source)	Satisfactory	28-01-2022	Public Health Engineering, GOS	16-08-2022	Shikarpur	96.52
Non-ADP	Water Supply Tank Alongwith Distribution Network for Old Sukkur (SDG # 6).	Satisfactory	30-07-2022	Public Health Engineering, GOS	20-02-2023	Sukkur	100
2021-22 2138	Drainage Scheme Misri Khan Jarwar alongwith Disposal Taluka Tando Allahyar	Un-Satisfactory	13-06-2022	Public Health Engineering, GOS	29-08-2022	Tando Allahyar	25
2021-22 2144	Drainage Scheme Village Hussain Kalwhar Taluka Pano Aqil (SDG # 6).	Un-Satisfactory	16-03-2022	Public Health Engineering, GOS	16-08-2022	Sukkur	15
2021-22 2147	Rehabilitation & Improvemnet of Urban Drainage Scheme Shikarpur (Revised) (SDG # 6).	Satisfactory	25-11-2021	Public Health Engineering, GOS	16-08-2022	Shikarpur	1197.25
2021-22 2159	Improvement / Extension of Drainage Scheme Kamber (SDG # 6)	Un-Satisfactory	07-03-2022	Public Health Engineering, GOS	04-07-2022	Qambar Shahdadkot	648.5
2021-22 2161	Rural Drainage Scheme Aali Khabhar UC Khabhar Taluka Warah (SDG # 6).	Un-Satisfactory	11-01-2022	Public Health Engineering, GOS	28-07-2022	Qambar Shahdadkot	20

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2021-22 2162	Rural Drainage Scheme Mubarakpur Taluka Miro Khan (SDG # 6).	Un-Satisfactory	11-03-2022	Public Health Engineering, GOS	27-07-2022	Qambar Shahdadkot	15
2021-22 2174	Rural Drainge Scheme Dalel Dero UC-Punhal Khan Chandio (SDG # 6).	Satisfactory	24-03-2022	Public Health Engineering, GOS	21-10-2022	Shaheed Benazirabad	37.311
2021-22 2182	Improvement & Extension of Urban Drainage Scheme Behlani alongwith CC Block. @	Satisfactory	19-05-2022	Public Health Engineering, GOS	22-03-2023	Naushero Feroz	30
2021-22 2197	Drainage System of Village Adur Narejo Deh Golo Wahan Taluka Gambat (SDG # 6).	Satisfactory	13-04-2022	Public Health Engineering, GOS	10-01-2023	Khairpur	15
2021-22 2199	Improvement & Extension of Drainage Scheme Gadeji Taluka Sobho Dero (SDG # 6).	Un-Satisfactory	23-12-2021	Public Health Engineering, GOS	22-08-2022	Khairpur	30
2021-22 2201	Rural Drainge Scheme Maghanwari Taluka Kingri	Un-Satisfactory	21-01-2022	Public Health Engineering, GOS	25-11-2022	Khairpur	25
2021-22 2203	Construction of Surface Drains & Paver Bock for Village Haji Ali Nawaz Rajper, UC Karondi, Taluka Faiz Ganj, District Khairpur	Satisfactory	15-12-2021	Public Health Engineering, GOS	12-08-2022	Khairpur	13.325
2021-22 2315	Rehabilitation of Non-Functional Water Supply and Drainage Schemes Phase-I (Revised)(SDG # 6)	Satisfactory	16-11-2021	Public Health Engineering, GOS	16-08-2022	Dadu	5269
2021-22 2329	Construction of Power & Drainage Scheme for Village Qadir Bux Mugheri UC Wagan Taluka Warah (ADP No.1640/2018-19) (SDG # 6).	Un-Satisfactory	22-08-2022	Public Health Engineering, GOS	11-01-2023	Qambar Shahdadkot	8.458
2021-22 2330	Rural Drainage Scheme Khabri Taluka Lakhi (Non-ADP of 2018-19) (SDG # 6).	Satisfactory	11-02-2022	Public Health Engineering, GOS	29-07-2022	Shikarpur	17.627
2021-22 2341	Construction of Lalu Waggan Road from Village Muhammad Khan to Azeem Brohi UC Noor Abad Taluka Warah district Kamber-Shahdadkot (3km)(SDG # 1, 9, 11)	Un-Satisfactory	13-04-2022	Public Health Engineering, GOS	15-07-2022	Qambar Shahdadkot	16
2021-22 2343	Construction of Road from Village Haji Rustam Mehari to Village Manik Mangrio UC-Rahoki Taluka Shaheed Fazil Raho. (3KM) (SDG # 1, 9, 11 Rural Development Department	Satisfactory	20-09-2021	Public Health Engineering, GOS	02-09-2022	Badin	20
2021-22 2350	Construction of Road from Village Varasham Shodo to Ali Murad Barejo, U.C Sari, Taluka Thana Bulla Khan, District Jamshoro.(1.5 km) (SDG # 1, 9, 11 Rural Development Department	Satisfactory	23-09-2021	Public Health Engineering, GOS	02-09-2022	Jamshoro	12
2021-22 2356	Construction of Metalled Road / C.C Drain / Paver Block from Jurio Chandio to Haji Allah Dito House via Allah Warayo Chandio to Syed Zulfiqar Ali Shah Dargah, Mumtaz Colony.(SDG # 1, 9, 11)	Satisfactory	03-02-2022	Public Health Engineering, GOS	29-07-2022	Larkana	27.806
2021-22 2402	Construction of C.C Drain / Paver Block from I.B Khuro Public School to Baghan Shah Hotel via Roshan Chandio Shakh. (C:12.000)(SDG #6)	Un-Satisfactory	12-01-2022	Public Health Engineering, GOS	29-08-2022	Larkana	12
Non-ADP	Construction of paving block i/c drain from Raza Soomro Shop to Dadu Moro road via Agriculture workshop i/c link to Gov	Un-Satisfactory	28-07-2022	Public Health Engineering, GOS	30-11-2022	Dadu	30
Non-ADP	Construction of Severage Line from Railway Line, Essa Dall VIA Bihar Colony to Phatak Kotri, District Jamshoro	Un-Satisfactory	27-06-2022	Public Health Engineering, GOS	07-11-2022	Jamshoro	7
Non-ADP	Construction of Darinage Scheme at Malik, Shaikh and Channa Muhalla	Satisfactory	29-07-2022	Public Health Engineering, GOS	15-02-2023	Kashmore	10
Non-ADP	Remaining Work of Drainage Scheme Village Changar UC Shah Bhangio Tulka Khairpur	Satisfactory	16-06-2022	Public Health Engineering, GOS	22-03-2023	Khairpur	23.985
Non-ADP	Construction of CC Block & Drainage from House of Naban Mugheri to House of Akhtar Brohi Larkanao Taluka Larkano	Satisfactory	09-06-2022	Public Health Engineering, GOS	12-08-2022	Larkana	39.6

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
Non-ADP	Construction of CC Block & Drainage from Abdul Ghani House via Mumtaz Ali Borhi House to Muhammad Safar Baloach UC-7 Larkanao Taluka Larkano	Satisfactory	10-06-2022	Public Health Engineering, GOS	12-08-2022	Larkana	39.3
Non-ADP	Construction of Paver Block & CC drains from Hosue of Imam Din Chandio to House of Abdul Hameed Pathan Larkanao city Taluka Larkano	Satisfactory	13-06-2022	Public Health Engineering, GOS	12-08-2022	Larkana	39.1
2020-21 1671	Elimination of Urban Sewerage Discharging in Irrigation Canals and lakes in Sindh Phase-I (Revised) (SDG # 6)	Satisfactory	12-03-2021	Public Health Engineering, GOS	01-07-2022	Larkana	3764.65
2017-18 2145	Construction of CC Drains and CC Block at various UCs of Larkana (20 Villages) (SDG # 6)	Un-Satisfactory	21-04-2022	Public Health Engineering, GOS	16-08-2022	Larkana	40
2022-23 3075	Establishment of Regional Offices of PDMA (SDG # 13) (C:861.338+R:30.515). (Revisit As per decision of PDWP meeting)	Satisfactory	05-05-2023	Rehabilitation (PDMA), GOS	31-05-2023	Mirpurkhas	891.853
2022-23 3075	Establishment of Regional Offices of PDMA (SDG # 13) (C:861.338+R:30.515)	Un-Satisfactory	04-05-2023	Rehabilitation (PDMA), GOS	31-05-2023	Larkana	891.853
2022-23 3075	Establishment of Regional Offices of PDMA (SDG # 13) (C:861.338+R:30.515))	Satisfactory	03-05-2023	Rehabilitation (PDMA), GOS	31-05-2023	Shaheed Benazirabad	891.853
Non-ADP	Construction of road at Village Momin Panhwar Mile: 0/00/2+330 (0.5 Kms)	Un-Satisfactory	05-07-2022	Rural Development , GOS	07-11-2022	Mirpurkhas	7.5
Non-ADP	Construction of Road from KGM Dhenghan Road to Village Dhengan City Mile: 6/6+2207/0+550 (0.50 Kms)	Satisfactory	14-07-2022	Rural Development , GOS	15-11-2022	Mirpurkhas	18.9
2021-22 2338	Construction of Link Road Saleem Khan Khoso to Suhbat Khan Bajkani UC Jagirabad Taluka Tangwani District Kashmore (2.5 km) (SDG # 1, 9, 11)	Un-Satisfactory	22-03-2022	Rural Development , GOS	29-08-2022	Kashmore	18
2021-22 2352	Re-Construction / Repair of Road Karama Bagh Muhammad Pur.(SDG # 1, 9, 11)	Satisfactory	21-03-2022	Rural Development , GOS	13-07-2022	Larkana	18
2021-22 2358	Construction of Road Wado Wahan Taluka Bakrani. (SDG # 1, 9, 11)	Satisfactory	29-03-2022	Rural Development , GOS	13-07-2022	Larkana	16
Non-ADP	Construction of Road From Dahar Wah to Haji Malik Fareed Malik via Nihal Wah Mile 0/0 to 1/5 +330	Satisfactory	30-06-2022	Rural Development , GOS	30-11-2022	Ghotki	19.958
Non-ADP	Reconditioning of Link Road From Allah Wala Chowk up to Civil Hospital N.Feroz 0/0 0/1	Satisfactory	10-06-2022	Rural Development , GOS	30-11-2022	Naushero Feroz	7.1
Non-ADP	Reconditioning of Link Road From Moro Mithyani Road To Village Ali Murad Lanjar Road 0/0 to 1/2	Satisfactory	06-06-2022	Rural Development , GOS	16-01-2023	Naushero Feroz	20
Non-ADP	Construction of Road From Tharushah N.feroz to village Ismail Vistro UC Malan Road Mile 0/0 to 0/2 Tulka Bhriya	Satisfactory	09-06-2022	Rural Development , GOS	25-11-2022	Naushero Feroz	3.6
Non-ADP	Construction of Road From NHA To Imam Bux Mangrio Along Sehra Minor Road Mile 0/0 0/1+330 Tulka Kandiyaro	Satisfactory	07-06-2022	Rural Development , GOS	30-11-2022	Naushero Feroz	2.9
Non-ADP	Construction of Link Road from Deewan Jo Keerio Road Village Mukrari Via Darghah Mehar Ali Shah Road Mile 0/0 to 0/5+190	Satisfactory	08-06-2022	Rural Development , GOS	25-11-2022	Naushero Feroz	12
2021-22 2419	Construction of Circuit House, Larkano	Satisfactory	24-06-2022	S.G.A.and Coordination, GOS	13-09-2022	Larkana	72.081
2021-22 2431	Establishment of Deputy Commissioner office Complex, District Malir.	Satisfactory	02-02-2023	S.G.A.and Coordination, GOS	09-02-2023	Karachi	354.162
2018-19 1749	Renovation & rehabilitation of flats at GOR at Shadman Town Karachi.	Un-Satisfactory	07-03-2023	S.G.A.and Coordination, GOS	06-04-2023	Karachi	41.066

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 3159	Construction of Sports Stadium in Sindh (8 Nos.) (Matiari, Jamshoro, Hyderabad, Tharparkar, Sanghar, Shikarpur, Jacobabad & Tando Allahyar) (Revised on 20.02.20) (C:481.026+R:40.000)(SDG # 3)	Un-Satisfactory	16-11-2022	Sports & Youth Affairs, GOS	04-01-2023	Jamshoro	521.026
2022-23 3171	Construction of Multipurpose Sports Hall at Sports Complex	Satisfactory	06-10-2022	Sports & Youth Affairs, GOS	21-02-2023	Shikarpur	55
2022-23 3173	Construction of Grassy Cricket Ground with Pavilion i/c Installation of Flood Lights at Force Ground	Satisfactory	15-03-2023	Sports & Youth Affairs, GOS	16-05-2023	Jacobabad	93.5
2022-23 3181	Laying of New Blue Synthetic Hockey Turf & Digital Score Board at Existing Hockey Stadium NIPA	Satisfactory	30-09-2022	Sports & Youth Affairs, GOS	23-02-2023	Karachi East	88
2022-23 3182	Construction of Multipurpose Sports Hall i/c Walking Track Makhdoom Bilawal Cooperative Housing Society	Satisfactory	30-09-2022	Sports & Youth Affairs, GOS	23-02-2023	Karachi Korangi	66
2022-23 3189	Construction of Futsal Ground for Ladies at Government Girls College	Satisfactory	09-03-2023	Sports & Youth Affairs, GOS	18-04-2023	Jacobabad	44
2021-22 2503	Construction of Players Hostel at Ghotki (C:51.893+R:9.381)	Satisfactory	31-12-2021	Sports & Youth Affairs, GOS	05-09-2022	Ghotki	61.274
2021-22 2512	Construction of Sports Ground at Thul City Taluka Thul District Jacobabad (C:41.117+R:0.156)	Satisfactory	27-09-2022	Sports & Youth Affairs, GOS	21-02-2023	Jacobabad	41.273
2021-22 2512	Construction of Sports Ground at Thul City Taluka Thul District Jacobabad (C:41.117+R:0.156)	Un-Satisfactory	16-09-2021	Sports & Youth Affairs, GOS	06-07-2022	Jacobabad	41.273
2021-22 2513	Installation of Flood Litghts with stand by Generator and External Works at Football Turf Stadium Public School, Hyderabad (Phase-I) (C:49.813+R:0.186)	Satisfactory	25-05-2022	Sports & Youth Affairs, GOS	16-08-2022	Hyderabad	49.999
2021-22 2519	Construction of Sports Indoor Hall at Railway Ground, Sukkur	Satisfactory	15-04-2022	Sports & Youth Affairs, GOS	13-07-2022	Sukkur	54.346
2021-22 2531	Construction of Grassy Cricket Ground with Pavilion i/c Installation of Flood Lights at Force Ground	Un-Satisfactory	04-07-2022	Sports & Youth Affairs, GOS	09-01-2023	Jacobabad	85
2021-22 2548	Construction of Futsal Ground for Ladies at Government Girls College	Un-Satisfactory	23-05-2022	Sports & Youth Affairs, GOS	22-08-2022	Jacobabad	40
2021-22 2552	Construction of Lalkhmir Sports Ground at Taluka Jacobabad	Satisfactory	05-07-2022	Sports & Youth Affairs, GOS	13-02-2023	Jacobabad	45
2021-22 2569	Construciton of Youth Development Center at Kambar (C:54.978+R:5.022)	Un-Satisfactory	10-11-2021	Sports & Youth Affairs, GOS	11-11-2022	Qambar Shahdadkot	60
2022-23 789	Umbrella schemes transferred from Education & Labour Department to STEVTA Karachi (22 units)	Satisfactory	04-11-2022	STEVTA, GOS	28-03-2023	Karachi	5440
2021-22 796	Construction of B-Tech Department at Governmemnt College Technology (GCT) Hyderabad	Satisfactory	28-03-2023	STEVTA, GOS	30-03-2023	Hyderabad	140
2022-23 842	Development of Remaining Essential Facilities Required for Establishment of Mehran University College of Engineering and Technology at Khairpur Mir's (C:717.236 .+ R:130.492) (SDG#4)	Satisfactory	03-03-2023	Universities and Boards	06-04-2023	Khairpur	847.728
2022-23 863	Construction of Central/Digital Library at Chandka Medical College of SMBBMU Larkano (C:375.189 + R:101.340) (SDG#4)	Satisfactory	20-09-2022	Universities and Boards	18-11-2022	Larkana	476.529
2021-22 630	Development of Department of Food Engineering & Infrastructure at NED University of Engineering & Technology, Karachi (C:159.779 + R:167.564) (SDG#4).	Satisfactory	27-10-2021	Universities and Boards	06-07-2022	Karachi	327.343
2021-22 632	Extension of Educational Allied Facilities at Sukkur IBA and IBA Community College Khairpur(C: 861.716 + R: 438.284.) (SDG#4)	Satisfactory	06-03-2023	Universities and Boards	21-03-2023	Khairpur	1300
2021-22 632	Extension of Educational Allied Facilities at Sukkur IBA and IBA	Satisfactory	22-02-2022	Universities and Boards	29-03-2023	Sukkur	1300

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Community College Khairpur(C: 861.716 + R: 438.284) (SDG#4)						
2021-22 632	Extension of Educational Allied Facilities at Sukkur IBA and IBA Community College Khairpur(C: 861.716 + R: 438.284) (SDG#4)	Un-Satisfactory	18-02-2022	Universities and Boards	07-11-2022	Khairpur	1300
2022-23 3313	Renovation of Existing Building of Women Development Complex at Sanghar (C: 21.772+R:1.980) ,(SDG # 1,4, 5,8 & 9)	Satisfactory	21-10-2022	Women Development , GOS	16-01-2023	Sanghar	23.752
2022-23 3314	Establishment & Strengthening of Darul Aman at Mirpurkhas & Jacobabad (Revised on 16.05.17)(C:154.680 + R:32.014) (SDG # 2)	Satisfactory	22-09-2022	Women Development , GOS	08-02-2023	Mirpurkhas	186.694
2021-22 2610	Repair and Maintenance of Existing Building of Women Training Institute at Shaheed Benazir Abad.	Worst	10-06-2022	Women Development , GOS	04-01-2023	Shaheed Benazirabad	36.92
2021-22 2612	Renovation of Existing Building of Women Development Complex at Sanghar (C: 21.772+R:1.980) (SDG # 1,4, 5,8 & 9)	Un-Satisfactory	22-02-2022	Women Development , GOS	06-07-2022	Sanghar	23.752
2022-23 3330	W/R of road from Arrore Bachal Shah to Choundko (32.18 Kms) (SDG # 9)	Un-Satisfactory	30-11-2022	Work and Service, GOS	09-01-2023	Sukkur	540.878
2022-23 3334	W/R of Jacobabad Thull road (37.00 Kms) (SDG # 9)	Satisfactory	31-05-2023	Work and Service, GOS	28-05-2023	Jacobabad	1950.05
2022-23 3366	Improvement of road from Old Indus Highways City Portion Larkano to N.I.P Side of Rice Canal via Hashain Medical Center i/c Paver Link in Ghulam Akbar Jalbani Street upto SZABIST College and approaches to various streets Sachal Colony Larkana (4.40 Kms)	Satisfactory	31-10-2022	Work and Service, GOS	01-03-2023	Larkana	119.991
2022-23 3367	W/R of road from Sanhra Machi to Police Picket Post village Bosan, including approach to village Imam Bux Langah - Wassayo Bhutto road (6.00 Kms)	Satisfactory	21-10-2022	Work and Service, GOS	09-02-2023	Larkana	101.976
2022-23 3376	Reconditioning of road from Thouf Chosul - Bhand Chowk road Mahmoodabad Police Chowki to Miro Khan (7.00 Kms)	Satisfactory	05-12-2022	Work and Service, GOS	13-02-2023	Qambar Shahdadkot	76.932
2022-23 3391	Rehabilitation / Reconditioning of road from Hakra Panhwr Chowki to Bhiro (10.00 Kms)	Satisfactory	02-03-2023	Work and Service, GOS	18-04-2023	Sukkur	96.21
2022-23 3391	Rehabilitation / Reconditioning of road from Hakra Panhwr Chowki to Bhiro (10.00 Kms)	Un-Satisfactory	25-10-2022	Work and Service, GOS	09-01-2023	Sukkur	96.21
2022-23 3400	Reconditioning of road from Mehran N/Highway to Deparja Nawab Ali Shah Bhambhan via Khairi road (14.00 Kms)	Satisfactory	22-08-2022	Work and Service, GOS	20-12-2022	Khairpur	134.813
2022-23 3439	Reconditioning of road from Moro - Dadu road to village Jadal Shah 1-1/2	Satisfactory	11-10-2022	Work and Service, GOS	20-12-2022	Naushero Feroz	65.635
2022-23 3441	W/R / Construction / Reconditioning of various roads of Taluka Nawabshah (79.30 Kms))	Satisfactory	05-06-2023	Work and Service, GOS	19-06-2023	Shaheed Benazirabad	1235.78
2022-23 3442	Improvement / Rehabilitation of various roads / streets of Nawabshah City (42.23 Kms)	Satisfactory	05-06-2023	Work and Service, GOS	19-06-2023	Shaheed Benazirabad	971.082
2022-23 3448	W/R / Construction of road from 60th Mile - 3 Chak Suhallo road @ 18 Shak Stop to connect Ghazi Khan Bhurgari road @ Nim Stop via Sui Gas H.Q & link to village Masood Nabi Noor along Akdohi Minor mile 0/0-5/2+330 (8.50 Kms)	Satisfactory	14-11-2022	Work and Service, GOS	26-01-2023	Shaheed Benazirabad	175.451
2022-23 3459	Reconditioning of road from Daur - Kazi Ahmed road to connect Nawabshah - Naushahro Feroze road @ Basham Rind along Sim Nala road (5.00 Kms) (With 2	Satisfactory	15-11-2022	Work and Service, GOS	27-03-2023	Shaheed Benazirabad	58.292
2022-23 3463	Improvement of road from Oderolal to Shahdadpur (From Oderolal to	Satisfactory	31-08-2022	Work and Service, GOS	07-03-2023	Sanghar	168.111

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Mulla Mukhan road) (9.00 Kms) (with Asphalt Surface)						
2022-23 3511	Reconditioning Tando Adam road to village Suleman Palli, village Mitho Mirjat, village Ibrahim Shah, village Madan Mirjat, village Ghulam Nabi Shah, village Khair Shah via Pannah Shah road approach Barecha mile 0/0 - 7/4 (12.00 Kms)	Satisfactory	16-08-2022	Work and Service, GOS	28-11-2022	Tando Allahyar	100
2022-23 3520	Reconditioning of Asphalt Concrete road from Tando Fazal Chowk to village Baksho Leghari (6.00 Kms)	Satisfactory	08-12-2022	Work and Service, GOS	15-03-2023	Hyderabad	64.736
2022-23 3539	Improvement of road from Rajo Khanani Talhar road to Mehro Bhurgari i/c link to Dewani Faqeer (10.00 Kms)	Satisfactory	09-12-2022	Work and Service, GOS	02-02-2023	Badin	99.75
2022-23 3803	Construction of road from Larkana Kamber road @ Point Railway Phattak to connect Kamber Wagan road mile 0/0-3/5 (5.83 Kms) (SDG # 9)	Satisfactory	20-12-2022	Work and Service, GOS	08-02-2023	Qambar Shahdadkot	348.198
2022-23 3859	Reconditioning Of Road From Waggan Warah Road At Point Lalu Raunk To Ghabidero Road @ Point Thori Bijar (7.00 Kms)	Satisfactory	27-12-2022	Work and Service, GOS	09-02-2023	Qambar Shahdadkot	109.959
2022-23 3893	Construction / Reconditioning of road from National Highway near Jam Noorullah to village Yaral Ghanghro (Malokani Ghanghra) along Gul Minor (6.80 Kms)	Satisfactory	12-10-2022	Work and Service, GOS	20-12-2022	Naushero Feroz	65.92
2022-23 3991	Construction / Reconditioning of road from Phull Sadhuja road to National Highway via village Manghlo Solangi and Gul Mohammad Mubejo connecting villages Haji Mohammad Siddique Solangi & Haji Mohammad Qasim Solangi (11.00 Kms)	Satisfactory	10-10-2022	Work and Service, GOS	20-12-2022	Naushero Feroz	105.395
Non-ADP	Construction of Road From Mahar Road to Muhammad Usman Mahar	Un-Satisfactory	18-08-2022	Work and Service, GOS	13-12-2022	Sukkur	19.77
Non-ADP	Construction Of Prestressed Bridge 600Rft Including Road of Soomra Panhwari to Hussain Beli via Police Pict 00-50	Un-Satisfactory	14-07-2022	Work and Service, GOS	13-12-2022	Sukkur	209.351
Non-ADP	Construction of Pre-stressed 120'Rft i/c approaches(01) Bridge in District Kamber-ShahdadKot over Saifullah Canal atv	Un-Satisfactory	21-06-2022	Work and Service, GOS	25-11-2022	Qambar Shahdadkot	17
Non-ADP	Establishment/ Rehabilitation of Green Bets and Public Parks at District Kamber-Shahdadkot.	Un-Satisfactory	24-06-2022	Work and Service, GOS	25-11-2022	Qambar Shahdadkot	8
Non-ADP	R/Rehabil: of Deputy District Officer (Revenue) Office & Mukhtairkar Office Taluka Hala	Un-Satisfactory	22-08-2022	Work and Service, GOS	07-11-2022	Matlari	10.529
Non-ADP	Constt of Road from Malihar to Abdullah ji Dhani	Satisfactory	25-07-2022	Work and Service, GOS	02-09-2022	Tharparkar	38.9
Non-ADP	Constt of Road from Wadero Baboo Khan Birhamani Machine to Thana Arab Khan	Un-Satisfactory	15-07-2022	Work and Service, GOS	11-04-2023	Jamshoro	20
Non-ADP	Constt of Road from Wadero Saleh Mohammad to Birhamani Machine to Thana Arab Khan	Un-Satisfactory	18-07-2022	Work and Service, GOS	19-04-2023	Jamshoro	20
Non-ADP	Construction of office Accomodation for Assistant Engineer, Highway/ Buildings at Talhar & Matli.	Un-Satisfactory	11-08-2022	Work and Service, GOS	07-11-2022	Badin	12
Non-ADP	Reconditioning oflink road from Tando M Khan shaikh Bhirkio to Shienh Nizamani Road mile 0/0-1/6	Satisfactory	02-08-2022	Work and Service, GOS	24-11-2022	Tando Muhammad Khan	40
Non-ADP	Constt of CC Roads in different streets of Islamkot town	Satisfactory	26-07-2022	Work and Service, GOS	21-11-2022	Tharparkar	36.987
Non-ADP	Constt of CC Roads in different streets of Nangarparkar	Satisfactory	27-07-2022	Work and Service, GOS	11-10-2022	Tharparkar	38.998
Non-ADP	Construction of Rooms (Annexes) at Collectors Residence District Hyderabad	Satisfactory	19-06-2023	Work and Service, GOS	20-06-2023	Hyderabad	39.9

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
Non-ADP	Construction of Rooms (Annexes) at Collectors residence District Hyderabad	Un-Satisfactory	24-08-2022	Work and Service, GOS	07-11-2022	Hyderabad	39.929
2021-22 2648	Improvement of road from Faizu Jahan Khan Indus Highway Sardar Fateh Muhammad Khan Jatoi upto Npreiabad (12.010Kms) (SDG # 9)	Un-Satisfactory	19-07-2022	Work and Service, GOS	04-10-2022	Shikarpur	169.059
2021-22 2653	W/R / Construction of road from Kumb to Malheer Patto via Bkahu Khan Lashari Rais Bangal Khan Chandio upto Old N.H.Way Kotdiji road mile 0/0-12/6 (20.50 kms)	Un-Satisfactory	18-04-2022	Work and Service, GOS	13-07-2022	Khairpur	301.255
2021-22 2676	Reconditioning of road from Jam Sahib to Mundh Jamrao with 2\	Satisfactory	21-04-2022	Work and Service, GOS	06-07-2022	Shaheed Benazirabad	1049.56
2021-22 2683	Improvement of Road Network from Badin to Wango Mar, Rehabilitations of Damaged Road Portions (29.00 Kms) (Revised) (SDG # 11)	Satisfactory	05-04-2022	Work and Service, GOS	13-12-2022	Badin	2488.93
2021-22 2687	W/R of road from Badin Sujawal road, starting point Bachal Water to Kario Khorwah road via village Gul Mir Shah, Haroon Nadeh, Chak No. 6, Bajari Shareef 18.00 Kms = 11/1 + 376 mile (SDG # 9)	Satisfactory	19-04-2022	Work and Service, GOS	27-01-2023	Sujawal	334.953
2021-22 2691	Improvement of road from Patt Moori to village Dangar via link road village Andal Chandio UC Patt (6.44 Kms) (SDG # 9)	Satisfactory	22-02-2022	Work and Service, GOS	22-07-2022	Dadu	47.26
2021-22 2692	Widening & Reconditioning of road from Chowdagi to Phulji Village (4.00 Kms) (SDG # 9)	Satisfactory	18-05-2022	Work and Service, GOS	16-08-2022	Dadu	31.419
2021-22 2706	Reconditioning / Construction of road from Bhiria road Railway Station upto village Sattar Dino Mangrio road (10.00 Kms) (SDG # 9)	Satisfactory	15-03-2022	Work and Service, GOS	13-07-2022	Naushero Feroz	97.847
2021-22 2712	Reconditioning of road from Daur - Moro road to village Haji Noor Muhammad Dahri via Aijazabad road (4.00 Kms) (SDG # 9)@	Satisfactory	29-06-2022	Work and Service, GOS	11-10-2022	Shaheed Benazirabad	46.476
2021-22 2720	Reconditioning of link road from Saeedpur to old Bhorano Bungalow i/c village links (10.40 Kms) (Revised) (SDG # 9)	Satisfactory	17-05-2022	Work and Service, GOS	02-09-2022	Tharparkar	94.706
2021-22 2722	Improvement of road from Bathoro-Khorwah road mile 2/4 to Jhoke Shareef via Gul Mohammad Rahoo & Dali Dal road mile 0/0- 7/4 (12.00 Kms) (SDG # 9)	Satisfactory	16-05-2022	Work and Service, GOS	02-09-2022	Sujawal	104.496
2021-22 2725	Reconditioning of link road from Tando Muhammad Khan Bulri Shah Karim Ditta Wah road to Haji Muhammad Jat road mile 0/0- 5/0 (8.00 Kms) (SDG # 9)	Satisfactory	10-05-2022	Work and Service, GOS	02-09-2022	Tando Muhammad Khan	68.942
2021-22 2730	W/R of road from Saddiq Memon to Hafiz Sandhano road to Tando Allahyar Mirwah road @ 28 mile Mori i/c link road Darya Khan Mari mile 0/0-9/3 (15.08 Kms) (2\	Satisfactory	17-03-2022	Work and Service, GOS	02-09-2022	Tando Allahyar	243.55
2021-22 2733	Reconditioning of link road from National Highway Thatta City to Dargah Shah Murad Sheerazi upto Jungshahi road i/c links Dargah Abdullah Shah Ashabi (9.90 Kms) (Revised) (SDG # 9)	Satisfactory	23-02-2022	Work and Service, GOS	16-08-2022	Thatta	86.151
2021-22 2735	W/R of road from Ghulamaullah to Pirpatho (12.06 Kms) (SDG # 9)	Satisfactory	21-04-2022	Work and Service, GOS	31-10-2022	Thatta	215.128
2021-22 2736	Improvement of road from Thatta-Pirpatho-Ghorabari road to Gaho-Jo-Goth via Gail Mori Darvaish (20.00 Kms) (SDG # 9)	Satisfactory	22-04-2022	Work and Service, GOS	15-11-2022	Thatta	211.934
2021-22 2759	Reconditioning of road from Jaggan to Mir Altaf Ali Bhayoo road 0/0-3/1 (5.00 Kms) (SDG # 9)	Un-Satisfactory	19-04-2022	Work and Service, GOS	16-08-2022	Shikarpur	34.971
2021-22 2762	Reconditioning of road from Garhi Yaseen Indus Highway to village Jado Kalhoro via village Mohail,	Satisfactory	19-07-2022	Work and Service, GOS	14-11-2022	Shikarpur	47.498

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Hameed Jair Mairi (5.43 Kms) (SDG # 9)						
2021-22 2773	Reconditioning of road from Kandiyari to Akri (12.87 Kms)	Satisfactory	23-05-2022	Work and Service, GOS	13-09-2022	Khairpur	166.555
2021-22 2775	W/R of road from Badin Sujawal at point (Amir Shah Sim Nala)Phuleli Guni out fall Drain Inspection Path to connect Seerani Ahmed Rajo via Karo Mori Stop 0/0-15/0 (24.14 Kms) (Phase-I) (5.75 Kms) (SDG # 9)	Satisfactory	15-12-2021	Work and Service, GOS	19-08-2022	Badin	99.858
2021-22 2776	Improvement of road from Kadhan Behdmi Rupa Mari to connect Bhugra Memon (38.62 Kms) (2\	Satisfactory	16-12-2021	Work and Service, GOS	16-08-2022	Badin	99.895
2021-22 2782	W/R of Mithi to Diplo road (39.20 Kms)	Satisfactory	21-03-2022	Work and Service, GOS	16-08-2022	Tharparkar	1517.6
2021-22 2783	Improvement of road from Islamkot to Nagarparkar mile 21/0 - 56/0 (56 kms)	Satisfactory	18-05-2022	Work and Service, GOS	29-08-2022	Tharparkar	464.194
2021-22 2791	Widening / Reconditioning of road from Dakhan to Bado (9.00 Kms)	Un-Satisfactory	08-07-2022	Work and Service, GOS	04-10-2022	Shikarpur	100
2021-22 2937	Reconditioning of road from Mile Khan Thebo to Tando Adam - Mirpurkhas road via Old Mirabad, Muhabbat Shah, Tharejo Dars, Ghulam Nabi Shah, Soomar Khaskheli, Altaf Shah, Ibrahim Shah i/c Piyaro Lund road to Dasori Shakh via Jaffar Jamali Pir Azeem Shah, J	Satisfactory	07-07-2022	Work and Service, GOS	01-09-2022	Tando Allahyar	100
2021-22 3067	Construction of road from Khan Sahib Abdul Rehman to village Banhon Korejo (3.00 Kms) (SDG # 9)	Satisfactory	13-01-2022	Work and Service, GOS	01-09-2022	Badin	46.397
2021-22 3071	Construction / Improvement of various road in Taluka Hyderabad	Satisfactory	14-04-2022	Work and Service, GOS	11-10-2022	Hyderabad	211.609
2021-22 3073	Construction of remaining portion of Toug to Balpuri Thano Ahmed Khan road from mile 12/4-18/1 (9.00 Kms)	Satisfactory	12-01-2022	Work and Service, GOS	16-08-2022	Jamshoro	157.83
2021-22 3076	Construction of road from Karachi Hotel to Amb Mori via Yameen Kamrade Deh 266 (7.00 Kms)	Satisfactory	20-04-2022	Work and Service, GOS	29-08-2022	Mirpurkhas	64.669
2021-22 3085	Construction of road from Ghono Wingi to Butyano and Odhano via Geo Soomro UC Jhirmirio (7.00 Kms) (Phase-I) (SDG # 9)	Satisfactory	19-05-2022	Work and Service, GOS	29-08-2022	Tharparkar	125.44
2021-22 3110	Construction of road from link road village Abdul Rasheed to village Ghulam Muhammad village Muhammad Sharif village Juma Khan Jagirani (4.82 Kms) (SDG # 9)	Un-Satisfactory	09-03-2022	Work and Service, GOS	05-09-2022	Khairpur	59.046
2021-22 3116	Construction / Rehabilitation of various roads of UCs Akil, Agani and Phull (11.80 Kms) (SDG # 9)	Satisfactory	24-03-2022	Work and Service, GOS	08-09-2022	Larkana	164.591
2021-22 3315	Asset Management System and automation of composite schedule of rates for W&S Deptt. (SDG # 9) (LTBC)	Un-Satisfactory	12-05-2022	Work and Service, GOS	04-07-2022	Karachi	56.619
Non-ADP	Improvement of Road from Badin Sujawal Road @ mile 6/0 Fareed Farm to Pattan Parhiar Road Mile 1/1-2/4	Satisfactory	20-06-2022	Work and Service, GOS	29-08-2022	Badin	19.414
Non-ADP	Improvement of Road from Badin Sujawal Road @ mile 6/0 Fareed Farm to Pattan Parhiar Road Mile 2/4-3/7	Satisfactory	21-06-2022	Work and Service, GOS	21-11-2022	Badin	19.301
Non-ADP	Construction of Rooms and Maintainance of Community Center Mehar.	Un-Satisfactory	13-06-2022	Work and Service, GOS	08-09-2022	Dadu	19.2
Non-ADP	Remaining work at Irrigation Public Park Dadu	Un-Satisfactory	14-06-2022	Work and Service, GOS	08-09-2022	Dadu	10
Non-ADP	Construction of road from Bhand Mari to Sita Village via Ghulan JA Bhan Taluka Mehar mile 0/0-0/4+587	Satisfactory	16-06-2022	Work and Service, GOS	13-09-2022	Dadu	8
2021-22 DD19P00 081	Construction of Road from Sehwan road to village Ghulam Mustafa Janwari via Dargah Murad Shah Pir i/c Retaining Wall.	Satisfactory	17-06-2022	Work and Service, GOS	13-09-2022	Dadu	2.288
Non-ADP	Construction of paving block & drain from Dr. Santosh clinic to Jamil	Un-Satisfactory	27-07-2022	Work and Service, GOS	07-11-2022	Dadu	20

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Shaikh rice mill Ghari Road Mehar City						
Non-ADP	Improvement of Asphalt Road from Pakola Factory to Gujrati Para Taluka Latifabad	Satisfactory	08-06-2022	Work and Service, GOS	02-09-2022	Hyderabad	20
Non-ADP	Improvement of Road from Faqir ka Pir to Bera Manzil Taluka City Hyderabad	Satisfactory	14-06-2022	Work and Service, GOS	21-11-2022	Hyderabad	5.592
Non-ADP	Construction of CC Pavers/ CC Block & Drains from Barija to Mangrio House i/c Different Streets Barija Muhallaat Village Muhammad Yousif Baloch, Taluka Kotri, District Jamshoro	Satisfactory	13-06-2022	Work and Service, GOS	01-09-2022	Jamshoro	8.5
Non-ADP	Construction of Pavers Brick Road & MCP WAPDA Colony, Haji Juman Shoro Ward No: 09 Jamshoro, Taluka Kotri, District Jamshoro.	Satisfactory	24-06-2022	Work and Service, GOS	01-09-2022	Jamshoro	20
Non-ADP	Construction of Road New Metaled Road From NHA to Via Waris Goth To Wanko Goth UC Pir Mangio Taluka Khairpur	Un-Satisfactory	27-06-2022	Work and Service, GOS	04-10-2022	Khairpur	19.951
Non-ADP	Repair & Recondition of Road village Rasheed Waghan via Otaq of Nazir Ahmed Lahori to circular road	Satisfactory	17-08-2022	Work and Service, GOS	15-02-2023	Larkana	4
Non-ADP	Construction of Paver Block in the front and back side of main building of high court Larkano	Un-Satisfactory	08-06-2022	Work and Service, GOS	12-08-2022	Larkana	5
Non-ADP	Beuatification and green space of airport road Larkano	Satisfactory	08-06-2022	Work and Service, GOS	12-08-2022	Larkana	8
Non-ADP	Construction of Road Froam Nawab Bhawal Road To Village Gulab Khan Khaskheli To Village Haji Allah Dino Khaskheli 0/0 to 1	Un-Satisfactory	21-06-2022	Work and Service, GOS	07-11-2022	Shaheed Benazirabad	19.964
Non-ADP	Construction/Rehabilitation of Internal Roads in Sultan Kot City	Un-Satisfactory	20-06-2022	Work and Service, GOS	08-09-2022	Shikarpur	39.9
Non-ADP	Reconditioning of Road Abdu Buja Napar Road to Village Dhani Bux Malik	Un-Satisfactory	24-06-2022	Work and Service, GOS	30-11-2022	Shikarpur	19.9
Non-ADP	Rehabilitation of Internal roads of Village Jahan Khan Mahar i/c CC Block and Drains mile 0/0-0/3 (0.60 KM)	Un-Satisfactory	27-06-2022	Work and Service, GOS	10-11-2022	Shikarpur	9
Non-ADP	Rehabilitation/ Renovation of Old Deputy Commissioner House Shikarpur	Un-Satisfactory	28-06-2022	Work and Service, GOS	25-11-2022	Shikarpur	20
Non-ADP	Construction of Compound wall of graveyard Chingqi Maqam Shikarpur City	Un-Satisfactory	29-06-2022	Work and Service, GOS	25-11-2022	Shikarpur	10
Non-ADP	Construction of Bus Terminal Rohri UC Bedal Bekas	Un-Satisfactory	13-06-2022	Work and Service, GOS	19-01-2023	Sukkur	37.165
Non-ADP	Construction of Paying Block Flooring & drains Various Village of UC Sangi PanoAkil	Un-Satisfactory	28-06-2022	Work and Service, GOS	19-01-2023	Sukkur	10
Non-ADP	Construction of Paying Block Flooring & Drains @ Various Village UC Panhwari	Un-Satisfactory	17-06-2022	Work and Service, GOS	05-01-2023	Sukkur	10
Non-ADP	Improvement of road from Kapri Mori Dumbalo road to village Fateh Mohammad Rindhawa	Satisfactory	03-02-2022	Work and Service, GOS	05-08-2022	Badin	20
Non-ADP	Construction of road from Tando Bago Pangrio Mehboob Ali Shah road to Natho Rebari	Satisfactory	07-02-2022	Work and Service, GOS	03-08-2022	Badin	19.9
Non-ADP	Construction of Internal road of Pir Sakhi Usman Shah Meghwar Paro	Satisfactory	04-02-2022	Work and Service, GOS	05-08-2022	Badin	20
Non-ADP	Construction of road from Ali Mohammad Arain road to village Jalal Khan Khoso	Satisfactory	16-02-2022	Work and Service, GOS	03-08-2022	Badin	20
2019-20 2547	Construction of Road from Sagyoon Khan Wahan Road to Shah Nawaz Kalhoro UC Sagyoon Taluka Sobhodero Road mile 0/0- 1/2 (2.0 km) (SDG # 9)	Satisfactory	30-11-2022	Work and Service, GOS	15-12-2022	Khairpur	25.744

# Annexure (B)

## LIST OF RE-VISITED SCHEMES IN FY 2022-23

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 37	Construction of Office Building for On-Farm Water Management staff (Badin, Mirpurkhas, Sanghar, SBA, Sukkur, Khairpur, Shikarpur, Dadu, Ghotki, Kashmore & Jamshoro ).	Un-Satisfactory	10-10-2022	Agriculture, GOS	12-01-2023	Badin	96.389
2022-23 40	Additional Lining of Watercourses in Sindh. (Total Cost Rs.5664.404 M, GOS Share 4659.847 M & Farmer Share Rs.1004.530 M).	Satisfactory	02-02-2023	Agriculture, GOS	01-03-2023	Matiari	4659.874
2021-22 12	Construction / Rehabilitation of Agriculture Extension Office in Sindh	Satisfactory	06-07-2022	Agriculture, GOS	02-08-2022	Qambar Shahdaddock	439.149
2021-22 27	Provision of Agricultural Land Development Machinery & Equipments (On Subsidized Rate)	Satisfactory	09-03-2023	Agriculture, GOS	12-05-2023	Sukkur	759
2021-22 27	Provision of Agricultural Land Development Machinery & Equipments (On Subsidized Rate)	Satisfactory	18-11-2021	Agriculture, GOS	04-07-2022	Hyderabad	759
2021-22 3	Construction of Compound wall to ARI Campus Tando Jam including Experimental Field, Pavement of Approach Road and Rehabilitation of Residential Colony	Satisfactory	11-04-2022	Agriculture, GOS	19-08-2022	Hyderabad	148.864
2021-22 36	Integrated Water Resource Management in Sindh (Total Cost Rs.2393.495 M, GOS Share Rs.1932.447 M and Farmer Share Rs.400.00 M).	Satisfactory	21-02-2022	Agriculture, GOS	16-08-2022	Tando Muhammad Khan, Jamshoro	1932.447
2021-22 36	Integrated Water Resource Management in Sindh (Total Cost Rs.2393.495 M, GOS Share Rs.1932.447 M and Farmer Share Rs.400.00 M).	Satisfactory	21-12-2021	Agriculture, GOS	16-01-2023	Shaheed Benazirabad	1932.447
2022-23 47	Construction / Reconstruction / Rehabilitation & Allied Facilities of Dargahs in Sindh (6 Nos.), T.M Khan (01), Thatta (02), Khairpur (01), Hyderabad (01) and Larkano (01).	Satisfactory	06-03-2023	Auqaf, GOS	17-03-2023	Thatta	150.599
2021-22 50	Reconstruction of Musafirkhana / Construction of main Entrance Gate / Water Tank at Dargah Shah Abdul Latif Bhittai at Bhitshah	Satisfactory	20-06-2022	Auqaf, GOS	16-08-2022	Matiari	19.257
2021-22 51	Construction of Dargah Makhdoom Nooh Hala District Matiari	Satisfactory	02-08-2022	Auqaf, GOS	15-11-2022	Matiari	17.327
2021-22 53	Reconstruction of Shrine, Construction of Musafirkhana and other Allied Units at Dargah Syed Ubhan Shah Taluka Kot Diji District Khairpur Mirs	Un-Satisfactory	09-02-2022	Auqaf, GOS	10-11-2022	Khairpur	10.047
2021-22 64	Provision of Fiber Glass Shade, Installation of RO plants and Establishment of Museum at Dargah Qalander Lal Shahbaz Sehwan Sharif District Jamshoro	Satisfactory	28-07-2022	Auqaf, GOS	01-09-2022	Jamshoro	22.238
2021-22 65	Provision of Fiber Glass Shade and Improvement of Water Supply at Dargah Abdullah Shah Ashabi	Satisfactory	10-03-2023	Auqaf, GOS	14-03-2023	Thatta	18.3
2021-22 101	Construction of Sindh Government Cooperative College Hyderabad.	Un-Satisfactory	16-03-2023	Cooperative, GOS	11-04-2023	Hyderabad	118
2022-23 104	Auditorium Hall Rest House And Main Entrance Gate at Dargah Hazrat Sardar Ahmed Shah Lakyari Taluka Saeedabad District Matiari (Revised on 18.01.22). (C:86.833;+R:12.768)	Satisfactory	26-09-2022	Culture, GOS	11-01-2023	Matiari	99.601
2022-23 111	Provision of Missing Allied Facilities in Library at Sujawal. (Revised on 24.12.20) (C:39.909+R:26.905)	Satisfactory	25-10-2022	Culture, GOS	11-01-2023	Sujawal	66.814
2022-23 115	Provision of Additional Allied Facilities & External Development at Sindh Institute for Music & Performing Arts & DR. N.A Balouch Institute at Jamshoro. (C:60.277+R:8.683)	Satisfactory	24-10-2022	Culture, GOS	11-01-2023	Jamshoro	68.96

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 117	Establishment of Muhammad Ibrahim Joyo Translation Bureau at Jamshoro. (C:6.730+R:32.102)	Satisfactory	04-08-2022	Culture, GOS	15-11-2022	Jamshoro	38.832
2022-23 121	Establishment of Auditorium at Badin. (C:37.424+R:12.163)	Un-Satisfactory	08-08-2022	Culture, GOS	26-10-2022	Badin	49.587
2022-23 124	Provision of Allied Facilities at Cultural Complex Thatta. (C:64.564+R:14.941)	Un-Satisfactory	24-10-2022	Culture, GOS	19-01-2023	Thatta	79.505
2022-23 142	Establishment of Digitization & Conservation Laboratory for Providing Physical Treatments, Testing, Cleaning and Protecting of Decaying Artifacts, i.e. Stones, Coins, Manuscripts etc. (C:21.978+R:75.100)	Satisfactory	06-01-2023	Culture, GOS	18-01-2023	Karachi	97.078
2022-23 144	Provision of Additional Allied Facilities & External Development of Sub-office of Antiquities & Archaeological Museum Sukkur. (Revised on 24.12.20) (C:74.034+R:15.604)	Satisfactory	15-08-2022	Culture, GOS	07-03-2023	Sukkur	89.638
2021-22 114	Provision of Missing Allied Facilities & Construction of Auditorium Hall and Waiting area at Dargah Jaral Shah, Taluka Larkano District Larkano (Revised) (C:66.116+R:6.177)	Satisfactory	06-06-2022	Culture, GOS	23-11-2022	Larkana	72.293
2021-22 116	Provision of Additional Allied Facilities & External Development of Culture Department offices Near Rumi Graveyard at Northern Bypass, Karachi	Satisfactory	05-01-2023	Culture, GOS	18-01-2023	Karachi	80
2021-22 121	Establishment of Auditorium at Dadu. (C:42.208+R:24.830) (Revised) (ADP NO.83 of 2019-20)	Satisfactory	05-10-2022	Culture, GOS	01-12-2022	Dadu	67.038
2022-23 1900056	Repair, Renovation & rehabilitation work of GBPS Long Dalpota Taluka Jhando Mari District Tando Allah Yar	Satisfactory	10-03-2023	Education and Literacy, GOS	03-04-2023	Tando Allahyar	5.136
2022-23 350	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 40.000 + R: 3.395)	Un-Satisfactory	09-12-2022	Education and Literacy, GOS	17-01-2023	Sujawal	43.395
2022-23 431	Construction / Reconstruction of Govt. Boys High School Jhuddo (SDG#4)	Satisfactory	21-10-2022	Education and Literacy, GOS	15-03-2023	Mirpurkhas	43.241
2022-23 576	Construction of (Govt. Boys / Girls Secondary Schools) in Shirin Jinnah Colony Karachi (02 Units) (C:45.199+R:2.00) (SDG#4)	Satisfactory	15-03-2023	Education and Literacy, GOS	20-03-2023	Karachi South	47.199
2022-23 589	Establishment of Government Secondary School (Boys & Girls) in Chuhar Jamali Sujawal District (RGC) (Pertains to RGC Project under PRS assisted by European Union)	Satisfactory	22-11-2022	Education and Literacy, GOS	06-02-2023	Sujawal	205.5
2022-23 664	Improvement / Renovation of Govt.Boys` Degree College Gulzar-e-Hijri East Karachi (SDG#4)	Satisfactory	27-04-2023	Education and Literacy, GOS	09-06-2023	Karachi East	99.349
2022-23 708	Re-Construction of Building Govt. Boys Degree College Miro Khan District Kamber-Shahdadkot (SDG#4)	Satisfactory	08-11-2022	Education and Literacy, GOS	17-03-2023	Qambar Shahdadkot	70.62
2022-23 709	Rehabilitation & Provision of Missing Facilities in Existing GBDC / GGDC Naudero District Larkano (SDG#4)	Satisfactory	09-11-2022	Education and Literacy, GOS	17-03-2023	Larkana	62.784
2022-23 739	Establishment of Cadet College Khairpur (C:1141.114 + R:379.225) (Revised on 26.04.16) (SDG#4)	Satisfactory	23-11-2022	Education and Literacy, GOS	20-01-2023	Khairpur	1520.339
2022-23 743	Establishment of Cadet College, Badin (C:701.840 + R:127.194) (SDG#4)	Satisfactory	29-09-2022	Education and Literacy, GOS	06-02-2023	Badin	829.034
2022-23 746	Provision of Additional Facilities and Boundary Wall of Boys Cadet College Larkana (SDG#4)	Satisfactory	10-11-2022	Education and Literacy, GOS	15-03-2023	Larkana	99.808
2022-23 805	Establishment of Syed Qutab Ali Shah Government Polytechnic Institute at Shujabad (C:57.313 + R:42.687) (SDG # 1,4,9).	Satisfactory	08-03-2023	Education and Literacy, GOS	11-04-2023	Mirpurkhas	100
2022-23 835	Establishment of Shaheed Benazir Bhutto University of Veterinary and Animal Sciences Sakrand (C:852.257 + R:326.615)	Satisfactory	14-11-2022	Education and Literacy, GOS	02-02-2023	Shaheed Benazirabad	1178.872

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 839	Immediate Needs of QUEST at Nawabshah (C:176.182 + R:17.880) (SDG#4)	Un-Satisfactory	25-11-2022	Education and Literacy, GOS	27-01-2023	Shaheed Benazirabad	194.062
2022-23 844	Establishment of Shaheed Mohtarma Benazir Bhutto Chair & Convention Centre at Karachi University (C:345.005 + R:97.036) (SDG#4)	Satisfactory	17-05-2023	Education and Literacy, GOS	29-05-2023	Karachi	442.041
Non-ADP	Ingrated / Rehabilitation of Primary/Middle/ Elementary Schools Taluka Larkano (11units) (2016-17 programme)	Un-Satisfactory	26-09-2022	Education and Literacy, GOS	11-01-2023	Larkana	19.5
Non-ADP	Re-habilitation Govt. Boys High School Mir Nabi Bux Town Taluka City	Satisfactory	19-07-2022	Education and Literacy, GOS	21-11-2022	Hyderabad	9
Non-ADP	Construction/ Reconstruction of Existing GGHSS Kotri, (Old Black) Taluka Kotri, District Jamshoro.	Satisfactory	21-07-2022	Education and Literacy, GOS	08-02-2023	Jamshoro	10
2021-22 187	Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Primary / Elementary Schools) (155 Units) (C:1101.709+R:168.328)	Satisfactory	20-01-2022	Education and Literacy, GOS	07-07-2022	Shikarpur	1270.037
Non-ADP	Construction of Shelterless Government Primary School Gul Mir Mari Taluka Jhando Mari District Tando Allahyar (01 Unit)	Satisfactory	22-08-2022	Education and Literacy, GOS	21-11-2022	Tando Allahyar	2.401
2021-22 191	Construction of Six Room Buildings for Shelterless Primary Schools (01 Unit) (C: 12.154 + R: 1.210) (SDG#4)	Satisfactory	15-11-2021	Education and Literacy, GOS	19-08-2022	Tando Allahyar	13.364
2021-22 200	Rehabilitation of High Enrollment Dangerous Primary Schools with Additional Class Rooms and Provision of Missing Facilities (05 Units) (SDG#4)	Satisfactory	29-06-2022	Education and Literacy, GOS	31-08-2022	Matiari	24.327
2021-22 291	Sindh Basic Education Program (SBEP) (Approved Cost: Rs.14355 M USAID Grant: Rs.13485 M & G.O.S. Share: Rs.870 M) (C: 651.147 + R: 218.853) (SDG#4)	Satisfactory	28-09-2021	Education and Literacy, GOS	15-08-2022	Karachi	870
2021-22 296	Construction / Re-construction of Building in Existing Secondary Schools PAF Base Shahbaz Jacobabad (C: 54.000 + R: 2.397) (SDG#4)	Satisfactory	22-11-2021	Education and Literacy, GOS	04-07-2022	Jacobabad	56.397
2021-22 300	Purchase of Security Equipment and Construction of Boundary Wall & Other Remaining Work at Public School Shikarpur (C:78.534+R:14.292) (SDG#4)	Satisfactory	19-05-2022	Education and Literacy, GOS	01-09-2022	Shikarpur	92.826
2021-22 307	Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Secondary Schools) (7 Units) (C:93.023+R:51.420) (SDG#4)	Un-Satisfactory	27-09-2021	Education and Literacy, GOS	22-07-2022	Qambar Shahdaskot	144.443
2021-22 312	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 40.000 + R: 5.000)	Satisfactory	08-12-2021	Education and Literacy, GOS	22-07-2022	Dadu	45
2021-22 314	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 39.712 + R: 4.295)	Satisfactory	26-05-2022	Education and Literacy, GOS	16-08-2022	Tando Muhammad Khan	44.007
2021-22 315	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 40.000 + R: 4.214)	Satisfactory	19-04-2022	Education and Literacy, GOS	06-07-2022	Tando Allahyar	44.214
2021-22 318	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius	Satisfactory	22-02-2022	Education and Literacy, GOS	01-09-2022	Tharparkar	42.923
2021-22 326	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (02 Units) (C: Rs. 89.724 + R: 6.816)	Satisfactory	21-01-2022	Education and Literacy, GOS	22-08-2022	Larkana	96.54
2021-22 328	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 45.450 + R: 3.812)	Un-Satisfactory	26-05-2022	Education and Literacy, GOS	16-08-2022	Shikarpur	49.262

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2021-22 329	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 45.450 + R: 2.767)	Un-Satisfactory	11-05-2022	Education and Literacy, GOS	16-08-2022	Kashmore	48.217
2021-22 330	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 45.819 + R: 3.681)	Satisfactory	24-05-2022	Education and Literacy, GOS	01-12-2022	Jacobabad	49.5
2021-22 331	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 39.685 + R: 1.940)	Un-Satisfactory	13-04-2022	Education and Literacy, GOS	19-08-2022	Karachi East	41.625
2021-22 478	Establishment of Degree College at Garhi Khairo District Jacobabad (C:89.089 + R:7.963) (SDG#4)	Satisfactory	16-12-2021	Education and Literacy, GOS	22-08-2022	Jacobabad	97.052
2021-22 481	Establishment of Degree College in existing Nasarpur Higher Secondary School Tando Allah Yar (C:25.000 + R:2.500) (SDG#4)	Satisfactory	20-04-2022	Education and Literacy, GOS	06-07-2022	Tando Allahyar	27.5
2021-22 485	Establishment of Degree College in existing Warha Higher Secondary School District Kamber Shahdad Kot (C:25.905 + R:1.851) (SDG#4)	Satisfactory	21-12-2021	Education and Literacy, GOS	22-07-2022	Qambar Shahdadkot	27.756
2021-22 491	Rehabilitation & Provision of Missing Facilities in C&S Govt. Boys College Shikarpur (C:49.963 + R:5.000) (SDG#4)	Satisfactory	17-03-2022	Education and Literacy, GOS	27-07-2022	Shikarpur	50.963
2021-22 494	Improvement / Repair of D.J. Science College South Karachi (SDG#4)	Satisfactory	13-12-2021	Education and Literacy, GOS	07-07-2022	Karachi South	39.228
2021-22 495	Rehabilitation / Addition of Missing Facilities Govt. for Women College Shahrah-e-Liaquat Saddar Karachi (SDG#4)	Un-Satisfactory	19-04-2022	Education and Literacy, GOS	19-08-2022	Karachi	39.608
2021-22 497	Remaining Work of Law College Halla District Matiari (SDG#4)	Satisfactory	27-06-2022	Education and Literacy, GOS	02-09-2022	Matiari	20
2021-22 562	Establishment of Shaheed Benazir Bhutto Girls Cadet College Larkano (C:2039.382 + R:190.457) (Revised) (SDG#4)	Satisfactory	10-05-2022	Education and Literacy, GOS	22-07-2022	Larkana	2229.841
2021-22 592	Modernization of Government College of Technology, SITE Karachi & Mirpurkhas (Phase-I) (C:87.057 + R:10.904) (SDG # 1,4,9)(Planned as per request of Universities & Boards Deptt.)	Satisfactory	15-09-2021	Education and Literacy, GOS	06-07-2022	Karachi	97.961
2021-22 593	Establishment of Government Vocational Centres for Girls (09 Units) in Sindh (Larkano, Khairpur, & N.Feroze (2 Unit each), Mirpurkhas, Umerkot & Tharparkar (1 Unit each) (C: 218.696 + R: 35.075) (SDG # 1,4,9)	Satisfactory	14-06-2022	Education and Literacy, GOS	05-08-2022	Umerkot	253.771
Non-ADP	Repair/ Renovation and Rehabilitation work of Government Girls Community Model School Sultan Abad District Tando Allahyar	Satisfactory	19-10-2022	Education and Literacy, GOS	30-11-2022	Tando Allahyar	7.888
2020-21 114	Early Childhood Education (ECE) Intervention Larkana Division (C:16.980 + R:30.979) (SDG#4)	Satisfactory	24-11-2021	Education and Literacy, GOS	29-08-2022	Kashmore	47.959
2020-21 114	Early Childhood Education (ECE) Intervention Larkana Division (C:16.980 + R:30.979) (SDG#4)	Satisfactory	05-11-2021	Education and Literacy, GOS	29-08-2022	Jacobabad	47.959
2020-21 146	Up-gradation of Primary Schools to Middle Schools, District Thatta. (05 Units).(C:47.391 + R:7.500) (SDG#4).	Satisfactory	22-03-2023	Education and Literacy, GOS	30-03-2023	Thatta	54.891
2020-21 249	Establishment of Comprehensive Schools in Sindh ( 25 Units ) (C: 3550.998 + R: 191.550)	Satisfactory	24-08-2022	Education and Literacy, GOS	21-10-2022	Dadu	3742.548
2020-21 294	Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Secondary Schools) (16 Units) (C:71.438+R:30.406) (SDG#4)	Satisfactory	27-08-2021	Education and Literacy, GOS	01-07-2022	Larkana	101.844
2019-20 267	Rehabilitation of Existing High Schools & Higher Secondary Schools District Thatta (AASP)(C: 47.240 + R: 11.230) (SDG#4).	Satisfactory	20-03-2023	Education and Literacy, GOS	30-03-2023	Thatta	58.47

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2018-19 194	Immediate Needs for Public School Gadap Town, Karachi (C:231.328 + R:59.364) (SDG # 4)	Un-Satisfactory	08-02-2022	Education and Literacy, GOS	20-07-2022	Karachi	290.692
2018-19 211	Rehabilitation of Government Primary School / Government Girls Secondary School Khatoon- E-Pakistan Stadium Road Karachi (Phase-II) (AASP)	Satisfactory	11-01-2022	Education and Literacy, GOS	01-09-2022	Karachi	43.018
2018-19 294	Establishment of Boys / Girls Degree Colleges in Sindh (23 Units) ( Revised) (C:2093.709 + R: 200.100) (SDG # 4).	Satisfactory	21-03-2023	Education and Literacy, GOS	30-03-2023	Thatta	2864.585
2015-16 185	Up-gradation of Secondary Schools to Higher Secondary Schools in Sindh (2005-06 Programme) (Compliance)	Un-Satisfactory	24-03-2023	Education and Literacy, GOS	06-04-2023	Jamshoro	23.7
2022-23 885	Village Electrification Programme in Sindh (Phase-VIII)	Un-Satisfactory	16-08-2022	Energy, GOS	27-10-2022	Thatta	987.46
2020-21 516	Electrification of Primary Health Facilities Through Solar PV Technology (Revised) (SBA., Ghotki, Larkana, Badin, Dadu, Jamshoro, Khairpur, Shikarpur, Matiari, Sanghar, Mirpurkhas, T.A.Yar & N.Feroze)	Satisfactory	20-10-2022	Energy, GOS	27-01-2023	Shaheed Benazirabad	505.662
2020-21 516	Electrification of Primary Health Facilities Through Solar PV Technology (Revised) (SBA, Ghotki, Larkana, Badin, Dadu, Jamshoro, Khairpur, Shikarpur, Matiari, Sanghar, Mirpurkhas,, T.A.Yar & N.Feroze)	Satisfactory	29-07-2022	Energy, GOS	11-10-2022	Ghotki	505.662
2020-21 516	Electrification of Primary Health Facilities Through Solar PV Technology (Revised) (SBA, Ghotki,, Larkana, Badin, Dadu, Jamshoro, Khairpur, Shikarpur, Matiari, Sanghar, Mirpurkhas, T.A.Yar & N.Feroze)	Satisfactory	26-07-2022	Energy, GOS	11-10-2022	Sanghar	505.662
2022-23 937	Renovation of Excise and Taxation Office Thatta (SDG # 9)	Un-Satisfactory	19-08-2022	Excise & Taxation, GOS	07-12-2022	Thatta	26.417
2022-23 939	Renovation of Excise and Taxation Office Dadu (SDG # 9)	Satisfactory	15-11-2022	Excise & Taxation, GOS	26-01-2023	Dadu	23.786
2021-22 710	Integration / upgradation of Tax Database and Online Tax Collection (SDG # 9).(LTBC)	Un-Satisfactory	21-07-2022	Excise & Taxation, GOS	17-11-2022	Karachi	120
2022-23 954	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Satisfactory	20-03-2023	Food, GOS	18-04-2023	Kashmore	634.843
2022-23 954	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	06-03-2023	Food, GOS	10-04-2023	Badin	634.843
2022-23 955	Construction of District Food Controller (DFC) Offices, Residences and construction of Security Towers & Compound Walls at various locations of Hyderabad and Mirpurkhas Division (SDG # 2)	Un-Satisfactory	23-11-2022	Food, GOS	20-12-2022	Matiari	417.808
2022-23 955	Construction of District Food Controller (DFC) Offices, Residences and construction of Security Towers & Compound Walls at various locations of Hyderabad and Mirpurkhas Division (SDG # 2)	Un-Satisfactory	22-11-2022	Food, GOS	20-12-2022	Tando Muhammad Khan	417.808
2022-23 955	Construction of District Food Controller (DFC) Offices, Residences and construction of Security Towers & Compound Walls at various locations of Hyderabad and Mirpurkhas Division	Un-Satisfactory	21-11-2022	Food, GOS	13-12-2022	Badin	417.808
2021-22 720	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	14-07-2022	Food, GOS	21-10-2022	Mirpurkhas	634.843
2021-22 720	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	07-04-2022	Food, GOS	11-10-2022	Qambar Shahdaakot	634.843
2021-22 720	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	18-03-2022	Food, GOS	03-08-2022	Matiari	634.843
2021-22 720	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	09-03-2022	Food, GOS	04-08-2022	Jacobabad	634.843
2021-22 721	Construction of District Food Controller (DFC) Offices, Residences and construction of Security Towers & Compound Walls at various locations of Hyderabad and Mirpurkhas Division	Un-Satisfactory	04-07-2022	Food, GOS	19-08-2022	Hyderabad	417.808
2020-21 542	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	10-06-2021	Food, GOS	05-09-2022	Larkana	634.843

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m	Satisfactory	07-12-2022	Forest, Wildlife & CDA, GOS	18-01-2023	Tando Muhammad Khan	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m	Satisfactory	06-12-2022	Forest, Wildlife & CDA, GOS	01-03-2023	Mirpurkhas	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m	Satisfactory	05-12-2022	Forest, Wildlife & CDA, GOS	10-01-2023	Badin	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m	Satisfactory	19-08-2022	Forest, Wildlife & CDA, GOS	26-01-2023	Shikarpur	3016.35
2021-22 723	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter ( Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 m	Satisfactory	28-07-2022	Forest, Wildlife & CDA, GOS	10-01-2023	Tando Allahyar, Matiari, Hyderabad	3016.35
2021-22 724	Possible Role of Mangroves in Curbing Sea Intrusion in Indus Delta (SDG # 15)	Satisfactory	16-05-2022	Forest, Wildlife & CDA, GOS	15-08-2022	Sujawal	698.11
2021-22 725	Enhancing Tree Cover on State Forest Lands in Sindh (Revised) (Jamshoro, Dadu, Matiari, SBA, Sanghar, Shikarpur, Kashmore, Sukkur, Khairpur, Ghotki, N.Feroze, T.M. Khan, Umerkot, Thar, Badin, T.A.Yar, Kamber, Larkano & Jacobabad) (SDG # 15)	Satisfactory	14-06-2022	Forest, Wildlife & CDA, GOS	29-08-2022	Matiari, Jamshoro	708
2021-22 726	Sarsabz Sindh Making Sindh Green and Environment Friendly (SDG # 15)	Satisfactory	12-07-2022	Forest, Wildlife & CDA, GOS	23-11-2022	Larkana	599.944
2021-22 726	Sarsabz Sindh Making Sindh Green and Environment Friendly (SDG # 15)	Satisfactory	06-07-2022	Forest, Wildlife & CDA, GOS	14-12-2022	Kashmore, Jacobabad	599.944
2021-22 726	Sarsabz Sindh Making Sindh Green and Environment Friendly (SDG # 15)	Satisfactory	14-06-2022	Forest, Wildlife & CDA, GOS	14-12-2022	Shikarpur, Qambar Shahdadkot	599.944
2021-22 728	Completion of leftover/remaining targets of Bahman Nature Park Larkano (C: 44.802+R:15.198) (SDG # 15)	Satisfactory	06-09-2021	Forest, Wildlife & CDA, GOS	27-07-2022	Larkana	60
2022-23 1029	Construction of RHC in Village Dau Jahanpur, Taluka Garhi Khairo, District Jacobabad.(C:45.081+R:19.958)	Satisfactory	15-12-2022	Health, GOS	14-02-2023	Jacobabad	65.039
2022-23 1030	Expansion of Radiology and IPD Services at JIMS, Jacobabad (C:125.080+R:291.424) (SDG #3, 9)	Satisfactory	17-11-2022	Health, GOS	09-02-2023	Jacobabad	416.504
2022-23 1072	Up gradation of BHU to RHC Shadipalli, Taluka Pithoro (Revised on 07.04.21) (C:60.493+R:30.414)(SDG#3)	Un-Satisfactory	19-09-2022	Health, GOS	26-10-2022	Umerkot, Mirpurkhas	90.907
2022-23 1087	Up gradation of THQ Hospital to the level of DHQ Hospital in newly created district Sindh at Kashmore at Kandhkot (Revised on 13.01.16). (C: 545.542+R: 217.685) (SDG #3)	Satisfactory	13-09-2022	Health, GOS	15-03-2023	Kashmore	763.227

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3) (Sujawal, Mirpur Bathoro & Jati)	Un-Satisfactory	22-03-2023	Health, GOS	06-04-2023	Sujawal	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3) (Matli, Tando Bago & Golarchi)	Un-Satisfactory	21-03-2023	Health, GOS	06-04-2023	Badin	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3) (Digri & Kot Ghulam Mohammed)	Un-Satisfactory	20-03-2023	Health, GOS	06-04-2023	Mirpurkhas	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3) (Tando Jam)	Un-Satisfactory	17-03-2023	Health, GOS	06-04-2023	Hyderabad	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3) (Nangar & Diplo)	Un-Satisfactory	15-03-2023	Health, GOS	10-04-2023	Tharparkar	3334.161
2022-23 1179	Neonatal screening for Congenital Hypothyroidism (CH) in Sindh at NICH, Karachi (Revised on 04.06.21) (C:16.448+R:132.465+ PIU 61.373)(SDG#3)	Satisfactory	03-11-2022	Health, GOS	02-01-2023	Karachi	210.286
2022-23 995	Establishment of Psychiatry and Accident / Emergency Unit at Sindh Government Hospital Saudabad, Karachi. (Revised on 18.07.19) (C:177.536+R: 193.215) (SDG #3.4, 3.6)	Satisfactory	09-03-2023	Health, GOS	03-04-2023	Karachi	370.751
2021-22 777	Upgradation of Provincial Health Development Centre (PHDC) to the level of Sindh Health Institute of Training & Research. (SDG#3)	Un-Satisfactory	07-12-2021	Health, GOS	13-10-2022	Jamshoro	186.863
2021-22 782	Construction of Divisional Warehouse at Shaheed Benazirabad. (C:88.930+R:5.312)(SDG#3)	Satisfactory	25-05-2022	Health, GOS	16-08-2022	Shaheed Benazirabad	94.242
2021-22 783	Upgradation of RHC Daur to the level of Taluka Hospital Daur (Revised) (C: 35.534+R: 56.457) (SDG# 3)	Satisfactory	25-11-2021	Health, GOS	21-10-2022	Shaheed Benazirabad	91.991
2021-22 787	Upgradation of existing Rural Health Centre to Taluka Headquarter Hospital at Garhi Khairo, District Jacobabad.(C: 170.178+R:25.000) (SDG #3)	Satisfactory	12-04-2022	Health, GOS	04-07-2022	Jacobabad	195.178
2021-22 793	Renovation and Rehabilitation of Paramedical Institute, Larkano. (C: 47.948+R: 19.785) (SDG #3)	Un-Satisfactory	20-06-2022	Health, GOS	25-11-2022	Larkana	67.733
2021-22 794	Construction of Divisional Warehouse at Larkano. (C:88.930+R:5.312)(SDG#3)	Satisfactory	11-03-2022	Health, GOS	14-11-2022	Larkana	94.242
2021-22 795	Establishment of Thalassemia Day Care Centre at Dargah Jaral Shah, Larkano. (C:13.224+R:8.762)(SDG #3,9)	Satisfactory	12-11-2021	Health, GOS	27-07-2022	Larkana	21.986
2021-22 796	Upgradation of RHC to 50 bedded hospital at Garhi Khuda Bakhsh Bhutto (C:44.429+R:15.098) (SDG #3)	Satisfactory	25-05-2022	Health, GOS	18-11-2022	Larkana	59.527
2021-22 809	Upgradation of BHU to RHC at Wahi Pandhi, Taluka Johi.(C:44.972+R:19.958)(SDG#3)	Un-Satisfactory	20-09-2021	Health, GOS	11-10-2022	Dadu	64.93
2021-22 810	Upgradation of BHU to RHC Village Bhawalpur, Taluka Johi. (C:44.972+R:19.958)(SDG#3)	Un-Satisfactory	21-09-2021	Health, GOS	30-09-2022	Dadu	64.93
2021-22 820	Upgradation of BHU to RHC Sher Muhammad Bijarani, UC Saifal, Taluka Tangwani. (C:41.989+R:19.958)	Un-Satisfactory	15-12-2021	Health, GOS	04-08-2022	Kashmore	61.947
2021-22 821	Upgradation of Health facility at Village Ber Sharif, Taluka Kamber. (C:10.679+R:2.816)(SDG #3)	Un-Satisfactory	08-04-2022	Health, GOS	28-07-2022	Qambar Shahdaktot	13.495
2020-21 559	Establishment of 25 bedded Trauma Centre at Sindh Government Lyari	Satisfactory	26-01-2021	Health, GOS	06-07-2022	Karachi	797.137

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	General Hospital, Karachi. (C: 275.969+R: 521.168) (SDG #3)						
2020-21 563	Establishment of Cardio thoracic Surgery Department at Liaquat University Hospital, Hyderabad (Revised). (C: 23.594+R: 353.073)	Satisfactory	10-08-2021	Health, GOS	26-07-2022	Hyderabad	376.667
2020-21 670	Upgradation of BHU to RHC at Village Kantio, Taluka Chachro. (C:47.781+R:15.046)(SDG#3)	Satisfactory	07-12-2020	Health, GOS	21-10-2022	Tharparkar	62.827
2020-21 679	Upgradation of BHU to RHC Gulzar Khalil, Taluka Samaro. (C:43.209+R:19.958)(SDG#3)	Satisfactory	13-01-2021	Health, GOS	21-10-2022	Umerkot	63.167
2019-20 705	Upgradation of BHU to RHC Talhi City, Taluka Kunri. (43.209+R:19.958)(SDG#3)	Satisfactory	10-03-2020	Health, GOS	21-10-2022	Umerkot	63.167
2019-20 746	Sindh Immunization support program (SISP). (GoS:7648.920+ GoP:400.000 =8048.920) (SDG #3)	Un-Satisfactory	19-05-2022	Health, GOS	30-12-2022	Larkana, Dadu	7648.92
2018-19 525	Up gradation of BHU to RHC Phull. (C:43.874+R:19.958)(SDG# 3))GS	Satisfactory	14-10-2022	Health, GOS	26-01-2023	Naushero Feroz	63.832
2017-18 734	Expansion & Improvement of DHQ Hospitals (03 Nos) at (1) Khairpur (2) Badin & (3) Shikarpur (Revised) (C: 2516.747+R: 923.828) (SDG #3)	Satisfactory	12-10-2022	Health, GOS	14-02-2023	Shikarpur	3440.575
2022-23 1188	Construction of Buildings for Sindh Police at various locations under Police Package (Karachi, Hyderabad, Sujawal, Dadu, Thatta, Matiari, Shaheed Benazir Abad, Kamber & Sukkur)(Revised) (SDG # 16)	Un-Satisfactory	15-11-2022	Home, GOS	04-01-2023	Hyderabad	642.101
2022-23 1189	Raising / Construction of Watch Tower & Boundary Wall at RRF Base Al-Falah, Naval Colony Base & Police Head Quarter District South Garden Road, Karachi (SDG # 16)..	Un-Satisfactory	23-09-2022	Home, GOS	17-01-2023	Karachi	805.239
2022-23 1202	Construction of Police Station at Phulji	Satisfactory	18-05-2023	Home, GOS	08-06-2023	Dadu	44.998
2022-23 1209	Construction of Police Station (Category-C) at Dando Taluka Tando Ghulam Hyder District Tando Muhammad Khan. (613 of 2018-19) (Remaining work).	Satisfactory	14-03-2023	Home, GOS	06-04-2023	Badin	29.528
2021-22 909	Improvement / Strengthening of Security to SCTC Sakrand (Compound Wall with Watch Towers) (SDG # 16)	Un-Satisfactory	27-01-2022	Home, GOS	07-07-2022	Shaheed Benazirabad	48.629
2021-22 917	Construction of Police Station Building at PS Dehi (SDG # 16)	Un-Satisfactory	06-07-2022	Home, GOS	30-08-2022	Badin	34.136
2021-22 950	Construction of boundary wall around Jail & Residential Colony i/c strengthening of existing main wall, rehabilitation of Watch Towers (4 Nos) & improvement of drainage at Central Prison Larkano.	Un-Satisfactory	26-05-2022	Home, GOS	05-01-2023	Larkana	76.983
2021-22 962	Provision of basic facilities of Sewerage / CC Drain / CC topping in different Katchi Abadis in Sindh..	Un-Satisfactory	14-02-2022	Human Settlement, Spatial Development & Social Housing	04-01-2023	Karachi	40
2022-23 1289	Improvement of Basic Infrastructure at Small Industrial Estate, Industrial Park, Shershah Karachi (4.68 acre land)	Un-Satisfactory	17-11-2022	Industrial & Commerce, GOS	04-01-2023	Karachi	49.11
2021-22 982	Construction of RCC Drain, Allied Works and Road Culverts Along Karachi Circular Railway (KCR) at various locations of Site Area Karachi.	Satisfactory	18-01-2022	Industrial & Commerce, GOS	29-08-2022	Karachi	343.842
2021-22 990	Construction of District Information office at Badin (C: 11.073+R: 01.762)	Un-Satisfactory	06-06-2022	Information & Archives, GOS	19-08-2022	Badin	12.835
2021-22 996	Construction of District Information office at Sujawal (C: 11.138+R: 01.762)	Un-Satisfactory	07-06-2022	Information & Archives, GOS	31-10-2022	Sujawal	12.9
2021-22 1002	Upgradation of Video Conferencing System in Sindh (Revised)(LTBC)	Satisfactory	10-06-2022	Information, Science & Technology, GOS	24-11-2022	Karachi	189.15
2022-23 1435	Rehabilitation of Employees Residence Quarters including Construction of	Satisfactory	23-09-2022	Irrigation (Water &	27-03-2023	Sukkur	767.044

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Compound Wall of Irrigation Colonies in Irrigation Department.			Drainage), GOS			
2022-23 1442	Renovation, Reconstruction and Improvement of Executive Engineer Offices and Sub-Divisional Office Complexes in Sindh (Phase -I).	Satisfactory	29-08-2022	Irrigation (Water & Drainage), GOS	20-01-2023	Shaheed Benazirabad	169.521
2022-23 1444	Renovation, Reconstruction and Improvement of Landhi's on all Canal System of Sindh (Phase-I).	Satisfactory	19-08-2022	Irrigation (Water & Drainage), GOS	20-02-2023	Naushero Feroz	194.23
2022-23 1454	Remedial Works to improve Feeding of Manchar Lake from existing Irrigation System.	Satisfactory	05-10-2022	Irrigation (Water & Drainage), GOS	15-11-2022	Jamshoro	207.489
2022-23 1472	Re-sectioning and Sand Coring of Gharaghat Bund mile 0/0 to 2/4 and Haibat Bund mile 0/0 to 5/0 in Begari Division Kashmore.	Satisfactory	22-11-2022	Irrigation (Water & Drainage), GOS	06-03-2023	Kashmore	879.985
2021-22 1047	Surface Drainage Scheme near Village Alam Khan Odho (left over pocket) (Revised) (SDG # 6 & 15)	Satisfactory	16-06-2022	Irrigation (Water & Drainage), GOS	10-11-2022	Jacobabad	399.872
2021-22 1097	Rehabilitation / Resectioning of Johi Branch from Head to Tail (RD-0.0 to 238.560) in Southern Dadu Division & Lining of Pahore and Kharoo Minor (SDG # 6)	Un-Satisfactory	15-03-2022	Irrigation (Water & Drainage), GOS	01-09-2022	Dadu	299.837
2021-22 1123	Lining of Surhari, Brandi, Maldasi, Shahdadpur Minors and Ujjano, Lundo Disty (SDG # 6)	Un-Satisfactory	27-07-2022	Irrigation (Water & Drainage), GOS	23-11-2022	Sanghar	499.579
2021-22 1135	Construction of office Complex in Southern Dadu Division @ Dadu.	Satisfactory	16-03-2022	Irrigation (Water & Drainage), GOS	01-09-2022	Dadu	145.328
2021-22 1163	Removal of Encroachment from Irrigation Department's Property & Securing its possession including Schemes of Rehabilitation (Phase-I).	Satisfactory	14-04-2022	Irrigation (Water & Drainage), GOS	29-08-2022	Sukkur	150
2021-22 1205	Cement Concrete Lining of Ali Bahar Branch from RD-0+00 to RD-20+900	Satisfactory	28-03-2022	Irrigation (Water & Drainage), GOS	29-08-2022	Matiari	255.362
2021-22 1211	C.C. Lining of Wagherji Disty from RD-0+00 to 58+200	Satisfactory	23-03-2022	Irrigation (Water & Drainage), GOS	19-08-2022	Badin	479.415
2021-22 1232	Sindh Resilience Project (Irrigation Component) for Construction of Small Dams including System for Improving Resilience - Phase II (Through Additional Financing) - (Total Cost Rs. 24,493.841 Million (IDA Share Rs. 22,652.920 Million & GoS Share Rs. 1,840.9	Satisfactory	14-03-2022	Irrigation (Water & Drainage), GOS	31-10-2022	Tharparkar	1840.92
2021-22 1232	Sindh Resilience Project (Irrigation Component) for Construction of Small Dams including System for Improving Resilience - Phase II (Through Additional Financing) - (Total Cost Rs. 24,493.841 Million (IDA Share Rs. 22,652.920 Million & GoS Share Rs. 1,840.9	Satisfactory	14-02-2022	Irrigation (Water & Drainage), GOS	27-10-2022	Jamshoro	1840.921
2021-22 1232	Sindh Resilience Project (Irrigation Component) for Construction of Small Dams including System for Improving Resilience - Phase II (Through Additional Financing) - (Total Cost Rs. 24,493.841 Million (IDA Share Rs. 22,652.920 Million & GoS Share Rs. 1,840.9	Satisfactory	17-01-2022	Irrigation (Water & Drainage), GOS	27-10-2022	Tharparkar	2350.71
2021-22 1232	Sindh Resilience Project (Irrigation Component) for Construction of Small Dams including System for Improving Resilience - Phase II (Through Additional Financing) - (Total Cost Rs. 24,493.841 Million (IDA Share Rs. 22,652.920 Million & GoS Share Rs. 1,840.9	Satisfactory	30-12-2021	Irrigation (Water & Drainage), GOS	21-10-2022	Karachi Malir	2350.71
2019-20 904	Construction of Link Drain at RD 0.0 to 25 out-falling in Seerani Branch Drain at RD 40 IP side for Village Pir Buksho and	Un-Satisfactory	22-02-2022	Irrigation (Water &	03-08-2022	Badin	119.278

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	ARO Pusio, U.C Seerani; (ii) Construction of Link Drain RD 0.0 to 14 out-falling in 6-R Tando Bago Sub-Drain at RD 22 IP side for Vi			Drainage), GOS			
2018-19 789	Construction of Regulator at Dhoro Puran Intersection RD-261 of LBOD (SDG # 6)	Un-Satisfactory	10-03-2022	Irrigation (Water & Drainage), GOS	29-09-2022	Badin	84.843
Non-ADP	KQ15P00190- Construction of Zulfiqar Oil Tanker Parking Terminal , Zulfiqarabad Karachi, Phase-I (District ADP)	Un-Satisfactory	21-06-2022	Karachi Metropolitan Corporation, KWSB	07-11-2022	Karachi Malir	20
Non-ADP	KQ12P00195- Construction of Food Court in Safari Park Karachi (District ADP)	Satisfactory	17-06-2022	Karachi Metropolitan Corporation, KWSB	01-12-2022	Karachi East	20
Non-ADP	KQ16P00103- Renoation & Improvement outskirts of main lake at Safari Park Karachi (District ADP)	Satisfactory	17-06-2022	Karachi Metropolitan Corporation, KWSB	21-11-2022	Karachi East	19.9
2022-23 1590	Rehabilitation of Old Sessions Court Building / Re-Construction of Compound Wall and External Work at Judicial Complex District Badin (Revised)	Satisfactory	21-12-2022	Law P.A. & Prosecution	15-03-2023	Badin	72.95
2021-22 1283	Construction of Two (02) Courts at Mirokhan (SDG # 16)	Satisfactory	05-01-2022	Law P.A. & Prosecution	18-11-2022	Qambar Shahdaskot	48.833
2020-21 1050	Construction of Courts (32 Nos.) at District Court Building, Korangi Karachi (Re-Revised) Cap:1131.920 + Rev:129.601) (SDG # 16)..	Satisfactory	28-02-2022	Law P.A. & Prosecution	11-01-2023	Karachi	1261.521
2022-23 1618	Cement Concrete Lining of Masoodi Distry RD-0.00 to Tail(SDG # 6)	Satisfactory	16-03-2023	Lining of Main Canals	30-03-2023	Thatta	391.171
2022-23 1621	Cement Concrete Lining of Inam & Abad Minor from RD-0.00 to 32 & 2 RDs(SDG # 6)	Satisfactory	17-03-2023	Lining of Main Canals	09-06-2023	Thatta	138.517
2022-23 1632	Cement Concrete Lining of Husri Distry from RD-18+500 to 37+000 (SDG # 6)	Satisfactory	17-10-2022	Lining of Main Canals	06-02-2023	Hyderabad	219.617
2021-22 1302	Cement Concrete Lining of Mari Minor from RD-0.00 to 48.500	Satisfactory	25-03-2022	Lining of Main Canals	04-07-2022	Sanghar	218.67
2021-22 1304	C.C Lining of Daulatpur Distry from RD-38 + 150 TO RD 100	Satisfactory	24-01-2022	Lining of Main Canals	01-07-2022	Shaheed Benazirabad	331.099
2021-22 1325	Pilot Project on Establishment of Mobile Artificial Insemination & Extension Service Units in Sindh (Phase-I), (Sukkur, Shikarpur, Jacobabad, Sanghar, Dadu, Jamshoro & Sujawal)	Satisfactory	11-05-2022	Livestock and Fisheries, GOS	04-07-2022	Jamshoro	73.673
2021-22 1342	Completion of Missing Schemes of Livestock & Fisheries Department (Hyd., M.Khas, Thatta, T.M. Khan, Sanghar & Jamshoro) (C:82.074 + R:2.000) (SDG #2)(Missing scheme)	Satisfactory	23-03-2022	Livestock and Fisheries, GOS	16-08-2022	Thatta	84.074
2022-23 1700	Revamping of Mehmoodabad nala from Malir Bund/KPT Fly over to Mehoodbabd	Satisfactory	14-10-2022	Local Government, GOS	02-01-2023	Karachi	271
2022-23 1729	Rehabilitation / Replacement / Improvement of Water Supply and Sewerage System including Pumping Stations in District Central, Karachi	Un-Satisfactory	31-10-2022	Local Government, GOS	02-01-2023	Karachi	149.978
2022-23 1730	Rehabilitation / Replacement / Improvement of Water Supply and Sewerage system including Pumping Stations in District South, Karachi	Un-Satisfactory	03-10-2022	Local Government, GOS	11-01-2023	Karachi	133.771
2022-23 1745	Construction & Rehabilitation of Main / Internal Roads. Providing Sewerage line of 12	Satisfactory	14-03-2023	Local Government, GOS	28-03-2023	Karachi East	95.418
2022-23 1747	Construction / Rehabilitation of Main / Internal Roads and installation of Paver Blocks / CC flooring & Street lights in Sachal Goth Block A to G, Ayub Goth, Christian Para and Shaheed Zulfiqar Ali Bhutto Goth (Seeta Nagar), Bilawal Shah Noorani Goth and	Satisfactory	08-11-2022	Local Government, GOS	01-03-2023	Karachi East	96.098
2022-23 1749	Construction / Rehabilitation of Main Roads / Internal Roads and installation of Paver Blocks / CC flooring & Street Lights in Junejo Town, Chutta Gabol	Satisfactory	25-05-2023	Local Government, GOS	16-06-2023	Karachi East	98.023

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Goth, Saindad Village, Noor Khan Goth, Ahmed Jamal Goth, Khuda Bux Goth and various areas of UC-31						
2022-23 1753	Construction / Rehabilitation of Main / Internal Roads, Providing Sewerage line of 12	Satisfactory	31-05-2023	Local Government, GOS	16-06-2023	Karachi East	99.278
2022-23 1756	Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line 12	Satisfactory	15-03-2023	Local Government, GOS	28-03-2023	Karachi East	95.126
2022-23 1764	Road Carpeting, C.C Flooring Sewerage line, Manzoor Colony-II (UC-06)	Satisfactory	03-03-2023	Local Government, GOS	15-03-2023	Karachi East	84.749
2022-23 1764	Road Carpeting, C.C Flooring Sewerage line, Manzoor Colony-II (UC-06)	Un-Satisfactory	16-11-2022	Local Government, GOS	11-01-2023	Karachi East	84.749
2022-23 1771	Improvement of Storm Water Drain System alongwith Supreme Court and Rising & Wall of Nallah.	Satisfactory	30-11-2022	Local Government, GOS	16-06-2023	Karachi South	73
2022-23 1784	CC Flooring, Water Supply & Sewerage Line & Road Carpeting in UC-9, Islamia Colony.	Satisfactory	17-11-2022	Local Government, GOS	11-01-2023	Karachi West	66.827
2022-23 1788	Improvement of Water Supply line, installation of Sewerage line, CC Flooring, Ground and Road Carpeting in UC-18, UC-24 & UC-26.	Un-Satisfactory	04-10-2022	Local Government, GOS	24-01-2023	Karachi West	95.704
2022-23 1813	Water Supply line, Sewerage line, Paver Block and Carpeting of Roads in different areas of UC-3.	Satisfactory	05-10-2022	Local Government, GOS	05-12-2022	Karachi West	96.463
2022-23 1831	Improvement of Water Supply and installation of Sewerage line and Carpeting of Road in UC-3 Keamari Town.	Satisfactory	18-10-2022	Local Government, GOS	11-01-2023	Karachi Keamari	68.017
2022-23 1879	Laying of Paver Block at UC 16,17,18,19 and 20 Larkana City	Satisfactory	18-11-2022	Local Government, GOS	27-03-2023	Larkana	58.696
2022-23 1880	Providing & Laying of Paver Block in Taluka Dokri	Satisfactory	02-03-2023	Local Government, GOS	13-03-2023	Larkana	24.966
2022-23 1882	Providing & Laying of C.C. Paver in various roads & streets of Jacobabad	Satisfactory	16-11-2022	Local Government, GOS	13-02-2023	Jacobabad	300
2022-23 1883	Providing & Laying of Paver Block at Various Streets of Mubarakpur City Taluka Thul	Satisfactory	07-11-2022	Local Government, GOS	27-01-2023	Jacobabad	41.998
2022-23 1887	Providing of Paver Block in Various Streets of Different Villages of Taluka Khanpur	Satisfactory	24-10-2022	Local Government, GOS	08-02-2023	Shikarpur	93.66
2022-23 1888	Providing of Paver Block in various streets in different Ward-I to Ward-30, City Shikarpur	Satisfactory	16-12-2022	Local Government, GOS	23-02-2023	Shikarpur	113.413
2022-23 1889	Providing of Paver Block in various streets of Different villages of Taluka Shikarpur	Satisfactory	01-12-2022	Local Government, GOS	08-02-2023	Shikarpur	95.356
2022-23 1890	Improvement of Various Sreets with Paver Blocks in (i) Rustam Town (ii) Jahan Khan (iii) Village Pyaro Khan Bhayo (iv) Channar Goth (v) Village Qasim Bhayo (vi) Kot Altaf Bhayo	Satisfactory	02-12-2022	Local Government, GOS	08-02-2023	Shikarpur	92.565
2022-23 2156	Construction/Installation of 10 (TEN) No. Pedestrin Bridges at Different Locatios of Karachi	Satisfactory	02-03-2023	Local Government, GOS	14-03-2023	Karachi	284.446
2022-23 2236	Construction of Road alongwith drainage, Sewerage and Paver stones in UC Quaidabad and UC Cattle Colony Ward No. 1 District Malir Karachi	Satisfactory	20-10-2022	Local Government, GOS	11-01-2023	Karachi Malir	99.826
2022-23 2387	Construction of Government Dispensaries in Talukka Sakrand and Kazi Ahmed. District Shaheed Benazirabad (04 Nos.). 297+R: 2.888) (SDG # 3)	Satisfactory	21-12-2022	Local Government, GOS	17-05-2023	Shaheed Benazirabad	23.185
2022-23 2448	Development of Township in Major Urban Centers (50,000 120 Square Yard Plots with All Civic Services	Satisfactory	18-10-2022	Local Government, GOS	18-01-2023	Karachi	9420.88
Non-ADP	KQ16P00095- Supply & Installation of Flood Lights Power System at Cricket	Satisfactory	24-06-2022	Local Government, GOS	30-11-2022	Karachi Central	20

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Ground Nazeer Hussain Gulberg , Gym ,F.B Area, KMC Part-I (District ADP)						
Non-ADP	KQ16P00096- Supply & Installation of Flood Lights Power System at Cricket Ground Nazeer Hussain Gulberg , Gym ,F.B Area, KMC Part-II (District ADP)	Satisfactory	24-06-2022	Local Government, GOS	01-12-2022	Karachi Central	20
Non-ADP	KQ16P00073- Improvement/Repair of M.A Jinnah Road from Capri Cinema to Tower (South) (District ADP)	Un-Satisfactory	22-06-2022	Local Government, GOS	25-01-2023	Karachi South	20
Non-ADP	KQ16P00077- Patch Repair of Allama Rasheed Turabi Road from Rashid Minhas Road to Ziauddin Hospital, District Central Karachi (District ADP)	Un-Satisfactory	22-06-2022	Local Government, GOS	25-01-2023	Karachi Central	19.95
Non-ADP	KQ13P00042- Rehabilitation/Improvement of road from Old Clifton Bridge to PIDC brdge along Railway line Distrc South Karachi (District ADP)	Un-Satisfactory	20-06-2022	Local Government, GOS	25-01-2023	Karachi South	20
2021-22 1375	Improvement of Sewerage System of Sachal Colony, Larkano City (SDG # 6)	Satisfactory	13-07-2022	Local Government, GOS	10-01-2023	Larkana	50
2021-22 1377	Providing Sewerage lines in PS-24 (SDG # 6)	Un-Satisfactory	31-03-2022	Local Government, GOS	13-07-2022	Shaheed Benazirabad	60.409
2021-22 1385	Construction of RCC Nallah including paver Block and replacement of P,E Pipe lines in the route of RCC Nallah for Sehwan Town, District Jamshoro	Satisfactory	07-03-2022	Local Government, GOS	06-02-2023	Jamshoro	189.562
2021-22 1390	Improvement of Drainage System of Sukkur City,	Satisfactory	06-04-2023	Local Government, GOS	10-04-2023	Sukkur	552.66
2021-22 1417	Rehabilitation/Replacement/Improvement of Sewerage, System by replacement P/L 36" 1/2 dia, 24" 1/2 dia 18" 1/2 dia & 12" 1/2 dia Sewerage Line at Block No. 7, Clifton, District South, Karachi.	Un-Satisfactory	14-12-2021	Local Government, GOS	31-10-2022	Karachi	73.42
2021-22 1421	Rehabilitation/Replacement/Improvement of Water Supply System by P/L 12 (LTBC)	Un-Satisfactory	25-05-2022	Local Government, GOS	24-11-2022	Karachi	35.91
2021-22 1421	Replacement of P/F, 12 dia (315MM), 6" 1/2 (160MM) & 4" 1/2 dia (111MM) Polyethylene pipeline in Block No. 5 & Different Areas for the Improvement of Water Supply position in Clifton, District South, Karachi	Un-Satisfactory	17-12-2021	Local Government, GOS	26-10-2022	Karachi	35.91
2021-22 1423	Rehabilitation / Improvement and replacement of water and sewerage system in UC-29, 30 and 31 Saddar, DMC South (LTBC)	Un-Satisfactory	14-06-2022	Local Government, GOS	24-11-2022	Karachi	29.13
2021-22 1424	Construction of Underground Tank one lac gallon capacity at Ismail Shaheed Park, Shah Beg lane Pir Muhammad road Lyari, DMC South Karachi (LTBC)	Un-Satisfactory	26-05-2022	Local Government, GOS	11-10-2022	Karachi	27
2021-22 1426	Improvement / Rehabilitation of Strom water Drain along 8000 road and 5000 Road to Yousuf Goth Gadap Town Karachi (Revised) (TCM request)...	Satisfactory	27-04-2022	Local Government, GOS	05-07-2022	Karachi	488.7
2021-22 1427	Providing and Fixing CC paving block Dr. Ghulam Rasool to Baloch Chowk Resham Gali Aga Khan Hospital razzaq Kumbhar Chowk, Jamia Masjid old National Bank & Various Streets at Town Committee Mirpur Sakro District Thatta	Satisfactory	12-04-2022	Local Government, GOS	27-10-2022	Thatta	95
2021-22 1434	Construction of Cover Drain/Repair of existibg Drain Ward No. 1,2,3,4,5,6,7,8,9 & 10 MC Rohri District Sukkur(TCM)	Satisfactory	07-07-2022	Local Government, GOS	21-12-2022	Sukkur	82.797
2021-22 1437	Construction of Staff Quarter for Sweeper M.C Rohri	Satisfactory	12-04-2022	Local Government, GOS	27-03-2023	Sukkur	47
2021-22 1443	Construction of Paving block CC Drain and Water Supply for various Streets and Villages of UC Arrore, District Sukkuar	Satisfactory	06-01-2022	Local Government, GOS	01-07-2022	Sukkur	115.8
2021-22 1444	Construction of Paving blocks, CC Drains & Water Supply Scheme for	Satisfactory	06-07-2022	Local Government, GOS	22-08-2022	Sukkur	116.2

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Various Streets & Villages of UC Trimoonh, District Sukkur(TCM)						
2021-22 1445	Construction of Paving Block CC Drains for Various Streets & Villages of UC Kotri, District Sukku (TCM)	Satisfactory	08-07-2022	Local Government, GOS	21-12-2022	Sukkur	87.8
2021-22 1661	Widening / Reconditioning of road from Haji Juma Jokhio Goth Dumlottee No.03 to Waja Ali Muhammad Goth (2.0 km) (SDG # 9).	Satisfactory	15-12-2021	Local Government, GOS	08-02-2023	Karachi	18.23
2021-22 1672	Construction / Reconditioning of Roads (02 Units) in Shahdadkot City, Taluka Shahdadkot (6 km) (SDG # 9)	Satisfactory	16-02-2022	Local Government, GOS	22-07-2022	Qambar Shahdadkot	70
2021-22 1677	Rehabilitation of roads of Different Streets of S.M.C.H.S Block-B Karachi (SDG # 9)...	Satisfactory	05-07-2022	Local Government, GOS	05-08-2022	Karachi	45.007
2021-22 1687	Construction of Road # 15 from Dalmia Road to K-Electric Grid Station via Jamia Masjid Zia-ul-Islam Including RCC Sewerage Line System and Providing and Fixing Street Lights Block-19 Gulshan-e-Iqbal District East Karachi (1.67 Km)	Satisfactory	13-03-2023	Local Government, GOS	03-04-2023	Karachi East	56.238
2021-22 1688	Construction of Access Road around Malir Campus of Sindh Madressat-ul-Islam University (SMIU), Education City in Gadap Town Karachi (2.44 km)	Satisfactory	20-03-2023	Local Government, GOS	12-06-2023	Karachi	44.774
2021-22 1693	Construction of Dumlottee Road from Dumlottee Well to M-9 & M-5 Link Road (12.3 km)	Un-Satisfactory	22-12-2021	Local Government, GOS	27-10-2022	Karachi	494.823
2021-22 1733	Construction/Rehabilitation of Roads , Sewerage and C,C, Flooring in Dumba Goth, District Malir, Karachi	Satisfactory	28-04-2022	Local Government, GOS	05-07-2022	Karachi	159.931
2021-22 1848	Up-gradation of Rural Health Centre Chuhar Jamali to the level of Taluka Hospital Shah Bander at Chuhar Jamali (24 Bedded and Musafirkhana) District Sujawal (C: 27.118+R: 20.551) (SDG #	Un-Satisfactory	11-01-2022	Local Government, GOS	05-08-2022	Sujawal	47.669
2021-22 1854	Rehabilitation / Renovation of Jaral Shah Dargah at Larkano (Re-Revised)	Un-Satisfactory	10-05-2022	Local Government, GOS	05-01-2023	Larkana	30
2021-22 1861	Construction of Parks at Landhi Kotal Chowrangji, Karachi	Satisfactory	09-02-2022	Local Government, GOS	07-07-2022	Karachi	40
2021-22 1867	Beautification of M.C Rohri District Sukkur	Un-Satisfactory	17-03-2022	Local Government, GOS	04-08-2022	Sukkur	51.953
Non-ADP	Renovation of Volly Ball Ground Hussainabad, Hyderabad	Un-Satisfactory	07-06-2022	Local Government, GOS	22-08-2022	Hyderabad	12.867
Non-ADP	Construction of Watch Towers, Guard Rooms, Vehicle Shades and Renovation of other Structures of Deputy Commissioner	Un-Satisfactory	22-06-2022	Local Government, GOS	27-09-2022	Hyderabad	40
2020-21 1163	Providing of 10 Nos. Suction Machines and 10 Nos. High Pressure Jetting Machines including Up-gradation of existing machines for improvement of Sewer work in different Districts of Karachi (SDG # 6)..	Satisfactory	18-07-2022	Local Government, GOS	31-10-2022	Karachi	899.92
2022-23 2471	Rehabilitation / Reconstruction of Shahrah-e-Noor Jehan from Abdullah College to Qalandaria Chowk	Satisfactory	12-10-2022	Mega Schemes for Karachi City	11-01-2023	Karachi	1303.83
2022-23 2473	Rehabilitation / Reconstruction of Road from Cafe piyala (near Gulberg Chowrangji) to Rashid Minhas road near UBL Sports complex	Satisfactory	06-10-2022	Mega Schemes for Karachi City	11-01-2023	Karachi	491.895
2022-23 2477	Re-Construction / rehabilitation of Chakiwara Road, Mehrab Khan Essa Road and Tennery Road, Lyari Town (District South) Including SWD System	Satisfactory	11-10-2022	Mega Schemes for Karachi City	11-01-2023	Karachi	933.928
2022-23 2478	Rehabilitation of Approach Roads of Lyari Expressway.	Satisfactory	01-03-2023	Mega Schemes for Karachi City	14-03-2023	Karachi	219.502
2020-21 1476	Rehabilitation and Improvement of Karachi Zoo (Re-Revised) (SDG # 9)(visit after expiry of grace period)	Satisfactory	18-03-2022	Mega Schemes for Karachi City	19-08-2022	Karachi	391.934
2022-23 2498	Implementation of various Development Schemes of Minorities in	Satisfactory	03-03-2023	Minorities & Affairs, GOS	02-05-2023	Jamshoro	704.565

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Sindh (Jamshoro, Ghotki, Karachi, Khairpur, Jacobabad, Larkano, Kashmore, Sukkur, N.Feroze, Dadu, SBA, Sanghar, Mirpurkhas, Umerkot, Tharparkar, Matiari, Jacobabad, Jamshoro, Thatta, Shikarp						
2022-23 2498	Implementation of various Development Schemes of Minorities in Sindh (Jamshoro, Ghotki, Karachi, Khairpur, Jacobabad, Larkano, Kashmore, Sukkur, N.Feroze, Dadu, SBA, Sanghar, Mirpurkhas, Umerkot, Tharparkar, Matiari, Jacobabad, Jamshoro, Thatta, Shikarp	Satisfactory	13-10-2022	Minorities & Affairs, GOS	30-11-2022	Tando Allahyar	704.565
2022-23 2498	Implementation of various Development Schemes of Minorities in Sindh (Jamshoro, Ghotki, Karachi, Khairpur, Jacobabad, Larkano, Kashmore, Sukkur, N.Feroze, Dadu, SBA, Sanghar, Mirpurkhas, Umerkot, Tharparkar, Matiari, Jacobabad, Jamshoro, Thatta, Shikarp	Satisfactory	11-10-2022	Minorities & Affairs, GOS	15-11-2022	Matiari	704.565
2022-23 2498	Implementation of various Development Schemes of Minorities in Sindh (Jamshoro, Ghotki, Karachi, Khairpur, Jacobabad, Larkano, Kashmore, Sukkur, N.Feroze, Dadu, SBA, Sanghar, Mirpurkhas, Umerkot, Tharparkar, Matiari, Jacobabad, Jamshoro, Thatta, Shikarp	Satisfactory	05-10-2022	Minorities & Affairs, GOS	15-11-2022	Mirpurkhas	704.565
2022-23 2500	Repair / Renovation of various Mandirs in Hyderabad Division (Hyderabad, Tando Allahyar, T.M Khan, Matiari, Badin, Thatta, Jamshoro, Dadu & SBA)	Satisfactory	30-09-2022	Minorities & Affairs, GOS	21-11-2022	Badin	289.663
2022-23 2500	Repair / Renovation of various Mandirs in Hyderabad Division (Hyderabad, Tando Allahyar, T.M Khan, Matiari, Badin, Thatta, Jamshoro, Dadu & SBA)	Satisfactory	29-09-2022	Minorities & Affairs, GOS	15-11-2022	Matiari	289.663
2022-23 2500	Repair / Renovation of various Mandirs in Hyderabad Division (Hyderabad, Tando Allahyar, T.M Khan, Matiari, Badin, Thatta, Jamshoro, Dadu & SBA)	Satisfactory	28-09-2022	Minorities & Affairs, GOS	01-12-2022	Tando Muhammad Khan	289.663
2022-23 2500	Repair / Renovation of various Mandirs in Hyderabad Division (Hyderabad, Tando Allahyar, T.M Khan, Matiari, Badin, Thatta, Jamshoro, Dadu & SBA)	Satisfactory	22-09-2022	Minorities & Affairs, GOS	24-11-2022	Tando Allahyar	289.663
2022-23 2500	Repair / Renovation of various Mandirs in Hyderabad Division (Hyderabad, Tando Allahyar, T.M Khan, Matiari, Badin, Thatta, Jamshoro, Dadu & SBA)	Satisfactory	20-09-2022	Minorities & Affairs, GOS	30-11-2022	Hyderabad	289.663
2021-22 1941	Repair / Renovation of various Mandirs in Sindh (Karachi, Dadu, Thatta, Tharparkar, Jamshoro, Hyderabad, Larkano, N.Feroze, Khairpur Mirs, Matiari & T.Allahyar) (Revised)	Un-Satisfactory	13-05-2022	Minorities & Affairs, GOS	11-10-2022	Larkana	75.829
2021-22 1942	Reconstruction / Uplift / Expansion of Minorities Places in Sindh (Karachi, Shikarpur, Jamshoro, Umerkot, Thatta & Hyderabad) (Revised)	Un-Satisfactory	16-05-2022	Minorities & Affairs, GOS	14-11-2022	Shikarpur	62.691
2021-22 1944	Implementation of various Development Schemes of Minorities in Sindh (Jamshoro, Ghotki, Karachi, Khairpur, Jacobabad, Larkano, Kashmore, Sukkur, N.Feroze, Dadu, SBA, Sanghar, Mirpurkhas, Umerkot, Tharparkar, Matiari, Jacobabad, Jamshoro, Thatta, Shikarp	Un-Satisfactory	29-09-2021	Minorities & Affairs, GOS	01-09-2022	Ghotki	704.565
Non-ADP	Additional facilities of and solar system of DC office Dadu	Satisfactory	22-07-2022	Physical Planning & Housing (Buildings), GOS	30-11-2022	Dadu	19.2
Non-ADP	Construction of Compound Wall Around Graveyard @ Dado Yaqoob Shah Near Karo Ghat Tulka Ghotki	Un-Satisfactory	30-06-2022	Physical Planning & Housing (Buildings), GOS	13-12-2022	Ghotki	6.3

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
Non-ADP	Construction of Surface Drains CC Topping & Brick Pavement Union Counsel Darbelo Taluka Kandiyaro	Satisfactory	20-06-2022	Physical Planning & Housing (Buildings), GOS	15-02-2023	Naushero Feroz	4.95
2022-23 2623	Construction/Reconstruction & Rehabilitation of Field Offices-Cum-Residences of Sindh Bureau of Statistics at Meher	Satisfactory	25-08-2022	Planning & Development , GoS	27-01-2023	Dadu	19.993
2021-22 2009	Reconstruction, Renovation & Rehabilitation of Divisional/ District & Sub-Divisional Offices-cum- Residences of Bureau of Statistics, Sindh.(C:165.065 m + R:17.370 m) (Hyderabad, Jamshoro, Dadu, SBA, Badin, T.M.Khan, Sukkur, Ghotki, Larkano, Jacobabad,	Un-Satisfactory	04-07-2022	Planning & Development , GoS	05-09-2022	Jacobabad	302.149
2021-22 2019	Costed Implementation Plan (Revised) (R:2157.837) (SDG # 3, 5)	Satisfactory	07-06-2022	Population Welfare, GOS	25-11-2022	Dadu	2157.837
2021-22 2019	Costed Implementation Plan (Revised) (R:2157.837) (SDG # 3, 5)	Satisfactory	19-01-2022	Population Welfare, GOS	16-08-2022	Ghotki	2157.837
2021-22 2019	Costed Implementation Plan (Revised) (R:2157.837) (SDG # 3, 5)	Satisfactory	18-01-2022	Population Welfare, GOS	12-10-2022	Sukkur	2157.837
2020-21 1533	Costed Implementation Plan (Revised) (R:2157.837) (SDG # 3, 5)	Satisfactory	11-02-2022	Population Welfare, GOS	24-11-2022	Thatta	2157.837
2020-21 1533	Costed Implementation Plan (Revised) (R:2157.837) (SDG # 3, 5)	Satisfactory	10-02-2022	Population Welfare, GOS	24-11-2022	Karachi East	2157.837
2022-23 2676	Providing & Installtion of 200 submersible pumps in various villages of district Tharparkar	Satisfactory	27-03-2023	Public Health Engineering, GOS	08-05-2023	Tharparkar	200
2022-23 2677	Improvement of Water Supply Scheme in Town Committee Chhachhro & Town Committee Khome-jo-Par (SDG # 6).	Un-Satisfactory	06-10-2022	Public Health Engineering, GOS	27-01-2023	Tharparkar	65.833
2022-23 2678	Upgradation & Extention of Pipe Line Water Supply Scheme Kunri-Cheel Bund-Kantio-Chachro (WSL-3) (SDG # 6).	Satisfactory	13-10-2022	Public Health Engineering, GOS	06-02-2023	Tharparkar	137.495
2022-23 2714	Construction of Water Supply Scheme Deh Gulapur, Deh Kathgarh, Deh Line Purani and Deh Keenjhar (SDG#6)	Satisfactory	10-10-2022	Public Health Engineering, GOS	14-02-2023	Kashmore	100
2022-23 2777	Drainage Scheme Misri Khan Jarwar alongwith Disposal Taluka Tando Allahyar.	Satisfactory	22-03-2023	Public Health Engineering, GOS	19-04-2023	Tando Allahyar	25
2022-23 2809	Drainage Scheme Kaloi Town	Satisfactory	19-10-2022	Public Health Engineering, GOS	19-04-2023	Tharparkar	60
2022-23 2828	Providing and Fixing Paving Blocks with Road Drainage in Various Streets of Khanpur Town and Various Villages of UC Mian Jo Goth (SDG # 6).	Satisfactory	14-11-2022	Public Health Engineering, GOS	16-03-2023	Shikarpur	68.651
2022-23 2829	Drainage Scheme Garhi Yaseen (SDG # 6).	Satisfactory	11-10-2022	Public Health Engineering, GOS	09-02-2023	Shikarpur	94.386
2022-23 2843	Drainage Scheme of Radhan Town (SDG # 6).	Satisfactory	21-03-2023	Public Health Engineering, GOS	03-05-2023	Dadu	99.533
2022-23 2847	Construction of Paver Blocks & C.C Drains in Various Muhalla's City Shahdadkot (SDG # 6).	Satisfactory	12-12-2022	Public Health Engineering, GOS	09-02-2023	Qambar Shahdadkot	164.857
2022-23 2849	Construction of C.C Drains and Paver Blocks for Muhallas of Shahdadkot City (SDG # 6).	Satisfactory	13-12-2022	Public Health Engineering, GOS	27-02-2023	Qambar Shahdadkot	100
2022-23 2861	Drainage System for left over areas of City Naudero (SDG#6).	Satisfactory	08-12-2022	Public Health Engineering, GOS	28-02-2023	Larkana	124.851
2022-23 2862	Construction of Paver Block And C.C Drain in Various Areas of City Ratodero (SDG # 6).	Satisfactory	09-12-2022	Public Health Engineering, GOS	28-02-2023	Larkana	123.786
2022-23 2864	Construction of Paver Block & CC Drain in Various locations of UC-01 to 05 Larkano City (SDG # 6).	Satisfactory	07-12-2022	Public Health Engineering, GOS	27-02-2023	Larkana	150
2022-23 2865	Construction of Paver Block and CC Drains of Various Locations of UC-06 to 10 City Larkano (SDG # 6).	Satisfactory	06-12-2022	Public Health Engineering, GOS	27-02-2023	Larkana	150
2022-23 2871	Construction of Drains & Paver Block in Various Streets of Ward No.1,II,III,V&VII of Naudero, Taluka Ratodero(SDG#6).	Satisfactory	10-11-2022	Public Health Engineering, GOS	16-03-2023	Larkana	49.411

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 2873	Construction of Paver Block & CC Drain of Akil Circle ( UC's Akil, Aghani & Phull) (2.50 KMs), Taluka Larkano (SDG # 6).	Satisfactory	07-10-2022	Public Health Engineering, GOS	16-03-2023	Larkana	45.37
2022-23 2874	Construction of Paver/CC Block & CC Drain from Railway Station Badeh to Govt. Hospital Badeh, and Construction of CC Block Paver Block & CC Drain Channa Bridge Dokri to Dokri Bus Stand Via Village Babal Jarwar and various streets of City Badeh and City Do	Satisfactory	08-11-2022	Public Health Engineering, GOS	16-03-2023	Larkana	76.12
2022-23 2875	Construction of Paver/CC Block & CC Drain in diferent Villages of District Larkano (SDG # 6).	Satisfactory	09-11-2022	Public Health Engineering, GOS	28-02-2023	Larkana	94.616
2022-23 2994	Elimination of Urban Sewerage Discharging in Irrigation Canals and lakes in Sindh Phase-I (Revised on 19.02.19) (SDG # 6)	Satisfactory	06-03-2023	Public Health Engineering, GOS	03-05-2023	Dadu	3764.648
2022-23 2994	Elimination of Urban Sewerage Discharging in Irrigation Canals and lakes in Sindh Phase-I (Revised on 19.02.19) (SDG # 6)	Satisfactory	22-12-2022	Public Health Engineering, GOS	19-04-2023	Badin	3764.648
Non-ADP	Rural Water Supply Scheme Ramzan Rajar, Taluka Kotri, District Jamshoro.	Satisfactory	22-07-2022	Public Health Engineering, GOS	08-02-2023	Jamshoro	3.5
Non-ADP	CONSTRUCTION OF DRAINS, CC BLOCK & PAVER @ VARIOUS EIGHT (8) LOCATIONS OF UC-8,10,11 & 13 OF LARKANA CITY.	Satisfactory	05-04-2022	Public Health Engineering, GOS	04-07-2022	Larkana	19
2021-22 2040	Water Supply Scheme Hub Dam to 42 Various Village Construction of Surface with Pump Room i/c Electricity System near Hub Dam River Deh Allah Phai. (As per TCM request)	Satisfactory	04-07-2022	Public Health Engineering, GOS	02-09-2022	Karachi	144.337
2021-22 2049	Water Supply Line from Dhaknio to Bachu Mahendro-Ji-Dhani and Dargah Mehar Ali Faqeer (SDG # 6).	Satisfactory	17-03-2022	Public Health Engineering, GOS	16-08-2022	Tharparkar	10.975
2021-22 2050	Water Supply Scheme Sokliyo to Veeranio Sokiyo to Behrao Via Rahirari (SDG # 6).	Satisfactory	18-03-2022	Public Health Engineering, GOS	16-08-2022	Tharparkar	36.9
2021-22 2053	Water Supply Scheme Soomar Village (SDG # 6).	Satisfactory	18-05-2022	Public Health Engineering, GOS	15-11-2022	Sujawal	20
2021-22 2054	Water Supply Scheme Raj Malik (SDG # 6).	Un-Satisfactory	16-06-2022	Public Health Engineering, GOS	05-10-2022	Sujawal	13.093
2021-22 2059	Water Supply Scheme Jumma Khan Gabol Deh Amri Taluka Manjhhand (SDG # 6).	Satisfactory	15-06-2022	Public Health Engineering, GOS	19-08-2022	Jamshoro	29.978
2021-22 2062	Rehabilitation of Urban Water Supply Scheme Nindo City (SDG # 6).	Satisfactory	05-04-2022	Public Health Engineering, GOS	24-11-2022	Badin	25
2021-22 2074	Rural Water Supply Scheme Boohar Mathyoon Taluka Kamber (SDG # 6).	Satisfactory	11-11-2021	Public Health Engineering, GOS	29-07-2022	Qambar Shahdadt	20
2021-22 2081	Urban Water Supply Scheme Shahpur Chakkar Phase-II (SDG # 6).	Satisfactory	22-11-2021	Public Health Engineering, GOS	04-07-2022	Sanghar	306.405
2021-22 2085	Rural Water Supply Scheme Village Jaggan bhayo (Shifting of Source)	Satisfactory	28-01-2022	Public Health Engineering, GOS	16-08-2022	Shikarpur	96.52
Non-ADP	Water Supply Tank Alongwith Distribution Network for Old Sukkur (SDG # 6).	Satisfactory	30-07-2022	Public Health Engineering, GOS	20-02-2023	Sukkur	100
2021-22 2144	Drainage Scheme Village Hussain Kalwhar Taluka Pano Aqil (SDG # 6).	Un-Satisfactory	16-03-2022	Public Health Engineering, GOS	16-08-2022	Sukkur	15
2021-22 2147	Rehabilitation & Improvemnet of Urban Drainage Scheme Shikarpur (Revised) (SDG # 6).	Satisfactory	25-11-2021	Public Health Engineering, GOS	16-08-2022	Shikarpur	1197.25
2021-22 2159	Improvement / Extension of Drainage Scheme Kamber (SDG # 6)	Un-Satisfactory	07-03-2022	Public Health Engineering, GOS	04-07-2022	Qambar Shahdadt	648.5
2021-22 2174	Rural Drainage Scheme Dalel Dero UC-Punhal Khan Chandio (SDG # 6).	Satisfactory	24-03-2022	Public Health Engineering, GOS	21-10-2022	Shaheed Benazirabad	37.311

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2021-22 2182	Improvement & Extension of Urban Drainage Scheme Behlani alongwith CC Block. @	Satisfactory	19-05-2022	Public Health Engineering, GOS	22-03-2023	Naushero Feroz	30
2021-22 2197	Drainage System of Village Adur Narejo Deh Golo Wahan Taluka Gambat (SDG # 6).	Satisfactory	13-04-2022	Public Health Engineering, GOS	10-01-2023	Khairpur	15
2021-22 2199	Improvement & Extension of Drainage Scheme Gadeji Taluka Sobho Dero (SDG # 6).	Un-Satisfactory	23-12-2021	Public Health Engineering, GOS	22-08-2022	Khairpur	30
2021-22 2201	Rural Draingae Scheme Maghanwari Taluka Kingri	Un-Satisfactory	21-01-2022	Public Health Engineering, GOS	25-11-2022	Khairpur	25
2021-22 2203	Construction of Surface Drains & Paver Bock for Village Haji Ali Nawaz Rajper, UC Karoondi, Taluka Faiz Ganj, District Khairpur	Satisfactory	15-12-2021	Public Health Engineering, GOS	12-08-2022	Khairpur	13.325
2021-22 2315	Rehabilitation of Non-Functional Water Supply and Drainage Schemes Phase-I (Revised)(SDG # 6)	Satisfactory	16-11-2021	Public Health Engineering, GOS	16-08-2022	Dadu	5269
2021-22 2329	Construction of Power & Drainage Scheme for Village Qadir Bux Mugheri UC Wagan Taluka Warah (ADP No.1640/2018-19) (SDG # 6).	Un-Satisfactory	22-08-2022	Public Health Engineering, GOS	11-01-2023	Qambar Shahdadkot	8.458
2021-22 2330	Rural Drainage Scheme Khabri Taluka Laksi (Non-ADP of 2018-19) (SDG # 6).	Satisfactory	11-02-2022	Public Health Engineering, GOS	29-07-2022	Shikarpur	17.627
2021-22 2341	Construction of Lalu Waggan Road from Village Muhammad Khan to Azeem Brohi UC Noor Abad Taluka Warah district Kamber-Shahdadkot (3km)(SDG # 1, 9, 11)	Un-Satisfactory	13-04-2022	Public Health Engineering, GOS	15-07-2022	Qambar Shahdadkot	16
2021-22 2343	Construction of Road from Village Haji Rustam Mehari to Village Manik Mangrio UC-Rahoki Taluka Shaheed Fazil Raho. (3KM) (SDG # 1, 9, 11 Rural Development Department	Satisfactory	20-09-2021	Public Health Engineering, GOS	02-09-2022	Badin	20
2021-22 2350	Construction of Road from Village Varasham Shodo to Ali Murad Barejo, U.C Sari, Taluka Thana Bulla Khan, District Jamshoro.(1.5 km) (SDG # 1, 9, 11 Rural Development Department	Satisfactory	23-09-2021	Public Health Engineering, GOS	02-09-2022	Jamshoro	12
2021-22 2356	Construction of Metalled Road / C.C Drain / Paver Block from Jurio Chandio to Haji Allah Dito House via Allah Warayo Chandio to Syed Zulfiqar Ali Shah Dargah, Mumtaz Colony.(SDG # 1, 9, 11)	Satisfactory	03-02-2022	Public Health Engineering, GOS	29-07-2022	Larkana	27.806
2021-22 2402	Construction of C.C Drain / Paver Block from I.B Khuro Public School to Baghan Shah Hotel via Roshan Chandio Shakh. (C:12.000)(SDG #6)	Un-Satisfactory	12-01-2022	Public Health Engineering, GOS	29-08-2022	Larkana	12
Non-ADP	Construction of paving block i/c drain from Raza Soomro Shop to Dadu Moro road via Agriculture workshop i/c link to Gov	Un-Satisfactory	28-07-2022	Public Health Engineering, GOS	30-11-2022	Dadu	30
Non-ADP	Construction of Severage Line from Railway Line, Essa Dall VIA Bihar Colony to Phatak Kotri, District Jamshoro	Un-Satisfactory	27-06-2022	Public Health Engineering, GOS	07-11-2022	Jamshoro	7
Non-ADP	Construction of Darinage Scheme at Malik, Shaikh and Channa Muhalla	Satisfactory	29-07-2022	Public Health Engineering, GOS	15-02-2023	Kashmore	10
Non-ADP	Remaining Work of Drainage Scheme Village Changar UC Shah Bhangio Tulka Khairpur	Satisfactory	16-06-2022	Public Health Engineering, GOS	22-03-2023	Khairpur	23.985
Non-ADP	Construction of CC Block & Drainage from House of Naban Mugheri to House of Akhtar Brohi Larkanao Taluka Larkano	Satisfactory	09-06-2022	Public Health Engineering, GOS	12-08-2022	Larkana	39.6
Non-ADP	Construction of CC Block & Drainage from Abdul Ghani House via Mumtaz Ali Borhi House to Muhammad Safar Baloach UC-7 Larkanao Taluka Larkano	Satisfactory	10-06-2022	Public Health Engineering, GOS	12-08-2022	Larkana	39.3
Non-ADP	Construction of Paver Block & CC drains from Hosue of Imam Din Chandio to House of Abdul Hameed Pathan Larkanao city Taluka Larkano	Satisfactory	13-06-2022	Public Health Engineering, GOS	12-08-2022	Larkana	39.1

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2020-21 1671	Elimination of Urban Sewerage Discharging in Irrigation Canals and lakes in Sindh Phase-I (Revised) (SDG # 6)	Satisfactory	12-03-2021	Public Health Engineering, GOS	01-07-2022	Larkana	3764.648
2017-18 2145	Construction of CC Drains and CC Block at various UCs of Larkana (20 Villages) (SDG # 6)	Un-Satisfactory	21-04-2022	Public Health Engineering, GOS	16-08-2022	Larkana	40
2022-23 3075	Establishment of Regional Offices of PDMA (SDG # 13) (C:861.338+R:30.515). (Revisit As per decision of PDWP meeting)	Satisfactory	05-05-2023	Rehabilitation (PDMA), GOS	31-05-2023	Mirpurkhas	891.853
2022-23 3075	Establishment of Regional Offices of PDMA (SDG # 13) (C:861.338+R:30.515)	Un-Satisfactory	04-05-2023	Rehabilitation (PDMA), GOS	31-05-2023	Larkana	891.853
2022-23 3075	Establishment of Regional Offices of PDMA (SDG # 13) (C:861.338+R:30.515)	Satisfactory	03-05-2023	Rehabilitation (PDMA), GOS	31-05-2023	Shaheed Benazirabad	891.853
Non-ADP	Construction of road at Village Momin Panhwar Mile: 0/00/2+330 (0.5 Kms)	Un-Satisfactory	05-07-2022	Rural Development, GOS	07-11-2022	Mirpurkhas	7.5
Non-ADP	Construction of Road from KGM Dhenghan Road to Village Dhengan City Mile: 6/6+2207/0+550 (0.50 Kms)	Satisfactory	14-07-2022	Rural Development, GOS	15-11-2022	Mirpurkhas	18.9
2021-22 2338	Construction of Link Road Saleem Khan Khoso to Suhbat Khan Bajkani UC Jagirabad Taluka Tangwani District Kashmore (2.5 km) (SDG # 1, 9, 11)	Un-Satisfactory	22-03-2022	Rural Development, GOS	29-08-2022	Kashmore	18
2021-22 2352	Re-Construction / Repair of Road Karama Bagh Muhammad Pur.(SDG # 1, 9, 11)	Satisfactory	21-03-2022	Rural Development, GOS	13-07-2022	Larkana	18
2021-22 2358	Construction of Road Wado Wahan Taluka Bakrani. (SDG # 1, 9, 11)	Satisfactory	29-03-2022	Rural Development, GOS	13-07-2022	Larkana	16
Non-ADP	Construction of Road From Dahar Wah to Haji Malik Fareed Malik via Nihal Wah Mile 0/0 to 1/5 +330	Satisfactory	30-06-2022	Rural Development, GOS	30-11-2022	Ghotki	19.958
Non-ADP	Reconditioning of Link Road From Allah Wala Chowk up to Civil Hospital N.Feroz 0/0 0/1	Satisfactory	10-06-2022	Rural Development, GOS	30-11-2022	Naushero Feroz	7.1
Non-ADP	Reconditioning of Link Road From Moro Mithyani Road To Village Ali Murad Lanjar Road 0/0 to 1/2	Satisfactory	06-06-2022	Rural Development, GOS	16-01-2023	Naushero Feroz	20
Non-ADP	Construction of Road From Tharushah N.feroz to village Ismail Vistro UC Malan Road Mile 0/0 to 0/2 Tulka Bhriya	Satisfactory	09-06-2022	Rural Development, GOS	25-11-2022	Naushero Feroz	3.6
Non-ADP	Construction of Road From NHA To Imam Bux Mangrio Along Sehra Minor Road Mile 0/0 0/1+330 Tulka Kandiyaro	Satisfactory	07-06-2022	Rural Development, GOS	30-11-2022	Naushero Feroz	2.9
Non-ADP	Construction of Link Road from Deewan Jo Keerio Road Village Mukrari Via Darghah Mehar Ali Shah Road Mile 0/0 to 0/5+190	Satisfactory	08-06-2022	Rural Development, GOS	25-11-2022	Naushero Feroz	12
2021-22 2419	Construction of Circuit House, Larkano	Satisfactory	24-06-2022	S.G.A.and Coordination, GOS	13-09-2022	Larkana	72.081
2021-22 2431	Establishment of Deputy Commissioner office Complex, District Malir.	Satisfactory	02-02-2023	S.G.A.and Coordination, GOS	09-02-2023	Karachi	354.162
2018-19 1749	Renovation & rehabilitation of flats at GOR at Shadman Town Karachi.	Un-Satisfactory	07-03-2023	S.G.A.and Coordination, GOS	06-04-2023	Karachi	41.066
2022-23 3159	Construction of Sports Stadium in Sindh (8 Nos.) (Matari, Jamshoro, Hyderabad, Tharparkar, Sanghar, Shikarpur, Jacobabad & Tando Allahyar) (Revised on 20.02.20) (C:481.026+R:40.000) (SDG # 3)	Un-Satisfactory	16-11-2022	Sports & Youth Affairs, GOS	04-01-2023	Jamshoro	521.026
2022-23 3171	Construction of Multipurpose Sports Hall at Sports Complex	Satisfactory	06-10-2022	Sports & Youth Affairs, GOS	21-02-2023	Shikarpur	55
2022-23 3173	Construction of Grassy Cricket Ground with Pavilion i/c Installation of Flood Lights at Force Ground	Satisfactory	15-03-2023	Sports & Youth Affairs, GOS	16-05-2023	Jacobabad	93.5
2022-23 3181	Laying of New Blue Synthetic Hockey Turf & Digital Score Board at Existing Hockey Stadium NIPA	Satisfactory	30-09-2022	Sports & Youth Affairs, GOS	23-02-2023	Karachi East	88

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 3182	Construction of Multipurpose Sports Hall i/c Walking Track Makhdoom Bilawal Cooperative Housing Society	Satisfactory	30-09-2022	Sports & Youth Affairs, GOS	23-02-2023	Karachi Korangi	66
2022-23 3189	Construction of Futsal Ground for Ladies at Government Girls College	Satisfactory	09-03-2023	Sports & Youth Affairs, GOS	18-04-2023	Jacobabad	44
2021-22 2503	Construction of Players Hostel at Ghotki (C:51.893+R:9.381)	Satisfactory	31-12-2021	Sports & Youth Affairs, GOS	05-09-2022	Ghotki	61.274
2021-22 2512	Construction of Sports Ground at Thul City Taluka Thul District Jacobabad (C:41.117+R:0.156)	Satisfactory	27-09-2022	Sports & Youth Affairs, GOS	21-02-2023	Jacobabad	41.273
2021-22 2513	Installation of Flood Litghts with stand by Generator and External Works at Football Turf Stadium Public School, Hyderabad (Phase-I) (C:49.813+R:0.186)	Satisfactory	25-05-2022	Sports & Youth Affairs, GOS	16-08-2022	Hyderabad	49.999
2021-22 2519	Construction of Sports Indoor Hall at Railway Ground, Sukkur	Satisfactory	15-04-2022	Sports & Youth Affairs, GOS	13-07-2022	Sukkur	54.346
2021-22 2552	Construction of Lalkhmir Sports Ground at Taluka Jacobabad	Satisfactory	05-07-2022	Sports & Youth Affairs, GOS	13-02-2023	Jacobabad	45
2022-23 789	Umbrella schemes transferred from Education & Labour Department to STEVTA Karachi (22 units)	Satisfactory	04-11-2022	STEVTA, GOS	28-03-2023	Karachi	5440
2021-22 796	Construction of B-Tech Department at Governmemnt College Technology (GCT) Hyderabad	Satisfactory	28-03-2023	STEVTA, GOS	30-03-2023	Hyderabad	140
2022-23 842	Development of Remaining Essential Facilities Required for Establishment of Mehran University College of Engineering and Technology at Khairpur Mir's (C:717.236 .+ R:130.492)	Satisfactory	03-03-2023	Universities and Boards	06-04-2023	Khairpur	847.728
2022-23 863	Construction of Central/Digital Library at Chandka Medical College of SMBBMU Larkano (C:375.189 + R:101.340) (SDG#4)	Satisfactory	20-09-2022	Universities and Boards	18-11-2022	Larkana	476.529
2021-22 630	Development of Department of Food Engineering & Infrastructure at NED University of Engineering & Technology, Karachi (C:159.779 + R:167.564)	Satisfactory	27-10-2021	Universities and Boards	06-07-2022	Karachi	327.343
2021-22 632	Extension of Educational Allied Facilities at Sukkur IBA and IBA Community College Khairpur(C: 861.716 + R: 438.284.)) (SDG#4)	Satisfactory	06-03-2023	Universities and Boards	21-03-2023	Khairpur	1300
2021-22 632	Extension of Educational Allied Facilities at Sukkur IBA and IBA Community College Khairpur(C: 861.716 + R: 438.284) (SDG#4)	Satisfactory	22-02-2022	Universities and Boards	29-03-2023	Sukkur	1300
2022-23 3313	Renovation of Existing Building of Women Development Complex at Sanghar (C: 21.772+R:1.980) ,(SDG # 1,4, 5,8 & 9)	Satisfactory	21-10-2022	Women Development , GOS	16-01-2023	Sanghar	23.752
2022-23 3314	Establishment & Strengthening of Darul Aman at Mirpurkhas & Jacobabad (Revised on 16.05.17)(C:154.680 + R:32.014) (SDG # 2)	Satisfactory	22-09-2022	Women Development , GOS	08-02-2023	Mirpurkhas	186.694
2021-22 2610	Repair and Maintenance of Exiting Building of Women Training Institute at Shaheed Benazir Abad.	Un-Satisfactory	10-06-2022	Women Development , GOS	04-01-2023	Shaheed Benazirabad	36.92
2022-23 3330	W/R of road from Arrore Bachal Shah to Choundko (32.18 Kms) (SDG # 9)	Un-Satisfactory	30-11-2022	Work and Service, GOS	09-01-2023	Sukkur	540.878
2022-23 3334	W/R of Jacobabad Thull road (37.00 Kms) (SDG # 9)	Satisfactory	31-05-2023	Work and Service, GOS	28-05-2023	Jacobabad	1950.048
2022-23 3366	Improvement of road from Old Indus Highways City Portion Larkano to N.I.P Side of Rice Canal via Hasnain Medical Center i/c Paver Link in Ghulam Akbar Jalbani Street upto SZABIST College and approaches to various streets Sachal Colony Larkana (4.40 Kms)	Satisfactory	31-10-2022	Work and Service, GOS	01-03-2023	Larkana	119.991
2022-23 3367	W/R of road from Sanhra Machi to Police Picket Post village Bosan, including approach to village Imam Bux Langah - Wassayo Bhutto road (6.00 Kms)	Satisfactory	21-10-2022	Work and Service, GOS	09-02-2023	Larkana	101.976

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 3376	Reconditioning of road from Thouf Chosul - Bhand Chowk road Mahmoodabad Police Chowki to Miro Khan (7.00 Kms)	Satisfactory	05-12-2022	Work and Service, GOS	13-02-2023	Qambar Shahdadkot	76.932
2022-23 3391	Rehabilitation / Reconditioning of road from Hakra Panhwr Chowki to Bhiro (10.00 Kms)	Satisfactory	02-03-2023	Work and Service, GOS	18-04-2023	Sukkur	96.21
2022-23 3400	Reconditioning of road from Mehran N/Highway to Dejarja Nawab Ali Shah Bhambhan via Khairi road (14.00 Kms)	Satisfactory	22-08-2022	Work and Service, GOS	20-12-2022	Khairpur	134.813
2022-23 3439	Reconditioning of road from Moro - Dadu road to village Jadal Shah 1-1/2	Satisfactory	11-10-2022	Work and Service, GOS	20-12-2022	Naushero Feroz	65.635
2022-23 3441	W/R / Construction / Reconditioning of various roads of Taluka Nawabshah (79.30 Kms)	Satisfactory	05-06-2023	Work and Service, GOS	19-06-2023	Shaheed Benazirabad	1235.775
2022-23 3442	Improvement / Rehabilitation of various roads / streets of Nawabshah City (42.23 Kms)	Satisfactory	05-06-2023	Work and Service, GOS	19-06-2023	Shaheed Benazirabad	971.082
2022-23 3448	W/R / Construction of road from 60th Mile - 3 Chak Suhallo road @ 18 Shak Stop to connect Ghazi Khan Bhurgari road @ Nim Stop via Sui Gas H.Q & link to village Masood Nabi Noor along Akdohi Minor mile 0/0-5/2+330 (8.50 Kms)	Satisfactory	14-11-2022	Work and Service, GOS	26-01-2023	Shaheed Benazirabad	175.451
2022-23 3459	Reconditioning of road from Daur - Kazi Ahmed road to connect Nawabshah - Naushahro Feroze road @ Basham Rind along Sim Nala road (5.00 Kms) (With 2	Satisfactory	15-11-2022	Work and Service, GOS	27-03-2023	Shaheed Benazirabad	58.292
2022-23 3463	Improvement of road from Oderolal to Shahdadpur (From Oderolal to Mulla Mukhan road) (9.00 Kms) (with Asphalt Surface)	Satisfactory	31-08-2022	Work and Service, GOS	07-03-2023	Sanghar	168.111
2022-23 3511	Reconditioning Tando Adam road to village Suleman Palli, village Miitho Mirjat, village Ibrahim Shah, village Madan Mirjat, village Ghulam Nabi Shah, village Khair Shah via Pannah Shah road approach Barecha mile 0/0 - 7/4 (12.00 Kms)	Satisfactory	16-08-2022	Work and Service, GOS	28-11-2022	Tando Allahyar	100
2022-23 3520	Reconditioning of Asphalt Concrete road from Tando Fazal Chowk to village Baksho Leghari (6.00 Kms)	Satisfactory	08-12-2022	Work and Service, GOS	15-03-2023	Hyderabad	64.736
2022-23 3539	Improvement of road from Rajo Khanani Talhar road to Mehro Bhurgari i/c link to Dewani Faqeer (10.00 Kms)	Satisfactory	09-12-2022	Work and Service, GOS	02-02-2023	Badin	99.75
2022-23 3803	Construction of road from Larkana Kamber road @ Point Railway Phattak to connect Kamber Wagan road mile 0/0-3/5 (5.83 Kms) (SDG # 9)	Satisfactory	20-12-2022	Work and Service, GOS	08-02-2023	Qambar Shahdadkot	348.198
2022-23 3859	Reconditioning Of Road From Waggan Warah Road At Point Lalu Raunk To Ghabidero Road @ Point Thori Bijar (7.00 Kms)	Satisfactory	27-12-2022	Work and Service, GOS	09-02-2023	Qambar Shahdadkot	109.959
2022-23 3893	Construction / Reconditioning of road from National Highway near Jam Noorullah to village Yaral Ghanghro (Malokani Ghanghra) along Gul Minor (6.80 Kms)	Satisfactory	12-10-2022	Work and Service, GOS	20-12-2022	Naushero Feroz	65.92
2022-23 3991	Construction / Reconditioning of road from Phull Sadhuja road to National Highway via village Manghlo Solangi and Gul Mohammad Mubejo connecting villages Haji Mohammad Siddique Solangi & Haji Mohammad Qasim Solangi (11.00 Kms)	Satisfactory	10-10-2022	Work and Service, GOS	20-12-2022	Naushero Feroz	105.395
Non-ADP	Construction of Pre-stressed 120'Rft i/c approaches(01) Bridge in District Kamber-ShahdadKot over Saifullah Canal atv	Un-Satisfactory	21-06-2022	Work and Service, GOS	25-11-2022	Qambar Shahdadkot	17
Non-ADP	Establishment/ Rehabilitation of Green Bets and Public Parks at District Kamber-Shahdadkot.	Un-Satisfactory	24-06-2022	Work and Service, GOS	25-11-2022	Qambar Shahdadkot	8
Non-ADP	R/Rehabl: of Deputy District Officer (Revenue) Office & Mukhtairkar Office Taluka Hala	Un-Satisfactory	22-08-2022	Work and Service, GOS	07-11-2022	Mafiari	10.529

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
Non-ADP	Constt of Road from Malihar to Abdullah ji Dhani	Satisfactory	25-07-2022	Work and Service, GOS	02-09-2022	Tharparkar	38.9
Non-ADP	Constt of Road from Wadero Baboo Khan Birhamani Machine to Thana Arab Khan	Un-Satisfactory	15-07-2022	Work and Service, GOS	11-04-2023	Jamshoro	20
Non-ADP	Constt of Road from Wadero Saleh Mohammad to Birhamani Machine to Thana Arab Khan	Un-Satisfactory	18-07-2022	Work and Service, GOS	19-04-2023	Jamshoro	20
Non-ADP	Construction of office Accomodation for Assistant Engineer, Highway/ Buildings at Talhar & Matli.	Un-Satisfactory	11-08-2022	Work and Service, GOS	07-11-2022	Badin	12
Non-ADP	Reconditioning oflink road from Tando M Khan shaikh Bhirkio to Shienh Nizamani Road mile 0/0-1/6	Satisfactory	02-08-2022	Work and Service, GOS	24-11-2022	Tando Muhammad Khan	40
Non-ADP	Constt of CC Roads in different streets of Islamkot town	Satisfactory	26-07-2022	Work and Service, GOS	21-11-2022	Tharparkar	36.987
Non-ADP	Constt of CC Roads in different streets of Nangarparkar	Satisfactory	27-07-2022	Work and Service, GOS	11-10-2022	Tharparkar	38.998
Non-ADP	Construction of Rooms (Annexes) at Collectors Residence District Hyderabad	Satisfactory	19-06-2023	Work and Service, GOS	20-06-2023	Hyderabad	39.9
2021-22 2648	Improvement of road from Faizu Jahan Khan Indus Highway Sardar Fateh Muhammad Khan Jatoi upto Nepreiabab (12.010Kms) (SDG # 9)	Un-Satisfactory	19-07-2022	Work and Service, GOS	04-10-2022	Shikarpur	169.059
2021-22 2676	Reconditioning of road from Jam Sahib to Mundh Jamrao with 2\	Satisfactory	21-04-2022	Work and Service, GOS	06-07-2022	Shaheed Benazirabad	1049.558
2021-22 2683	Improvement of Road Network from Badin to Wango Mor, Rehabilitations of Damaged Road Portions (29.00 Kms) (Revised) (SDG # 11)	Satisfactory	05-04-2022	Work and Service, GOS	13-12-2022	Badin	2488.93
2021-22 2687	W/R of road from Badin Sujawal road, starting point Bachal Water to Kario Khorwah road via village Gul Mir Shah, Haroon Nadeh, Chak No. 6, Bajari Shareef 18.00 Kms = 11/1 + 376 mile	Satisfactory	19-04-2022	Work and Service, GOS	27-01-2023	Sujawal	334.953
2021-22 2691	Improvement of road from Patt Moori to village Dangar via link road village Andal Chandio UC Patt (6.44 Kms) (SDG # 9)	Satisfactory	22-02-2022	Work and Service, GOS	22-07-2022	Dadu	47.26
2021-22 2692	Widening & Reconditioning of road from Chowdagi to Phulji Village (4.00 Kms) (SDG # 9)	Satisfactory	18-05-2022	Work and Service, GOS	16-08-2022	Dadu	31.419
2021-22 2706	Reconditioning / Construction of road from Bhiria road Railway Station upto village Sattar Dino Mangrio road (10.00 Kms) (SDG # 9)	Satisfactory	15-03-2022	Work and Service, GOS	13-07-2022	Naushero Feroz	97.847
2021-22 2712	Reconditioning of road from Daur - Moro road to village Haji Noor Muhammad Dahri via Aijazabad road (4.00 Kms) (SDG # 9)@	Satisfactory	29-06-2022	Work and Service, GOS	11-10-2022	Shaheed Benazirabad	46.476
2021-22 2720	Reconditioning of link road from Saeedpur to old Bhorano Bungalow i/c village links (10.40 Kms) (Revised)	Satisfactory	17-05-2022	Work and Service, GOS	02-09-2022	Tharparkar	94.706
2021-22 2722	Improvement of road from Bathoro-Khorwah road mile 2/4 to Jhoke Shareef via Gul Mohammad Rahoo & Dali Dal road mile 0/0- 7/4 (12.00 Kms)	Satisfactory	16-05-2022	Work and Service, GOS	02-09-2022	Sujawal	104.496
2021-22 2725	Reconditioning of link road from Tando Muhammad Khan Bulri Shah Karim Ditta Wah road to Haji Muhammad Jat road mile 0/0- 5/0 (8.00 Kms) (SDG # 9)	Satisfactory	10-05-2022	Work and Service, GOS	02-09-2022	Tando Muhammad Khan	68.942
2021-22 2730	W/R of road from Saddiq Memon to Hafiz Sandhano road to Tando Allahyar Mirwah road @ 28 mile Mori i/c link road Darya Khan Mari mile 0/0- 9/3 (15.08 Kms)	Satisfactory	17-03-2022	Work and Service, GOS	02-09-2022	Tando Allahyar	243.55
2021-22 2733	Reconditioning of link road from National Highway Thatta City to Dargah Shah Murad Sheerazi upto Jungshahi road i/c links Dargah Abdullah Shah Ashabi (9.90 Kms)	Satisfactory	23-02-2022	Work and Service, GOS	16-08-2022	Thatta	86.151
2021-22 2735	W/R of road from Ghulamaullah to Pirpatho (12.06 Kms) (SDG # 9)	Satisfactory	21-04-2022	Work and Service, GOS	31-10-2022	Thatta	215.128
2021-22 2736	Improvement of road from Thatta-Pirpatho-Ghorabari road to Gaho- Jo-	Satisfactory	22-04-2022	Work and Service, GOS	15-11-2022	Thatta	211.934

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Goth via Gail Mori Darvaish (20.00 Kms) (SDG # 9)						
2021-22 2759	Reconditioning of road from Jaggan to Mir Altaf Ali Bhayoo road 0/0-3/1 (5.00 Kms) (SDG # 9)	Un-Satisfactory	19-04-2022	Work and Service, GOS	16-08-2022	Shikarpur	34.971
2021-22 2762	Reconditioning of road from Garhi Yaseen Indus Highway to village Jado Kalhoro via village Mohail, Hameed Jair Mairi (5.43 Kms) (SDG # 9)	Satisfactory	19-07-2022	Work and Service, GOS	14-11-2022	Shikarpur	47.498
2021-22 2773	Reconditioning of road from Kandhari to Akri (12.87 Kms)	Satisfactory	23-05-2022	Work and Service, GOS	13-09-2022	Khairpur	166.555
2021-22 2775	W/R of road from Badin Sujawal at point (Amir Shah Sim Nala)Phuleli Guni out fall Drain Inspection Path to connect Seerani Ahmed Rajo via Karo Mori Stop 0/0-15/0 (24.14 Kms) (Phase-I) (5.75 Kms) (SDG # 9)	Satisfactory	15-12-2021	Work and Service, GOS	19-08-2022	Badin	99.858
2021-22 2776	Improvement of road from Kadhan Behdmi Rupa Mari to connect Bhugra Memon (38.62 Kms) (2\	Satisfactory	16-12-2021	Work and Service, GOS	16-08-2022	Badin	99.895
2021-22 2782	W/R of Mithi to Diplo road (39.20 Kms)	Satisfactory	21-03-2022	Work and Service, GOS	16-08-2022	Tharparkar	1517.601
2021-22 2783	Improvement of road from Islamkot to Nagarparkar mile 21/0 - 56/0 (56 kms)	Satisfactory	18-05-2022	Work and Service, GOS	29-08-2022	Tharparkar	464.194
2021-22 2791	Widening / Reconditioning of road from Dakhan to Bado (9.00 Kms)	Un-Satisfactory	08-07-2022	Work and Service, GOS	04-10-2022	Shikarpur	100
2021-22 2937	Reconditioning of road from Mile Khan Thebo to Tando Adam - Mirpurkhas road via Old Mirabad, Muhabbat Shah, Tharejo Dars, Ghulam Nabi Shah, Soomar Khaskheli, Altaf Shah, Ibrahim Shah i/c Piyaro Lund road to Dasori Shakh via Jaffar Jamali Pir Azeem Shah, J	Satisfactory	07-07-2022	Work and Service, GOS	01-09-2022	Tando Allahyar	100
2021-22 3067	Construction of road from Khan Sahib Abdul Rehman to village Banhon Korejo (3.00 Kms) (SDG # 9)	Satisfactory	13-01-2022	Work and Service, GOS	01-09-2022	Badin	46.397
2021-22 3071	Construction / Improvement of various road in Taluka Hyderabad (SDG # 9)	Satisfactory	14-04-2022	Work and Service, GOS	11-10-2022	Hyderabad	211.609
2021-22 3073	Construction of remaining portion of Toung to Balpuri Thano Ahmed Khan road from mile 12/4-18/1 (9.00 Kms) (SDG # 9)	Satisfactory	12-01-2022	Work and Service, GOS	16-08-2022	Jamshoro	157.83
2021-22 3076	Construction of road from Karachi Hotel to Amb Mori via Yameen Kamrade Deh 266 (7.00 Kms) (SDG # 9)	Satisfactory	20-04-2022	Work and Service, GOS	29-08-2022	Mirpurkhas	64.669
2021-22 3085	Construction of road from Ghono Wingi to Butyano and Odhano via Geo Soomro UC Jhimiri (7.00 Kms) (Phase-I) (SDG # 9)	Satisfactory	19-05-2022	Work and Service, GOS	29-08-2022	Tharparkar	125.44
2021-22 3110	Construction of road from link road village Abdul Rasheed to village Ghulam Muhammad village Muhammad Sharif village Juma Khan Jagirani (4.82 Kms) (SDG # 9)	Un-Satisfactory	09-03-2022	Work and Service, GOS	05-09-2022	Khairpur	59.046
2021-22 3116	Construction / Rehabilitation of various roads of UCs Akil, Agani and Phull (11.80 Kms) (SDG # 9)	Satisfactory	24-03-2022	Work and Service, GOS	08-09-2022	Larkana	164.591
2021-22 3315	Asset Management System and automation of composite schedule of rates for W&S Deptt. (SDG # 9) (LTBC)	Un-Satisfactory	12-05-2022	Work and Service, GOS	04-07-2022	Karachi	56.619
Non-ADP	Improvement of Road from Badin Sujawal Road @ mile 6/0 Fareed Farm to Pattan Parhiar Road Mile 1/1-2/4	Satisfactory	20-06-2022	Work and Service, GOS	29-08-2022	Badin	19.414
Non-ADP	Improvement of Road from Badin Sujawal Road @ mile 6/0 Fareed Farm to Pattan Parhiar Road Mile 2/4-3/7	Satisfactory	21-06-2022	Work and Service, GOS	21-11-2022	Badin	19.301
Non-ADP	Construction of Rooms and Maintainance of Community Center Mehar.	Un-Satisfactory	13-06-2022	Work and Service, GOS	08-09-2022	Dadu	19.2
Non-ADP	Remaining work at Irrigation Public Park Dadu	Un-Satisfactory	14-06-2022	Work and Service, GOS	08-09-2022	Dadu	10
Non-ADP	Construction of road from Bhand Mari to Sita Village via Ghulan JA Bhan Taluka Mehar mile 0/0-0/4+587	Satisfactory	16-06-2022	Work and Service, GOS	13-09-2022	Dadu	8

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2021-22 DD19P00 081	Construction of Road from Sehwan road to village Ghulam Mustafa Janwari via Dargah Murad Shah Pir i/c Retaining Wall.	Satisfactory	17-06-2022	Work and Service, GOS	13-09-2022	Dadu	2.288
Non-ADP	Construction of paving block & drain from Dr. Santosh clinic to Jamil Shaikh rice mill Ghari Road Mehar City	Un-Satisfactory	27-07-2022	Work and Service, GOS	07-11-2022	Dadu	20
Non-ADP	Improvement of Asphalt Road from Pakola Factory to Gujrati Para Taluka Latifabad	Satisfactory	08-06-2022	Work and Service, GOS	02-09-2022	Hyderabad	20
Non-ADP	Improvement of Road from Faqir ka Pir to Bera Manzil Taluka City Hyderabad	Satisfactory	14-06-2022	Work and Service, GOS	21-11-2022	Hyderabad	5.592
Non-ADP	Construction of CC Pavers/ CC Block & Drains from Barija to Mangrio House i/c Different Streets Barija Muhallaat Village Muhammad Yousif Baloch, Taluka Kotri, District Jamshoro	Satisfactory	13-06-2022	Work and Service, GOS	01-09-2022	Jamshoro	8.5
Non-ADP	Construction of Pavers Brick Road & MCP WAPDA Colony, Haji Juman Shoro Ward No: 09 Jamshoro, Taluka Kotri, District Jamshoro.	Satisfactory	24-06-2022	Work and Service, GOS	01-09-2022	Jamshoro	20
Non-ADP	Construction of Road New Metaled Road From NHA to Via Waris Goth To Wanko Goth UC Pir Mangio Taluka Khairpur	Un-Satisfactory	27-06-2022	Work and Service, GOS	04-10-2022	Khairpur	19.951
Non-ADP	Repair & Recondition of Road village Rasheed Waghan via Otaq of Nazir Ahmed Lahori to circular road	Satisfactory	17-08-2022	Work and Service, GOS	15-02-2023	Larkana	4
Non-ADP	Construction of Paver Block in the front and back side of main building of high court Larkano	Un-Satisfactory	08-06-2022	Work and Service, GOS	12-08-2022	Larkana	5
Non-ADP	Beuatification and green space of airport road Larkano	Satisfactory	08-06-2022	Work and Service, GOS	12-08-2022	Larkana	8
Non-ADP	Construction of Road Froam Nawab Bhawal Road To Village Gulab Khan Khaskheli To Village Haji Allah Dino Khaskheli 0/0 to 1	Un-Satisfactory	21-06-2022	Work and Service, GOS	07-11-2022	Shaheed Benazirabad	19.964
Non-ADP	Construction/Rehabilitation of Internal Roads in Sultan Kot City	Un-Satisfactory	20-06-2022	Work and Service, GOS	08-09-2022	Shikarpur	39.9
Non-ADP	Reconditioning of Road Abdu Buja Napar Road to Village Dhani Bux Malik	Un-Satisfactory	24-06-2022	Work and Service, GOS	30-11-2022	Shikarpur	19.9
Non-ADP	Rehabilitation of Internal roads of Village Jahan Khan Mahar i/c CC Block and Drains mile 0/0-0/3 (0.60 KM)	Un-Satisfactory	27-06-2022	Work and Service, GOS	10-11-2022	Shikarpur	9
Non-ADP	Rehabilitation/ Renovation of Old Deputy Commissioner House Shikarpur	Un-Satisfactory	28-06-2022	Work and Service, GOS	25-11-2022	Shikarpur	20
Non-ADP	Construction of Compound wall of graveyard Chingi Maaam Shikarpur City	Un-Satisfactory	29-06-2022	Work and Service, GOS	25-11-2022	Shikarpur	10
Non-ADP	Construction of Bus Terminal Rohri UC Bedal Bekas	Un-Satisfactory	13-06-2022	Work and Service, GOS	19-01-2023	Sukkur	37.165
Non-ADP	Construction of Paying Block Flooring & drains Various Village of UC Sangi PanoAkil	Un-Satisfactory	28-06-2022	Work and Service, GOS	19-01-2023	Sukkur	10
Non-ADP	Construction of Paying Block Flooring & Drains @ Various Village UC Panhwari	Un-Satisfactory	17-06-2022	Work and Service, GOS	05-01-2023	Sukkur	10
Non-ADP	Improvement of road from Kapri Mori Dumbalo road to village Fateh Mohammad Rindhawa	Satisfactory	03-02-2022	Work and Service, GOS	05-08-2022	Badin	20
Non-ADP	Construction of road from Tando Bago Pangrio Mehboob Ali Shah road to Natho Rebari	Satisfactory	07-02-2022	Work and Service, GOS	03-08-2022	Badin	19.9
Non-ADP	Construction of Internal road of Pir Sakhi Usman Shah Meghwar Paro	Satisfactory	04-02-2022	Work and Service, GOS	05-08-2022	Badin	20
Non-ADP	Construction of road from Ali Mohammad Arain road to village Jalal Khan Khoso	Satisfactory	16-02-2022	Work and Service, GOS	03-08-2022	Badin	20
2019-20 2547	Construction of Road from Sagyoon Khan Wahan Road to Shah Nawaz Kalhoro UC Sagyoon Taluka Sobhodero Road mile 0/0- 1/2 (2.0 km) (SDG # 9)	Satisfactory	30-11-2022	Work and Service, GOS	15-12-2022	Khairpur	25.744

# Annexure (C)

## COMPLETED SCHEMES IN FY 2022-23

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Construction of Compound wall to ARI Campus Tando Jam including Experimental Field, Pavement of Approach Road and Rehabilitation of Residential Colony	Agriculture, Supply & Prices	148.864	61.430
Introduction of Maize, Millet, Sorghum and Mungbean in water short environment and linking crops.	Agriculture, Supply & Prices	78.672	58.932
Production of Compost/Bio-Fertilizers for Assistance of Small Growers.	Agriculture, Supply & Prices	78.484	58.989
Establishment of GIS and Remote Sensing Center for Monitoring of Natural Resources.	Agriculture, Supply & Prices	11.545	10.102
Establishment of Centre of Excellence in Seed Science and Technology in Collaboration with Sindh Agriculture University, Tandojam.	Agriculture, Supply & Prices	42.779	35.429
Capacity Building of field Extension Staff by Providing Training and refresher courses.	Agriculture, Supply & Prices	80.000	30.508
Construction of compound walls of various building of Agriculture Extension Sindh.	Agriculture, Supply & Prices	82.773	72.773
Strengthening/ Construction of Cotton Commissionerate Sindh at Hyderabad for Enhancing Clean and Organic Cotton Production.	Agriculture, Supply & Prices	86.000	70.449
Establishment of Directorate General Research & Training for Agricultural Engineering & Water Management	Agriculture, Supply & Prices	46.050	22.543
Feasibility Study of On Farm Drainage and Designing System (Ghotki, Kashmore, N.Feroze, Sanghar, Badin, Thatta, T.M.Khan & Mirpurkhas)	Agriculture, Supply & Prices	42.150	26.316
Enhancement/ up-gradation of International Weights & Measures Laboratory at Karachi.	Agriculture, Supply & Prices	99.025	86.525
Provision of Agricultural Land Development Machinery & Equipments (On Subsidized Rate)	Agriculture, Supply & Prices	759.000	348.006
Provision of Subsidy Assistance on Controlled Atmosphere/ Cold Storage Units to the Small to Medium Sized Farmers in Sindh (Total cost Rs. 988.000 M GoS Share Rs. 800.000 M. & Farmers Share Rs. 188.800 M)	Agriculture, Supply & Prices	800.000	500.000
Construction of Compound Wall and other Allied Facilities at Dargah & Graveyard Shaikh Tayyab Nangal District Khairpur	Auqaf, Zakat, Ushr & R.A.	8.093	1.525
Rehabilitation & Reconstruction of Dargah Adham Sultan (Abu Bin Abdullah) Taluka Kot Diji District Khairpur Mirs	Auqaf, Zakat, Ushr & R.A.	11.950	2.251
Construction of Mosque at Village Saindad Bhanbhan Taluka Mehrabpur District N.Feroze (Revised on 17-09-2021)	Auqaf, Zakat, Ushr & R.A.	24.335	16.469
Construction of Remaining work Jamia Masjid near Bungalow Pir Abdul Qadir Shah Jeelani Ranipur.	Auqaf, Zakat, Ushr & R.A.	15.000	13.144
Construction of Roza, Masjid & Musafirkhana at Dargah Syed Haider Ali Shah Bukhari UC Naich, Taluka Bakrani.	Auqaf, Zakat, Ushr & R.A.	15.000	14.062
Construction / Rehabilitation of Dargah Syed Sachal Shah Bukhari village Naoabad Taluka Bakrani.	Auqaf, Zakat, Ushr & R.A.	15.000	14.063
Construction of Masjid Jamia Imamia Sahib-ul-Asar near Khichi Imam Bargha, Bahar Shah City.	Auqaf, Zakat, Ushr & R.A.	10.000	8.750
Construction / Rehabilitation of Dargah Syed Juman Shah village Mahar Wada Taluka Bakrani.	Auqaf, Zakat, Ushr & R.A.	16.000	15.000
Rehabilitation of Imam Bargah Syed Ahmed Ali Shah Village Madbao Taluka Bakrani.	Auqaf, Zakat, Ushr & R.A.	10.000	9.375
Rehabilitation of Dargah Hazrat Wahl Shah i.e Allied Facilities & Re-Construction of Boundary wall of Gravyard at Gulistan-e-Sajjad, Qasimabad	Auqaf, Zakat, Ushr & R.A.	19.000	17.812
Reconstruction of Dargah Tillan Shah Taluka Chohar Jamali.	Auqaf, Zakat, Ushr & R.A.	25.000	23.437
Rehabilitation of Dargah of Syed Abdul Rehman Shah Bukhari i.e Compound Wall of Adjacent Children Graveyard, U.C Lakha Manjhand.	Auqaf, Zakat, Ushr & R.A.	15.000	14.063
Construction / Rehabilitation of Masjid & Maddressa i.e Lavatory Block at Degan Bhurgri Taluka Kot Ghulam Muhammad.	Auqaf, Zakat, Ushr & R.A.	18.000	16.875
Construction / Repair / Renovation of Dargah Miran Peer Baghdadi.	Auqaf, Zakat, Ushr & R.A.	30.000	28.125
Construction & Provision of Allied Facilities at Dargah Mian Mangho village Mian Illyas Muhammad UC Fareedabad.	Auqaf, Zakat, Ushr & R.A.	15.000	14.062
Construction & Provision of Allied Facilities at Dargah Sain Yousuf Shah Jilani UC Ratokot.	Auqaf, Zakat, Ushr & R.A.	15.000	14.062
Repair / Renovation at Dargah Ain-ul-Haq Village Wazir Phulpoto U.C Agani and Construction of Compound Wall at Kamal Shah Graveyard Village & UC Phull.	Auqaf, Zakat, Ushr & R.A.	6.000	6.000
Construction of Sindh Government Cooperative College at Hyderabad (C:107.693+R:10.728)	Cooperative	118.421	11.000
Establishment of Amjad Sabri Institute of Sufi Music and Qawali at Karachi.(Revised on 17.09.20)	Culture, Tourism, Antiquities & Archives	49.406	11.981

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Provision of Missing Allied Facilities in Culture Complex at Umerkot (Revised 24.12.20) (C:69.008+R:20.571)	Culture, Tourism, Antiquities & Archives	89.579	58.956
Provision of Missing Allied Facilities in Culture Centre at Kotri. (Revised on 24.12.20) (C:57.918+R:14.172)	Culture, Tourism, Antiquities & Archives	72.090	29.062
Provision of Missing Allied Facilities in Library at Sujawal. (Revised on 24.12.20) (C:39.909+R:26.905)	Culture, Tourism, Antiquities & Archives	66.814	42.643
Provision of Missing Allied Facilities & Construction of Auditorium Hall and Waiting area at Dargah Jaral Shah, Taluka Larkano District Larkano (Revised on 24.12.20) (C:66.116+R:6.177)	Culture, Tourism, Antiquities & Archives	72.293	43.372
Establishment of Culture Centre at Moro. (C:38.378+R:14.622)	Culture, Tourism, Antiquities & Archives	53.000	26.910
Provision of Missing Allied Facilities in Sindhi Dictionary Board, Hyderabad (R:38.265)	Culture, Tourism, Antiquities & Archives	38.265	29.572
Establishment of Model Library in Gulzar Khalil, District Umerkot (Revised 24.12.20) (C:73.844+R:21.055)	Culture, Tourism, Antiquities & Archives	94.899	75.121
Provision of Missing Allied facilities and Extension of Pakistan Institute of Tourism & Hotel Management (PITHM) Karachi C:18.159+R:11.628)	Culture, Tourism, Antiquities & Archives	29.787	1.001
Conservation / Rehabilitation of Mitha Ram Hostel, Karachi (C:47.231+R:39.645)	Culture, Tourism, Antiquities & Archives	86.876	0.500
Missing Allied Facilities at Site Office Bhodesar, Nagarparkar (C:29.398+R:5.087)	Culture, Tourism, Antiquities & Archives	34.485	4.757
Rehabilitation of Archaeological Museum & Missing Facilities at Umerkot (C:85.009+R:14.539) (ADP No.75 of 2018-19) (For Liabilities)	Culture, Tourism, Antiquities & Archives	99.548	13.529
Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Primary / Elementary Schools) (84 Units) (C:486.970+R:95.330) (Revised on 22.04.2021 ) (SDG#4)	Education (School)	582.300	95.330
Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Primary / Elementary Schools) (68 Units) (SDG#4)	Education (School)	289.383	63.136
Rehabilitation / Expansion/ Improvement of High Priority 4560 Schools (Primary / Elementary Schools) (118 Units) (C:261.868+R:68.587) (SDG#4)	Education (School)	330.455	75.497
Rehabilitation / Expansion/ Improvement of High Priority 4560 Schools (Primary / Elementary Schools) (96 Units) (SDG#4)	Education (School)	277.660	57.491
Rehabilitation / Expansion/ Improvement of High Priority 4560 Schools (Primary / Elementary Schools) (82 Units) (C:334.274+R:33.620) (SDG#4)	Education (School)	367.894	66.115
Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Primary / Elementary Schools) (196 Units) (C:923.891+R:108.902) (SDG#4)	Education (School)	1032.793	148.115
Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Primary / Elementary Schools) (185 Units) (SDG#4)	Education (School)	834.490	99.870
Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Primary / Elementary Schools) (191 Units) (C:1022.768+R:23.592) (SDG#4)	Education (School)	1046.360	74.022
Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Primary / Elementary Schools) (169 Units) (C:751.686+R:575.141) (SDG#4)	Education (School)	1326.827	120.100
Construction of Six Room Buildings for Shelterless Primary Schools (01 Unit) (C: 12.374 + R: 1.210) (SDG#4)	Education (School)	13.584	7.584
Construction of Buildings for Shelterless Primary Schools (04 Units) (C:55.937 + R:5.516) (SDG#4)	Education (School)	61.453	47.453
Construction of Buildings for Shelterless Primary Schools (02 Units) (C:27.187 + R:2.758) (SDG#4)	Education (School)	29.945	28.195
Construction of Buildings for Shelterless Primary Schools (02 Units) (C:27.820 + R:2.758) (SDG#4)	Education (School)	30.578	27.078
Construction of Buildings for Shelterless Primary Schools (03 Units) (C:42.061 + R: 4.137) (SDG#4)	Education (School)	46.198	40.948
Rehabilitation / Reconstruction of High Enrollment Dangerous Primary / Elementary Schools and Provision of Missing Facilities	Education (School)	64.447	56.947
Up-gradation of Primary Schools to Elementary Schools (03 Units) (C:45.197 + R:7.596) (SDG#4)	Education (School)	52.793	46.793
Rehabilitation & Provision of Missing Facilities in Existing GBPS Rahim Ali Khoso UC Kolachi / GBLSS & GGPS Masoo Jalbani Taluka Mehar (C:19.899 + R:0.457) (SDG#4)	Education (School)	20.356	17.856
Re-construction of Existing GPS Satiani Sharif Mirpur Bathoro (SDG#4) (C:4.385 + R:0.404)	Education (School)	4.789	2.564
Up-gradation of Primary School to Elementary Schools (02 Units) (C:30.044 + R:5.064) (SDG#4)	Education (School)	35.108	31.108
Repair / Rehabilitation / Reconstruction of Existing Primary / Elementary / High Schools in Taluka Kotdiji & Faiz Ganj (SDG#4)	Education (School)	58.838	43.838
Establishment of Comprehensive Schools in Sindh (15 Units) (C: 2931.500 + R: 358.996) (Revised on 15.09.20) (SDG#4)	Education (School)	3290.450	432.301

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Rehabilitation of Government Primary School / Government Girls Secondary School Khatoon-E-Pakistan Stadium Road Karachi (Phase-II) (AASP) (C: 77.794 + R: 5.000) (SDG#4) (Revised on 26.08.2021 )	Education (School)	82.794	37.945
Rehabilitation / Construction of Campus School Khair Shah, Niazi Khan Siyal, H.M Khoja, D.C High School No.1 and GGHS Society Nawab Shah (Revised on 06.10.2021) (SDG#4)	Education (School)	82.995	20.440
Construction / Re-Construction GGHS Qazi Ahmed Taluka Qazi Ahmed (Revised on 17.09.2021) (SDG#4)	Education (School)	64.273	32.894
Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (02 Units) (C: Rs. 79.955 + R: 10.000)	Education (School)	89.955	15.505
Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 38.765 + R: 2.815)	Education (School)	41.580	2.815
Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 40.000 + R: 5.000)	Education (School)	45.000	7.813
Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (02 Units) (C: Rs. 88.830 + R: 5.846)	Education (School)	94.676	5.848
Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 45.819 + R: 3.681)	Education (School)	49.500	5.681
Provision of Essential Amenities in the Existing Auditorium Hall and Installation of Surveillance System at GGHS Mira Taluka City Hyderabad (C: Rs. 10.913 + R: 4.575) (SDG#4)	Education (School)	15.488	5.303
Up-gradation of Middle School to High School (01 Unit) (C:26.436 + R:5.357) (SDG#4)	Education (School)	31.793	28.043
Up-gradation of Middle Schools to High Schools (02 Units) (C:50.858 + R:8.182) (SDG#4)	Education (School)	59.040	44.040
Up-gradation of Middle Schools to High School (01 Unit) (C:24.648 + R:4.091) (SDG#4)	Education (School)	28.739	24.989
Up-gradation of Middle School to High School (01 Unit) (C:25.182 + R:4.091) (SDG#4)	Education (School)	29.273	25.523
Up-gradation of Middle School to High School (01 Unit) (25.215 + R:4.051) (SDG#4)	Education (School)	29.266	25.516
Emergent Works / Schemes of Education & Literacy Department (C:82.170 + R:1.565) (Revised on 26.08.21)	Education (School)	83.735	47.455
Schools Improvement through Adopt a Schools Intervention Shaheed Benazirabad Division (02 units) (C:25.851+R:0.990)	Education (School)	26.841	0.495
Schools Improvement Through Adopt a School Intervention Hyderabad Division Phase-II (AASP) (C:55.406+R:6.630)	Education (School)	62.036	14.773
Rehabilitation / Renovation & Provision of Missing Facilities in Existing GBPS & GBLS Police Line and GBHS Sanghar (C:177.828 + R: 12.945) (03 Units) (SDG#4)	Education (School)	190.773	54.945
Repair / Rehabilitation/ Reconstruction of field offices of Education & Literacy (SDG#4)	Education (School)	49.996	43.808
Remaining Work of GBHS Joungal, GBHS Lal Bhatti, GBMS Noor Malik & GGPS / GBPS Hazoor Bux Buriro Taluka Thull (05 Units)	Education (School)	35.768	31.437
Renovation and Provision of Basic Facilities in Selected Educational Management Organization (EMO) Cluster Schools (04 Units) (SDG#4)	Education (School)	10.024	8.774
Up-gradation of Middle School to High School at GBMS Sher Muhammad Thora (01 Unit) (C:18.484 + R:3.419) (SDG#4)	Education (School)	21.903	19.039
Up-gradation of Middle School to High School (i) GBMS Vakryo (ii) GBMS Pabuvero & Up-gradation of Primary School to Middle School (i) GBPS Vee Hingorja (ii) GBPS Jaroombhar (iii) GBPS Aqib Junejo Taluka Islamkot & Chachro (05 Units) (C:80.660 + R:15.778) (SDG#4)	Education (School)	96.439	85.439
Establishment of Shaheed Benazir Bhutto Girls Cadet College Larkano (C:2039.382 + R:190.457) (Revised on 01.10.2020)	Education (College)	2229.841	1055.452
Provision of Additional Facilities and Boundary Wall of Boys Cadet College Larkana (SDG#4)	Education (College)	99.808	74.782
Sindh Persons with Disabilities Data Base Management Project (SDDMP) (SDG#4)	Education (Emp)	45.000	40.050
Development of Department of Food Engineering & Infrastructure at NED University of Engineering & Technology, Karachi (C:159.779 + R:167.564) (SDG#4)	Education (U&B)	327.343	150.004
Construction of Blocks B&C of New Boys Hostel at I.B.A. Main Campus, Karachi. Total Cost: Rs. 270.590 M GOS Share: Rs.230.002 M I.B.A Share: Rs. 40.588 M (C:175.215 + R:54.788)	Education (U&B)	230.002	98.513
Construction of Tensile Fiber Sunshade along both sides of main dual Carriage way at Shah Abdul Latif University, Khairpur	Education (U&B)	39.040	39.040
Village Electrification Programme in Sindh (Phase-VIII)	Energy	987.460	370.820
Electrification of Goths (Villages) in and around Karachi. (Phase-VII)	Energy	550.000	424.980
Village Electrification Schemes of District Thatta and surrounding areas	Energy	99.987	87.612
Rehabilitation of Treasury Office (Old Block) Hyderabad	Finance	79.753	64.903
Enhancing Tree Cover on State Forest Lands in Sindh (Revised) (Jamshoro, Dadu, Matiari, SBA, Sanghar, Shikarpur, Kashmore, Sukkur, Khairpur,	Forest & Wildlife	708.000	248.666

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Ghotki, N.Feroze, T.M. Khan, Umerkot, Thar, Badin, T.A.Yar, Kamber, Larkano & Jacobabad) (SDG # 15)			
Constt. of Advisors' block and extension/ reconstruction of Administration Block at Sindh Governor House (Revised) (C:15.628+R:9.734)	Governor's Secretariat	25.362	9.734
Establishment of 50 bedded Medical & Surgical ICU and expansion of Casualty & OPD Department at CMC Hospital, Larkano (Revised on 18.01.17). (C: 84.397+R: 183.101) (SDG #3)	Health	267.498	46.777
Establishment of Benazir Institute of Urology & Transplantation (BIUT) at District Shaheed Benazirabad (Revised on 14.03.19) (C: 568.262+R: 964.664) (SDG #3)	Health	1532.926	101.400
Up gradation of Provincial Health Development Centre (PHDC) to the level of Sindh Health Institute of Training & Research. (C:130.193+R:56.670)(SDG#3)	Health	186.863	17.578
Strengthening of Pir Abdul Qadir Shah Jeelani Institute of Medical Sciences at Gambat (Revised on 02.03.12). (C: 1129.670+R: 299.551) (SDG #3)	Health	1429.221	0.001
Neonatal screening for Congenital Hypothyroidism (CH) in Sindh at NICH, Karachi (Revised on 04.06.21) (C:16.448+R:132.465+ PIU 61.373) (SDG#3)	Health	210.286	106.575
Strengthening of Monitoring and Surveillance of Health System Govt. of Sindh. (GoS:123.235 + USAID:157.790 = 281.025)	Health	123.235	116.823
Establishment of Sindh Safe Blood Transfusion Services Project (Phase-II) (Government of Germany through KfW Bank Rs. 88.294+ GoS Rs. 27.000 =115.294) (SDG #3,4,6)	Health	27.000	27.000
Construction of Mall Khana at City Court Karachi	Home	29.838	0.001
Construction of Police Station (Category-C) at Punhal Khan Chandio Taluka Sakrand. (771 of 2019-20) (Remaining work)	Home	33.107	3.682
Construction of Canine Unit in Karachi (30 units). (778 of 2019-20) (Remaining work)	Home	55.767	6.063
Construction of Building of Maripur Police Station on the land of Hawksbay PP in deh Lal Bakhar Karachi. (791 of 2019-20) (Remaining work)	Home	34.136	10.620
Construction of new building for SSP sujawal (SDG # 16)	Home	17.866	3.210
Construction of partition wall for keeping Juvenile and Women prisoners i/c complete Rehabilitation building of old District Prison Mirpurkhas declared as YOIS & Women Jail for Mirpurkhas Division.	Home	10.909	0.001
Construction of Additional Training Block / Facilities at Sindh Prison Staff Training Institute, Nara Hyderabad	Home	62.142	47.142
Provision of basic facilities of Sewerage / CC Drain / CC topping in different Katchi Abadis in Sindh	Human Settlement	40.000	4.066
Provision of essential civic facilities in different Katchi Abadis in Sindh	Human Settlement	38.600	16.987
Upgradation plan of CC Drain & CC Flooring at Katchi Abadis Jogi Jamali Colony, Khairpur	Human Settlement	10.000	0.625
Providing and Laying Paver Blocks and Drains at Katchi Abadi Panjo Mirbahar, Ghotki	Human Settlement	16.610	16.610
Survey and Feasibility Study of scheme "Establishment of Combined Effluent Treatment Plant at SITE Hyderabad 3.0 MGD"	Industries & Commerce	39.143	19.571
Survey and Feasibility Study of scheme "Establishment of Combined Effluent Treatment Plant at SITE Sukkur 2.0 MGD"	Industries & Commerce	31.260	15.632
Infrastructure Development of Industrial Estate, Larkano (Revised on 31.12.20)	Industries & Commerce	1366.420	65.478
Ground Water Investigation and Mapping in Sindh.	Irrigation	50.000	6.250
Construction of Sub-Drain (2L) of Panhwaro Main Drain System RD-0 to 12+500 in Deh Lakhtia Khai Meenho & Excavation of Ghar Main Drain from Thorhi Bajar to Sodhar Village & Excavation of Panhwaro Drains System with Damage Structure	Irrigation	499.676	27.321
Rehabilitation of Drains and allied structures in Thatta District (SDG#6) (Revised on 27.04.22)	Irrigation	436.890	147.842
Construction of Jakhra Link Drain from RD - 0.0 to 10.0 out-falling in 19-L of LBOD at RD. 60.00	Irrigation	19.643	18.643
Solar Tubewells (4x) in various Dehs of District Shaheed Benazirabad. (a) Deh Jamal Keerio, (b) Deh 18 Dad Sakrand, (c)Deh Yakhtiar Khan, Sakrand & (d)Goth Imamuddin Keerio, U.C. Nathiani, Daur.	Irrigation	33.874	29.874
Constructing Relief Escape for Nasrat Branch at RD-195 NIP side and Constructing Relief Escape for Gajrah Branch at RD-60 NIP side and Constructing Relief Escape for tail of Nasrat Branch system along Chan Bandhni distry at RD-22 (SDG # 6)	Irrigation	98.400	6.940
Providing Embankment and Common Bank at Thull Mohabbad Chori from Hakim Shah Regulator of Warach Branch (SDG # 6)	Irrigation	84.498	32.249
Left Over Essential Works of Sehwan Area District Jamshoro & Dadu (Construction of Lift Channels over RBOD System for Feeding Tail Reaches of Dadu Canal) - (SDG # 6)	Irrigation	206.119	96.119
Renovation / Re-Construction of road Bridge over Mirwah Canal at RD-33 near Railway Station Begmangi, Installation of Steel grill over Retaining Wall along Mirwah Canal B/S RD-69 to 79, 70+200, 72+180, 73+450, 74+200, 75+150, 76+200, 77+15 & 78+570 Both Sides & Garhi Pull to	Irrigation	450.271	235.057

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Bhurghari X-Regulator, Providing Stone Ptching along Mirwah Canal from RD-208 to 230 & 231 to 291 B/S (Revised on 23.02.22)			
Renovation, Reconstruction and Improvement of Executive Engineer Offices and Sub-Divisional Office Complexes in Sindh (Phase -I).	Irrigation	169.521	88.021
Renovation, Reconstruction and Improvement of Landhi's on all Canal System of Sindh (Phase-I).	Irrigation	194.230	96.230
Constructinn Stone Pitching along RMC from RD-25 to 191.2 @ Eroded Portion. (Revised on 23.02.22)	Irrigation	339.006	167.406
Rehabilitaiton of Salar Distry and its off-taking system and stone pitching along Mastoi Distry RD-8 to RD-16 and construction of protection wall along Kehar Minor RD-15+500 to RD-18+000 B/S (2500 ft.). Construction of culvert (Two) along Kehar Minor @ RD-16+500 and 170+000.	Irrigation	197.430	172.430
Retaining Wall and C C Lining of Abul Wah at Ranipur Town Committee from RD - 94 to 97 and Onward and Retaining Wall and C C Lining Ghulam Shakh Abul Wah from 0 to Onward	Irrigation	51.960	39.210
Construction of Bridges along Dhamra Minor at Village Bakar Khan Jatoi, Dokia Minor at Village Khameso Khan Brohi, Road Culvert Bridge over Tatri Minor near Village Jadam U.C. Yaro Lakher, Construction of Bridges over Garhi Distry at RD-14, 19, 24, 30 and Arther Branch at RD-22 in Northern Dadu & Rice Canal Division, Larkano.	Irrigation	39.869	32.369
Construction / Replacement of X-Regulator @ mile 43 & 47 of Begari Canal Ex: Begari Sindh Feeder of Begari Division.	Irrigation	746.491	196.491
C.C. Lining of Bhutta Minor from RD-0 to RD-22 off-taking from Phileri Regulator Shahdackot Branch and Replacement of Headwork (Gate), Taluka Sujawal Junejo.	Irrigation	149.417	134.417
Construction of Judges Bungalow (01 No.) Thana Bula Khan (SDG # 16)	Law, P.A & Prosecution	15.810	5.073
Construction of New Annexe Building No. I & II (Re-Re-Revised) (C:897.717+R:60.230)	Law, P.A & Prosecution	957.947	1.800
Construction of Four (04) No. Courts at Pano Aqil.(Revised)	Law, P.A & Prosecution	95.990	38.446
Const. of 2 Court Building at Khipro (Revised) (SDG # 16)	Law, P.A & Prosecution	79.690	26.793
Introduction of Bio-Floc Aquaculture in Sindh (Jamshoro, Thatta, Badin, Sujawal, TM Khan, Ghotki & Larkana) (R: 100.000) (SDG #2)	Livestock & Fisheries	100.000	87.500
Up-gradation of Dhabeji Pumping Station (SDG # 6)	LG (Water Supply)	1233.720	395.017
Sewerage System (Phase-II) Works at Taluka Qasimabad Hyderabad (SDG # 6)	LG (Water Supply)	1283.930	50.457
Installation of Paver Blocks at various streets of City Khairpur (Revised)(SDG # 6)	LG (Water Supply)	330.518	80.526
Revamping of Mehmoodabad Nallah from Malir Bund / KPT Flyover to Mehmoodabad (SDG # 6) (Revised)	LG (Water Supply)	271.613	31.257
Providing & Laying Water supply pipe lines from Umer Sons to Old Thano for improvement of Water Supply schemes of Murad Memon, Jam Goth, Mullah Essa Goth and Old Thano District Malir, Karachi (SDG # 6) (Revised)	LG (Water Supply)	387.888	270.461
Rehabilitation of Water Supply System By Providing & Laying 16" Dia M.S Pipe from 48" Dia Pipe To Kashmir Road to Corporation Gate for Improvement of Water Supply System Mehmoodabad, Chanesar Goth, Azam Basti in Jamshed Town, Karachi (Revised)	LG (Water Supply)	167.170	68.495
Construction of Filter Plant at Hussainabad (SDG # 6)	LG (Water Supply)	817.530	188.216
Phase-I of 25 years Sewerage/ Drainage Master Plan of Mirpurkhas (Revised on 01.4.21)	LG (Water Supply)	3762.379	1474.277
Phase-I of 25 years Sewerage, Drainage, Water Supply System & Roads System & Road Master Plan, Taluka Matli, District Badin. (Revised on 06.05.21)	LG (Water Supply)	1846.670	551.579
Rehabilitatioon of the existing distribution system in Hyderabad (Providing Laying Jointing & Testing 4", 6", 8" 12", 20" and 24" dia MS / PE Pipe replcement / by Passing the faulty and damaged water supply lines to aviod contamination in Taluka City Latifabad and Qasimabad)	LG (Water Supply)	399.747	119.650
CC Block Roads in Various Villages of Qasimabad PS-47 (SDG # 9)	LG (Water Supply)	299.000	18.638
Improvement & Enhancement of Sewerage System in Taluka City Area District Hyderabad	LG (Water Supply)	414.135	188.139
Rehabilitation / Replacement / Improvement of Water Supply and Sewerage system including Pumping Stations in District East, Karachi	LG (Water Supply)	149.559	120.495
Rehabilitation / Replacement / Improvement of Water Supply and Sewerage system including Pumping Stations in District Malir, Karachi	LG (Water Supply)	135.504	106.440
Rehabilitation / Replacement / Improvement of Water Supply and Sewerage System including Pumping Stations in District Korangi, Karachi	LG (Water Supply)	130.481	101.671
Main Water Supply System in Block 13-A to 11-A & Block 11-B to Block-2, 3 & 3-A of Hawksbay Scheme-42 LDA Karachi	LG (Water Supply)	150.986	68.486
Improvement / Rehabilitation of Strom water Drain along 8000 road and 5000 Road to Yousuf Goth Gadap Town Karachi (Revised on 06.5.21, Re-Revised on 19.05.22)	LG (Water Supply)	798.710	310.019

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Construction of Paver Block Road	LG (Water Supply)	137.270	119.945
Construction of Water Supply Scheme and Under Ground Tank in UC-09 Sharafi Goth, District Malir Karachi	LG (Water Supply)	95.635	83.135
Providing / Lying Sewerage Line, Water Supply Line, & CC Paver Block at Union Council No. 28 Moriro District Malir Karachi	LG (Water Supply)	93.295	68.795
Providing Sewerage Lines of 12", 15" and 18" dia RCC Pipe & Water Supply P.E Pipe Line of 4", 6" dia in Saifal Goth, Sukhia Goth Wazeer Goth, Noor Muhammad Goth, Rind Muhalla, Khadim Solangi Goth, Laasi Goth and Various Areas of UC-31 District East	LG (Water Supply)	99.278	86.778
Construction / Rehabilitation of Main / Internal Roads and installation of Paver Blocks / CC flooring & Street lights in Sachal Goth Block A to G, Ayub Goth, Christian Para and Shaheed Zulfiqar Ali Bhutto Goth (Seeta Nagar), Bilawal Shah Noorani Goth and various areas of UC-30 District East	LG (Water Supply)	96.098	71.098
Construction / Rehabilitation of Main / Internal Roads, providing, sewerage line of 12", 15" and 18" dia RCC pipe, water line of 4", 6" dia PE Pipe and installation of Paver blocks / CC flooring & Street Lights in Jannat Gul Town, Al-Azam Town, Qayyum Abad, Hasan Noman Colony, Machar Colony, Allah Bux Goth Street No. 1, 6,38 to 43, Muhammadi Goth, and various areas of UC-31	LG (Water Supply)	96.466	71.466
Construction / Rehabilitation of Main Roads / Internal Roads and installation of Paver Blocks / CC flooring & Street Lights in Junejo Town, Chutta Gabol Goth, Saindad Village, Noor Khan Goth, Ahmed Jamal Goth, Khuda Bux Goth and various areas of UC-31	LG (Water Supply)	98.023	73.022
Construction / Rehabilitation of Main / Internal Roads, Providing Sewerage line of 12" and 18" dia RCC pipe, 4 " dia P.E Water Supply Pipe line, installation of Paver Blocks and Street Lights in Umar Colony I & II, UC-5 Mehmoodabad Ward 1 & 2.	LG (Water Supply)	98.666	86.291
Construction / Rehabilitation of Main / Internal Roads, Providing Sewerage line of 12" and 18" dia RCC pipe, 4 " dia P.E Water Supply Pipe line, installation of Paver blocks and street lights in Baloch Colony, LAC II UC-06 Street 01 to 31,	LG (Water Supply)	98.456	85.956
Construction / Rehabilitation of Main / Internal Roads, providing Sewerage line of 12" and 18" dia RCC pipe, 4 " dia P.E Water Supply Pipe line, installation of Paver blocks in Zigre Goth Block 2 Gulistan-e-Johar, Katchi Abadi C Area Block 12 and Service road from Pehlwan Goth to Munawar Chowrangji, Sindh Baloch Society Block 12 of Gulistan-e-Johar,	LG (Water Supply)	96.159	71.159
Construction / Rehabilitation of Main / Internal Roads, Providing Sewerage line of 12", 15" and 18" dia RCC pipe, 4" & 6" dia P.E Water Supply line in Rabia City, Rabia Banglows to Classic Apartment, Service road from Rabia City via Johar Square, Muneer Bridge view to Johar Mar Gulistan-e-Johar.	LG (Water Supply)	99.278	74.278
Construction / Rehabilitation of Main / Internal Roads, Street lights Providing Sewerage line of 12", 15" and 18" dia RCC Pipe, Water Supply line of 4", 6" dia PE Pipe in Block 13, 14, 15, 17, 19 of Gulistan-e-Johar.	LG (Water Supply)	95.554	70.554
Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line of 12", 15" and 18" dia RCC Pipe, Water Supply line of 4" 6" dia PE Pipe and installation of Paver blocks in Haji Ramzan Gabol Goth, Ali Gabol Goth, Paryo Goth, Chutta Goth, Sher Muhammad Palari Goth, Baloch Khan Gabol Goth, Gahnwar Khan Gabol Goth and various areas of UC-30.	LG (Water Supply)	96.170	71.170
Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line 12", 15" and 18" dia RCC Pipe, Water Supply line of 4", 6" dia P.E Pipe and installation of Paver Blocks, in Muhammad Khan Goth, Darya Khan Goth, Abdullah Shah Ghazi Goth, New Maroora Goth, Shahnawaz Sghar Goth and various areas of UC-30 District East	LG (Water Supply)	95.126	70.126
Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line of 12", 15" and 18" dia RCC pipe, Water Supply line of 4" 6" dia PE Pipe and installation of Paver Blocks, Haroon Bangalows, Arif Arcade, Muslim Society, City Villas, Rizwan Society, Maroora Goth, Johar Complex and various areas of UC-30.	LG (Water Supply)	100.000	75.000
Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line of 12" and 18" dia RCC Pipe, Water Supply line of 4" dia PE Pipe and installation of Paver Blocks in Sher Pao Basti, Darwesh Colony, Sindh Muslim Society, Dhoraji, Dehli Mercantile.	LG (Water Supply)	95.338	70.338
Construction / Rehabilitation of Drain System from Johar Chowrangji to Pehlwan Goth including maintenance of Service Road and Construction of Pedestrian bridge at Rabia City Gulistan-e-Johar .	LG (Water Supply)	98.949	86.574
Construction / Rehabilitation of Roads from Evacue Banquet Rashid Minhas Road (Lal Flats) to K-Electric IBC Johar -I and surrounding areas of Lal Flats including Sewerage line of 15" and 18" dia RCC Pipe, Water Supply line of 4" dia PE Pipe	LG (Water Supply)	95.674	70.674
Construction of Double Road from Pehlwan Goth to Johar Police Station Gulistan-e-Johar including street lights, footpath with paving blocks, Cat eyes road markings including Sewerage line of 12" & 18" dia RCC Pipe, Water Supply line of 4" dia PE pipe and Repairing of various areas Roads District East	LG (Water Supply)	98.881	86.506

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Construction of Road & Installation of Paver Blocks, Sewerage & Water Supply Line, Akhtar Colony & Kashmir Colony (UC-01)	LG (Water Supply)	98.608	86.233
Road Carpeting (Mehmoodabad Police Station to Quetta Rangeen Hotel). Main Watersupply line with Branches, UC-03 District East	LG (Water Supply)	98.835	86.460
Providing and laying of Water Supply 4", 8" dia from Ayub Police Chowki to Bhattai Chowk & from Shahbaz Chowki to Junejo Colony PS-99.	LG (Water Supply)	90.000	78.750
Providing and laying of Water Supply 4", 8" , 12" and 18" dia from Yusrab Goth to Muhammadi Goth & from Khadim Hussain Goth to Wazir Goth	LG (Water Supply)	89.893	78.643
Rehabilitation / Improvement of Road / Sewerage Line & Water Supply System	LG (Water Supply)	98.613	86.238
Construction / Rehabilitation of Main & Internal Roads and Providing of Sewerage lines of 12",18", RCC Pipe, WaterSupply Line of 4" dia PE Pipe, Installation of Paver Blocks & Street Lights in Baloch Colony, LAC II, Street 01 to31, UC-06	LG (Water Supply)	98.663	86.288
Improvement of Storm Water Drain System alongwith Supreme Court and Rising & Wall of Nallah.	LG (Water Supply)	73.000	73.000
Construction of Road, C.C Flooring, Foot Paths, Paver Blocks, Sewerage line, Water Supply line UC - 25 & 26	LG (Water Supply)	30.275	26.525
Construction of CC Flooring & Road Carpeting in UC-13, Mujahidabad, District West, Karachi	LG (Water Supply)	58.250	43.250
CC Flooring, Sewerage Line, Water Supply Line & Establishment of Basic Health Center ( Dispensary) in UC-11 Baloch Goth.	LG (Water Supply)	122.284	122.284
CC Flooring, Water Supply & Sewerage Line & Road Carpeting in UC-9, Islamia Colony.	LG (Water Supply)	66.827	49.327
Road Carpeting, CC Flooring, Water Supply line in UC-12, Data Nagar.	LG (Water Supply)	58.342	43.342
Improvement of Water Supply & Sewerage line, CC Flooring, Ground and Road Carpeting in UC-19.	LG (Water Supply)	66.211	57.461
Improvement of Water Supply line, installation of Sewerage line, CC Flooring, Ground and Road Carpeting in UC-18, UC-24 & UC-26.	LG (Water Supply)	95.704	70.704
Improvement of Water Supply line, installation of Sewerage line, CC Flooring, Ground and Road Carpeting in UC-20, UC-21 & UC-22.	LG (Water Supply)	86.039	63.539
Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-12, UC-16 & UC-25	LG (Water Supply)	116.828	101.978
Construction of Roads, laying of Paver Blocks, Installation of Sewerage System in UC-16, Ghaziabad	LG (Water Supply)	46.910	34.410
Construction of Pumping Station with Pipelines in Khuda ki Basti, Surjani, Lyari & Taiser Areas	LG (Water Supply)	100.000	87.500
Rehabilitation / Improvement of Road / Sewerage Line & Water System in the area of PS-92	LG (Water Supply)	96.842	71.842
Rehabilitation / Improvement of Road / Sewerage Line & Water System in the area of PS-93	LG (Water Supply)	95.736	83.236
Improvement of Sewerage line Boosting Pump, Drainage line and Carpeting of Road in UC-2 Labour Square	LG (Water Supply)	81.093	71.811
Improvement of Water Supply, Sewerage line Paver Block in UC-4 Metroville	LG (Water Supply)	84.637	62.137
Improvement of Water Supply, Sewerage line and Road carpeting in UC-5 Pak Colony	LG (Water Supply)	56.222	41.222
Improvement & installation of Water Supply and Sewerage lines, CC Flooring, Ground and Road Carpeting in UC-16.	LG (Water Supply)	75.871	65.871
Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-19	LG (Water Supply)	177.953	155.678
Improvement & installation of Water Supply and Sewerage lines, CC Flooring, Ground and Road Carpeting in UC-24.	LG (Water Supply)	76.009	56.009
Improvement & installation of Water Supply and Sewerage lines, CC Flooring, Ground and Road Carpeting in UC-26.	LG (Water Supply)	76.330	56.330
Improvement & installation of Water Supply and Sewerage lines in UC-21 & 22.	LG (Water Supply)	75.774	55.774
Improvement & installation of Water Supply and Sewerage lines, CC Flooring, Ground and Road Carpeting in UC-21 & 22, District West, Karachi	LG (Water Supply)	66.846	49.346
Improvement & installation of Water Supply and Sewerage lines, CC Flooring, Ground and Road Carpeting in UC-18.	LG (Water Supply)	47.452	34.952
Improvement & installation of Water Supply and Sewerage lines, CC Flooring, Ground and Road Carpeting in UC-20.	LG (Water Supply)	57.562	42.562
Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-11 & 12	LG (Water Supply)	160.000	140.200
Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-13, UC-17 & UC-19	LG (Water Supply)	156.085	136.285
Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-27 & UC-28	LG (Water Supply)	116.065	101.215
Water Supply line, Sewerage line, Paver Block and Carpeting of Roads in different areas of UC-3.	LG (Water Supply)	96.463	71.463
Water Supply line, Sewerage line, Paver Block and Carpeting of Roads in different areas of UC-14.	LG (Water Supply)	107.747	94.134
Water Supply line, Sewerage line, Paver Block and Carpeting of Roads in different areas of UC-15.	LG (Water Supply)	85.785	63.285

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Water Supply line, Sewerage line, Paver Block and Carpeting of Roads in different areas of UC-10.	LG (Water Supply)	77.714	60.214
Water Supply line, Sewerage line, Paver Block and Carpeting of Roads in different areas of UC-8 & 9.	LG (Water Supply)	127.906	111.818
Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-4, 5 & 39	LG (Water Supply)	136.454	119.129
Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-4	LG (Water Supply)	116.906	102.056
Improvement of Water Supply line and Installation of Sewerage line and CC Flooring, Grounds Road Carpeting in UC-5.	LG (Water Supply)	115.040	100.190
Improvement of Water Supply line and Installation of Sewerage line and CC Flooring, Grounds Road Carpeting in UC-6.	LG (Water Supply)	113.859	99.000
Providing & Laying of Paver Block Flooring in Noor Shah Muhalla, Kachhi Muhalla Bismillah Colony, Bukhari Muhalla, Mianwali Muhalla, Qasim Ali Shah Colony and Kachela Goth UC 2 Mowach Goth.	LG (Water Supply)	126.184	110.411
Providing & Laying of Paver Block in Different Streets of UC-41, UC-42, UC-43, UC-44, UC-45 and UC-46 in DMC Keamari	LG (Water Supply)	95.990	71.152
Improvement of Water Supply and installation of Sewerage line and Paver Block in UC-1 Gabo Pat.	LG (Water Supply)	75.515	65.515
Paver Block and Carpeting of Road in different areas of UC-2 Mowach Goth.	LG (Water Supply)	96.326	71.326
Improvement of Water Supply and installation of Sewerage line and Carpeting of Road in UC-3 Keamari Town.	LG (Water Supply)	68.017	50.517
Improvement of Water Supply and installation of Sewerage line and Carpeting of Road in UC-3 Keamari Town.	LG (Water Supply)	106.576	92.826
Improvement of water supply and installation of Sewerage line and Paver Block in UC-40 & UC-42 District Keamari Karachi	LG (Water Supply)	137.009	137.009
Providing / Laying Paver R.C.C Sewerage Pipe Line and C.C Flooring I/C Cleaning of Nallahs at different places of UC-41, UC-42, UC-43, UC-44, UC-45 & UC-46 in DMC Keamari	LG (Water Supply)	92.880	68.055
Improvement of water Supply and installation of Sewerage line and Paver Block in UC-29.	LG (Water Supply)	67.874	50.374
Improvement of Water Supply and installation of Sewerage line and Carpeting of Road in UC-30 & 31 Baldia Town.	LG (Water Supply)	146.796	128.046
Improvement of water supply and installation of Sewerage line and Paver Block in UC-32 Baldia Town.	LG (Water Supply)	87.490	76.240
Improvement of water Supply and installation of Sewerage line and Paver Block in UC-35 Baldia Town	LG (Water Supply)	68.367	50.867
Improvement of water Supply and installation of Sewerage line and Paver Block in UC-36.	LG (Water Supply)	157.519	137.519
Improvement of Water Supply and installation of Sewerage line and Carpeting of Road in UC-37 Baldia Town.	LG (Water Supply)	157.739	137.739
Construction of Drains in different wards of UC-36	LG (Water Supply)	70.000	70.000
Construction of Drains in different wards of UC-37	LG (Water Supply)	98.049	85.549
Providing / Laying & Replacement of Damaged & Unserviceable Sewerage lines in different areas of PS-97	LG (Water Supply)	75.857	65.857
Providing / Laying & Replacement of Damaged & Unserviceable Sewerage line in UC-32 & UC-37 Ward 1	LG (Water Supply)	56.481	41.481
Providing and Laying of CC flooring / Paver Blocks in Different Streets of UC-32	LG (Water Supply)	29.694	22.194
Providing & Laying & Replacement of Damaged & Unserviceable Sewerage line in UC-8 Natha Khan & UC-23 Awami Colony	LG (Water Supply)	56.368	41.368
Rehabilitation / Improvement of Road / Sewerage Line & Water Supply System in the area of PS-129.	LG (Water Supply)	96.956	84.456
Rehabilitation / Improvement of Road / Sewerage Line & Water System in the area of PS-123, 124,	LG (Water Supply)	96.900	71.900
Rehabilitation / Improvement of Road / Sewerage line & Water System in the area of PS-130 District Central	LG (Water Supply)	48.135	35.635
Rehabilitation / Improvement of Road / Sewerage Line & Water System in the area of PS-125, 126.	LG (Water Supply)	96.173	71.173
P/L/J & Testing of 20" dia PE Rising main from 8 MGD Preetabad filter plant & distribution main (P.E) upto Tando Tayyab/Islamabad Chowk i/c construction of low services reservoirs pump hous, pumping machinery & allied accessories etc. in all respect	LG (Water Supply)	229.328	229.328
Providing & Laying of Paver Block at Various Streets / Roads of UC-1, UC-2, UC-22 to UC-39 and UC-45 to UC-50 and Ward 1 to 9 Cantt: Taluka City Hyderabad	LG (Water Supply)	292.952	217.952
Paver Block Road from Mirpurkhas Ring Road to Siyal Colony & Others (5.00 KMs)	LG (Water Supply)	95.829	83.454
Providing & Laying of Paver Block in Hingorno Town Taluka Sindhri 8000 RFT	LG (Water Supply)	44.477	31.977
Construction of CC / Paver Block Roads in Different Muhalla in Mithi Town	LG (Water Supply)	52.950	40.450
Providing Sewerage Lines in Various wards / UCs of Taluka Nawabshah Juma Khan Zardari, Village Ghazi Khan Hoat and village Khairshah,	LG (Water Supply)	72.593	62.805

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Haqani Colony, Badal Colony, Sumera Colony, Ghulam Hyder Shah Colony, Bhattai Colony, Housing Society, Society & Hanif Katiyar Muhallah, Chandia Colony, Jamali Colony, Bhangwar Colony and Oad Bhatti Para, Mehran Colony, Azim Colony, Muhammadi Town & Pathan Para, Ghulam Rasool Shah Colony, Sain Bux Khaskheli, New Sabzi Mandi road, Fouji Colony, Faizan Madina Colony, Muhammadi Ali Shah More, Ghazali Town, Shafi Muhammad Baloch, Umar Daraz Colony, Village Eid Muhammad Brohi, Railway Colony, Camp No. 2, Taj Colony near Abdul Haque Jamali & Madrsa Street, Bhatti Para, Brohi Goth, Khan Pump Back side, Afzal Shah Town, Shalimar Town, Sanghar road Ayesha College disposal work, Taj Colony & various portions (UCs - 1 to 9)			
Dual Carriage Road of Johi City, Drainage and Paving Block	LG (Water Supply)	98.550	73.550
Improvement of Drainage and Paving Block from Town Committee Via Phulji Station	LG (Water Supply)	98.613	73.613
Improvement of Drainage and Paving Block of Piyaro Station Road	LG (Water Supply)	98.826	73.826
Improvement of Road from Indus Highway Degree College to Theba VIP Road Mehar Link to Dua Hospital i/c Drainage on both sides & Paving Block	LG (Water Supply)	98.400	73.400
Improvement of Road from Haji Khan to Drigh Bala Road i/c Paving Block & Drainage at Village Drigh Bala	LG (Water Supply)	98.284	73.284
Laying of Paver Block at UC 16,17,18,19 and 20 Larkano City	LG (Water Supply)	58.696	53.033
Providing & Laying of Paver Block in Taluka Dokri	LG (Water Supply)	24.966	21.253
(i) Providing & Laying of Paver Block from Naudero-Ratodero Road to Governemnt Boys Degree College Naudero (0.50 KMs) (ii) Construction of Paver Block from Allah Waro Chowk to Jug Chowk at Naudero (0.50 KMs) (iii) Construction of road from Karim Bux Khuhro Petrol Pump to Allah Warayo Solangi (0.60 KMs) (iv) Construction of Road from Naudero Larkano Road to Naudero By Pass via Dastagir Colony (0.60 KMs) (v) Construction / Reconditioning of Road from Naudero Jag chowk to Peer-Jo-goth via Qutub Shah Nursery (0.70 KMs)	LG (Water Supply)	80.000	70.100
Providing & Laying of C.C. Paver in various roads & streets of Jacobabad	LG (Water Supply)	300.000	300.000
Providing & Laying of Paver Block at Various Streets of Mubarakpur City Taluka Thul	LG (Water Supply)	41.998	36.998
Providing & Laying of Paver Block at various Villages of UC Meral Pur and UC Mubarak Pur (i) Wali Muhammad Tanwari (ii) Din Muhammad Tanwar (iii) Jhngal Tanwari (iv) Band Tanwari (v) Khamiso Bambal (vi) Nasar Muhammad Brohi (vii) Gujo Tanwari Dhani (viii) Bux Mastoi Raheem Bux Mastoi (ix) Sahab Khan Mastoi (x) / Aamir Khoso (xi) Qaim Din Tanwari (xii) Jam Khan Khoso(xiii) Liaquat Khan Mahar (xiv) Rozi Shar (xv) Hamzo Mahar (xvi) Muhammad Ramzan Mahar (xvii) Piyaro Mahar (xviii) Beer Jo Goath and (xix) Sardar Bux Shar	LG (Water Supply)	52.500	46.250
Construction of Paver Block Road Kandhkot Muncpal Committee Ward No. 1 to 16	LG (Water Supply)	99.405	99.405
i) Providing Paver Block at Village Muhammad Ali Marfani Shop to Sarwar Marfani, (ii) Mehrab Marfani, Jabal Bhayo, Veesar, (iii) Arain Muhalla, Chohan Muhalla, Sarmastani Muhallah, City Shikarpur (Ward-25) (vi) Samadha Ashram, City Shikarpur (v) Village Shahzado Bhand to Jamia Masjid (vi) Village Jamshed Khan Pathan, (vii) Village Bhoora Khan Lohar & Construction of road from Village Gul Bar Marfani Mile 0/0-0/4.	LG (Water Supply)	94.953	69.953
Providing of Paver Block in Various Streets of Different Villages of Taluka Khanpur	LG (Water Supply)	93.660	68.660
Providing of Paver Block in various streets in different Ward-I to Ward-30, City Shikarpur	LG (Water Supply)	113.413	98.563
Providing of Paver Block in various streets of Different villages of Taluka Shikarpur	LG (Water Supply)	95.356	70.356
Improvement of Various Sreets with Paver Blocks in (i) Rustam Town (ii) Jahan Khan (iii) Village Pyaro Khan Bhayo (iv) Channar Goth (v) Village Qasim Bhayo (vi) Kot Altaf Bhayo	LG (Water Supply)	92.565	67.565
Providing and Laying of Paving Blocks in various Streets of villages of Union Councils Mureed Sethar, UC Karan Sharif, UC Lodra, UC Sultan Kot, UC Hamayoon Sharif, UC Machi & Shahul Sadhayo	LG (Water Supply)	156.873	117.273
Construction of Paver Block Road in villages (1) Jhali Kalwari (2) Ruk (3) Sakhji (4) Kalhora Muhallah (5) Juneja Muhallah (6) Ghulam Qadir Jagerani (7) thenda (8) Syed Amanullah (9) Janib Bhayo to Lutfullah Khan (10) Bashir Ahmed Mirani to village Arbelo Abro (11) Soomra Muhalla (12) Chohan & different village of Taluka Laksi	LG (Water Supply)	95.612	70.612
Construction of Paver Block Road (1) Town Committee Rustam (2) Jarar Pahore (3) Garhi Teigo (4) Abdul Ghafoor Brohi (5) Ali Hassan Brohi (6) Tarai (7) Piyaro Khan Bhayo & different village of UC-Garhi Dakho & Areja UC-Pir Bux Shujrah	LG (Water Supply)	100.000	75.000
Construction of Paver Block Road (1) village Khan Muhammad Channa (2) Rais Hizbullah (3) Chodio Sadhayo road to village Jaggan UC-Zerkhail & different villages of UC Tarai	LG (Water Supply)	98.628	73.628

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Construction of Paver Block Road (1) Village Arbab Marfani (2) Village Chak to Kot Nawab Khan Bhayo & different Village of Taluka Khanpur	LG (Water Supply)	97.328	72.328
Construction and Widening of Road with Paver Blocks i/c Providing drains: (1) from Shikarpur Jacobabad Road Naka to Gah Piri Sukhpul Via Panj Guli with 2 Links @ Tharoorpur Road and Masana (Graveyard) (2) From Old Mall Piri to Qazi Mohalla via Larik Mohalla with Link to Kumbhar Mohalla (3) From Wagno Gate Road Shikarpur Sikander Achaar Goodam to Karan Gate via link Road through Petrol Pump (4) From Phatak at Kanak Shah peer to Old Railway Crossing via Link to Dawan Shah Road	LG (Water Supply)	98.240	73.240
Construction of Road & providing of Paver	LG (Water Supply)	296.914	222.664
Construction of Paver Block Road at different streets of Town Khanpur, Village Abdu, Dahar, Mangria Muhalla, Master Bhayo House, Town Committee Chak, Qasim Bhayo & Different Villages of UC Mungrani & UC Ruk	LG (Water Supply)	98.781	73.781
Providing & Laying of Paver Blocks from N.H Way Baiji Chowk Degree College Pano Akil Kacha Phatak to Mukhtiar office Panjal Mahesar Chowk to Bozdar Chowk Sakhi Baba Hospital Chowk to old Sadhooja Bus Stop Shainshah Bukhari Chowk to Bozdar Chowk Pir Wah to Mai Jindo graveyard Mehran School NADRA Office to Benazir Park Pano Akil Cantt: road to Faizan-e-Madeena Masjid near Old Water Tank Masjid Seddiqiya H/O Ahsan Khan to Ustad Muhammad Tahir Achrani G-T Road Noor Masjid to Shaikh Muhallah, H/O Dr. Muzaffar Kalhoru upto Ashique Hussain Shah Road via Jumo Bhutto and adjacent areas (6.0 KMs)	LG (Water Supply)	80.990	55.990
Construction of various Paver Block Roads in Taluka Kotdiji	LG (Water Supply)	163.000	163.000
Providing & Laying of Paver Blocks from old Bus Stand Ranipur via Gambat road (Rehman CNG) and from National Highway to Dr. Fatah Hospital and from National Highway to Kauser Masjid (Katchiabadi) and from Ranipur Sobhodero Road to Dargah Sharif Town Committee Ranipur Taluka Sobhodero Ranipur	LG (Water Supply)	99.217	70.417
Providing of Drainage System & Paver Block City Pir Esso U.C Kamal Dero Taluka Gambat,	LG (Water Supply)	50.000	37.500
Construction of Remaining Work of Surface Drains & Paver Block of Sobhodero City Taluka Sobhodero	LG (Water Supply)	45.861	33.361
Providing & Laying of CC Paver from Civil Hospital to Mangrio Petrol Pump Daharki City	LG (Water Supply)	106.340	91.340
Providing & Laying of CC Paver Mirpur Mathelo City	LG (Water Supply)	112.605	96.542
Construction of Office Building for UC Haji Daim Khan Dhamrah, Taluka Shahdadpur, District Sanghar (SDG # 9)	LG (Water Supply)	6.188	1.547
Providing & Laying 110 MM Polyethylene Pipe Line for solving Water Problem in Gulshan-e- Sikandarabad Keamari Town, District West Keamari ( Keamari Package)	LG (Water Supply)	30.531	15.266
Rehabilitation of Roads & Sewerage System at P&T Colony, Gizri Karachi (Revised on 13.05.2022)	LG (Water Supply)	566.847	200.702
Construction / Improvement of surface drain, CC paving block, CC block and asphalt road in various areas PS-67, Taluka City District Hyderabad	LG (Water Supply)	400.000	100.000
Establishment of City Hall at Khairpur (SDG # 9)	LG (Bldgs)	142.000	105.354
Construction of Town Committee Naukot, Taluka Jhudo District Mirpurkhas (SDG # 9)	LG (Bldgs)	20.000	17.500
Construction / Renovation / Rehabilitation of Office Building for Town Committee Garhi Khairo (SDG # 9)	LG (Bldgs)	20.000	20.000
Widening / Improvement of Main Hawksbay Road, Karachi	LG (Roads)	1136.000	266.763
Providing Access to Shaheed Benazirabad town (Deh Mandiari Hawksbay) and adjoining villages (LDA) (SDG # 9)	LG (Roads)	818.000	281.421
Widening /Reconditioning of link road from Tail Mori to Tando Allahyar Sugar Mill via Sobhraj mile 2/0-5/6 (6.03 Km)	LG (Roads)	77.409	1.802
Construction of Storm Water Drains and Rehabilitation of Damaged roads of Nawabshah Town during rains 2011. (Revised on 14.11.14) (SDG # 9)	LG (Roads)	484.650	3.607
Construction of road from Tando Jan Muhammad Dehi road at point 57 Mori to village Muhammad Salim Dada Deh 197 and Link to Muhammad Asif Deh 201 District Mirpur Khas (4.5 Km) (SDG # 9)	LG (Roads)	49.809	1.078
Renovation with asphalt dual carriage way road in Tando Allahyar town portion mile 0/0-3/0 (7.8 Km) (Revised on 06.05.21) (SDG # 9)	LG (Roads)	1225.673	170.404
Construction of road (Bye Pass) at Kumb City District Khairpur mile 0/0-2/4 (6.6 Km) (Revised on 19.05.22)	LG (Roads)	155.912	66.990
Construction of Road from Village Toung Shareef to Thana Ahmed Khan mile 0/0 - 12/4 (20 Km), Taluka Thana Bula Khan, District Jamshoro (SDG # 9)	LG (Roads)	247.581	0.001
Construction of Road Dodapur Garhi Khairo Road to Jafferabad Buledi 10 Km (SDG # 9)	LG (Roads)	104.891	2.509
Construction / Reconditioning of Roads (7 units) in UC Arzi Bhutto, Taluka Sijawal Junejo (18.4 Km) (SDG # 9)	LG (Roads)	164.681	0.199
Construction of Road (in 165 feet R.O.W) from Azeem pura (Milat Town) to Juma Goth Noor Din Garden shah Faisal Town Karachi (1.5 Km)	LG (Roads)	147.680	100.762

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Construction / Rehabilitation & Improvement of Road, Water Supply, Drainage & Storm water drain from Five Star chowrangi to Landi kotal chowrangi District Central (3.8 Km) (Revised on 01.04.21)	LG (Roads)	550.089	0.013
Rehabilitation/Re-construction Road of UC Pipri District Malir Karachi (2.74 Km) (Revised on 27.01.22)	LG (Roads)	98.409	45.976
Improvement / Rehabilitation of Storm Water Drain & Dual Road at Hazara Chowk to Pareshan Chowk, Via Al Sadaf Chowk, Karachi (3.6 Km)	LG (Roads)	231.088	165.818
Improvement / Rehabilitation of Mubarak Shaheed Road from Cantt General Hospital to Shahrah-e-Faisal, Karachi (2.65 Km) (Revised on 04.06.21)	LG (Roads)	224.612	100.319
Construction of paver, CC block, Asphalt road i/c drain in Pano Aqil District Sukkur (2.768 Km)	LG (Roads)	78.180	0.001
Rehabilitation / Development of Infrastructure of Block-3 of Hawksbay Scheme-42 allocated to the members of KPC (8 Km)	LG (Roads)	109.896	44.896
Rehabilitation / Development of Infrastructure of Block-2 of Hawksbay Scheme-42 allocated to the members of KPC (6.87 Km)	LG (Roads)	215.180	144.680
Construction of dual carriageway Manghopir Road to Shahrah-e-Qaddafi Orangi-Surjani Link Road (Revised on 07.04.22)	LG (Roads)	1219.200	937.420
Construction/Rehabilitation of Roads , Sewerage and C.C, Flooring in Dumba Goth, District Malir, Karachi (Revised on 19.05.22)	LG (Roads)	311.883	151.952
(i) Providing Paver Block / Bridge at Village Allahdad Marfani (ii) Providing Paver Block at Village Abdul Jabbar Marfani (iii) Providing Paver Block at Village Ghulam Muhammad Marfani (iv) Providing Paver Block from Jaggan Sharanpur road to Village Ali M. Marfani (v) Rabdino Marfani (vi) Repair of road from from Shah Jalil Badshah at Village Jaggan, Paver Block from GBHS Lakhi to Googi Ram House & Bilal Petrol Pump to Bagri Muhalla (vii) Wada Machi (v) construction of road from Jaggan Wakro road to Ali Hassan Khoso (vi) Construction of road from Hamayun Wakro road to Sadoro Bhatti (vii) Construction of road from Hamayun Wakro road to Village Akbar Rind (viii) Construction of road from Jaggan Wakro road to Village pahar Brohi (ix) Construction of road from Jaggan Bus Stand road to Ali Dost Bhatti (x) Construction of Bridges (i) Hidayatullah Chachar (ii) Ali Hassan Khoso (xi) Paver Block from Abdul Rasheed Bhutto Rice Mill to Makhno Khan Bhutto House @ Village Jano.	LG (Roads)	75.063	65.163
Rehabilitation of internal roads of City (5.0 Km)	LG (Roads)	98.278	85.903
Construction of roads in various UCs of District Shaheed Benazirabad (a) Reconditioning / Construction of road from Sakrand Majeed Keerio road to village Haji Keerio (0.92 Km) (b) Reconditioning of road from Lashari Stop Keeria Mori to Bachal Keerio Nathiyani, Deh 80 Nusrat Mile 0/0-0/5 (1 Km) (Dhora Portion) (1/2 thick carpet with paver machine) (c) Reconditioning of road from Nawabshah - Daur road Lashari Stop to village Imamuddin Keerio road Mile 0/0-1/1 (1.80 Km) (1/2 thick carpet with paver machine) (d) W/R/ Construction of road from Sakrand - Nawabshah road to village Sikandar Hayat Rind, Mile 0/0-0/2 + 330) (0.50 Km) (1/2 thick carpet with paver machine) (e) Construction of road from Nawabshah - Sakrand road to village Ali Sher Rind including link to village Porho Machi (3 Km) (1-1/2 " thick carpet with paver machine)	LG (Roads)	79.442	70.400
Improvement of various streets of Sarhari Town 4-5 Km	LG (Roads)	44.627	38.440
Construction / Reconditioning of various roads of Taluka Qasimabad & Taluka Rural Hyderabad	LG (Roads)	127.760	97.760
Construction of road Village Rawal Kandra, Construction of Road village Mubeen Jakhro, Construction of Road village Yasin Bhai, Construction of Road village Wadero Gul Muhammad Babro, Construction of Road village Gulsher Machi, Construction of Road village Haji Ahmed Khoso, Construction of Road village Rahim Charan, Construction of Road village Lakha Dino Lothiya, Construction of Road village Haji Mirbhar. Improvement of road village Walro repair, Improvement of road village Muhammad Khan Magsi repair, Improvement of road village Abdulullah Sodho repair	LG (Roads)	77.857	58.732
Construction of roads alongwith drainage, sewerage and paver stones in UC Khuldabad District Malir Karachi	LG (Roads)	59.779	44.779
Construction of roads alongwith drainage, sewerage and paver stones in UC Bhitaiabad District Malir Karachi	LG (Roads)	89.970	67.470
Construction of roads alongwith drainage, sewerage and paver stones in UC Ghazi Dawood Brohi, UC Jaffar Tyar and UC Ghareebabad District Malir Karachi	LG (Roads)	137.338	121.250
Construction of roads alongwith drainage, Sewerage, Pipes and paving blocks in UC-1 Sherpao, Malir Karachi	LG (Roads)	79.905	69.905
Construction of roads alongwith drainage, Sewerage, Pipes and paving blocks in UC-3, Muzafarabad, Malir Karachi	LG (Roads)	89.936	67.436
Construction of roads alongwith drainage, Sewerage, Pipes and paving blocks in UC-4, Majeed Colony, UC-5 Cattle Colony, Malir Karachi	LG (Roads)	107.620	94.007
Construction of roads alongwith drainage, Sewerage, Pipes and paving blocks in UC-7, Quaidabad, UC-8 Mominabad, Malir Karachi	LG (Roads)	99.675	87.175
Reconstruction / Rehabilitation of roads, Drain work and Paver Blocks C.C flooring at UC45 Gulshan e Sikandarabad District Keamari Karachi	LG (Roads)	99.493	74.493
Construction / Rehabilitation of Roads, Drain Work and Paver Blocks at UC 40 Maripur District Keamari Karachi	LG (Roads)	99.884	87.384

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Construction / Rehabilitation of Roads, Pipe Drain Work and C.C flooring at UC 01 Gulbai District Keamari Karachi	LG (Roads)	99.986	74.986
Construction / Rehabilitation of Roads, Drain Work and Paver Blocks C.C flooring at UC 42 Machar Colony District Keamari Karachi	LG (Roads)	49.809	37.309
1. Repair of Roads U.C Hatiri (3 Km) 2. Repair of Roads U.C Masoo Bughri (1.5 Km) 3. Construction of roads U.C Hatiri (1.5 Km) 4. Construction of C.C Blocks in various streets of village Sobho Khan U.C Tando Qaisar 5. Construction of Drainage village Sobho Khan U.C Tando Qaisar	LG (Roads)	27.042	19.542
Construction of metal road / tough tile / solar lights at various streets of Thul City Taluka Thul District Jacobabad	LG (Roads)	99.028	74.028
Rehabilitation / Construction of internal roads of M.C. Kandhkot, Ward no. 1 to 16	LG (Roads)	80.000	70.100
Construction of Metalled Road / Repair / Paving Blocks from Mari Road to Veeram Jafferri with link of Internal Road via Kedo Jafferri i/c Construction of Paving Blocks in various streets of Villages UC Jano Sharif with road Drain	LG (Roads)	78.746	58.746
Construction / Repair of Metalled Road from Village Baid to Village Nabi Bux Brohi with 4 links. (1) From Sahib Khan Kakepoto to Shikarpur Larkana Indus Highway i/c Paver Blocks in Streets. (2) From Khaman to Shikarpur Larkana Indus Highway (3) From Village Baid to Village Dil Murad Kakepoto (4) From Baid Road to Bugro Luhur Via Mian Wahi	LG (Roads)	78.837	58.837
Construction of Road & Installation of Paver Blocks, Manzoor Colony-I (UC-02 District East)	LG (Roads)	74.518	65.855
Construction of Metal road at different places of UC-42 & UC-43 in PS-113, Keamari Zone, DMC (Keamari)	LG (Roads)	99.134	74.334
Construction of Metal road at different places of UC-44, UC-45 & UC-46 in PS-113, Keamari Zone, DMC (Keamari)	LG (Roads)	99.087	74.287
W/R of road from Larkana Khairpur road to village Fareedabad W/R of road from village Bakrani to village Mad Bahu via Shafquat Hussain Khan Unar House & Paver Block for different Uc's Mad Bahu, Fareedabad, Puranoabad, Mahar Wada, Baqapur @ Naich	LG (Roads)	140.000	122.675
Construction / Re-construction of road from Gerello bus stand city to Ghulam Ali Zuhrani & Ghulam Muhammad Buledi Kully, Muhammad Ali Brohi, Mehboob Ali birohi to Derra Bridge mile: 0/0-1/4 (2.25 Km).	LG (Roads)	50.000	43.813
Construction asphalt road (New / Repair) various roads with drainage Municipal Committee Rohri. Repair of Pedestrian path ways. Roads surface and repairing of old Sukkur Channel and landsdown bridge, road	LG (Roads)	99.144	74.144
Rehabilitation / Reconditioning of road from Khairpur Machiyoon road at Mang tagar bridge towards from village Gagri at Dargah Hajna Shah road including link from Dargah Pir Ghaffar Shah Road to village Baddai Machi, Buxo wahanwuth 1-1/2 Premixed Carpet including masonry structure and construction, providing / fixing C.C paving block (55000 Sft) in Taluka Khairpur mile 0/0-4/0 (6.40 Km)	LG (Roads)	98.500	86.125
Reconditioning / Rehabilitation of road from old National Highway over towards from Khairpur old Khajoor Mandi road to village Ali Dino Burdi at District Council road village Khokhar, Village Mahar Tariyo including link to Wari Goth upto Umrani village leading through under Railway Phattak Khairpur with masonry structure and construction, providing / fixing C.C paving block (165255 Sft) with 1-1/2 premixed carpet mile 0/0-6/3 (10.20 Km)	LG (Roads)	98.597	86.222
Rehabilitation / Reconditioning of road from New National Highway village Pir Mangio to village Qaimuddin Khorkhani Baloch towards with Parallel to the Pir Mangio Shakh at Bandani Phulpoto including approach from village Waris Gambhir, Dur Muhammad Phulpoto upto Razi Goth road with 1/2 premixed carpet including retaining wall for protection of road (1320 Rft) including construction and providing / fixing C.C paving block (222200 Sft) Taluka Khairpur Mile 0/0-7/1 (11.40 Km)	LG (Roads)	117.500	102.650
Widening & reconditioning of road, paver block streets and drainage at Moro city	LG (Roads)	160.062	139.994
Construction of roads in various U.Cs in Taluka Nawabshah and Daur ( a) Construction of road from Nawabshah 60th Mile road to village Sim Nala Murad Bux Brohi Mile 0/0-4/0 (0.80 Km) (Ghandtar) (b) Reconditioning of road from old Sugar Mill Road to village Allah Dino Phanwar Mile 0/0-0/3+330 (0.70 Km) (Ghandtar) (c) Construction of road from Nawabshah - Daur road to village Jamal Shah mile 0/0-0/3+220 (0.66 Km) (Ghandtar) (d) reconditioning of road from Nawabshah 60th Mile road @ 87 Mori to viallge Rais Karam Ali Khan Jamali various streets mile 0/0-3+440 (0.73 Km) (Ghandtar) (e) Reconditioning of road from Nawabshah Sanghar road to viallge Mehmood Jamali mile 0/5-1/0 0.60 Km) (Sakhi Umed Ali Jamali) (f) Reconditioning of road from Nawabshah Sanghar road to village Baig Muhammad Mugheri mile 0/0-1/0 (1.60 Km) (Sakhi Umed Ali Jamali) (g) Construction of road from Nawabshah Sanghar road to Choudhry Ismail Arain road to Doro Naro @ Path village Muhammad Saleh Khaskheli Mile 0/0-0/2+330 (0.50 Km) I/C 23*21 Slab (Sakhi Umed Ali Jamali) (h) Construction of road from Nawabshah Sanghar road - Ali Jan Brohi Mile 0/4 to village Ghulam Mustafa Brohi mile 0/0-0/2 (0.40 Km) & various portion (Sakhi Umed Ali Jamali) (i) Construction of road from desert area road @ mile 11/3 to New village Ch. Manzoor Arain I/C approach length	LG (Roads)	232.240	205.830

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
mile 0/0-0/2 (0.40 Km) (Obhari Sawari) ( j) Reconditioning of road from Nawabshah - Qazi Ahmed Road @ mile 7/0 to village Bahawal Khan Zardari road mile 0/0-0/4 + 220(0.87 Km) (Chanesar-I) K) Reconditioning or road from Nawabshah - Qazi Ahmed road @ mile 9/0 to village Chanesar mile 0/0-1/0 (1.60 Km) (Chanesar -I) L) Reconditioning of road from Nawabshah Qazi Ahmed road Chanesar Stop to village Hameer Kaniyo via Allah Rakhio Kaniyo and Khair Muhammad Rind road mile 0/0-1/5 +440(2.73 Km) (Chanesar-I) M) Construction of road from Nawabshah Jam Sahib road @ mile 1/2 village Abdul Qayoom Arain (II) Nawabshah Sanghar road to 2/4 village Khushahl Zardari road mile 0/0-0/4 -1 10 (Sakhi Umed Ali Jamali) N) Reconditioning of road from Wali Muhammad Rind road - Bhambo minor IP path to village Kamil Khan Rind mile 0/0-1/7 (3.0 Km) (Wali Muhammad Rind) O) Reconditioning of road from Nawabshah - Daur road @ mile 4/4 to village Haji Mitho Khan Zardari road mile 0/0-0/2 (0.40 Km) ( Khair Shah) P) Reconditioning / Construction of road from Nawabshah to Daur road @ mile 7/0 to village Lal Chand via Village Haji Muhammad Bux Zardari road mile 0/0-2/0 (3.20 Km) (Mureed Khan Zardari) Q) Reconditioning of road from Laique Zardari @ mile 1/0 to Dargah Malook Peer road mile 0/0-2/4 (4.00 Km) (Mureed Khan Zardari) R) Reconditioning of road from Tri Mor road Laique Zardari road to Allah Wasiyo Zardari and Dr. Fateh Ali (Mureed Khan Zardari) (S) Reconditioning of road from Dargah Malook Peer road to village Ali Khan Zardari (Mureed Khan Zardari)			
(A) Construction of link road from Hayat Chaniho road to village Dr. Ramzan Dars road 0.0 to 1.00 Km (B) Construction of link road from Khipro Ghulam Nabi Shah road to village Gabool Shar 0.0 to 1.00 Km (C) Construction of link road from Mianad Bhanbhro road to village Bangul Khan Bhanbhro 0.0 to 1.00 Km (D) Reconditioning / Construction of link road from Sanghar Khipro Offtacking road Wassan Hinorjo road via village Anb Dars 0.0 to 2.00 Km (E) Reconditioning of link road from Khipro Ghulam Nabi Shah Road to Dargha Qabool Shah via Jama Masjid Bhit Bhaiti 0.0 to 1.00 Km (F) Construction of link road from Saddique Khaskheli to village Arbab Ali Samoon via Khalifo Rahmatullah Dars 0.0 to 2.00 Km (G) Construction of link road from Jamal Shah road to Village Abdul Sattar Wassan 0.0 to 1.00 Km (H) Construction of link road from aqil Hingoro road to village Tayyab Bozdar 0.0 to 1.00 Km from A to H Total 10.00 Km	LG (Roads)	97.305	75.005
1-1/2 Thick Asphalt W/R Shahdadpur - Gupchani road to PTC Barhoon road mile 0/0-1/4 (2.40 Km) (18F")	LG (Roads)	44.014	31.514
Const: of Road village Uamid Ali Jamali to Raheem Mirmani to Sher Muhammad Kamboh to Dost Muhammad Otho to connect Najma Sugar Mill Road	LG (Roads)	99.238	74.488
Recond: / Imp: of Road Naoukot Fazal Bhambro Road to Nafees Nagar to Ali Hassan Gurgez to Shanker Bheel to Shadman Gurgez.	LG (Roads)	139.552	104.552
Recond: / Imp: of Road Tedi Mori to Arif Khan Kapri to Daria Khan Pitafi to Karim Bux Bhatti to Mir Manzoor Talpur to Khero Kolhi to connect Jhodo to Samroo Road	LG (Roads)	83.489	62.489
Construction / Rehabilitation of various Roads, CC & Paver Block Roads and Streets in UC Husri i/c Main Husri Road to Village Khameeso Jogi, Taluka Latifabad Hyderabad	LG (Roads)	181.055	137.305
Construction / Rehabilitation of various Roads in PS-64 Ganjo Takar Phatak to New Ali Asgarabad Phatak, Ganjo Takar Phatak to Allah Dino Khumam, Village Jani Rind Road to Noonari Goth & UC 86,87,91,92,94 & Other City Areas Taluka Latifabad Hyderabad	LG (Roads)	174.332	130.562
Various Roads of Hyderabad City	LG (Roads)	187.328	72.328
Construction of road from Seerani Kadhan road @ point Ahmed Shah Mori to Lakho Pir alongwith inspection path of Noor Wah (12.00 Km)	LG (Roads)	99.316	74.360
Construction of road from Iqbal Sarejo Umer Mallah road to Village Mir Hoat Haji Vikio Khaskheli and Bakar Mori upto Arab Mallah i/c link Ramzan Mandhro (11.80 Km)	LG (Roads)	99.331	74.363
Improvement / Construction of road from Badin Seerani road to connect Pathan Parhyar road via Haji Parhyar (Construction 3.40 Km, improvement 9.00 Km)	LG (Roads)	99.323	74.398
Improvement / Construction of road from water supply post office road to abu Shaikha (Allah Dino Soomro) i/c link road from Badin Seerani road Ghulam Rasool Lutter (Construction 6.00 Km, improvement 7.60 Km)	LG (Roads)	99.215	74.315
Construction of Link road village Abdul Razzaque Jamari, Construction of road village Malook Jhurko, Construction of road village Allah Bachayo Babar, Construction of road village Khan Muhammad Babar, Construction of road village Allah Parhayo Gabbar, Construction of road village Babu Khamiso Babar, Construction of road village Achar Kandero Keengar, Construction of road village Dargah Qureshi Baba Babu Shoro, Construction of road Ilyas Jakhro, Construction of road village Daim Shoro, Construction of road village Suleman Brohi, Construction of road village Ali Muhammad Panhwar, Construction of road village Missan Abad road, Construction of road village Ali Muhammad Khaskheli, Construction of road village Khan Jakhro to Ameer Bux Jakhro, Improvement of road Punhal Jamali, Improvement of road village Haji	LG (Roads)	203.180	203.180

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Mehmood Dal, Improvement of road village Ber Machi, Improvement of road village Saleh Bhambhro, Improvement of road village Ali Hassan Brohi road, Improvement of road village Muhammad Ramzan Gopang, Improvement of road National Highway to Band Mori road, Improvement of road National Highway to Brhio Sheedi Mori, Improvement of road Sattiyoun road to village Sajjan Jakhro, Improvement of road village Raju Nizamani, Improvement of main road to Mureed Roonjho via Shabir Abdani			
Construction of road village Ali Muhammad Shoro, Construction of road village Gul Hassan Shah Chattan Nahiyo, Construction of road village Gul Hassan Lashari, Construction of road village Muhammad Akyal Kehar pacca road, Construction of road village Abdullah Kehar, Construction of road village Hashim Shohlani. Improvement of road village Muhammad Umar Bhatti, Construction of main road Arbab Muhammad Qasim	LG (Roads)	70.500	70.500
Improvement of road from Indus Highway to Baid village via Kande Chukhi Connecting to Gozo Village, Including paving block, drain & retaining wall. Mile 0/0-5/6	LG (Roads)	99.590	74.590
W/R road from Piaro Station to Patt and improvement of road village Shahabad via village Jamal Panhwer and village Bag Chandio and construction of Paving and Block and Drainage of above mentioned villages.	LG (Roads)	99.900	74.900
Construction of road from I.H.R / Side Burria Shakhk to Yaseen Leghari Petrol Pump Via L/5 Deeta Shakhk to Panjmor Construction of Paving Block and Drainage from Shahjana Park to Dual Carriages Way Road to Govt: Girls High School Via Najam Colony / Mazdoorabad and Pir Colony i/c Retaining Wall and 2 nos. 12-meter span skew bridges mile 0/0-1/6	LG (Roads)	99.500	74.500
Improvement of road / paving block / foot paths / sign boards / drainage from Hassan Darwesh Graveyard to Rr. Manzoor Leghari Chowk i/c Kheer Mori to Johi Chinni road via Mank Kingrani & Johi Bhan road	LG (Roads)	98.509	73.509
Construction of Roads for Ghaghar City UC-18 Chandparo, District Malir Karachi	LG (Roads)	70.246	52.746
Construction of Roads & C.C Streets of UC-19, Pipri, District Malir Karachi	LG (Roads)	71.215	53.715
Construction of Main Roads & Internal Street Roads of Gulshan-e-Hadeed Ph-1 & Ph-11, District Malir, Karachi	LG (Roads)	99.897	74.897
Construction of Road alongwith drainage, Sewerage and Paver stones in UC Sharafi District Malir Karachi	LG (Roads)	99.877	74.877
Construction of Road alongwith drainage, Sewerage and Paver stones in UC Quaidabad and UC Cattle Colony Ward No. 1 District Malir Karachi	LG (Roads)	99.826	74.826
Construction of Road alongwith drainage, Sewerage and Paver stones in UC Mominabad and UC Dawood Chowrangi, Ward No. 4, District Malir Karachi	LG (Roads)	84.919	63.669
Construction of Road alongwith drainage, Sewerage and Paver stones in UC Ghazi Dawood Brohi, UC Gharibabad and UC Jaffar Tyar, District Malir Karachi	LG (Roads)	99.853	87.353
Construction of Roads Paver Block Street and improvement of Sewerage system in UC Khaldabad and UC Cattal Colony (PS-90) District Malir, Karachi	LG (Roads)	92.256	79.756
Construction of Metaled Road Union Council No-28	LG (Roads)	99.990	74.490
Improvement / Rehabilitation of roads from Machar Colony Lala Hotel to fateh Muhammad School and from Lasi Goth Graveyard to Naddi & from Aimeri Building to Rupali Centre, from Dost Muhammad Khan Wazir Goth to Faqeer Goth and from Sikh Goth to Noor Khan Goth, PS-99, District East, Karachi	LG (Roads)	97.002	84.627
Improvement / Rehabilitation of roads in different areas of PS-99, District East Karachi	LG (Roads)	97.230	86.092
Construction of Roads, Underpasses and Drainage at Taluka Daharki, District Ghotki	LG (Roads)	150.000	131.437
Construction of roads at Taluka Matli District Badin (1) Village Sanpo Shah to main Tando Gh. Ali road (1.5 Km) (2) Village Soomar Chandio to vikio Jatoi UC Budho Qambrani (1 Km) (3) Village Ramzan Chandio to Jamarroo Mori Dumbalo (1 Km) (4) Village M. Azeem Khoso to main T. Gh. Ali Road	LG (Roads)	49.356	36.856
Improvement of Road from Bhan-Johi road to village Makki to Village Mushtaq Jamali and Paver Block Streets and drains at various streets of town Committee Phulji Station	LG (Roads)	99.166	74.166
Construction / Rehabilitation of Primary & Secondary Roads of Sukkur District	LG (Roads)	198.950	49.475
Construction / Rehabilitation of various roads of District Sukkur i/c culverts, paver blocks, C.C. Drain and Boundary Wall	LG (Roads)	296.002	74.000
Up-gradation of Basic Health Unit (BHU) to the level of Rural Health Centre (RHC) at Kolab Jail, Taluka Kingri, District Khairpur. (C:44.695+R:14.448) (SDG # 3)	LG (Health)	59.143	0.001
Construction of BHU at Village Khuwaja Ghulam Rasool UC Noorpur, Taluka Kingri, District Khairpur. (C: 20.073+R: 3.145) (SDG # 3)	LG (Health)	23.218	0.001
Providing and Fixing of Animatronics' Dinos at Safari Park - Karachi (Revised on 21.01.22)	LG (Community Services)	99.956	77.456

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Constt: of 05 Nos. Union Council Offices in PS-73 (C:40.000+R:5.000) (SDG # 11)	LG (Community Services)	45.000	2.464
Construction of Parks at Landhi Kotal Chowrangi, Karachi (Revised on 21.01.22)	LG (Community Services)	99.185	59.187
Construction & Rehabilitation of Parks in 8/A, 8/B, 8/C UC-32 Bilal Colony, Korangi	LG (Community Services)	90.000	78.862
Rehabilitation of Parks Behbood Ladies Park Shirin Jinnah Colony, Adjoining to Two Sword UC-30 & 31, DMC South	LG (Community Services)	33.328	29.615
Construction of Multipurpose Sports Playground with Walking Track including Pavilion, Restrooms, Flood Lights, Standby Generator in Sachal Goth, UC-30	LG (Community Services)	99.846	87.471
Construction of KDA Park including Walking Track, Rides, Boundary Fencing, Food Street, Grassy area & LED Park Lights, Beautification of Surrounding areas Adjacent to Kings Residency in Front of Corniche Comforts flats Block-13 Gulistan-e-Johar	LG (Community Services)	99.768	87.393
Construction of Park and Playground in UC - 30 & 31	LG (Community Services)	100.000	87.625
Establishment of Public Grounds & Public Parks in UC-11, 12, 13, 17, 27 & 28	LG (Community Services)	64.439	57.014
Construction of Numaish Ground & Numaish Gah Zoo Park Along with Boundary Wall Sukkur	LG (Community Services)	250.000	250.000
Rehabilitation & Development of Khalid Khan Park / Green Belt at Airport Sukkur	LG (Community Services)	50.000	50.000
Construction of U-Turn at Natha Khan Bridge (SDG # 9)	Mega Projects for Karachi	214.466	102.343
Rehabilitation of Approach Roads of Lyari Expressway.	Mega Projects for Karachi	219.502	120.502
Rehabilitation of all Major Storm Water Drains of Karachi	Mega Projects for Karachi	1075.891	580.891
Improvement / Rehabilitation of Shaheed-e-Millat Expressway from KPT Flyover to Manzoor Colony Fire Station (Both Track) including Service road at District East	Mega Projects for Karachi	516.000	516.000
Improvement of roads from MA Jinnah Road to I I Chundrigar Road (Mumtaz Hassan road, Hasrat Mohani road, Paper Market road) District South	Mega Projects for Karachi	62.797	62.797
Repair / Renovation of various Mandirs in Hyderabad Division (Hyderabad, Tando Allahyar, T.M Khan, Matiar, Badin, Thatta, Jamshoro, Dadu & SBA)	Minorities Affairs	289.663	49.003
Re-Construction of Anandpur Ashram Clifton Karachi (Re-Revised on 23.02.22)	Minorities Affairs	232.586	100.053
Re-Construction /Rehabilitation of Prayer Hall (Barat Ghar) Street No.6, Essa Nagri Gulshan-e-Iqbal Karachi	Minorities Affairs	10.000	8.750
Construction of Hall and Cremation Place at Hindu Shamshan Ghat New Chhor Taluka & District Umerkot	Minorities Affairs	15.000	13.125
Construction of Community Hall at Sant Shewa Das Temple Shahi Bazaar Gharhi Yaseen, District Shikarpur	Minorities Affairs	10.000	7.500
Construction of Compound Wall, Thalla (Cremation Place) at Hindu Massan Khairpur Town Taluka & District Khairpur	Minorities Affairs	10.000	8.750
Rehabilitation of RTI, Karachi (C:39.77+R:26.149) (SDG # 3, 5)	Population Welfare	65.919	31.770
Remaining works of RHS-A Centre at Garhi Khairo (C:5.817) (SDG # 3, 5)	Population Welfare	5.817	3.263
Remaining works of RHS-A Centre at Dokri (C:2.847) (SDG # 3, 5)	Population Welfare	2.847	1.597
Installation of 10 Reverse Osmosis Plant (RO Plants) in UC Gabo Pat Keamari Town Karachi (SDG # 6).	Public Health Engineering	97.876	86.751
Laying of New Water Supply Line and Construction of Underground water Tank in UC Sahle Muhammad, UC Wali Muhammad UC Razzakabad and UC Chokundi (SDG # 6).	Public Health Engineering	96.793	71.793
Rural Water Supply Scheme Rehri Mian Goth Phase-II (SDG # 6).	Public Health Engineering	99.719	74.542
Construction of Water supply Scheme in UC Ghareebabad, Sahibdad Goth and UC Ghazi Dawood Brohi (SDG # 6).	Public Health Engineering	99.884	74.134
Water Supply Scheme for Jam Goth, Kofiraro, Ghulam Mohammad Goth, Hashim Goth (SDG # 6)	Public Health Engineering	45.470	32.970
Improvement of Raw Water Source for Satellite Town Water Works Urban Water Supply Scheme Mirpurkhas City	Public Health Engineering	79.668	10.000
Construction of RCC Underground Reservoir for R.O Plant, Improvement / Extension of Distribution Network for Miithi and Islamkot (SDG # 6)	Public Health Engineering	485.690	113.275
Water Supply Scheme Sokliyo to Veeranio Sokliyo to Behrao Via Rahirari (SDG # 6)	Public Health Engineering	36.900	15.000
Upgradation & Extention of Pipe Line Water Supply Scheme Kunri-Cheel Bund-Kantio-Chachro (WSL-3) (SDG # 6).	Public Health Engineering	137.495	102.555
Change of Source and Rehabilitation of existing Urban Water Scheme Supply Diplo (SDG # 6)	Public Health Engineering	246.600	40.093
Extension & Rehabilitation of Water Supply Scheme of Brohi Muhalla and Irrigation Muhalla of City Mirpur Bathoro (SDG#6)	Public Health Engineering	71.979	67.604

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Water Supply of Village Syedpur (SDG # 6).	Public Health Engineering	25.373	22.248
Rehabilitation of Urban Water Supply Scheme Ketu Bander (SDG#6)	Public Health Engineering	214.411	20.411
Water Supply Scheme Jhimpir Taluka Thatta (SDG # 6).	Public Health Engineering	20.000	7.000
Improvement/Extension Water Supply Scheme Matiari City (SDG#6).	Public Health Engineering	100.000	3.000
Extension of Rural Water Supply Scheme Village Barchani Sharif, District Tando Muhammad Khan (SDG#6).	Public Health Engineering	29.382	22.382
Water Supply Tank Alongwith Distribution Network for Old Sukkur (SDG # 6).	Public Health Engineering	97.405	72.405
Improvement & Extension Water Supply Scheme Bhiriya City (Revised on 20.04.17) (SDG # 6).	Public Health Engineering	98.370	16.497
Rehabilitation of Urban Water Supply Scheme Nawabshah Town for Additional Rising main 28" Dia from Rohri Canal Water Works up to UF Plant QUEST (SDG # 6)	Public Health Engineering	486.862	13.536
Improvement of Rural Drainage Scheme Mureed Khan Zardari & Ali Hassan Zardari (Revised on 26.08.21) (SDG # 6)	Public Health Engineering	46.038	21.088
Construction of Water Supply Scheme Deh Gulanpur, Deh Kathgarh, Deh Line Purani and Deh Keenjhar (SDG#6)	Public Health Engineering	100.000	87.500
Improvement / Extension of Water Supply Scheme Kandh Kot (SDG # 6)	Public Health Engineering	300.840	49.923
Providing of Drinking Water through Tube Wells for K.N Shah City and adjoining villages Muhammd Murad Chandio & Fatihpur Taluka K.N Shah (SDG # 6).	Public Health Engineering	100.000	75.000
Water Supply Scheme Thariri Mohabat Town (SDG # 6).	Public Health Engineering	54.539	42.039
Construction of Water Supply Scheme in Village Ghaibi Dero, Sono Khan Chandio, Rabban Khan Chandio, Matara & Kajlo Khan Chandio, Taluka Kamber (SDG#6)	Public Health Engineering	100.000	87.500
Water Supply Schemes for Village Fateh Ali Lashari, Samano Chakrani, Ali Dino Burdi and Abdul Hakeem Chakrani, Village Mehar, Village Lique Rajper, Village Aleem Rajper, Village Wada Bhatti. (SDG # 6).	Public Health Engineering	81.468	61.440
Installation of 02 Nos R.O Plant for Village Hashim Chawro UC Ratokot, Jaro Khan Jogi UC Kothi Kandhoro Taluka Larkano 09 Nos. of Colverts for Village Sabzal Mugheri, Taj Muhammad Mugheri (Bado Wah, Mahi Khan Talo Khan Jagirani (Bdo Wah) Kirir Khan Mugheri (Bado Wah), Syed Ameer Ali Shah (Sim Shaakh Khaipur) Ghulam Muhammad Mugheri Near Hassan (Mittho Dero) Sim Shaakh Kambir Khan Mugheri (Bado Wah), Qambeer Jagirani (Earther Wah Gerello), Hukumdad Brohi (Kothi Kalhoro) (SDG # 6).	Public Health Engineering	35.000	26.250
Construction of Water Supply Scheme for Old Nauabad City and adjoining areas (SDG # 6).	Public Health Engineering	22.587	19.462
Construction of Water Supply Scheme for Lemo Khaskheli Deh Raharoo and adjoining Villages (SDG # 6).	Public Health Engineering	54.446	40.446
Improvement & Extension of Urban Water Supply Scheme Shahdadpur Tando Adam Zone-A including filtration	Public Health Engineering	99.790	18.000
Construction of New Drainage System & CC Blocks at UC Halepoto, UC Seri & UC Almani. (SDG # 6)	Public Health Engineering	78.019	68.644
Providing Sewerage System in various Ucs of Taluka Murad Memon (SDG # 6).	Public Health Engineering	99.922	74.922
Providing & Laying of Sewerage & Paver Blocks and internal roads at various villages (Pir Sarhandi, Jam Kando, Satal, Usman) of UC- 16 Kotraro, Bin Qasim (SDG # 6).	Public Health Engineering	65.279	50.279
Improvement & Extension of Urban Drainage Scheme Tando Allahyar Phase II.	Public Health Engineering	75.000	13.250
Drainage Scheme Misri Khan Jarwar alongwith Disposal Taluka Tando Allahyar	Public Health Engineering	25.000	16.106
Drainage Scheme Gujo City District Thatta	Public Health Engineering	20.000	5.000
Drainage Scheme of Belo City and C.C of Sujawal (SDG # 6)	Public Health Engineering	56.335	52.897
Rehabilitation of Urban Drainage Scheme Chuhar Jamali District Sujawal (RGC)	Public Health Engineering	77.143	38.571
Improvement of Existing Drainage System in Bau Khan Pathan & Rural Drainage Scheme Paljani Station Taluka & District Matiari (SDG # 6).	Public Health Engineering	99.500	93.173
Extension of Rural Drainage Scheme Village Barchani Sharif, District Tando Muhammad Khan (SDG#6).	Public Health Engineering	44.799	37.691
Drainage Scheme Kaloi Town	Public Health Engineering	60.000	28.125
CC Paving Blocks & Drains for Various Villages of UC Patni Taluka Rohri (SDG # 6).	Public Health Engineering	60.000	1.756
CC Paving Blocks & Drains for Various Villages of UC Loung Bhatti Taluka Rohri (SDG # 6).	Public Health Engineering	80.000	7.576
Construction of Drainage Scheme at Various Village of Union Council Akbarpur (SDG # 6).	Public Health Engineering	49.816	37.316

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Construction of Drainage Scheme at Bachal Shah Miani Sukkur	Public Health Engineering	133.300	95.800
Construction of Drainage Scheme Allahabad Colony Sukkur (SDG # 6).	Public Health Engineering	90.793	65.793
Construction of Drainage Schemes on one side of Peer Wah Pano Akil town (SDG # 6).	Public Health Engineering	44.669	32.044
Drainage Scheme for left over Area of City Pano Akil (SDG#6).	Public Health Engineering	44.050	31.425
Providing and Fixing Paving Blocks with Road Drainage in Various Streets of Khanpur Town and Various Villages of UC Mian Jo Goth (SDG # 6).	Public Health Engineering	68.651	58.651
Drainage Scheme Garhi Yaseen (SDG # 6).	Public Health Engineering	94.386	81.886
Rural Drainage Scheme Khabri Taluka Lakh (SDG # 6) (Revised on 29.04.22)	Public Health Engineering	35.996	19.369
Sanghar Drainage Scheme Ph-IV (SDG # 6)	Public Health Engineering	322.781	34.228
Construction of Sewerage System for Old Nauabad City and Adjoining Areas (SDG # 6).	Public Health Engineering	26.246	23.121
Construction of Surface Drainage/CC Paver Streets for Kurkili, Jafar Leghari, Kandiari Jam Nawaz Ali Taluka (SDG#6).	Public Health Engineering	123.850	108.350
Improvement and Extension of Drainage Scheme (including C.C Paver) Village Mulla Makhani, Tando Adam (SDG # 6).	Public Health Engineering	44.324	38.074
Rural Drainage Scheme of Village, Ghundan preetamabad, Allahdad Leghari & sher Leghari (SDG # 6).	Public Health Engineering	118.290	89.540
Improvement and Extension of Urban Drainage Scheme Sinjhor	Public Health Engineering	105.278	91.528
Drainage Scheme of Radhan Town (SDG # 6).	Public Health Engineering	99.533	74.533
Construction of Paver Blocks & C.C Drains in Various Muhalla's City Shahdadkot (SDG # 6).	Public Health Engineering	164.857	139.857
Construction of C.C Drains and Paver Blocks in UC's (05 Nos.) of Taluka Shahdadkot (SDG # 6).	Public Health Engineering	100.000	87.500
Construction of Renovation Road & Paver Block & CC Drain in Various Location in City Warah & Taluka Warah (SDG#6).	Public Health Engineering	96.424	83.924
Construction of C.C Drain, CC Block & Paver Blocks at Various Villages of Taluka Warah (SDG # 6).	Public Health Engineering	100.000	87.500
Construction of C.C Drain, CC Block & Paver Blocks at Various Villages of Taluka Naseerabad (SDG # 6).	Public Health Engineering	78.759	68.759
Construction of Renovation Road & Paver Block & CC Drain in various location in City Nasirabad & Taluka Nasirabad (SDG#6)	Public Health Engineering	96.426	83.926
Rural Drainage Scheme Abri Taluka Kamber (SDG # 6).	Public Health Engineering	20.000	3.609
Drainage System for left over areas of City Naudero (SDG#6).	Public Health Engineering	124.851	93.601
Construction of Paver Block And C.C Drain in Various Areas of City Ratodero (SDG # 6).	Public Health Engineering	123.786	92.536
Paver Block/ Drain for different Villages of UC's Bero Chandio, Maheto, Fatehpur, Rasheed Wagan, Mithodero, vikya Sangi, Lund, Dhamrah, Ratokot, Kothi Kalhoro Taluka Larkana (SDG#6).	Public Health Engineering	115.000	86.250
Construction of Paver Block & CC Drain in Various locations of UC-01 to 05 Larkano City (SDG # 6).	Public Health Engineering	150.000	112.500
Construction of Paver Block and CC Drains of Various Locations of UC-06 to 10 City Larkano (SDG # 6).	Public Health Engineering	150.000	113.000
Construction of Paver Block and CC Drains of Various Locations of UC-11 to 15 City Larkano (SDG # 6).	Public Health Engineering	150.000	113.000
Construction of CC Drains & Paver Blocks in various streets of Union Committees No. 16 to 20 of City Larkano (SDG#6).	Public Health Engineering	200.000	150.000
Paver Block & CC Drains from Allah Park Tower to Shahdadkot Naka Bab-e-Zulfiqar via Rest House and Kamber Lashari Road (2.0 Kms) at Taluka Ratodero (SDG # 6).	Public Health Engineering	66.508	46.508
Paver Block & CC Drains from Allah Wali Masjid to Abdul Wahid Soomro Gate via New Eid Gah and Massan (1.50 kms) at Taluka Ratodero (SDG # 6).	Public Health Engineering	45.734	30.734
Paver Block & CC Drains from Allah park Tower to Wado Alam pak via VIP Bakery, Harijan Road and Amroti Mashid at Taluka Ratodero (1.5 kms) (SDG # 6).	Public Health Engineering	45.834	30.834
Construction of Drains & Paver Block in Various Streets of Ward No. I,II,III,V&VII of Naudero, Taluka Ratodero(SDG#6).	Public Health Engineering	49.411	34.411
Construction of Paver Block & C.C Drains in Various Uc's of Taluka Ratodero (SDG # 6).	Public Health Engineering	144.969	126.969
Construction of Paver Block & CC Drain of Akil Circle ( UC's Akil, Aghani & Phull) (2.50 KMs), Taluka Larkano (SDG # 6).	Public Health Engineering	45.370	32.870
Construction of Paver/CC Block & CC Drain from Railway Station Badeh to Govt. Hospital Badeh, and Construction of CC Block Paver Block & CC Drain Channa Bridge Dokri to Dokri Bus Stand Via Village Babal Jarwar and various streets of City Badeh and City Dokri (SDG # 6).	Public Health Engineering	76.120	51.120

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Construction of Paver/CC Block & CC Drain in diferent Villages of District Larkano (SDG # 6).	Public Health Engineering	94.616	69.616
Construction of Drainage Scheme at Mohallah Jam Hassan Khan Dahar & CC Paver in various Streets Ubauro City	Public Health Engineering	106.540	76.540
Drainage Scheme Village Pir Muhammad Bhutto, UC Ranwati, Taluka Ubauro (SDG # 6).	Public Health Engineering	72.966	52.591
Drairage Scheme Village Mari, UC Kamoon Shaheed Taluka Ubauro (SDG # 6).	Public Health Engineering	48.126	34.958
Rural Drainage for Village Syed Ibrahim Shah UC-Buchery Taluka Daur (SDG # 6).	Public Health Engineering	26.150	6.469
Drainage Scheme for Various Wards of Nawabshah City (SDG#6)	Public Health Engineering	118.835	103.210
Drainage Scheme in Various Streets of Town Committee Bucheri	Public Health Engineering	29.519	25.769
Improvement & Extension of Urban Drainage Scheme Behlani alongwith CC Block (SDG #6)	Public Health Engineering	30.000	3.657
Drainage Scheme Village Dewan and Sawan Shaito (SDG # 6).	Public Health Engineering	40.000	3.119
Construction of Surface Drains, C.C Topping, C.C Paver Block, Culverts & Bricks Pavement and Sewer Line at Town Committee Mehrabpur Taluka Mehrabpur (SDG#6).	Public Health Engineering	48.196	41.946
Drainage Scheme i/c CC Topping and Paver Block of Village Saleemabad UC Ghulam Shah (SDG # 6).	Public Health Engineering	49.894	43.019
Providing & Fixing Paver Block including Drain Nalla Bhiria Road (SDG # 6).	Public Health Engineering	46.630	40.380
Drainage Scheme Dargah Nasir Faqir Jalalani & Wassan Muhalla	Public Health Engineering	34.534	12.297
Construction of Surface Drain & C.C Paver of Village Neer Waro Bhanbhan Kashif Raza (SDG # 6).	Public Health Engineering	27.869	20.244
Drainage Scheme Mohammad Moosa Thebo Taluka Kot Digi (SDG #6).	Public Health Engineering	25.819	6.435
Drainage and Paver Schemes in Various Villages of Khairpur and Kotdiji (SDG # 6)	Public Health Engineering	94.020	69.020
Water Supply Scheme Nasarpur (ADP No.1549)(2020-21) (SDG#6)	Public Health Engineering	98.540	31.621
Construction of drain in various street of Abbas Bhai Town Firdos Colony, Akber Colony, Pigril Colony, Mehran Colony, Kamber Colony, Soomro Colony, Shahjahan Town, Watayo Fakir Baloch Colony Ward-13 (ADP No.1729)(2020-21) (SDG#6)	Public Health Engineering	15.000	4.094
Drainage Scheme Verhar (ADP No.1636)(2020-21) (SDG#6)	Public Health Engineering	30.738	5.725
Tube Well Village Dhamboro UC Khokhrapar (ADP No.1725)(2020-21) (SDG#6)	Public Health Engineering	13.181	4.959
Recondition & Extension of Metalled Road from Kotri Kabeer Khan Wahan Road to Village Madd Koondhar Taluka Mehrabpur, Construction of Road from Naushero Feroz Padidan to Village Mevo Kalhoro and Widening & Repair of Road from New Sabzi Mandi to Railway Phatak.	Rural Development	24.000	12.000
Construction of Road from Shahpur Chakar-Maqsoodo Rind Road to Village Mehrab Rind Taluka Shahdadpur and Construction of Road for Village Ali Hassan Chandio Deh Mano Chandio.	Rural Development	15.000	7.500
Construction of Link Road from Shahpur Chakar Sarhari Road to Village Badal Machhi.	Rural Development	10.000	5.000
Construction of Road from Village Rasheed Khan Laghari to Goth Taj Muhammad Laghari via Shafi Muhammad Laghari, Umer Laghari, Hashim Laghari and Construction of internal street Roads with Paver Block at Village Ghulam Qadir Narejo.	Rural Development	20.000	10.000
Construction of Road from Main Shaikh Bhirkioy Road to Mukhan Morri via Buksho Leghari to Link Road Village Urs Talpur via Gothana Minor side UC Tando Mari.	Rural Development	20.000	10.000
Construction of Road from Jivan Mirbahar to Khatian Station Link Road UC Narejani.	Rural Development	20.000	10.000
Construction of Road from Mahfouzabad (Mirjee Kahee) to Mir Mahmood Talpur Link Road Tando Muhammad Khan, Tando Fazil Road UC Halepota.	Rural Development	20.000	10.000
Construction of Road from Mian Shaikh Bhirkioy Road to Village Ahmed Jakhro via Village Tahro khan Mari UC Chukhi / Tando Mari.	Rural Development	20.000	10.000
Construction of Road from Link Road Muhammad Thebo to Khari Mir Khadim Hussain via Haji Bux Ali Tangri.	Rural Development	20.000	10.000
Reconditioning of Road and Retaining Wall from Indus Highway to Watio Khoso Road and Improvement of Road from Indus Highway to Village Khudad Pathan.	Rural Development	20.000	10.000
Construction of Road Chaho Khatan to Digach via Vagoondar UC Sarhore, Taluka Kaloi.	Rural Development	25.000	12.500
Construction of Metalled Road from National Highway to Village Khanpur and Construction of Road from Village Danwaro to Village Waryo Phulpoto.	Rural Development	25.000	18.750

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Construction of Retaining Wall i/c Culvert of Sim Nala & Providing / Fixing of C.C Paver Block Pavement and Fiber Glass Shade at Ganj Shaheedan and Mazar Ali Haider Shah Luqman.	Rural Development	10.000	8.750
Construction of Road from Village Kangro Shabani to Umaid Ali Lodro UC Juna and Construction of Road from Village Moula Bux to Imam Bux UC Baiji.	Rural Development	20.000	15.000
Reconditioning / Construction of Link Road from Village Naseer Khan Bhangar to Village Sardar Umar Daraz Bhangar, Taluka Thul.	Rural Development	10.000	8.750
Construction of Road from village Ali Bux Murghan Road to Haji Moosa Khan via Haji Sukhio Khan village, Taluka Ghorabari, District Thatta.	Rural Development	10.000	5.000
Construction of Road from Dondari to village Haji Allah Bachayo Jat, Taluka Ghorabari, District Thatta.	Rural Development	10.000	5.000
Construction of CC Paver Block Pavement & Open Surface Drain at Village Aghamani and Balishah Taluka Mehar.	Rural Development	10.000	5.000
Construction of Open Surface Drains i/c CC Topping / Paver Block at Village Chhatan Shah, Shah Muhammad Junejo and Saleh Khaskeli, Taluka Kingri, Village Morio Narejo and Wad Pagia Taluka Sobhodero & Gambat.	Rural Development	25.000	18.750
Renovation / Rehabilitation of Circuit House Jacobabad	SGA&CD	25.374	13.149
Youth Skill Development Programme, Phase-II	Sports & Youth Affairs	30.000	26.250
YOUCAN Programme (Youthcan)	Sports & Youth Affairs	20.000	10.000
YOUCAN Programme (Youthcan)	Sports & Youth Affairs	20.000	10.000
Boring & Installation of 150 Nos Tubewells on Solar Energy for Assured Supply of 100 cusecs for Thar Coal from LBOD Spinal Drain RD-362 (Revised on 08.11.16)	Thar Coal Infrastructure	1936.266	33.528
Alternate Arrangement Water Supply for Thar Coal Field Block - II @ Vajihar (From Makhi Farash Link Canal)	Thar Coal Infrastructure	348.180	83.280
Dualization of Hyderabad to Tando Muhammad Khan (33.00 Kms) (Revised) (SDG # 9)	Works & Services	4540.105	349.235
Widening / Reconditioning of road from Dilmurad Railway Station to Manjhipur via Karim Bux (28.00 Kms) (SDG # 9)	Works & Services	595.264	340.064
Widening / Reconditioning of road from Bosan to Miranpur Buriro via Dodapur (24.00 Kms) (SDG # 9)	Works & Services	521.185	369.372
Reconditioning of link road from Moro Bandhi road to village Qamaruddin Chandio to Morcho road mile 0/0-4/4+258' (7.28 Kms)	Works & Services	66.273	0.001
Reconditioning of road from Daur - Moro road to village Haji Noor Muhammad Dahri via Ajjazabad road (4.00 Kms)	Works & Services	46.476	0.001
W/R Construction of Circular road from Nawabshah-Jam Sahib road to Dargah Jam Datar Town 0.00-10.00 Kms	Works & Services	315.266	0.001
Reconditioning of Thull - Tangwani road (14.00 Kms)	Works & Services	174.106	143.763
W/R Construction of road from N.H.way Amri Kazi Ahmed road to connect N.H. way at Tremore via include links Jado Joono, Chhatoo Khoso, Model village Saleh Shah, Lakhaat & other roads 0.00-40.00 Kms (with asphalt surface)	Works & Services	678.762	0.001
Construction / Reconditioning of road from Hayat Pitafi road via Miani Sharif, Donkey & Donkey Pull via Jamsheed Bozdar connect Masan Hayat Pitafi & Kamal Mashori Pitafi Kamal Mashori (19.00 Kms) (SDG # 9)	Works & Services	160.787	9.078
W/R of road from N-55 Jail Chowrangri to Mari Chowk via Shahi Bagh and approach to Court Complex at City Shikarpur 7.0km	Works & Services	165.277	54.716
W/R of Mithi to Diplo road (39.20 Kms) (SDG # 9) (UR Rs. 2085.065 million)	Works & Services	1517.601	138.201
Reconditioning of road from Son Wah to Chakar Khan Bagdar via Qaim Khan Wadhyo (18.00 Kms)	Works & Services	175.853	135.853
Reconditioning of road from village Samandar Gopang to village Shahbaz Seelro (8.60 Kms)	Works & Services	76.254	58.754
W/R of road from Sanhra Machi to Police Picket Post village Bosan, including approach to village Imam Bux Langah - Wassayo Bhutto road (6.00 Kms)	Works & Services	101.976	78.227
Reconditioning of link road from Naudero-Sukkur road @ Point Jat Bhutta Stop to Mubarak Jeho i/c M. Structure (4.80 Kms)	Works & Services	80.710	59.461
Reconditioning of road from Moen-Jo-Daro Airport road Bagi Bridge to village Ghulam Hussain Butt via Karani road (i/c M. Structure)	Works & Services	80.413	60.413
Reconditioning / Construction of link road of village Masoodero and village Muhammad Sharif Jalbani @ village Mir Muhammad Jalbani (3.40 Kms)	Works & Services	60.191	46.441
Reconditioning of road from Garhi Khuda Bux Bhutto Saidudero road to Dhamrah Mahota via village Kubro, village Sanwan Khan Gopang (Gulsher Gopang) & Wandh Khuda Bux Bhutto (5.00 Kms)	Works & Services	79.624	59.624
Reconditioning / Construction of road from Raharki Seedpur road at village Lal Bux Mirani i/c link road Mohammadpur road mile 0/0-6/2 (8.50 Kms)	Works & Services	127.744	98.517
W/R of road from Reti to Daharki Taluka Ubauro (4.00 Kms)	Works & Services	69.546	53.358
W/R of road from Old Keenjhur to Yaro Lund via Bari Adda, Taluka Daharki (11.00 Kms)	Works & Services	187.014	140.764

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Reconditioning of road from Gulo Pitafi Chowki to Meer Mor approach village Gulo Pitafi, Taluka Mirpur Mathelo	Works & Services	107.744	80.494
Reconditioning of road from Lohi Pull to village Roshan Shar, Taluka Daharki (8.50 Kms)	Works & Services	91.188	67.813
Reconditioning / Construction of road from Kori Khooh to village Dino Mako via village Kamal Khan Mahar, village Esso Soomro, village Sardar Muhammad Bux Khan Mahar, Deh Khansar (9.00 Kms)	Works & Services	98.115	74.213
Reconditioning of road from Adilpur to Qazi Badal (14.00km)	Works & Services	195.746	148.977
Rehabilitation / Widening and Reconditioning of road from Dhandi to Sultanpur via Bhatti Chowk (8.00 Kms)	Works & Services	99.807	74.807
Rehabilitation / Construction of road from Dodanka to Arore Bachal Shah road @ Thariri village (6.50 Kms)	Works & Services	96.678	84.178
Rehabilitation / Reconditioning of road from Hakra Panhwr Chowki to Bhiro (10.00 Kms)	Works & Services	96.210	71.210
Reconditioning of road from Mohalla Ali Cheechro road to Mahesro Wah via Moli Dino, Motu Mirbahar, Mehar Mirbahar, Jado Indhar, Ahsan Khokhar and Muhammad Sachal Mallah, Gul Hassan Gamb enclosed various links (6.00 Kms)	Works & Services	94.648	69.648
Reconditioning of road from Haleji Dhandi Road to Wagah Chowki, Qasi Wah road via Qadu Indhar, Shahmir Indhar, Fateh Mohammad Bado Shar, Arib Wagho and Haleji link, Allah Yar Indhar, Jalal Goth Parallel to Thath Minor and enclosed various links (7.00 Kms)	Works & Services	93.293	68.293
Reconditioning / Construction of road from Rojho Mahesro Main Chowk road to village Jalal Indhar via Adam Gopan, Allah Diyayo Malano, Wali Mohammad Arain enclosed various links (8.75 Kms)	Works & Services	96.995	71.995
A) Rehabilitation of road Salehpat Sikandarabad to village Wadero Allah Jurio Bhanbhro, Dinal Mallah and Ali Dost Bhanbhro (4.00 Kms) B) Rehabilitation of road Salehpat Sikandarabad to Arore Bachal Shah road via Channel RD-186 Bridge Nara Canal (4.00 Kms)	Works & Services	87.512	62.512
Reconditioning of road from NHA Halani to Khanwahan (9.50 Kms)	Works & Services	129.992	97.492
Reconditioning of road from Halani to Tando Gul Shah (i/c various approaches) (13.00 Kms)	Works & Services	130.666	98.166
Reconditioning of road from Bharya City Bypass to Tharushah (7.75 Kms)	Works & Services	110.323	96.573
Construction/Reconditioning of road from Mohabat Dero Jatoi Road to Pir Qadir Bux Shah via Allahdad Tanwari (i/c various approaches) (8.50 Kms)	Works & Services	79.285	59.285
Reconditioning / Construction of road from Mango Road to Jalbani Minor via Belawah, Taluka Bhiria	Works & Services	147.227	109.727
Reconditioning / Construction of road from village Abdul Raheem Keerio to Chaheen Suleman via Panwari, Taluka Bhiria (11.50 Kms)	Works & Services	114.508	99.508
Reconditioning of road from Railway Phatak Mehrabpur to Pir Wassan connect to Mehran Highway @ Pir Wassan, Taluka Mehrabpur = (13.50 Kms)	Works & Services	128.260	95.760
Reconditioning of road from Tharushah Mithani road to Fazul Mohammad Motomal via Moosa Siyal road (5.00 Kms)	Works & Services	49.893	37.393
Reconditioning of road from National Highway to Chuttal Rajper, Adh Khahi Mahi Waggan, Naik Muhammad Mooro, Tagar road, Khoro Shareef, Tharushah to Bhorti (14.50 Kms)	Works & Services	119.876	104.876
Reconditioning of road from Naushehro Feroze - Mithani road to village Niaz Ali Mashori, Pir Juman, Haji Sain Rakhio Chandio, Ameer Bux Mari, Moro road to Late Chandio (10.00 Kms)	Works & Services	78.615	58.615
Reconditioning of road from Naushehro Feroze - Padidan road to Dangeja, Dr. Kamil Rajpar, Nawab Khan Mari, Indus Highway to Khaliq Rajpar road (10.00 Kms)	Works & Services	81.575	61.575
W/R of road from Dejarja to Chowdagi (with Asphalt) (11.50)	Works & Services	204.421	155.912
Reconditioning / Construction of Road from Qamar Din Chandio Morcho via Dewan Ja Karia upto Moro Bandhi road (10.00 Kms) (1-1/2" Carpet with Paver)	Works & Services	81.878	72.278
Reconditioning of road from Moro - Dadu road to village Jadal Shah 1-1/2 " Carpet With Paver (6.00 Kms)	Works & Services	65.635	48.885
Reconditioning / Construction of road from Daur Open Phattak @ Kothri Stop to Kari Mori via village Zawar Loung Khan Gorchani road mile 0/0-3/6 (6.00 Kms)	Works & Services	81.185	60.035
Widening / Reconditioning / Construction of road from Varr Stop to Connect Nawabshah - Ghupchani Shakal Jamali road via Khando Stop, Dost Pir, Hassan Jamali & Baksho Jamali (15.00 Kms) (with 5 cm Thick Asphalt Surface)	Works & Services	239.600	180.972
Reconditioning of road from National Highway to Mir Khan Pakhrio via Hanif Chandio and Nagar Khan Chandio road (6.60 Kms) (with 3.80 cm Thick Carpet with Paver Machine)	Works & Services	65.726	49.726
Reconditioning of road from Daur - Kazi Ahmed road to connect Nawabshah - Naushahro Feroze road @ Basham Rind along Sim Nala road (5.00 Kms) (With 2" Thick Asphalt)	Works & Services	58.292	43.541
Reconditioning of road from Workshop to Nawabshah road via Chak # 32, 62 Shafiabad, Chak # 74, Chak # 22 Alf road (20.00 Kms) (With Paver Carpet 1-1/2") (in portion)	Works & Services	198.703	149.953

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Reconditioning of road from Sinjhora to Baig Stop via Jaffer Khan Leghari road mile 0/0 - 9/3 (15.00 Kms) (in portions) (With Paver Carpet 1-1/2" )	Works & Services	50.272	37.647
W/R / Construction of road from Perumal More to Tando Mitha Khan via Perumal road mile (16.40 Kms) (Phase-I)	Works & Services	498.314	73.314
Improvement of road from Oderolal to Shahdadpur (From Oderolal to Mulla Mukhan road) (9.00 Kms)	Works & Services	168.111	16.881
Reconditioning of Circular road around Tando Adam (Northern Side) (Tando Adam Shahdadpur road to Tando Adam Berani road via Tando Adam Branch) road mile 3/2+330 - 5/5 =3.70 Kms (2" Asphalt Surface) (18' Width)	Works & Services	80.313	60.313
W/R of road from Shahdadpur City to UC Maldesi (18ft road) (with Asphalt Surface) (10.40 Kms)	Works & Services	198.163	19.816
(A) Reconditioning of road from Head Jamrao road Gujri to Chak No.71 road mile 0/0 - 7/4 = (12.00 Kms) TST 12' Width (B) Reconditioning of road from Sanghar Nawabshah road Kundho to Chak No.70 Chak No. 66 via Chak No. 5 road mile 0/0 - 9/3 (15.00 Kms) (1-1/2" thick Carpet Paver) (12' Width) (C) Reconditioning of road from Sanghar Head Jamrao road to link road Chak No. 19 Chak No. 21 Dr. Muhammad Sharif Khaskheli road mile 0/0 - 3/6 = (6.00 Kms) TST 12' Width	Works & Services	260.255	199.817
(A) Reconditioning of road from Khipro to Khahi via village Ismail Chanhio road mile 0/0 - 8/2 = (13.20 Kms) (TST 12' Width) (B) Reconditioning / Construction of road from Khipro Khahi road to Khipro Ghulam Nabi Shah Road via village Haroon Samejo road mile 0/0 - 3/2 (5.20 Kms) (TST 12' Width) (C) Reconditioning of road from Khahi to Dolatabad road mile 0/0 - 3/6 (6.00 Kms)	Works & Services	142.916	107.716
(A) Reconditioning of link road from Khipro Khahi road Khipro Phullahdiyoan road via Dargah Manthar Faqir road mile 0/0 - 3/1 = (5.00 Kms) (TST 12' Width) (B) Reconditioning / Construction of link road from Nangna road to Miandad Bhanbhro road via Dargha Ubhando Faqeer road 0/0 - 3/1 (5.00 Kms) (TST 12' Width)	Works & Services	73.300	54.300
Improvement / Widening & Reconditioning of road from Bhudho Chandio to Mulla Makhan (with Asphalt) (9.00 Kms)	Works & Services	170.723	17.073
Improvement / Widening & Reconditioning of road from Tando Adam Landhi road to Shahdadpur Sanghar road via Tayyab Thahim and Yar Muhammad Thahim road mile 0/0 - 1/6 = 2.80 Kms (2" Asphalt Surface 12' to 18' width)	Works & Services	50.456	37.956
Repairing of Circular Road from Tando Adam Oderolal road to Tando Adam Shahdadpur road via Tando Adam Bhit Shah road 0/0 - 3/2+330 = 5.30 Kms (2" Asphalt Surface)	Works & Services	89.405	66.905
W/R of Sarhari to Gupchani road mile 0/0-4/4 (7.20 Kms) (18ft) ( 1-1/2" Thick Carpet)	Works & Services	109.825	82.325
W/R of Golo Pir Mori road to village Sultan Mallano road mile 0/0-1/7 (3.00 Kms) (12 to 18 Width) ( 1-1/2" Thick Asphalt Surface)	Works & Services	64.172	48.047
Reconditioning of road from Chowdagi to Sarhari road mile 0/0-5/6 (9.20 Kms) (1-1/2" Thick Asphalt Surface 18' Width)	Works & Services	126.585	12.659
Reconditioning / Construction of road from Nawabshah - Sanghar road to village Rasool Bux Dahri via Qubba Shahdad Road mile 0/0-5/0 = 8.00 Kms (1-1/2" Thick Carpet)	Works & Services	81.585	62.835
Widening / Reconditioning of Sinjhora Khadro road mile 0/0-5/0 @ Dhanda Mori (8.00 Kms) ( 1.5 inches Thick Asphalt 12' to 18' Width)	Works & Services	112.617	12.275
Widening / Reconditioning of Sinjhora Khadro road mile 5/0-10/0 = 8.00 Kms (1-1/2" Thick Asphalt Surface 12' to 18' Width)	Works & Services	111.876	85.626
Reconditioning of road from Sindhri Khipro road to Shakir Shaheed road (with Asphalt) (4.40 Kms)	Works & Services	49.633	36.976
Reconditioning road from Mirpurkhas - Umerkot road @ 78 Mori to Jhillori road (with Asphalt) mile 0/0-6/2 (10.00 Kms)	Works & Services	105.804	92.028
Widening / Reconditioning of road from Muhammad Hashim Bhurgri to connect Kot Ghulam Muhammad (with Asphalt ) (7.00 Kms)	Works & Services	123.332	93.895
Improvement of road from Soofi Fakir to Dhoronaro Road 8.00 Kms	Works & Services	99.270	74.220
Improvement of road from Shadi Palli Pithoro road 8.00 Kms	Works & Services	99.199	73.999
Construction / Improvement of road from Umerkot to Kunri via Diggu / Gapno Phase-II (18.40 Kms)	Works & Services	185.954	90.504
Improvement of road from Umerkot - Bodar to Point Bund Stop to More Jhango via Monium Palli, Hashim Palli and Karo Palli (6.50 Kms)	Works & Services	55.160	42.610
W/R of Dhoronaro to Nohyoon road via Sadher (14.40 Kms)	Works & Services	285.697	169.447
W/R of road Chhore Bypass from Foji Chowk to Railway Phatak (3.63 Kms)	Works & Services	99.428	74.428
Reconditioning of road from Chhore - Umerkot road to Ahori Farm, Morand Pattu, Muhammad Hassan Mari, Mahar Ali Mari to connect Umerkot Dhoronaro road (14.60 Kms)	Works & Services	150.639	64.139
Reconditioning of road from Nabisar road to Nohto (10.00 Kms)	Works & Services	97.603	72.366
Reconditioning of road from Kunri to Nabisar road (Phase-II) (8.25 Kms)	Works & Services	114.841	88.161
W/R of road from Faqeer Nazar Pump to Bostan (4.22 Kms)	Works & Services	88.536	67.864
Reconditioning of road from Samaro Kunri road @ Toban Shakh to Manjhakar (6.40 Kms)	Works & Services	54.171	41.615
Repair and Reconditioning of road from Baloch Chowk (Badin-Mithi Road) to Kaloi Town (3.50 Kms)	Works & Services	52.055	39.555

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Reconditioning of link road from Jamal Hajano road to village Maari Muhammad Khan road (7.20 Kms) (with Asphalt)	Works & Services	83.693	62.993
Reconditioning of link road Chamber road Bukera road, Mirwah road, Nasarpur road i/c approaches Shafi Pitafi, Nagori Plot mile 0/0-2/4+330 (4.20 Kms)	Works & Services	100.000	75.000
Reconditioning Tando Adam road to village Suleman Palli, village Mitho Mirjat, village Ibrahim Shah, village Madan Mirjat, village Ghulam Nabi Shah, village Khair Shah via Pannah Shah road approach Barecha mile 0/0 - 7/4 (12.00 Kms)	Works & Services	100.000	75.000
Widening & Reconditioning of road from Dumbalo to Chhato Mori mile 0/0-3/0 (4.83 Kms)	Works & Services	121.900	91.223
Improvement of road from Matli Tando Ghulam Ali at mile 3/7 Saleh Soomro Bagh to Haroo Talpur (9.65 Kms)	Works & Services	99.782	74.745
Improvement of road from Chhato Mori to Rajo Khanani Degri road via Ghulam Muhammad Arain mile 0/0-7/0 (11.26 Kms)	Works & Services	124.660	93.430
Improvement of road from Bhugra Memon to Dargah Shaikh Kariyo via Model village Golo Mandhro and Roopa Mari (7.50 Kms) (Phase-I)	Works & Services	104.620	29.640
Improvement of road from Kario Ghanwar i/p T.M.Khan Sim Nala to 70 Mori (9.40 Kms)	Works & Services	96.483	21.488
Improvement of road from Shadi Large to Signal Chak 20.00 Kms and Qabili Chak Taluka Tando Bago (8.80 Kms)	Works & Services	96.413	71.440
Improvement of road from Ali Bandar road to village Pagaro Ghulam Rasool Chandio via General Sir Anjam (8.80 Kms)	Works & Services	96.554	71.564
(A) Improvement of road from Matli Tando Ghulam Ali at mile 2/1 Jara Water Stop to Mara Wah mile 0/0-4/3 (7.00 Kms)(B) Improvement of road from Hyderabad - Badin at mile 25/0 Baran Mori to Shanani Mori mile 0/0-1/3 (2.21)	Works & Services	124.240	92.990
Improvement / Construction of Road from Nawab Saifuddin Leghari to Peeral Mori via Tharoo Dull mile 0/0- 3/1 (5.028 Kms)	Works & Services	114.710	24.765
Improvement of road from Rajo Khanani Talhar road to Mehro Bhurgari i/c link to Dewani Faqeer (10.00 Kms)	Works & Services	99.750	74.750
Improvement of road from Saeedpur to Dabahro (11.66)	Works & Services	99.590	74.590
Improvement of road from Dabahro to Ghulam Shah i/c link to Khadaro (12.06 Kms)	Works & Services	99.810	74.810
Improvement of road from Tando Bago Talhar road to Shah Turail road i/c Mirzo Dalwani (12.06 Kms)	Works & Services	99.950	24.950
Improvement / Construction of road from Tando Ghulam Ali road to Arab Khaskheli i/c link to Jani Jalalani & Umer Jaskani Mile 0/0 - 6/0 (9.66 Kms)	Works & Services	96.100	83.600
Improvement of road from Khorwah to Mirpur Bathoro road (7.00 Kms) (12ft to 18ft) (With 2" Asphalt Concrete)	Works & Services	135.220	34.415
Improvement / Construction of road from Khorwah - Mirpur Bathoro road at point 4.00 Kms (Ghungro Sim Nala) to village Haseeb Lashari & Qaim Khan Rind (5.00 Kms) (12ft) (With 1-1/2" Thick Permixed Carpet)	Works & Services	77.441	55.541
Improvement / Construction of road from Badin - Sujawal road at Buxal Brohi to Chak No. 22 via village Ramzan Lund. Allah Bachayo Mallah, Parsoo Kolhi, Ali Hassan Nohrio, Muhammad Khan Brohi, Hassan Chandio (16.00 Kms) (12ft) (With 1-1/2" Premixed Carpet)	Works & Services	255.870	48.596
Reconditioning of link road from Bathoro Sujawal road Dari Mori to Village Jar i/c Links (7.00 Kms)	Works & Services	70.000	52.500
Maintenance & Rehabilitation of Inter-City Road / Streets of Taluka Mirpur Bathoro (7.00 Kms)	Works & Services	69.933	52.433
Rehabilitation / Construction of road from Shahpur to Dhandhari via Udasi road (6.20 Kms)	Works & Services	68.571	51.425
Improvement of Road from Thatta - Hyderabad National Highway to village Raju Nizamani (5.00 Kms)	Works & Services	50.421	37.811
Widening / Reconditioning of road from 105 Mori via Maher Mitho Shaikh to connect Gharo Keti Bunder road	Works & Services	449.885	37.385
Reconditioning of road from Baghan -Keti Bunder road to Sadar Bridge (4.50 Kms)	Works & Services	49.984	37.484
Improvement of road from Main Road Khuda-ke-Basti road to Garaho Goth via Main Bazar Bihar Colony & various streets (5.00 Kms) i/c M/S	Works & Services	50.160	43.910
Improvement of road from Khuhara Rice Mill to Taluka Hospital via Tower Chowk Mehar City i/c Drain (3.00 Kms)	Works & Services	97.882	72.882
Rehabilitation of road from Indus Highway to Bughia Service Goli Marr road i/c Drain & Meer Hassan Chowk to K.N Shah Bypass along Paving Blocks Both Side of road	Works & Services	99.533	74.533
Improvement of road from Kakar Piaro road to Muhab Ali Junejo via Andryan Taga & Danger village road ( 10.66 Kms)	Works & Services	99.276	74.276
Construction / Improvement of road from Sita Piaro road to Hussain Arain via Ameer Bux Khoso village i/c Phatak to Gorar Street & Bundo Chowk to Prechared Canal & Memon Muhalla School to Prechared Canal (4.80 Kms)	Works & Services	98.136	73.136
Improvement of road from Mehar Gahi road to village Mangwani via Raza Mohammad Rind connecting village Khondi & village Qazi Arif mile 0/0-7/4 in portions connecting villages mile 0/0-2/4 i/c Masonary Structure	Works & Services	98.309	73.309

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Improvement of road from Indus Highway to village Poracho connecting village Mubarak Khoso mile 0/0-2/2 connecting mile 0/0-3/0 i/c Masonary Structure	Works & Services	47.307	34.807
Improvement of Road from Indus Highway Baridarao to Bothro i/c Construction of road village Jani Chandio Kamalpur UC Bothro (17.70 Kms)	Works & Services	99.008	74.008
Improvement of road from Indus Highway to village Rais Ali Bux via Khondi (10.00 Kms)	Works & Services	97.809	72.809
Improvement of road from Shah Panjo Phattak Kisho Chandio road to Mehar Aghamani road link to Bali Shah Masonary Structure (10.00 Kms)	Works & Services	98.153	73.153
W/R of Road from Phuliji Dawach Road to L.S Bund and Improvement of road from Phuliji Dawach road to village Piaro Arain via village Pir Tarho via village Qazi Pir Muhammad via village Sher Muhammad Dawach and village Lashkari Brohi and Construction of Paving Block / Drainage of above mentioned villages (7.86 Kms)	Works & Services	99.860	74.860
Improvement / Construction road from Luwari Shreef to connect Kadhan Seerani road via village Ishque Samoon (10.00 Kms) (Phase-I 0.0-6.0 Kms)	Works & Services	100.000	25.000
W/R of road from Shahdadpur to Gupchani road mile 0/0-19/3 (31.00 Kms)	Works & Services	957.450	838.964
W/R of road from Shahdadpur to Khadro via Barhoon road @ mile 3/2 + 440-17/5 (23.00 Kms)	Works & Services	554.874	486.212
Reconditioning of road from Gharo Ketu Bunder road @ Sakro Branch to village Khair Muhammad Rind, Lal Muhammad Rind, (8.00 Kms)	Works & Services	149.032	37.258
Reconditioning of road from Baghan to Jeety Kharo Chaan via Sajawari (25.00 Kms)	Works & Services	428.187	366.374
W/R of Jhudo Nabisar road (18.00 Kms)	Works & Services	679.551	593.542
W/R of road of Samaro Kot Ghulam Muhammad road (15.40 Kms)	Works & Services	758.894	664.981
W/R of Samaro Umerkot road Mile 0/0 - 24/7 (40.00 Kms)	Works & Services	1745.963	1529.930
Dualization / W/R of road from N'shah Sanghar road to connect 60th Mile Town (0.0-17.50 Kms)	Works & Services	847.289	742.437
W/R of road from Kadhan to Ali Bandar road 25.74-44.25 Kms + 18.50 Kms	Works & Services	666.451	583.978
W/R of road from Tando Bago Jhudo road from 4.40 - 40.0 = 35.00 Kms	Works & Services	1360.624	1192.247
Improvement of road from Naukot to Nabisar via Noohato mile 0/0-27/4 (44.00 Kms)	Works & Services	1076.447	934.237
Improvement of road from Naukot Mithi road to Sufi Lachman Das mile 0/0 - 3/1 (5.00 Kms)	Works & Services	147.741	73.871
Widening / Reconditioning of road from Naukot Mithi road to Piloro Stop (20.00 Kms)	Works & Services	760.637	666.509
Reconditioning / Construction of various roads in UC's of Bet Mahar, Ketu Bandar, Bhagan Mehal Buhara, TC Garho, Maher, Ginnar and Indo (31.80 Kms)	Works & Services	500.000	438.125
Reconditioning / Construction of various roads in UC's of TC Ghorabari, Jaradali, Khan, Gulel, Doomani, Juna, Ghulamullah, Karampur and Kaghan (32.80 Kms)	Works & Services	491.148	491.148
Construction of link road from Ghazi Khan Hingorjo - ADP road to village Tar @ Mile 0/0-8/1 (13.0 Kms) (Revised)	Works & Services	257.206	114.513
Construction of Mirpurkhas By pass road connect Hyderabad road Tando Adam road Khan road and Sindhri road with over head bridge near Ratanabad Road Mile 0/0-11/0 (M) = 17.7k	Works & Services	248.017	0.001
Construction of Dualization Tando Allahyar Bye Pas road (Northern Side) (6.40 Kms) (Modified) (SDG # 9)	Works & Services	1346.679	675.799
Construction of road from Larkana Kamber road @ Point Railway Phattak to connect Kamber Wagan road mile 0/0-3/5 (5.83 Kms) (SDG # 9)	Works & Services	348.198	142.729
Construction of road from Mithi to Trighatio (Tagai via Godhgar & Mahayari mile 0/0-31/0 = 31-0 (M) = 50.0 Kms (Revised)	Works & Services	1014.062	352.764
Construction of road from Indus Highway to Connect kandhkot Thull road along inspection Path of Shran Minor & Soon Wah (15.00 Kms) (SDG # 9)	Works & Services	176.281	128.281
Construction / Improvement of various roads in District Jamshoro (42.10 Kms) (SDG # 9)	Works & Services	507.255	115.749
Construction of Additional Carriageway of Larkano Naudero Road mile 3/1-11/0 (12.70 Kms) (I/C M.Structure)	Works & Services	763.146	0.001
Construction / Reconditioning of various roads in District Larkano (14.10 Kms) (SDG #9)	Works & Services	141.813	107.439
Construction of link road from Kamber-Shahdadkot road to village Chibar Khan Magsi along Warah Canal mile 0/0-3/3 (5.40 Kms) UC Mastoi Taluka Miro Khan (SDG # 9)	Works & Services	69.728	0.001
Construction / Reconditioning of road from Mouladad road to village Sharbat Mundrani via Ali Hassan Jakhriani, Abdul Rasheed, Mir Khalid Nawaz, Ali Hassan, Sohrab Khan Jan Jakhriani (11.00 Kms)	Works & Services	116.933	86.933
Construction / Reconditioning of road from Thul Bahoo Khoso road village to Sardar Khan Nindvani via village Haji Faiz M. Khoso, village Hafiz Ali M. Khoso, village Haji Jaffar Sundrani, village Mandov Marheta, village Arsalah Jakhriani, village Raza M. Tanvri, village Usman Marheta, village Jan M. Kandran, UC Tajo Khoso, UC Maloi, Taluka Thull	Works & Services	99.858	75.108
Reconditioning of road from Thull Bahoo road to Allahabad (Manjhipur) via M. Ayub Khoso, Abdul Qadir Brohi, Muhammad Yousif Khoso, Idressabad, M. Pannah Khoso, Payaro Khoso (8.00 Kms)	Works & Services	70.682	53.182

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Construction / Reconditioning of road Nasir Muhammad Brohi (Jam Khan Khoso) to village Dr. Abdul Jabbar Khan Khoso via Zulfiqar Goloo / Lutufabad / Anisabad / Zarak Brohi / Juman Shah / Nizam Mastoi / Abdul Ghani Khoso and village Ghunci (5.00 Kms)	Works & Services	58.781	43.781
Construction of road Paver / Tuff Tile at various streets of Jacobabad City Taluka Jacobabad	Works & Services	120.000	105.150
Construction of road from Shahghazi road village Babu Bhangar (6.25 Kms)	Works & Services	70.000	52.500
Construction / Reconditioning of road from Thul road Laahi Charhi to via village Nasar Muhammad Brohi / village Jaam Khan Khoso / Village Shahnawaz Diyo / Budho Diyo / Village Ghous Bux Mastoi and Meral Purano at Jacobabad (3.00 Kms)	Works & Services	60.474	45.474
Construction of road UC Bahadurpur village Shahzaman Khoso / Village Shah Murad Brohi / Village Muhammad Brohi / Village Muhammad Khan Khoso / Village Gulab Banglani / Village New Karachi / Village Shoukat Banglani	Works & Services	48.732	36.356
Construction / Reconditioning of road from Mirpur Buriro upto Sanhri Sarak via village Shabir Buriro / Muhammad Ismail Buriro / Punhal Channa / Allah Wadhayo Channo / Galib Channo & village Sohrab Channo, Taluka Thull (9.00 Kms)	Works & Services	99.980	74.980
Construction of link road from Railway Phatak to G. Khairo Bypass via Seer with (Ring Band G. Khairo) Mile 0/0-3/1 (5.00 Kms)	Works & Services	128.940	128.940
Construction / Reconditioning of road from Mouladad road to village Ghaibi Khan Mundrani via village Noor Muhammad Jiskani, Pathar Mor, Bhooro Jakhriani, Janhwar Gulwani, Meva Gulwani, Dip village Pinya Sarghani, Sobha Jikhriani (10.50 Kms)	Works & Services	115.386	85.686
Construction / Reconditioning of road from Noor Wah Bridge to Thull Jacobabad road via village Mehran Brohi, Nepar Gorshani, M. Ayoub Unar \ Syed Zahir Shah, Habibullah Kehar, Raja Khan Khoso, Ashiq Ali Pathan, Zulfiqar Gorshani, Naseer Khan Khoso (10.00 Kms)	Works & Services	98.717	73.717
Construction of link road from Muhammadpur Bosan road to Ratodero Sher Muhammad Thahim road via Liaqat Sarghani, Zia Rehman Jakhriani, Ali Hassan Mari, Bhooro Sarghani, Dodo Rozrani (5.75 Kms)	Works & Services	74.774	55.524
Construction / Reconditioning of road from Kashmir Minor along Lachhi Wah and various villages upto Sui Line Purani road (8.00 Kms)	Works & Services	89.294	66.794
Construction / Reconditioning of road from Indus Highway Ali Gohar Brohi Petrol Pump to village Phero Arija, Mehmood Dero, Eidan Khan Brohi, Ghulam Ali Khauhawar, Khedkar, Noor Mohammad Korkani, Sache Dino Kalhoro, Mubarak Chandio, Lund, Kadero Mugheri, Sayed Sardar Shah, Tharo Khan Jagirani, Loung Mugheri approaches	Works & Services	153.251	118.251
Construction of road from New Bypass Larkana Miro Khan to Kamber, Mirokhan road (3.00 Kms)	Works & Services	179.153	156.878
Construction of road from Nara Bagh link road to village Dilshad Gadani (2.50 Kms)	Works & Services	31.496	23.667
Construction of road from Landiyoon Mahar Nonhdhi to village Kanbir Mahar (4.00 Kms)	Works & Services	51.379	38.467
Reconditioning of road from Mohdpur to Chak Shahbazpur Taluka Ubauro (12.00 Kms)	Works & Services	126.726	93.976
Reconditioning of road from Rati to Barota (8.20 Kms)	Works & Services	106.431	81.431
Reconditioning of road from Daharki to Barota (9.00 Kms)	Works & Services	108.284	83.284
Widening / Reconditioning of road from Daharki to Reti upto Narley Minor (6.00 Kms)	Works & Services	100.000	75.000
Construction of road from National Highway Mirpur Minor Inspection Path to village Noor Muhammad Chijjan, village Bangul Sial, Taluka Mirpur Mathelo (4.00 Kms)	Works & Services	50.586	37.461
Construction of road from FFC Maso Wah Bridge to Allah Diwayo Lashari approach to Sultan Lashari, Abdullah Malano, Allah Ditto Jalbani & Bagh Ali, Taluka Mirpur Mathelo (4.20 Kms)	Works & Services	65.334	50.334
Construction / Reconditioning of New Metal road from village Pathan Goth to Hekal Patt via Alam Toba Jeewan Garh road Gul Bahar Mangi (17.00 Kms)	Works & Services	250.010	191.712
Construction of road from Sardargarh Dahar Wah to Izzat Wari via Phullo Malik (10.00 Kms)	Works & Services	159.921	122.938
Construction of road from Baghsar road to village Jan Muhammad Mahar (8.00 Kms)	Works & Services	122.776	107.609
Construction of road from Murad Ghoto link road to Bakro Wah, Deh Hussain Beli (2.00 Kms)	Works & Services	25.137	18.848
Construction of road from Izzat Wari to village Kaman Mahar via Raza Muhammad Mahar and village Aleem Malik	Works & Services	111.690	84.877
Construction of Bridge Piling at village Lal Muhammad Mahar and connected road of various areas (6.00 Kms)	Works & Services	95.536	84.286
Construction of road from National Highway to Hussain Kalwar via Mehsro Wah (7.10 Kms)	Works & Services	76.985	59.485
(A) New Construction of link road Baga Khan Shambani to village Gaji Bux Shambani (5.50 Kms)	Works & Services	107.623	107.623
(B) New Construction of link road village Ghulam Sarwar Shambani to			

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Safar Shambani, Ghulam Shambani and Ali Gohar Shambani via Channel RD-186 (4.00 Kms)			
Construction / Reconditioning of Road Village Sultan Ahmed Siyal to Village Ali Muhammad Mubejo via Village Lahano Khan Siyal via Tatri Minor UC Bhanbhri and UC Dangeja (8.50 Kms)	Works & Services	97.215	72.215
Construction of Moro Mithani Road at point Manaheen to Village Gh.Hyder Kario via Seth Allah Warayo Behan via Muhammad Ismail Jesar via Koji Jesar via Golo Potho via Qadir Bux Lund via Dhani Bux Kario UC Manaheen and UC Daris Taluka Moro (14.50 Kms)	Works & Services	164.255	126.755
Construction of road village Tagar to Village Baloo Chandio via Umer Saihito via Sain Bux Chandio via Qasim Chandio, UC Detha (4.50 Kms)	Works & Services	50.860	38.360
Construction / Reconditioning of road from National Highway to Hashim Lanjar along Sehra Minor and protective bund crossing Trimor Sehra Branch Gumoo Mori (11.00 Kms)	Works & Services	125.306	95.306
Construction / Reconditioning of road from National Highway near Jam Noorullah to village Yaral Ghanghro (Malokani Ghanghra) along Gul Minor (6.80 Kms)	Works & Services	65.920	49.670
Construction of Road Ranjhan Khan Panhwar to Haji Saeed Khan Panhwar, Attal Bohio to Raham Ali Khoso Nim Wara Khoso, Naushehro Feroze road to Bagan Kalhoro (10.50 Kms)	Works & Services	122.704	107.704
Construction of Road from Sanghar Chotiaryoon Road to Link Road Kot Nawab Road to Gulzar Shar Road mile 0/0-5/5=9.00 KM (1-1/2" Thick Paver Carpet 12' Width)	Works & Services	99.921	76.484
Construction of Road from Mirpurkhas Road to Loharao via Gullan Khan Banbhro, Khuda Bux Chandio, Raja Bisharat Road mile 0/0-3/1 = 5.00 KM (With 1-1/2" Thick Carpet 12' Width)	Works & Services	55.724	43.036
Construction of Road from Toori Mori Road to village Mangal Khan Bugti via Ali Nawaz Shar, Akbar Chandio Samaro Minor Village Kondho Chandio Road mile 0/0-3/1=5.00 KMs (With 1-1/2" Thick Paver Carpet 12' Width)	Works & Services	65.704	49.704
Construction of Road from Baan Mori to Naukot from link road to Tamachi Wassan via Sain Habibullah Shah, Nobat Shar Road 0/0-3/3+330=5.50 KMs (With 1-1/2" Thick Paver Carpet 12' Width).	Works & Services	67.920	51.983
Construction of Road from Dhani Parto Rajpar to Qadir Bux Lohar Jhando Khan Kumbhar Allah Wassayo Bhatti Photo Khan Mari Stop to Samoon Deapar Hadi Bux Deapar Road mile 0/0-3/2=5.20 KMs (With 1-1/2" thick Paver Carpet 12' Width)	Works & Services	64.724	49.099
Construction of Road from Sanghar to Chotiaryoon road to Village Khamiso Laghari via Shah Baig Bakadar Bughti Qalandar Bux Lashari Naseer Laghari road mile 0/0-3/3+330 =5.50 KM (1-1/2" Thick Paver Carpet 12' Width)	Works & Services	68.015	51.015
(A) Construction of link road from Tayab Dars road to village Haji Noor Hassan Dars Moorhadi road 0/0-3/1=5.00 KMs (TST 12' Width) (B) Construction Of Link Road From Jamal Shah Road To Village Garhar Mori Via Dost Muhammad Moor Road 0/0-3/1 =5.00 Kms (With TST 12' Width)	Works & Services	97.023	74.273
Construction of New road from Mazar Khaskheli Road to Mushtaq Ahmed Bajwa via Hakim Magsi, Umardin Rajpoot, Ghulam Qadir Arain, Sidiq Jat, Shafiq Bajwa, Khadim Jat road mile 0/0 - 4/6 = 7.60 Kms (TST 12' Width)	Works & Services	70.379	61.629
Construction of road from Muhammad Hassan Makrani to village Haji Afzal Mehar Taluka Shujabad (5.60 KMS)	Works & Services	79.555	59.428
Construction of road from Siloor Mori to Adam Mori via Village Soomar Junejo, Taluka Jhudo (16.00 Kms)	Works & Services	198.285	143.285
Construction of road from Sattar Hotel to Jhulluri village Ch: Barkat Kolhi Colony, Sher Shah Mamora Khan Meo & Jhulluri (8.00 Kms)	Works & Services	95.102	60.102
Construction of road from Mirwah Digri Road Bandhi Shakh Stop to Village Mehran Khan Laghari U.C Kangoro, Taluka Digri (8.00 Kms)	Works & Services	98.057	63.057
Reconditioning / Construction of road Tedi More to Village Haji Niaz Muhammad Kapri Taluka Jhuddo (6.00 Kms)	Works & Services	50.233	37.733
Improvement of Road from Mirpurkhas Khipro road to Maghan More via Jhurbi (with Aphalt) mile 0/0-11/0 (17.671 Kms)	Works & Services	283.844	211.832
Construction of road Dengan Rasti to Pir Bux Dhonkai to LBOD Mori Ramzan Khoso to LBOD Mori Ubedullah Bhurgari (8.5 Kms)	Works & Services	93.666	68.916
Construction of road Alim Bhurgari to Noor Ahmed Bhurgari UC Ahmed Khan Bhurgari (8.00 Kms)	Works & Services	79.563	69.119
Construction of road Molvi Ibrahim Nohani Haji Siddique Khaskheli Molvi Abdul Hai Nohani (5.00 Kms)	Works & Services	47.628	35.203
Construction of road from Rano Solangi to village Qamar Din Shar via Kaloo Khan Lashari (5.00 km)	Works & Services	74.892	56.392
Construction of road from Dhalo jo Tar to Jetrar road (7.00 Kms)	Works & Services	154.062	134.812
Construction of road from Tar Ahmed to Samoon Rind via Umaid Ali Rind Faqir Tar (7.00 Kms)	Works & Services	112.000	84.000
Construction of road from Sakiryo Road to Piyaro Dal via Risham jo Tar Datar Dino Thebu (7.00 Kms)	Works & Services	112.000	84.000
Construction of road from Sohilo Sahu Sand Road to Danbhario via Sahu Sand (7.00 Kms)	Works & Services	112.000	84.000
Construction of road from Khenser to Graveyard Khansar (3.75 Kms)	Works & Services	55.967	41.967

Name of Scheme	Department	Estimated Cost	Allocation for 2022-23
Construction of Road Talo Jaam to Pabuhar via Balhiari, Jetria, Edri, Malkar (11.00 Kms)	Works & Services	216.670	162.503
Construction of Road from Sarah to Jahirmiryo (5.00 Kms)	Works & Services	110.096	82.571
Construction of Road from Lakhmiar to Nikno Bheel via Sange Jo Tar, Nau Tar, Chando Kolhi (10.00 Kms)	Works & Services	173.034	129.751
Construction of road from Ramlani to Allah Rakhe jo Par Waya Menhlani, Chaudio & Gaje Jo Par (11.00 Kms)	Works & Services	175.000	131.250
Construction of road from Shivo Charan to Tharo Rind & Karimdad Jo Tar	Works & Services	92.958	69.708
Construction of road from Jete Jo Tar to Khiyaro Nohri (6.00 Kms)	Works & Services	93.000	69.750
Construction of Road from Tugosar to Rinpario via Jethyar 5.50 Kms	Works & Services	99.950	74.962
Construction of Road from Soondar to Bhaki via Manserio, Gunga Veri, Soomrat 6.00 Kms.	Works & Services	99.943	74.955
Construction of Road from Sakrio to Umar Unar via Rawatsar 6.00 Kms.	Works & Services	99.967	74.971
Construction of Road from Sakrio to Kharuruo via Bisarnio 5.75 Kms	Works & Services	99.950	74.950
Construction of Road from Naryasar to Burtala via Ranpur 5.25 Kms	Works & Services	99.886	74.910
Construction of road from Chibhryal to Gangan 4.00 KM and Construction of road from Veenjhniyari to Batangari	Works & Services	148.330	111.205
Construction of road from Meenhoon Lanjo to Mohantar 4.00 Kms and Momin Mangrio to Megh Khawria(5.00 kms)	Works & Services	147.490	111.490
Construction of Road from Bitri Road to Khadhari (near Villages Roojhan, Charakharo, Thouharchaho, Sabankhoi Kehari) mile 0/0-4/2 (6.00 Kms)	Works & Services	99.825	87.347
Construction of Road from Diplo Badin Road to Hathni (Near Villages Darr & Wango Rahiman) Mile 0/0 - 4/3 (7.00 Kms)	Works & Services	99.837	74.877
Construction of Road from Abdullah je Wandh to Kathurio Saman & Kathurio Samejo via Karam Ali Saman, Bajhliar Katho Bheel, Katho Saman (6.50 Kms)	Works & Services	99.856	74.888
Construction of Road from Chhaho Rahiman to Turkini via Pireho, Phulano, Phulani (6.00 Kms)	Works & Services	99.808	74.853
Construction of Road from Village Kharo Bajir to Connect village Alamsar (6.80 Kms)	Works & Services	99.882	74.963
Construction of road from Mithi Islamkot bypass to village Beperboh Taluka Mithi (4.00 Kms)	Works & Services	94.867	71.141
Construction of road from Airport road @ Point Dhorio to Shivo Jo Tar	Works & Services	89.249	66.934
Construction of Road from Valasai Colony Kaloi Town to Mithi Badin Road	Works & Services	99.998	74.998
Construction of road from Pangrio Wango road to village Ibrahim Khaskheli via Choudhry Waseem i/c to link Salar Nahrio / Ahmedani village link to Bachal Khaskheli from Sono Jamali road 6.00 Kms	Works & Services	99.528	74.528
Construction of road from Badin Nindo road to Talho Khan Bhurgri, Otiya Rai Singh, Saeed Khan Bhurgri, Haji Abdul Karim Bhurgri i/c Mir Muhammad Rind, Zubair Rind, via Karo Wah connect Tando Bago Nindo road 6.15 Kms	Works & Services	99.856	74.856
Construction of various Metaled Roads in Taluka Sehwan & Manjhand District Jamshoro	Works & Services	172.292	128.542
Construction of road from Bhand Mari to Rais Ali Ahmed Chandio village via Maroof Ja Bhan, Gullan Ja Bhan mile 0/5-3/5 i/c Masonary Structure	Works & Services	54.262	41.762
Construction of road from Mitho Babar to Ibrahim Channa Village Bridge along Johi Barrage Path 0/0-5/1 (8.30 Kms)	Works & Services	99.823	74.823
Construction / Improvement of different roads of Taluka Tando Bago	Works & Services	987.027	493.514
Construction of road from Dhandari road to village Usman Lohar, village Malook Lakho, village Usman Otho, village Hashim Gujrio, village Wali Muhammad Jatt, village Qadir Palani, Dargah Ghulam Ali Shah and village Khair Muhammad Lakho (13.00 Kms)	Works & Services	313.797	276.348
Sindh Provincial Road Improvement Project Assisted by Asian Development Bank (328 Kms), ADB Assisted (Total Rs.22750.00 million (87% ADB Loan Rs.20670.10 million, 13% GOS Share Rs.2079.90 million) (SDG # 9)	Works & Services	2079.900	43.295
Construction of road from Nooriabad to Gujjo via Jung Shahi mile 2/4-39/0 (58.76 Kms).	Works & Services	161.193	2.523
Construction of Link road from S.B.A Choudhri Munawar (Bashir Ahmed Arain) road to village Muhammad Rafique Lahori and surrounding of various villages approaches road i/c 15 RFT Bridge 6.40 Km (2019-20)	Works & Services	79.285	0.001
Construction of Bilawal Bhutto Zardari Flyover Bridge Jail Phatak (Railway Crossing) Jacobabad (SDG # 9)	Works & Services	582.748	0.001
Renovation / Rehabilitation of Sindh House Islamabad (Re-revised) (SDG # 9)	Works & Services	497.834	87.094

# Annexure (D)

## LIST OF SPECIAL ASSIGNMENT SCHEMES IN FY 2022-23

ADP NO	Name of Scheme	Department / Sector	Location	Cost
570	Rehabilitation / Reconstruction & Provision of Missing Facilities in Existing GGSS / GGHSS Schools Bhiro Goth UC Thano (02 Units) (C:56.898 + R:3.000) (SDG#4)	Education (School)	Karachi (M)	59.90
571	Construction of Two Rooms New School Building for Shelterless Schools Taluka Khangarh (48 Units) (C:254.483 + R:23.616) (SDG#4)	Education (School)	Ghotki	278.10
573	Up-gradation of Middle School to High School at GBMS Sher Muhammad Thora (01 Unit) (C:18.484 + R:3.419) (SDG#4)	Education (School)	Matiari	21.90
574	Construction / Re-construction of Govt. Boys High School Mati City (01 Unit)	Education (School)	Badin	159.73
575	Construction of ECE Class Rooms / Rehabilitation / Up-gradation of Various Schools of UC 1 to 19 (SDG#4)	Education (School)	Karachi (S)	99.78
576	Construction of (Govt. Boys / Girls Secondary Schools) in Shirin Jinnah Colony Karachi (02 Units) (C:45.199 + R:2.00) (SDG#4)	Education (School)	Karachi (S)	47.20
577	Rehabilitation / Re-construction & Provision of Missing Facilities in GHS G. Jaffar (01 Unit) (SDG#4)	Education (School)	Khairpur	32.97
578	Rehabilitation of Government Schools of Taluka Kamber, Warah & Naseerabad (07 Units) (SDG#4)	Education (School)	Kamber	19.35
579	Rehabilitation & Provision of Computer Lab & Science Lab in GBHSS Mirpur Bathoro (SDG#4)	Education (School)	Sujawal	53.12
580	Rehabilitation & Provision of Missing Facilities in Existing GBHS Baberlo, GGHS Luqman, GBHSS Talpur Wada & GHSS Faiz Kotdiji (04 Units) (SDG#4)	Education (School)	Khairpur	65.91
581	Rehabilitation / Provision of Missing Facilities / Up-gradation of Schools of Taluka Garhi Yasin (08 Units) (SDG #4)	Education (School)	Shikarpur	51.92
582	Up-gradation of Middle School to High School (i) GBMS Vakryo (ii) GBMS Pabuvero & Up-gradation of Primary School to Middle School (i) GBPS Vee Hingorja (ii) GBPS Jaroombhar (iii) GBPS Aqib Junejo Taluka Islamkot & Chachro (05 Units) (C:80.660 + R:15.778) (SDG#4)	Education (School)	Tharparkar	96.44
583	Rehabilitation / Re-construction & Up-gradation of Government schools of District Karachi Malir (04 Units) (SDG#4)	Education (School)	Karachi (M)	121.01
584	Construction of Building for Shelterless Primary schools Hazoor Jami Rind UC- Hoat Faqeer, Abdul Ghani Brohi (Chakar Brohi Deh-54 Nusrat), Muhammad Uris Sehto UC-Obhari Sewari and Muhammad Ramzan Chandio UC-Jhuro Shar (04 Units) (C:16.862 + R:2.000) (SDG#4)	Education (School)	S.B.A	18.86
585	Rehabilitation / Re-construction and Up-gradation of Government School in Mulla Essa Goth, UC-38 (01 Unit) (C:52.430 + R:6.885) (SDG#4)	Education (School)	Karachi (W)	59.32
586	Rehabilitation / Re-construction & Provision of Missing Facilities in existing Government Schools District Karachi Malir (13 Units) (SDG#4)	Education (School)	Karachi (M)	45.88
587	Repair, Rehabilitation and Provision of Missing Facilities in various Government Schools of UC-3,4,5,6, 11,12,13,14,15,16,17,18 & 44 of District Hyderabad (07 Units) (SDG#4)	Education (School)	Hyderabad	38.89
588	Provision of missing facilities and remaining work at GGMS Garibabad, GGMS Piaro Goth, GBHS Piaro Goth, GBHS Sita Village & GGHS Garibabad (05 Units) (C: 99.649 + R: 9.370) (SDG#4)	Education (School)	Dadu	109.02
633	Establishment of Girls Education Model Schools Complex Matiari City (SDG#4)	Education (School)	Matiari	170.00
705	Establishment of Boys / Girls Degree College Jam Madad Ali Taluka Jam Nawaz District Sanghar (SDG#4) (C: 193.594 + R: 17.136)	Education (College)	Sanghar	210.73
706	Reconstruction of Building in Existing Girls Degree College Kamber District Kamber-Shahdadkot (SDG#4)	Education (College)	Kamber	50.60
707	Rehabilitation / Renovation of Govt. Boys Degree College Shahdad Kot District Kamber-Shahdadkot (SDG#4)	Education (College)	Kamber	50.00
708	Re-Construction of Building Govt. Boys Degree College Miro Khan District Kamber-Shahdadkot (SDG#4)	Education (College)	Kamber	70.62
709	Rehabilitation & Provision of Missing Facilities in Existing GBDC / GGDC Naudero District Larkano (SDG#4)	Education (College)	Larkano	62.78
710	Conversion of Higher Secondary School to Degree College at Khanpur Maher Taluka Khangarh District Ghotki (SDG#4)	Education (College)	Ghotki	145.00
711	Conversion of Higher Secondary School to Degree College at Hingorja District Khairpur (SDG#4) (C: 38.457 + R: 2.100)	Education (College)	Khairpur	40.56
712	Rehabilitation / Renovation & Provision of Missing Facilities in Existing Colleges of UC-1 to 19 District Karachi South (SDG#4)	Education (College)	Karachi (S)	99.97
713	Establishment of Girls Degree College Ubauro District Ghotki (SDG#4)	Education (College)	Ghotki	164.95
732	Provision of Missing and Allied Facilities for Government Degree College Taluka Thano Bulla Khan District Jamshoro (SDG#4)	Education (College)	Jamshoro	50.00
876	Construction of Academic Block of Sindh University, Daudu Campus	Education (U&B)	Dadu	100.00

ADP NO	Name of Scheme	Department / Sector	Location	Cost
881	Construction of Academic Block for Institute of Arts and Design at Sindh University Campus Dadu (SDG#4)	Education (U&B)	Dadu	50.00
887	Village Electrification Schemes of District Thatta and surrounding areas	Energy	Thatta	99.99
889	Gas Supply to Villages in Gadap Town Including Surrounding Areas	Energy	Karachi & Thatta	300.00
1012	Establishment of Dispensaries at UC-03, New Sabzi Mandi Taluka City Hyderabad, UC-05 at New Hyderabad City and New Manthar Petrol pump Hala Naka City Hyderabad & Up gradation of BHU to 10 Bedded Mother & Child Healthcare Center UC-16 at Liaquat Colony Hyderabad.	Health	Hyderabad	48.39
1092	Establishment of 25 bedded Hospital at UC Razaqabad, Main National Highway	Health	Karachi	100.00
1093	Establishment of Maternity Home at Shireen Jinnah Colony (SDG #3,6)	Health	Karachi	120.00
1131	Establishment of 20 bedded Shaheed Sher Muhammad Dero Hospital at Joharabad, Tando Adam (SDG #3)	Health	Sanghar	140.00
1146	Up gradation of 03 GDs to BHUs at villages Kalario, Lalu jo Tar & Sair Jo Par; Taluka Dahli (SDG #3)	Health	Tharparkar	76.00
1147	Establishment of RHC at village Karoora, Taluka Chachro (SDG #3)	Health	Tharparkar	115.41
1385	Solar Tubewells (4x) in various Dehs of District Shaheed Benazirabad. (a) Deh Jamal Keerio, (b) Deh 18 Dad Sakrand, (c)Deh Yakhtiar Khan, Sakrand & (d)Goth Imamuddin Keerio, U.C. Nathiani, Daur.	Irrigation	S.B.A	33.87
1462	Retaining Wall and C C Lining of Abul Wah at Ranipur Town Committee from RD - 94 to 97 and Onward and Retaining Wall and C C Lining Ghulam Shakh Abul Wah from 0 to Onward	Irrigation	Khairpur	51.96
1741	Construction of Paver Block Road	LG (Water Supply)	Karachi (M)	137.27
1742	Construction of Water Supply Scheme and Under Ground Tank in UC-09 Sharafi Goth, District Malir Karachi	LG (Water Supply)	Karachi (M)	95.64
1743	Construction of Water Supply scheme and Under Ground Tanks	LG (Water Supply)	Karachi (M)	97.97
1744	Providing / Lying Sewerage Line, Water Supply Line,& CC Paver Block at Union Council No. 28 Moriro District Malir Karachi	LG (Water Supply)	Karachi (M)	93.30
1745	Construction & Rehabilitation of Main / Internal Roads. Providing Sewerage line of 12" and 18" dia RCC Pipe, Water line of 4" dia PE Pipe and Installation of Paver Blocks / CC flooring & Street lighting in Bukhar Goth, Sikander Goth, Abbas town, Abdullah Palari Goth and Various Areas of UC-29.	LG (Water Supply)	Karachi (E)	95.42
1746	Providing Sewerage Lines of 12", 15" and 18" dia RCC Pipe & Water Supply P.E Pipe Line of 4", 6" dia in Saifal Goth, Sukhia Goth Wazeer Goth, Noor Muhammad Goth, Rind Muhalla, Khadim Solangi Goth, Laasi Goth and Various Areas of UC-31 District East	LG (Water Supply)	Karachi (E)	99.28
1747	Construction / Rehabilitation of Main / Internal Roads and installation of Paver Blocks / CC flooring & Street lights in Sachal Goth Block A to G, Ayub Goth, Christian Para and Shaheed Zulfiqar Ali Bhutto Goth (Seeta Nagar), Bilawal Shah Noorani Goth and various areas of UC-30 District East	LG (Water Supply)	Karachi (E)	96.10
1748	Construction / Rehabilitation of Main / Internal Roads, providing, sewerage line of 12", 15" and 18" dia RCC pipe, water line of 4", 6" dia PE Pipe and installation of Paver blocks / CC flooring & Street Lights in Jannat Gul Town, Al-Azam Town, Qayyum Abad, Hasan Noman Colony, Machar Colony, Allah Bux Goth Street No. 1, 6,38 to 43, Muhammadi Goth, and various areas	LG (Water Supply)	Karachi (E)	96.47
1749	Construction / Rehabilitation of Main Roads / Internal Roads and installation of Paver Blocks / CC flooring & Street Lights in Junejo Town, Chutta Gabol Goth, Saindad Village, Noor Khan Goth, Ahmed Jamal Goth, Khuda Bux Goth and various areas of UC-31	LG (Water Supply)	Karachi (E)	98.02
1750	Construction / Rehabilitation of Main / Internal Roads, Providing Sewerage line of 12" and 18" dia RCC pipe, 4" dia P.E Water Supply Pipe line, installation of Paver Blocks and Street Lights in Umar Colony I & II, UC-5 Mehmoodabad Ward 1 & 2.	LG (Water Supply)	Karachi (E)	98.67
1751	Construction / Rehabilitation of Main / Internal Roads, Providing Sewerage line of 12" and 18" dia RCC pipe, 4" dia P.E Water Supply Pipe line, installation of Paver blocks and street lights in Baloch Colony, LAC II UC-06 Street 01 to 31,	LG (Water Supply)	Karachi (E)	98.46
1752	Construction / Rehabilitation of Main / Internal Roads, providing Sewerage line of 12" and 18" dia RCC pipe, 4" dia P.E Water Supply Pipe line, installation of Paver blocks in Zigre Goth Block 2 Gulistan-e-Johar, Katchi Abadi C Area Block 12 and Service road from Pehlwan Goth to Munawar Chowrangi, Sindh Baloch Society Block 12 of Gulistan-e-Johar,	LG (Water Supply)	Karachi (E)	96.16
1753	Construction / Rehabilitation of Main / Internal Roads, Providing Sewerage line of 12", 15" and 18" dia RCC pipe, 4" & 6" dia P.E Water Supply line in Rabia City, Rabia Banglows to Classic Apartment, Service road from Rabia City via Johar Square, Muneer Bridge view to Johar Mor Gulistan-e-Johar.	LG (Water Supply)	Karachi (E)	99.28
1754	Construction / Rehabilitation of Main / Internal Roads, Street lights Providing Sewerage line of 12", 15" and 18" dia RCC Pipe, Water Supply line of 4", 6" dia PE Pipe in Block 13, 14, 15, 17, 19 of Gulistan-e-Johar.	LG (Water Supply)	Karachi (E)	95.55
1755	Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line of 12", 15" and 18" dia RCC Pipe, Water Supply line of 4" 6" dia PE Pipe and installation of Paver blocks in Haji Ramzan Gabol Goth, Ali Gabol Goth, Paryo Goth, Chutta Goth, Sher Muhammad Palari Goth, Baloch Khan Gabol Goth, Gahnwar Khan Gabol Goth and various areas	LG (Water Supply)	Karachi (E)	96.17

ADP NO	Name of Scheme	Department / Sector	Location	Cost
1756	Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line 12" , 15" and 18" dia RCC Pipe, Water Supply line of 4" , 6" dia P.E Pipe and installation of Paver Blocks, in Muhammad Khan Goth, Darya Khan Goth, Abdullah Shah Ghazi Goth, New Maroora Goth, Shahnawaz Sghar Goth and various areas of UC-30 District East	LG (Water Supply)	Karachi (E)	95.13
1757	Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line of 12", 15" and 18" dia RCC pipe, Water Supply line of 4" 6" dia PE Pipe and installation of Paver Blocks, Haroon Bangalows, Arif Arcade, Muslim Society, City Villas, Rizwan Society, Maroora Goth, Johar Complex and various areas of UC-30.	LG (Water Supply)	Karachi (E)	100.00
1758	Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line of 12" and 18" dia RCC Pipe, Water Supply line of 4" dia PE Pipe and installation of Paver Blocks in Sher Pao Basti, Darwesh Colony, Sindhi Muslim Society, Dhoraji, Dehli Mercantile.	LG (Water Supply)	Karachi (E)	95.34
1759	Construction / Rehabilitation of Drain System from Johar Chowrangi to Pehlwan Goth including maintenance of Service Road and Construction of Pedestrian bridge at Rabia City Gulistan-e-Johar .	LG (Water Supply)	Karachi (E)	98.95
1760	Construction / Rehabilitation of Roads from Evacue Banquet Rashid Minhas Road (Lal Flats) to K-Electric IBC Johar -I and surrounding areas of Lal Flats including Sewerage line of 15" and 18" dia RCC Pipe, Water Supply line of 4" dia PE Pipe	LG (Water Supply)	Karachi (E)	95.67
1761	Construction of Double Road from Pehlwan Goth to Johar Police Station Gulistan-e-Johar including street lights, footpath with paving blocks, Cat eyes road markings including Sewerage line of 12" & 18" dia RCC Pipe, Water Supply line of 4" dia PE pipe and Repairing of various areas Roads District East	LG (Water Supply)	Karachi (E)	98.88
1762	Construction of Road & Installation of Paver Blocks, Sewerage & Water Supply Line, Akhtar Colony & Kashmir Colony (UC-01)	LG (Water Supply)	Karachi (E)	98.61
1763	Road Carpeting (Mehmoodabad Police Station to Quetta Rangeen Hotel). Main Watersupply line with Branches, UC-03 District East	LG (Water Supply)	Karachi (E)	98.84
1764	Road Carpeting, C.C Flooring Sewerage line, Manzoor Colony-II (UC-06)	LG (Water Supply)	Karachi (E)	84.75
1765	Water & Sewerage line, Installation of Paver Block and Road carpeting, Channesar Goth (UC-04)	LG (Water Supply)	Karachi (E)	150.28
1766	Providing and laying of Water Supply 4", 8" dia from Ayub Police Chowki to Bhattai Chowk & from Shahbaz Chowki to Junejo Colony PS-99.	LG (Water Supply)	Karachi (E)	90.00
1767	Providing and laying of Water Supply 4", 8" , 12" and 18" dia from Yusrab Goth to Muhammadi Goth & from Khadim Hussain Goth to Wazir Goth	LG (Water Supply)	Karachi (E)	89.89
1768	Rehabilitation / Improvement of Road / Sewerage Line & Water System	LG (Water Supply)	Karachi (E)	206.18
1769	Rehabilitation / Improvement of Road / Sewerage Line & Water Supply System	LG (Water Supply)	Karachi (E)	98.61
1770	Construction / Rehabilitation of Main & Internal Roads and Providing of Sewerage lines of 12",18", RCC Pipe, WaterSupply Line of 4" dia PE Pipe, Installation of Paver Blocks & Street Lights in Baloch Colony, LAC II, Street 01 to31, UC-06	LG (Water Supply)	Karachi (E)	98.66
1772	Improvement / Rehabilitation & Construction of Sewerage, Paver, Water & Street Lights UC-1 to UC-19	LG (Water Supply)	Karachi (S)	1924.96
1773	Providing & laying of Paver block, Water Supply & Sewerage lines, Road Carpeting	LG (Water Supply)	Karachi (S)	119.22
1774	Construction of strom water drain, Road Carpet, C.C Flooring, Paver Block street Lights and change of Sewerage and Water Supply line, supply 300 Rings and 600 Main Hole Covers in UC - 29, 30 & 31	LG (Water Supply)	Karachi (S)	195.70
1775	Construction of Road, C.C Flooring, Foot Paths, Paver Blocks, Sewerage line, Water Supply line UC - 25 & 26	LG (Water Supply)	Karachi (S)	30.28
1776	Providing & Laying of Paver Block, Sewerage & Water Supply Lines, Road Carpeting Street Lights, R.O/Filter Plants in District South	LG (Water Supply)	Karachi (S)	296.50
1777	Construction of CC Flooring & Road Carpeting in UC-13, Mujahidabad, District West, Karachi	LG (Water Supply)	Karachi (W)	58.25
1778	Water Supply Schemes for UC-36	LG (Water Supply)	Karachi (W)	100.00
1779	Water Supply Schemes for UC-29 and UC-31	LG (Water Supply)	Karachi (W)	100.00
1780	Water Supply Schemes for UC-33	LG (Water Supply)	Karachi (W)	100.00

ADP NO	Name of Scheme	Department / Sector	Location	Cost
1781	Water Supply Schemes for UC-37	LG (Water Supply)	Karachi (W)	99.92
1782	Water Supply Schemes for UC-30 and UC-32	LG (Water Supply)	Karachi (W)	99.97
1783	CC Flooring, Sewerage Line, Water Supply Line & Establishment of Basic Health Center ( Dispensary) in UC-11 Baloch Goth.	LG (Water Supply)	Karachi (W)	122.28
1784	CC Flooring, Water Supply & Sewerage Line & Road Carpeting in UC-9, Islamia Colony.	LG (Water Supply)	Karachi (W)	66.83
1785	Road Carpeting, CC Flooring, Water Supply line in UC-12, Data Nagar.	LG (Water Supply)	Karachi (W)	58.34
1786	Improvement of Water Supply & Sewerage line, CC Flooring, Ground and Road Carpeting in UC-19.	LG (Water Supply)	Karachi (W)	66.21
1787	Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-17, UC-27 & UC-28	LG (Water Supply)	Karachi (W)	117.58
1788	Improvement of Water Supply line, installation of Sewerage line, CC Flooring, Ground and Road Carpeting in UC-18, UC-24 & UC-26.	LG (Water Supply)	Karachi (W)	95.70
1789	Improvement of Water Supply line, installation of Sewerage line, CC Flooring, Ground and Road Carpeting in UC-20, UC-21 & UC-22.	LG (Water Supply)	Karachi (W)	86.04
1790	Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-12, UC-16 & UC-25	LG (Water Supply)	Karachi (W)	116.83
1791	Construction of Roads, laying of Paver Blocks, Installation of Sewerage System in UC-16, Ghaziabad	LG (Water Supply)	Karachi (W)	46.91
1792	Construction of Pumping Station with Pipelines in Khuda ki Basti, Surjani, Lyari & Taiser Areas	LG (Water Supply)	Karachi (W)	100.00
1793	Rehabilitaion / Improvement of Road / Sewerage Line & Water System in the area of PS-92	LG (Water Supply)	Karachi (W)	96.84
1794	Rehabilitaion / Improvement of Road / Sewerage Line & Water System in the area of PS-93	LG (Water Supply)	Karachi (W)	95.74
1795	Improvement of Water Supply and installtion of Drainage line in UC-1 Shershah	LG (Water Supply)	Karachi (W)	85.00
1796	Improvement of Sewerage line Boosting Pump, Drainage line and Carpeting of Road in UC-2 Labour Square	LG (Water Supply)	Karachi (W)	81.09
1797	Improvement of Water Supply, Sewerage line Paver Block in UC-4 Metroville	LG (Water Supply)	Karachi (W)	84.64
1798	Improvement of Water Supply, Sewerage line and Road carpeting in UC-5 Pak Colony	LG (Water Supply)	Karachi (W)	56.22
1799	Water supply line, Sewerage line, Paver Block in UC-6 & UC-7 Golimar, Karachi	LG (Water Supply)	Karachi (W)	187.12
1800	Boosting Pump Water Supply line, Sector 14 to Ethad Town, Block-A UC-36, Baldia Town.	LG (Water Supply)	Karachi (W)	49.64
1801	Improvement & installation of Water Supply and Sewerage lines, CC Flooring, Ground and Road Carpeting in UC-16.	LG (Water Supply)	Karachi (W)	75.87
1802	Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-19	LG (Water Supply)	Karachi (W)	177.95
1803	Improvement & installation of Water Supply and Sewerage lines, CC Flooring, Ground and Road Carpeting in UC-24.	LG (Water Supply)	Karachi (W)	76.01
1804	Improvement & installation of Water Supply and Sewerage lines, CC Flooring, Ground and Road Carpeting in UC-26.	LG (Water Supply)	Karachi (W)	76.33
1805	Improvement & installation of Water Supply and Sewerage lines in UC-21	LG (Water Supply)	Karachi (W)	75.77
1806	Improvement & installation of Water Supply and Sewerage lines, CC Flooring, Ground and Road Carpeting in UC-21 & 22, District West, Karachi	LG (Water Supply)	Karachi (W)	66.85

ADP NO	Name of Scheme	Department / Sector	Location	Cost
1807	Improvement & installation of Water Supply and Sewerage lines, CC Flooring, Ground and Road Carpeting in UC-18.	LG (Water Supply)	Karachi (W)	47.45
1808	Improvement & installation of Water Supply and Sewerage lines, CC Flooring, Ground and Road Carpeting in UC-20.	LG (Water Supply)	Karachi (W)	57.56
1809	Improvement & installation of Water Supply and Sewerage lines, Paver Blocks & Road Carpeting & Construction in UC-23 & UC-25.	LG (Water Supply)	Karachi (W)	239.71
1810	Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-11 & 12	LG (Water Supply)	Karachi (W)	160.00
1811	Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-13, UC-17 & UC-19	LG (Water Supply)	Karachi (W)	156.09
1812	Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-27 & UC-28	LG (Water Supply)	Karachi (W)	116.07
1813	Water Supply line, Sewerage line, Paver Block and Carpeting of Roads in different areas of UC-3.	LG (Water Supply)	Karachi (W)	96.46
1814	Water Supply line, Sewerage line, Paver Block and Carpeting of Roads in different areas of UC-14.	LG (Water Supply)	Karachi (W)	107.75
1815	Water Supply line, Sewerage line, Paver Block and Carpeting of Roads in different areas of UC-15.	LG (Water Supply)	Karachi (W)	85.79
1816	Water Supply line, Sewerage line, Paver Block and Carpeting of Roads in different areas of UC-10.	LG (Water Supply)	Karachi (W)	77.71
1817	Water Supply line, Sewerage line, Paver Block and Carpeting of Roads in different areas of UC-8 & 9.	LG (Water Supply)	Karachi (W)	127.91
1818	Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-4, 5 & 39	LG (Water Supply)	Karachi (W)	136.45
1819	Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-4	LG (Water Supply)	Karachi (W)	116.91
1820	Improvement of Water Supply line and Installation of Sewerage line and CC Flooring, Grounds Road Carpeting in UC-5.	LG (Water Supply)	Karachi (W)	115.04
1821	Improvement of Water Supply line and Installation of Sewerage line and CC Flooring, Grounds Road Carpeting in UC-6.	LG (Water Supply)	Karachi (W)	113.86
1822	Improvement of Water supply line and Installation of Sewerage line and Paver Block, Road Carpeting in UC-38.	LG (Water Supply)	Karachi (W)	170.26
1823	Improvement of Water supply line and Installation of Sewerage line and Paver Block, Road Carpeting in UC-39.	LG (Water Supply)	Karachi (W)	173.52
1824	CC Flooring, Sewerage Line, Road Carpeting and Establishment of in UC-38 and UC-5, Grounds in UC-39.	LG (Water Supply)	Karachi (W)	140.00
1825	Providing & Laying of Paver Block Flooring in Noor Shah Muhalla, Kachhi Muhalla Bismillah Colony, Bukhari Muhalla, Mianwali Muhalla, Qasim Ali Shah Colony and Kachela Goth UC 2 Mawach Goth.	LG (Water Supply)	Karachi (Kea)	126.18
1826	Providing & Laying of Paver Block in Different Streets of UC-41, UC-42, UC-43, UC-44, UC-45 and UC-46 in DMC Keamari	LG (Water Supply)	Karachi (Kea)	95.99
1827	Water Supply line and Sewerage line in Muripur Grex Fathers Colony, Customs Colony, Oranchi Mohallah, Budhani Goth, Javed Bahria & different areas of Mauripur.	LG (Water Supply)	Karachi (Kea)	150.00
1828	Sawerage Line in UC 37 Naval Colony Baldia Town	LG (Water Supply)	Karachi (Kea)	131.67
1829	Improvement of Water Supply and installtion of Sewerage line and Paver Block in UC-1 Gabo Pat.	LG (Water Supply)	Karachi (Kea)	75.52
1830	Paver Block and Carpeting of Road in different areas of UC-2 Mowach Goth.	LG (Water Supply)	Karachi (Kea)	96.33
1831	Improvement of Water Supply and installtion of Sewerage line and Carpeting of Road in UC-3 Keamari Town.	LG (Water Supply)	Karachi (Kea)	68.02
1832	Improvement of Water Supply and installation of Sewerage line and Carpeting of Road in UC-3 Keamari Town.	LG (Water Supply)	Karachi (Kea)	106.58

ADP NO	Name of Scheme	Department / Sector	Location	Cost
1833	Improvement of water supply and installtion of Sewerage line and Paver Block in UC-40 & UC-42 District Keamari Karachi	LG (Water Supply)	Karachi (Kea)	137.01
1834	Providing / Laying Paver R.C.C Sewerage Pipe Line and C.C Flooring I/C Cleaning of Nallahs at different places of UC-41, UC-42, UC-43, UC-44, UC-45 & UC-46 in DMC Keamari	LG (Water Supply)	Karachi (Kea)	92.88
1835	Providing / Laying Water Supply Pipe line at P.R.C Tower to Gold line, M.A Jinnah Road in UC-43, DMC Keamari	LG (Water Supply)	Karachi (Kea)	99.10
1836	Improvement of water Supply and installtion of Sewerage line and Paver Block in UC-29.	LG (Water Supply)	Karachi (Kea)	67.87
1837	Improvement of Water Supply and installation of Sewerage line and Carpeting of Road in UC-30 & 31 Baldia Town.	LG (Water Supply)	Karachi (Kea)	146.80
1838	Improvement of water supply and installation of Sewerage line and Paver Block in UC-32 Baldia Town.	LG (Water Supply)	Karachi (Kea)	87.49
1839	Improvement of water supply and installation of Sewerage line and Paver Block in UC-33 & 34 Baldia Town.	LG (Water Supply)	Karachi (Kea)	116.60
1840	Improvement of water Supply and installation of Sewerage line and Paver Block in UC-35 Baldia Town	LG (Water Supply)	Karachi (Kea)	68.37
1841	Improvement of water Supply and installtion of Sewerage line and Paver Block in UC-36.	LG (Water Supply)	Karachi (Kea)	157.52
1842	Improvement of Water supply and installation of Sewerage line and Carpeting of Road in UC-33 Baldia Town.	LG (Water Supply)	Karachi (Kea)	133.99
1843	Improvement of Water Supply and installation of Sewerage line and Carpeting of Road in UC-37 Baldia Town.	LG (Water Supply)	Karachi (Kea)	157.74
1844	Construction of Drains in different wards of UC-36	LG (Water Supply)	Karachi (Kor)	70.00
1845	Construction of Drains in different wards of UC-37	LG (Water Supply)	Karachi (Kor)	98.05
1846	Providing / Laying & Replacement of Damaged & Unserviceable Sewerage lines in different areas of PS-97	LG (Water Supply)	Karachi (Kor)	75.86
1847	Construction of Pumping Station & Providing & Laying of Water Supply Lines in Mehran Town UC-37 Ward-1	LG (Water Supply)	Karachi (Kor)	100.00
1848	Providing & Laying of Water Supply Lines in UC-32 Bilal Colony UC-8 Natha Khan Colony & UC-23 Awami Colony	LG (Water Supply)	Karachi (Kor)	150.00
1849	Providing / Laying & Replacement of Damaged & Unserviceable Sewerage line in UC-32 & UC-37 Ward 1	LG (Water Supply)	Karachi (Kor)	56.48
1850	Providing and Laying of CC flooring / Paver Blocks in Different Streets	LG (Water Supply)	Karachi (Kor)	29.69
1851	Providing & Laying & Replacement of Damaged & Unserviceable Sewerage line in UC-8 Natha Khan & UC-23 Awami Colony	LG (Water Supply)	Karachi (Kor)	56.37
1852	Construction of Pumping Station Providing & Laying of Water Supply Lines & Replacement of old Pipe lines in Bhattai Colony & Qayyumabad	LG (Water Supply)	Karachi (Kor)	100.00
1853	Improvement & Reconstruction of Roads & Foot path UC-32 Bilal Colony to Murtaza Chowk (Double Tracked Road with Culverts and Sewerage System)	LG (Water Supply)	Karachi (Kor)	141.79
1855	Rehabilitation / Improvement of Road / Sewerage Line & Water System	LG (Water Supply)	Karachi (Kor)	96.81
1856	Rehabilitation / Improvement of Road / Sewerage Line & Water Supply System in the area of PS-129.	LG (Water Supply)	Karachi (C)	96.96
1857	Rehabilitation / Improvement of Road / Sewerage Line & Water System in the area of PS-123, 124,	LG (Water Supply)	Karachi (C)	96.90
1858	Rehabilitation / Improvement of Road / Sewerage line & Water System in the area of PS-130 District Central	LG (Water Supply)	Karachi (C)	48.14
1859	Rehabilitation / Improvement of Road / Sewerage line & Water system in the area of PS-127, 128.	LG (Water Supply)	Karachi (C)	150.00

ADP NO	Name of Scheme	Department / Sector	Location	Cost
1860	Rehabilitation / Improvement of Road / Sewerage Line & Water System in the area of PS-125, 126.	LG (Water Supply)	Karachi (C)	96.17
1861	Construction of CC Block for Various Streets of Taluka Qasimabad & Taluka Rural Hyderabad	LG (Water Supply)	Hyderabad	30.94
1862	P/L/J & Testing of 4", 6", 8" & 12" dia P.E /PVC Water Supply lines at Different Areas of Hyderabad	LG (Water Supply)	Hyderabad	48.65
1863	Rehabilitation of Mir Khan Drainage Pumping Station and Providing of Nullah / Sewer Line from SRC to Bostan House Unit No. 12, Taluka Latifabad Hyderabad	LG (Water Supply)	Hyderabad	100.00
1864	P/L/J & Testing of 24" dia PE -PN 10 Pipe line from 8 MGD Hala Naka Treatment Plant to Bail Khana Pumping Station i/c Pumping Machinery for Improvement of Water Supply System of Khai Road, Memon Para, Tando Wali Muhammad and adjacent area of Taluka City Hyderabad	LG (Water Supply)	Hyderabad	201.48
1865	P/L/J & Testing of 20" dia PE Rising main from 8 MGD Preetabad filter plant & distribution main (P.E) upto Tando Tayyab/Islamabad Chowk i/c construction of low services reservoirs pump hous, pumping machinery & allied accessories etc. in all respect	LG (Water Supply)	Hyderabad	229.33
1866	Providing & Laying of Paver Block at Various Streets / Roads of UC-1, UC-2, UC-22 to UC-39 and UC-45 to UC-50 and Ward 1 to 9 Cantt: Taluka City Hyderabad	LG (Water Supply)	Hyderabad	292.95
1867	P/L/J of Paver Block Roads of U-C #04, 05, 06, 08 Mirpurkhas Length. 6.12 KMs	LG (Water Supply)	Mirpurkhas	97.31
1868	Providing & laying of Paver Block Roads in U.C. # 02, 03 (1.54 km) & Construction of Road in U.C. Old Mipur, U.C. Mir Aachan (3.00 km) Taluka H.B Mari	LG (Water Supply)	Mirpurkhas	45.89
1869	Paver Block Road from Mirpurkhas Ring Road to Siyal Colony & Others (5.00 KMs)	LG (Water Supply)	Mirpurkhas	95.83
1870	Providing & Laying of Paver Block in Hingorno Town Taluka Sindhri 8000 RFT	LG (Water Supply)	Mirpurkhas	44.48
1871	Construction of CC / Paver Block Roads in Different Muhalla in Mithi Town	LG (Water Supply)	Tharparkar	52.95
1872	Providing Sewerage Lines in Various wards / UCs of Taluka Nawabshah Juma Khan Zardari, Village Ghazi Khan Hoat and village Khairshah, Haqani Colony, Badal Colony, Sumera Colony, Ghulam Hyder Shah Colony, Bhattai Colony, Housing Society, Society & Hanif Katiyar Muhallah, Chandia Colony, Jamali Colony, Bhangwar Colony and Oad Bhatti Para, Mehran Colony, Azim Colony, Muhammadi Town & Pathan Para, Ghulam Rasool Shah Colony, Sain Bux Khaskheli, New Sabzi Mandi road, Fouji Colony, Faizan Madina Colony, Muhammadi Ali Shah More, Ghazali Town, Shafi Muhammad Baloch, Umar Daraz Colony, Village Eid Muhammad Brohi, Railway Colony, Camp No. 2, Taj Colony near Abdul Haque Jamali & Madrsa Street, Bhatti Para, Brohi Goth, Khan Pump Back side, Afzal Shah Town, Shalimar Town, Sanghar road Ayesha College disposal work, Taj Colony & various portions (UCs - 1 to 9)	LG (Water Supply)	S.B.A	72.59
1873	Dual Carriage Road of Johi City, Drainage and Paving Block	LG (Water Supply)	Dadu	98.55
1874	Improvement of Drainage and Paving Block from Town Committee Via Phulji Station	LG (Water Supply)	Dadu	98.61
1875	Improvement of Drainage and Paving Block of Piyaro Station Road	LG (Water Supply)	Dadu	98.83
1876	Improvement of Road from Indus Highway Degree College to Theba VIP Road Mehar Link to Dua Hospital i/c Drainage on both sides & Paving Block	LG (Water Supply)	Dadu	98.40
1877	Improvement of Road from Haji Khan to Drigh Bala Road i/c Paving Block & Drainage at Village Drigh Bala	LG (Water Supply)	Dadu	98.28
1878	Improvement of Link Road with Paver Block from Allah Wala Chowk to Kambeer - Shahdadkot road via Sui Gas Office i/c Approaches to Various Streets (2.60 kms) Shahdadkot City	LG (Water Supply)	Kamber	98.17
1879	Laying of Paver Block at UC 16,17,18,19 and 20 Larkano City	LG (Water Supply)	Larkano	58.70
1880	Providing & Laying of Paver Block in Taluka Dokri	LG (Water Supply)	Larkano	24.97
1881	(i) Providing & Laying of Paver Block from Naudero-Ratodero Road to Governemnt Boys Degree College Naudero (0.50 KMs) (ii) Construction of Paver Block from Allah Waro Chowk to Jug Chowk at Naudero (0.50 KMs) (iii) Construction of road from Karim Bux Khuhro Petrol Pump to Allah Warayo Solangi (0.60 KMs) (iv) Construction of	LG (Water Supply)	Larkano	80.00

ADP NO	Name of Scheme	Department / Sector	Location	Cost
	Road from Naudero Larkano Road to Naudero By Pass via Dastagir Colony (0.60 KMs) (v) Construction / Reconditioning of Road from Naudero Jag chowk to Peer-Jo-goth via Qutub Shah Nursery (0.70 KMs)			
1882	Providing & Laying of C.C. Paver in various roads & streets of Jacobabad	LG (Water Supply)	Jacobabad	300.00
1883	Providing & Laying of Paver Block at Various Streets of Mubarakpur City Taluka Thul	LG (Water Supply)	Jacobabad	42.00
1884	Providing & Laying of Paver Block at various Villages of UC Meral Pur and UC Mubarak Pur (i) Wali Muhammad Tanwari (ii) Din Muhammad Tanwar (iii) Jhngal Tanwari (iv) Band Tanwari (v) Khamiso Bambal (vi) Nasar Muhammad Brohi (vii) Gujo Tanwari Dhani (viii) Bux Mastoi Raheem Bux Mastoi (ix) Sahab Khan Mastoi (x) / Aamir Khoso (xi) Qaim Din Tanwari (xii) Jam Khan Khoso(xiii) Liaquat Khan Mahar (xiv) Rozi Shar (xv) Hamzo Mahar (xvi) Muhammad Ramzan Mahar (xvii) Piyaro Mahar (xviii) Beer Jo Goath and (xix) Sardar Bux Shar	LG (Water Supply)	Jacobabad	52.50
1885	Construction of Paver Block Road Kandhkot Muncipal Committee Ward No. 1 to 16	LG (Water Supply)	Kashmore	99.41
1886	i) Providing Paver Block at Village Muhammad Ali Marfani Shop to Sarwar Marfani, (ii) Mehrab Marfani, Jabal Bhayo, Veesar, (iii) Arain Muhalla, Chohan Muhalla, Sarmastani Muhallah, City Shikarpur (Ward-25) (vi) Samadha Ashram, City Shikarpur (v) Village Shahzado Bhand to Jamia Masjid (vi) Village Jamsheed Khan Pathan, (vii) Village Bhoora Khan Lohar & Construction of road from Village Gul Bar Marfani Mile 0/0-0/4.	LG (Water Supply)	Shikarpur	94.95
1887	Providing of Paver Block in Various Streets of Different Villages of Taluka Khanpur	LG (Water Supply)	Shikarpur	93.66
1888	Providing of Paver Block in various streets in different Ward-I to Ward-30, City Shikarpur	LG (Water Supply)	Shikarpur	113.41
1889	Providing of Paver Block in various streets of Different villages of Taluka Shikarpur	LG (Water Supply)	Shikarpur	95.36
1890	Improvement of Various Sreets with Paver Blocks in (i) Rustam Town (ii) Jahan Khan (iii) Village Pyaro Khan Bhayo (iv) Channar Goth (v) Village Qasim Bhayo (vi) Kot Altaf Bhayo	LG (Water Supply)	Shikarpur	92.57
1891	Providing and Laying of Paving Blocks in various Streets of villages of Union Councils Mureed Sethar, UC Karan Sharif, UC Lodra, UC Sultan Kot, UC Hamayoon Sharif, UC Machi & Shahul Sadhaya	LG (Water Supply)	Shikarpur	156.87
1892	Construction of Paver Block Road in villages (1) Jhali Kalwari (2) Ruk (3) Sakhji (4) Kalhora Muhallah (5) Juneja Muhallah (6) Ghulam Qadir Jagerani (7) thenda (8) Syed Amanullah (9) Janib Bhayo to Lutfullah Khan (10) Bashir Ahmed Mirani to village Arbelo Abro (11) Soomra Muhalla (12) Chohan & different village of Taluka Lakhi	LG (Water Supply)	Shikarpur	95.61
1893	Construction of Paver Block Road (1) Town Committee Rustam (2) Jarar Pahore (3) Garhi Teigo (4) Abdul Ghafoor Brohi (5) Ali Hassan Brohi (6) Tarai (7) Piyaro Khan Bhayo & different village of UC-Garhi Dakho & Areja UC-Pir Bux Shujrah	LG (Water Supply)	Shikarpur	100.00
1894	Construction of Paver Block Road (1) village Khan Muhammad Channa (2) Rais Hizbullah (3) Chodio Sadhaya road to village Jaggan UC-Zerkhail & different villages of UC Tarai	LG (Water Supply)	Shikarpur	98.63
1895	Construction of Paver Block Road (1) Village Arbab Marfani (2) Village Chak to Kot Nawab Khan Bhayo & different Village of Taluka Khanpur	LG (Water Supply)	Shikarpur	97.33
1896	Construction and Widening of Road with Paver Blocks i/c Providing drains: (1) from Shikarpur Jacobabad Road Naka to Gah Piri Sukhpul Via Panj Guli with 2 Links @ Tharoorpur Road and Masana (Graveyard) (2) From Old Mall Piri to Qazi Mohalla via Larik Mohalla with Link to Kumbhar Mohalla (3) From Wagno Gate Road Shikarpur Sikander Achaar Goodam to Karan Gate via link Road through Petrol Pump (4) From Phatak at Kanak Shah peer to Old Railway Crossing via Link to Dawan Shah Road	LG (Water Supply)	Shikarpur	98.24
1897	Construction of Road & providing of Paver	LG (Water Supply)	Shikarpur	296.91
1898	Construction of Paver Block Road at different streets of Town Khanpur, Village Abdu, Dahar, Mangria Muhalla, Master Bhayo House, Town Committee Chak, Qasim Bhayo & Different Villages of UC Mungrani	LG (Water Supply)	Shikarpur	98.78
1899	Providing & Laying of Paver Blocks from N.H Way Baiji Chowk Degree College Pano Akil Kacha Phatak to Mukhtiarkar office Panjal Mahesar Chowk to Bozdar Chowk Sakhi Baba Hospital Chowk to old Sadhooja Bus Stop Shainshah Bukhari Chowk to Bozdar Chowk Pir Wah to Mai Jindo graveyard Mehran School NADRA Office to Benazir Park Pano Akil Cantt: road to Faizan-e-Madeena Masjid near Old Water Tank Masjid Seddiqiya H/O Ahsan Khan to Ustad Muhammad Tahir Achrani G-T Road Noor Masjid to Shaikh Muhallah, H/O Dr. Muzaffar Kalhoro upto Ashique Hussain Shah Road via Jumo Bhutto and adjacent areas (6.0 KMs)	LG (Water Supply)	Sukkur	80.99
1900	Providing & Laying of Paver Block in Various Links of Muhallah Osta Gahi, Muhallah Dabar, Muhallah Shaikh and Internal Streets of Muhallah Bhurgari upto Bhurgari Regular Khairpur including Masonery Structure (340426 Sff) Taluka Khairpur	LG (Water Supply)	Khairpur	80.00

ADP NO	Name of Scheme	Department / Sector	Location	Cost
1901	Providing & Laying of Paver Block from Ferdous Masjid, Mill Colony, Jinnah Colony, Madina Colony Road to Technical University Road via Food Goodown including Various Streets of Khannan Shah Muhallah, Mangi Muhallah, Nizamani Muhallah and Kamangar Muhallah UC Shah Latif upto Bhutta village on west of east Feeder near Khaki Shah Bridge i/c Masonery Structure Taluka Khairpur	LG (Water Supply)	Khairpur	100.00
1902	Construction of various Paver Block Roads in Taluka Kotdiji	LG (Water Supply)	Khairpur	163.00
1903	Providing & Laying of Paver Blocks from old Bus Stand Ranipur via Gambat road (Rehman CNG) and from National Highway to Dr. Fatah Hospital and from National Highway to Kausar Masjid (Katchiabadi) and from Ranipur Sobhodero Road to Dargah Sharif Town Committee Ranipur Taluka Sobhodero Ranipur	LG (Water Supply)	Khairpur	99.22
1904	Providing of Drainage System & Paver Block City Pir Esso U.C Kamal Dero Taluka Gambat,	LG (Water Supply)	Khairpur	50.00
1905	Construction of Remaining Work of Surface Drains & Paver Block of Sobhodero City Taluka Sobhodero	LG (Water Supply)	Khairpur	45.86
1906	Providing & Laying of CC Paver from Civil Hospital to Mangrio Petrol Pump Daharki City	LG (Water Supply)	Ghotki	106.34
1907	Providing & Laying of CC Paver Mirpur Mathelo City	LG (Water Supply)	Ghotki	112.61
1919	Providing and laying of Sewerage line of 12", 15", 18" and 30" dia RCC Pipe from Rupali Centre to Chakar Hotel & Different Areas	LG (Water Supply)	Karachi (E)	130.00
1920	Storm Water Drain in Clifton Block 2 and Ward 2 Hazara Colony CBC underground water tank Jhamuriya colony Ward 3 replacement of Pumps and Turbines Machines and renovation of Bazarta Pumping station	LG (Water Supply)	Karachi (S)	105.00
1921	Replacement of Water Supply Lines from Bhattai Colony to Qayumabad, Malir River	LG (Water Supply)	Karachi (Kor)	100.00
1922	Providing & Laying of Paver Block in various wards / mohallas / colonies of UC- 1,2,3,4,5,6,7,8 and 9 of Nawabshah City	LG (Water Supply)	S.B.A	160.02
2104	Construction of Parking Plaza at Flower Market Bunder Road Larkano	LG (Bldgs)	Larkano	99.36
2159	(i) Providing Paver Block / Bridge at Village Allahdad Marfani (ii) Providing Paver Block at Village Abdul Jabbar Marfani (iii) Providing Paver Block at Village Ghulam Muhammad Marfani (iv) Providing Paver Block from Jaggan Sheranpur road to Village Ali M. Marfani (v) Rabdino Marfani (vi) Repair of road from from Shah Jalil Badshah at Village Jaggan, Paver Block from GBHS Lakhi to Googi Ram House & Bilal Petrol Pump to Bagri Muhalla (vii) Wada Machi (v) construction of road from Jaggan Wakro road to Ali Hassan Khoso (vi) Construction of road from Hamayun Wakro road to Sadoro Bhatti (vii) Construction of road from Hamayun Wakro road to Village Akbar Rind (viii) Construction of road from Jaggan Wakro road to Village pahar Brohi (ix) Construction of road from Jaggan Bus Stand road to Ali Dost Bhatti (x) Construction of Bridges (i) Hidayatullah Chachar (ii) Ali Hassan Khoso (xi) Paver Block from Abdul Rasheed Bhutto Rice Mill to Makhno Khan Bhutto House @ Village Jano.	LG (Roads)	Shikarpur	75.06
2160	Rehabilitation of internal roads of City (5.0 Km)	LG (Roads)	Khairpur	98.28
2161	Construction of roads in various U.Cs: (a) Construction / Remodeling of road from 68 Mori road to connect Jam Wah Mori 2.5 k.m (b) Construction of road from Chak road to village Jangi Khan Mari Deh 5-Chak (2.00 Km) (c) Construction of road from Preshan stop to village Shabir Shahani via Raheem Bux Brohi 1.5 Km Deh 44-Narat. (d) Construction of road from Dost Ali rind road to village Sono Khan Mari, Approaches (04 Furlong). (e) Road from 60th Mile main Phatak to Rehmatullah Jamali House via Hafiz Amjad Ali Abro House, Daur City 1000 ft. (f) Road from Mehran Highway to village Mubarak Chandio 3000 ft. (g) Construction of road from Nabi Dad Brohi road to village Amjad Shah Ji Kubi Deh 40 Dad road mile 0/0-0/3+110 (0.63 Km). (h) Paver Block in various streets of Town Committee, Bandhi. (i) Paver Block in various streets of Town Committee, Jam Sahib. (j) Paver Block in various streets of Star Colony, Town Committee, Daur.	LG (Roads)	S.B.A	161.90
2162	Construction of roads in various UCs of District Shaheed Benazirabad (a) Reconditioning / Construction of road from Sakrand Majeed Keerio road to village Haji Keerio (0.92 Km) (b) Reconditioning of road from Lashari Stop Keeria Mori to Bachal Keerio Nathiyani, Deh 80 Nusrat Mile 0/0-0/5 (1 Km) (Dhora Portion) (1/2 thick carpet with paver machine) (c) Reconditioning of road from Nawabshah - Daur road Lashari Stop to village Imamuddin Keerio road Mile 0/0-1/1 (1.80 Km) (1/2 thick carpet with paver machine) (d) W/R/ Construction of road from Sakrand - Nawabshah road to village Sikandar Hayat Rind, Mile 0/0-0/2 + 330) (0.50 Km) (1/2 thick carpet with paver machine) (e) Construction of road from Nawabshah - Sakrand road to village Ali Sher Rind including link to village Porho Machi (3 Km) (1-1/2" thick carpet with paver machine)	LG (Roads)	S.B.A	79.44
2163	Improvement of various streets of Sarhari Town 4-5 Km	LG (Roads)	Sanghar	44.63
2164	Construction / Reconditioning of various roads of Taluka Qasimabad & Taluka Rural Hyderabad	LG (Roads)	Hyderabad	127.76

ADP NO	Name of Scheme	Department / Sector	Location	Cost
2165	Construction of road Village Rawal Kandra, Construction of Road village Mubeen Jakhro, Construction of Road village Yasin Bhai, Construction of Road village Wadero Gul Muhammad Babro, Construction of Road village Gulsher Machi, Construction of Road village Haji Ahmed Khoso, Construction of Road village Rahim Charan, Construction of Road village Lakha Dino Lothiya, Construction of Road village Haji Mirbhar. Improvement of road village Walro repair, Improvement of road village Muhammad Khan Magsi repair, Improvement of road village Abdullah Sodho repair	LG (Roads)	Sujawal	77.86
2166	Construction of road Village Hassan Dohar, Construction of road village Master Hidayatullah Mallah via Dad Jat, Construction of road village Nooro Thahmoor, Construction of road village Ibrahim Madhro, Construction of road village Nazir Mallah, Construction of road village Wadero Sindhu Mundro, Construction of road village Mir Muhammad Rind Wahiya Khaskheli Bridge: Sim Nali village Sindhu Mundro	LG (Roads)	Sujawal	90.78
2167	Construction / Improvement of 19 nos. roads of District Sujawal (35.41 Km)	LG (Roads)	Sujawal	197.45
2168	Construction / Rehabilitation of Roads at various Ucs (14,15,24,25) of PS 90 / NA-236, District Malir Karachi	LG (Roads)	Karachi (M)	147.48
2169	Construction / Reconstruction / Roads and Laying of Sewerage Line at various Ucs (UC-01, UC-04, UC-09, UC-17) of NA-236, District Malir Karachi	LG (Roads)	Karachi (M)	138.40
2170	Construction of roads alongwith drainage, sewerage and paver stones in UC Khuldabad District Malir Karachi	LG (Roads)	Karachi (M)	59.78
2171	Construction of roads alongwith drainage, sewerage and paver stones in UC Bhitaiabad District Malir Karachi	LG (Roads)	Karachi (M)	89.97
2172	Construction of roads alongwith drainage, sewerage and paver stones in UC Ghazi Dawood Brohi, UC Jaffar Tyar and UC Ghareebabad District Malir Karachi	LG (Roads)	Karachi (M)	137.34
2173	Construction of roads alongwith drainage, sewerage and paver stones in UC Sharafi, UC Moinabad & UC Quaidabad, District Malir Karachi	LG (Roads)	Karachi (M)	121.85
2174	Construction of roads alongwith drainage, Sewerage, Pipes and paving blocks in UC-1 Sherpao, Malir Karachi	LG (Roads)	Karachi (M)	79.91
2175	Construction of roads alongwith drainage, Sewerage, Pipes and paving blocks in UC-2 Muslimabad, Malir Karachi	LG (Roads)	Karachi (M)	118.30
2176	Construction of roads alongwith drainage, Sewerage, Pipes and paving blocks in UC-3, Muzafarabad, Malir Karachi	LG (Roads)	Karachi (M)	89.94
2177	Construction of roads alongwith drainage, Sewerage, Pipes and paving blocks in UC-4, Majeed Colony, UC-5 Cattle Colony, Malir Karachi	LG (Roads)	Karachi (M)	107.62
2178	Construction of roads alongwith drainage, Sewerage, Pipes and paving blocks in UC-7, Quaidabad, UC-8 Mominabad, Malir Karachi	LG (Roads)	Karachi (M)	99.68
2179	Improvement & Reconstruction of Roads in UC-36, 35, 30 Fishermen Chowrangi to Nasir Colony	LG (Roads)	Karachi (Kor)	157.00
2180	Construction / Rehabilitation of Roads, Drain Work, and Paver Blocks at UC 41 Baba / Bhiit / Shamspir / Younusabad / Salehabad Island's District Keamari Karachi	LG (Roads)	Karachi (Kea)	160.00
2181	Reconstruction / Rehabilitation of roads, Drain work and Paver Blocks C.C flooring at UC45 Gulshan e Sikandarabad District Keamari Karachi	LG (Roads)	Karachi (Kea)	99.49
2182	Construction / Rehabilitation of Roads, Drain Work and Paver Blocks at UC 40 Maripur District Keamari Karachi	LG (Roads)	Karachi (Kea)	99.88
2183	Construction / Rehabilitation of Roads, Pipe Drain Work and C.C flooring at UC 01 Gulbai District Keamari Karachi	LG (Roads)	Karachi (Kea)	99.99
2184	Construction / Rehabilitation of Roads, Drain Work and Paver Blocks C.C flooring at UC 42 Machar Colony District Keamari Karachi	LG (Roads)	Karachi (Kea)	49.81
2185	1. Repair of Roads U.C Hatari (3 Km) 2. Repair of Roads U.C Masoo Bughri (1.5 Km) 3. Construction of roads U.C Hatari (1.5 Km) 4. Construction of C.C Blocks in various streets of village Sobho Khan U.C Tando Qaisar 5. Construction of Drainage village Sobho Khan U.C Tando Qaisar	LG (Roads)	Maliari	27.04
2186	Construction of metal road / tough tile / solar lights at various streets of Thul City Taluka Thul District Jacobabad	LG (Roads)	Jacobabad	99.03
2187	Rehabilitation / Construction of internal roads of M.C. Kandhkot, Ward no. 1 to 16	LG (Roads)	Kashmore	80.00
2188	Construction of Metalled Road / Repair / Paving Blocks from Mari Road to Veeram Jafferi with link of Internal Road via Kedo Jafferi i/c Construction of Paving Blocks in various streets of Villages UC Jano Sharif with road Drain	LG (Roads)	Shikarpur	78.75
2189	Construction / Repair of Metalled Road from Village Baid to Village Nabi Bux Brohi with 4 links. (1) From Sahib Khan Kakepoto to Shikarpur Larkana Indus Highway i/c Paver Blocks in Streets. (2) From Khaman to Shikarpur Larkana Indus Highway (3) From Village Baid to Village Dil Murad Kakepoto (4) From Baid Road to Bugro Luhur Via Mian Wah	LG (Roads)	Shikarpur	78.84
2190	Construction of Road & Installation of Paver Blocks, Manzoor Colony-I (UC-02 District East)	LG (Roads)	Karachi (E)	74.52
2191	Construction of Metal road at different places of UC-42 & UC-43 in PS-113, Keamari Zone, DMC (Keamari)	LG (Roads)	Karachi (Kea)	99.13
2192	Construction of Metal road at different places of UC-44, UC-45 & UC-46 in PS-113, Keamari Zone, DMC (Keamari)	LG (Roads)	Karachi (Kea)	99.09
2193	W/R of road from Larkana Khairpur road to village Fareedabad W/R of road from village Bakrani to village Mad Bahu via Shafquat Hussain Khan Unar House & Paver Block for different Uc's Mad Bahu, Fareedabad, Puranoabad, Mahar Wada, Baqapur @ Naich	LG (Roads)	Larkano	140.00
2194	Construction / Re-construction of road from Gerello bus stand city to Ghulam Ali Zuhri & Ghulam Muhammad Buledi Kully, Muhammad Ali Brohi, Mehboob Ali birohi to Derra Bridge mile: 0/0-1/4 (2.25 Km).	LG (Roads)	Larkano	50.00
2195	Reconditioning of road Bakhar Mehesar 2.5. Km, road from village Haji Khan Soomro to Altaf Boadar 1.5 Km. Mehmoobabad Police to village Pandhi Jarwar via village	LG (Roads)	Kamber	159.45

ADP NO	Name of Scheme	Department / Sector	Location	Cost
	Akbar Jarwar 2.Km, 1 Km road form Mirokhan to village Jamaluddin Gopang. 2.5 Km road from Mirokhan via Purano Tharo to village M. Jurial Umrani, 1.5. Km road Motorway to Jiand Luk, road from village Bhatti Allah Dino Tunio 2.5. Km. New road from Garello Khaipur juso connecting to village Ghulam Muhammad Isran via Khuhri Imam Bargah 1 Km and 1 Km New road connecting to Indus High via Deh Fati Bilawal to Ghulam Muhammad Khan Isran, Construfction 2 Km road from Heera Wah to village Paryya , 1 Km from village to Akber Mugheri. 3Km road Badalabad, New Road from village Essa Khan Brohi to Mughall Khan Brohi 1.2 Km, 0.5 Km new road in village Ali Muhammad from Main Road to Otaq of Ghulam Shabbir Aheer, 1 Km road from BHU Behram to Khokhar Mohalla (Sirai Quran Khokhar Otaq)			
2196	Construction asphalt road (New / Repair) various roads with drainage Municipal Committee Rohri. Repair of Pedestrian path ways. Roads surface and repairing of old Sukkur Channel and landsdown bridge, road	LG (Roads)	Sukkur	99.14
2197	Construction of road Milad Mustafa Chowk via Long Bhatti to National Highway and Ghulam Ali Shaikh Chowk via Piyaro Chohan construction C.C Topping Umer Khas wah village Jatoi to Eidan Shaikh, paver block and drains UC Hingoro and UC Nindapur Kot Bullo, Kolachi Sirohi	LG (Roads)	Sukkur	96.43
2198	Rehabilitation / Reconditioning of road from Khairpur Machiyoon road at Mang tagar brdge towards from village Gagri at Dargah Hajna Shah road including link from Dargah Pir Ghaffar Shah Road to village Badai Machi, Buxo wahanwuth 1-1/2 Premixed Carpet including masonry structure and construction, providing / fixing C.C paving block (55000 Sft) in Taluka Khairpur mile 0/0-4/0 (6.40 Km)	LG (Roads)	Khairpur	98.50
2199	Reconditioning / Rehabilitation of road from old National Highway over towards from Khairpur old Khajoor Mandi road to village Ali Dino Burdi at District Council road village Khokhar, Village Mahar Tariyo including link to Wari Goth upto Umrani village leading through under Railway Phattak Khairpur with masonry structure and construction, providing / fixing C.C paving block (165255 Sft) with 1-1/2 premixed carpet mile 0/0-6/3 (10.20 Km)	LG (Roads)	Khairpur	98.60
2200	Rehabilitation / Reconditioning of road from New National Highway village Pir Mangio to village Qaimuddin Khorkhani Baloch towards with Parallel to the Pir Mangio Shakh at Bandani Phulpoto including approach from village Waris Gambhir, Dur Muhammad Phulpoto upto Razi Goth road with 1/2 premixed carpet including retaining wall for protection of road (1320 Rft) including construction and providing / fixing C.C paving block (222200 Sft) Taluka Khairpur Mile 0/0-7/1 (11.40 Km)	LG (Roads)	Khairpur	117.50
2201	Widening & reconditioning of road, paver block streets and drainage at Moro city	LG (Roads)	N. Feroze	160.06
2202	Construction of roads in various U.Cs in Taluka Nawabshah and Daur ( a) Construction of road from Nawabshah 60th Mile road to village Sim Nala Murad Bux Brohi Mile 0/0-4/0 (0.80 Km) (Ghandtar) (b) Reconditioning of road from old Sugar Mill Road to village Allah Dino Phanwar Mile 0/0-0/3+330 (0.70 Km) (Ghandtar) (c) Construction of road from Nawabshah - Daur road to village Jamal Shah mile 0/0-0/3+220 (0.66 Km) (Ghandtar) (d) reconditioning of road from Nawabshah 60th Mile road @ 87 Mori to viallge Rais Karam Ali Khan Jamali various streets mile 0/0-3+440 (0.73 Km) (Ghandtar) (e) Reconditioning of road from Nawabshah Sanghar road to viallge Mehmoood Jamali mile 0/5-1/0 0.60 Km) (Sakhi Umed Ali Jamali) (f) Reconditioning of road from Nawabshah Sanghar road to village Baig Muhammad Mugheri mile 0/0-1/0 (1.60 Km) (Sakhi Umed Ali Jamali) (g) Construction of road from Nawabshah Sanghar road to Choudhry Ismail Arain road to Doro Naro @ Path village Muhammad Saleh Khaskheli Mile 0/0-0/2+330 (0.50 Km) I/C 23*21 Slab (Sakhi Umed Ali Jamali) (h) Construction of road from Nawabshah Sanghar road - Ali Jan Brohi Mile 0/4 to village Ghulam Mustafa Brohi mile 0/0-0/2 (0.40 Km) & various portion (Sakhi Umed Ali Jamali) (i) Construction of road from desert area road @ mile 1 1/3 to New village Ch. Manzoor Arain I/C approach length mile 0/0-0/2 (0.40 Km) (Obhari Sawari) ( j) Reconditioning of road from Nawabshah - Qazi Ahmed Road @ mile 7/0 to village Bahawal Khan Zardari road mile 0/0-0/4 + 220(0.87 Km) (Chanesar-I) K) Reconditioning or road from Nawabshah - Qazi Ahmed road @ mile 9/0 to village Chanesar mile 0/0-1/0 (1.60 Km) (Chanesar -I) L) Reconditioning of road from Nawabshah Qazi Ahmed road Chanesar Stop to village Hameer Kaniyo via Allah Rakhio Kaniyo and Khair Muhammad Rind road mile 0/0-1/5 +440(2.73 Km) (Chanesar-I) M) Construction of road from Nawabshah Jam Sahib road @ mile 1/2 village Abdul Qayoom Arain (II) Nawabshah Sanghar road to 2/4 village Khushahl Zardari road mile 0/0-0/4 -110 (Sakhi Umed Ali Jamali) N) Reconditioning of road from Wali Muhammad Rind road - Bhambo minor IP path to village Kamil Khan Rind mile 0/0-1/7 (3.0 Km) (Wali Muhammad Rind) O) Reconditioning of road from Nawabshah - Daur road @ mile 4/4 to village Haji Miitho Khan Zardari road mile 0/0-0/2 (0.40 Km) ( Khair Shah) P) Reconditioning / Construction of road from Nawabshah to Daur road @ mile 7/0 to village Lal Chand via Village Haji Muhammad Bux Zardari road mile 0/0-2/0 (3.20 Km) (Mureed Khan Zardari) Q) Reconditioning of road from Laique Zardari @ mile 1/0 to Dargah Malook Peer road mile 0/0-2/4 (4.00 Km) (Mureed Khan Zardari) R) Reconditioning of road from Tri Mor road Laique Zardari road to Allah Wasiyo Zardari and Dr. Fateh Ali (Mureed Khan Zardari) (S) Reconditioning of road from Dargah Malook Peer road to village Ali Khan Zardari (Mureed Khan Zardari)	LG (Roads)	S.B.A	232.24
2203	(A) Construction of link road from Hayat Chaniho road to village Dr. Ramzan Dars road 0.0 to 1.00 Km (B) Construction of link road from Khipro Ghulam Nabi Shah road to village Gabool Shar 0.0 to 1.00 Km (C) Construction of link road from Miandad Bhanbhro road to village Bangul Khan Bhanbhro 0.0 to 1.00 Km (D) Reconditioning / Construction of link road from Sanghar Khipro Offtacking road Wassan Hinorjo road via village Anb Dars 0.0 to 2.00 Km (E) Reconditioning of link road from Khipro	LG (Roads)	Sanghar	97.31

ADP NO	Name of Scheme	Department / Sector	Location	Cost
	Ghulam Nabi Shah Road to Dargha Qabool Shah via Jama Masjid Bhit Bhaiti 0.0 to 1.00 Km (F) Construction of link road from Saddique Khaskheli to village Arbab Ali Samoon via Khalifa Rahmatullah Dars 0.0 to 2.00 Km (G) Construction of link road from Jamal Shah road to Village Abdul Sattar Wassan 0.0 to 1.00 Km (H) Construction of link road from aqil Hingoro road to village Tayyab Bozdar 0.0 to 1.00 Km from A to H Total 10.00 Km			
2204	1-1/2 Thick Asphalt W/R Shahdadpur - Gupchani road to PTC Barhoon road mile 0/0-1/4 (2.40 Km) (18F")	LG (Roads)	Sanghar	44.01
2205	Const: of Road Tando Jan Muhammad to Soomro Khan Kalohi (Balo jo kunb) to village Mir Hayat Talpur Deh 265 to Mir yar Muhamamd (Rabou) connect to Tando Jan Muhammad Digri Road	LG (Roads)	Mirpurkhas	98.57
2206	Const: of Road village Uamid Ali Jamali to Raheem Mirnani to Sher Muhammad Kamboh to Dost Muhammad Otho to connect Najma Sugar Mill Road	LG (Roads)	Mirpurkhas	99.24
2207	Recond: / Imp: of Road Naoukot Fazal Bhambro Road to Nafees Nagar to Ali Hassan Gurgez to Shanker Bheel to Shadman Gurgez.	LG (Roads)	Mirpurkhas	139.55
2208	Recond: / Imp: of Road Tedi Mori to Arif Khan Kapri to Daria Khan Pitafi to Karim Bux Bhatti to Mir Manzoor Talpur to Khero Kolhi to connect Jhodo to Samroo Road	LG (Roads)	Mirpurkhas	83.49
2209	Construction of Road from Main Jamshoro Road to Sehrish Nagar Railway Phatak via Hyderabad Bypass (8.0 Km) Taluka Qasimabad Hyderabad	LG (Roads)	Hyderabad	205.98
2210	W/R of Road from Hyderabad Bypass 8/1 to Darya Baig Mughal (2.35 Km) Taluka Qasimabad Hyderabad	LG (Roads)	Hyderabad	88.98
2211	Construction of Road from Dargah Shah Bukhari to Ayoub Hotel N-5 (3.50 Km) Taluka Qasimabad Hyderabad	LG (Roads)	Hyderabad	94.12
2212	Improvement / Construction of Road from Sanjhar Mir Bahar to Hyderabad Bypass via Sajjan Detho (3.60 Km) Taluka Qasimabad Hyderabad	LG (Roads)	Hyderabad	83.04
2213	Construction / Rehabilitation of various Roads, CC & Paver Block Roads and Streets in UC Husri i/c Main Husri Road to Village Khameeso Jogi, Taluka Latifabad Hyderabad	LG (Roads)	Hyderabad	181.06
2214	Construction / Rehabilitation of various Roads in PS-64 Ganjo Takar Phatak to New Ali Asgarabad Phatak, Ganjo Takar Phatak to Allah Dino Khumarn, Village Jani Rind Road to Noonari Goth & UC 86,87,91,92,94 & Other City Areas Taluka Latifabad Hyderabad	LG (Roads)	Hyderabad	174.33
2215	Various Roads of Hyderabad City	LG (Roads)	Hyderabad	187.33
2216	Construction of road from Seerani Kadhan road @ point Ahmed Shah Mori to Lakho Pir alongwith inspection path of Noor Wah (12.00 Km)	LG (Roads)	Badin	99.32
2217	Construction of road from Iqbal Sarejo Umer Mallah road to Village Mir Hoat Haji Vikio Khaskheli and Bakar Mori upto Arab Mallah i/c link Ramzan Mandhro (11.80 Km)	LG (Roads)	Badin	99.33
2218	Improvement / Construction of road from Badin Seerani road to connect Pathan Parhyar road via Haji Parhyar (Construction 3.40 Km, improvement 9.00 Km)	LG (Roads)	Badin	99.32
2219	Improvement / Construction of road from water supply post office road to abu Shaikha (Allah Dino Soomro) i/c link road from Badin Seerani road Ghulam Rasool Lutter (Construction 6.00 Km, improvement 7.60 Km)	LG (Roads)	Badin	99.22
2220	Construction of road Village Juman Ketlo Thaheem, Construction of road village Sawan Rind, Construction of road village Pehroz Magsi & Muhammad Khan Magsi, Construction of road village Rakhiyo Jakhro, Construction of road village Nim Mallah, Construction of road village Ghulam Hussain Leghari, Construction of road Saleh Muhammad Rind, Construction of road village Pir Ali Qutub, Construction of road village Jakhra and Chandia Construction of road Muradpur Wahiya Basar Charan, Construction of road village Taju Panhwar via Wago Panhwar to Ali Hassan Jakhro, Construction of road village Miran Mallah	LG (Roads)	Sujawal	156.88
2221	Construction of road Sujawal Bathoro road to Sheerazi village, Construction of road village Hassan Sain Dad Magsi, Construction of road Village Ibrahim Lund, Construction of road village Chaniyo Stop, Construction of road village Mir Khair Muhammad Zaur Abral Road, Construction of road village Gul Muhammad Bhatti, Construction of road village Haji Misri Lund village, Construction of road village Abdul Rasheed Palejo, Improvement of road Dar Malook Shah, Improvement of road village Saleh Muhammad Abro, Improvement of road Daro Bathoro road to village Raees Shahnawaz Leghari, Improvement of road village Haji Papan Shaikh	LG (Roads)	Sujawal	151.80
2222	Construction of Link road village Abdul Razzaque Jamari, Construction of road village Malook Jhurko, Construction of road village Allah Bachayo Babar, Construction of road village Khan Muhammad Babar, Construction of road village Allah Parhayo Gabbar, Construction of road village Babu Khamiso Babar, Construction of road village Achar Kadero Keengar, Construction of road village Dargah Qureshi Baba Babu Shoro, Construction of road Ilyas Jakhro, Construction of road village Daim Shoro, Construction of road village Suleman Brohi, Construction of road village Ali Muhammad Panhwar, Construction of road village Missan Abad road, Construction of road village Ali Muhammad Khaskheli, Construction of road village Khan Jakhro to Ameer Bux Jakhro. Improvement of road Punhal Jamali, Improvement of road village Haji Mehmood Dal, Improvement of road village Ber Machi, Improvement of road village Saleh Bhambro, Improvement of road village Ali Hassan Brohi road, Improvement of road village Muhammad Ramzan Gopang, Improvement of road National Highway to Band Mori road, Improvement of road National Highway to Brhio Sheedi Mori, Improvement of road Sattiyoun road to village Sajjan Jakhro, Improvement of road village Raju Nizamani, Improvement of main road to Mureed Roonjho via Shabir Abdani	LG (Roads)	Thatta	203.18
2223	Construction of road village Abdul Kareem Lashari, Construction of road village Mubarak Lashari, Construction of road village Muhammad Khan Katiyar,	LG (Roads)	Thatta	63.50

ADP NO	Name of Scheme	Department / Sector	Location	Cost
	Construction of road village Mitho Lashari to Ragwah Mori, Construction of main road Ghulamullah to Dargah Dars Dad, Construction of road village Jharo Khan Lashari			
2224	Construction of road village Ali Muhammad Shoro, Construction of road village Gul Hassan Shah Chattan Nahiyo, Construction of road village Gul Hassan Lashari, Construction of road village Muhammad Akyal Kehar pacca road, Construction of road village Abdullah Kehar, Construction of road village Hashim Shohlani, Improvement of road village Muhammad Umar Bhatti, Construction of main road Arbab Muhammad Qasim	LG (Roads)	Thatta	70.50
2225	Construction of road from Chaudhry Nek Muhammad road (near Ali Muhammad Katiar) to village Ramzan Jokhio (via village Khaman Jokhio, Kabil Bathro and Ramzan Jokhio water supply point), Taluka Mirpur Sakro, District Thatta	LG (Roads)	Thatta	60.00
2226	"(i)Construction of 30 Nos. RCC box culverts on Nai Desvi along with approaches city portion at Mukhi Pump Thano Bula Khan, Taluka Thano Bula Khan District Jamshoro (ii) Rehabilitation of road Thano Bula Khan City Portion mile 0/0-1/2 District Jamshoro (iii) Construction of Road from Toung Near Phang Luck to Village Ghazi Khaskheli along with rain Drain Nala Phang Luck and Retaining wall of Phang Luck Deh Ball UC Toung Taluka Thano Bula Khan District Jamshoro	LG (Roads)	Jamshoro	102.39
2227	Improvement of road from Indus Highway to Baid village via Kande Chukhi Connecting to Gozo Village, Including paving block, drain & retaining wall. Mile 0/0-5/6	LG (Roads)	Dadu	99.59
2228	W/R road from Piaro Station to Patt and improvement of road village Shahabad via village Jamal Panhwer and village Bag Chandio and construction of Paving and Block and Drainage of above mentioned villages.	LG (Roads)	Dadu	99.90
2229	Construction of road from I.H.R / Side Burria Shakh to Yaseen Leghari Petrol Pump Via L/5 Deeta Shakh to Panjmor Construction of Paving Block and Drainage from Shahjana Park to Dual Carriages Way Road to Govt: Girls High School Via Najam Colony / Mazdoorabad and Pir Colony i/c Retaining Wall and 2 nos. 12-meter span skew bridges mile 0/0-1/6	LG (Roads)	Dadu	99.50
2230	Improvement of road / paving block / foot paths / sign boards / drainage from Hassan Darwesh Graveyard to Rr. Manzoor Leghari Chowk i/c Kheer Mori to Johi Chinni road via Mank Kingrani & Johi Bhan road	LG (Roads)	Dadu	98.51
2231	Construction of Roads for Ghaghar City UC-18 Chandparo, District Malir Karachi	LG (Roads)	Karachi (M)	70.25
2232	Construction of Bridge Over Malir Nadi near Goth Siddique Jokhio, UC Choochar, District Malir Karachi	LG (Roads)	Karachi (M)	175.00
2233	Construction of Roads & C.C Streets of UC-19, Pipri, District Malir Karachi	LG (Roads)	Karachi (M)	71.22
2234	Construction of Main Roads & Internal Street Roads of Gulshan-e-Hadeed Ph-1 & Ph-11, District Malir, Karachi	LG (Roads)	Karachi (M)	99.90
2235	Construction of Road alongwith drainage, Sewerage and Paver stones in UC Sharafi District Malir Karachi	LG (Roads)	Karachi (M)	99.88
2236	Construction of Road alongwith drainage, Sewerage and Paver stones in UC Quidabad and UC Cattle Colony Ward No. 1 District Malir Karachi	LG (Roads)	Karachi (M)	99.83
2237	Construction of Road alongwith drainage, Sewerage and Paver stones in UC Maminabad and UC Dawood Chowrangi, Ward No. 4, District Malir Karachi	LG (Roads)	Karachi (M)	84.92
2238	Construction of Road alongwith drainage, Sewerage and Paver stones in UC Ghazi Dawood Brohi, UC Gharibabad and UC Jaffar Tyar, District Malir Karachi	LG (Roads)	Karachi (M)	99.85
2239	Construction of Roads Paver Block Street and Improvement of Sewerage System in UC Salij Muhammad Wali Muhammad and UC Razzakabad (PS-90) District Malir, Karachi	LG (Roads)	Karachi (M)	99.97
2240	Construction of Roads Paver Block Street and improvement of Sewerage system in UC Chokhundi and UC Jumma Hemayti (PS-90) District Malir, Karachi	LG (Roads)	Karachi (M)	99.81
2241	Construction of Roads Paver Block Street and improvement of Sewerage system in UC Khaldabad and UC Cattal Colony (PS-90) District Malir, Karachi	LG (Roads)	Karachi (M)	92.26
2242	Construction of Metaled Road Union Council No-28	LG (Roads)	Karachi (M)	99.99
2243	Rehabilitation and Reconstruction of Roads & Laying of CC flooring / Paver Block at different areas of PS-97	LG (Roads)	Karachi (Kor)	147.75
2244	Improvement & Reconstruction of Roads in UC-37 Ward 1	LG (Roads)	Karachi (Kor)	81.01
2245	Improvement / Rehabilitation of roads from Machar Colony Lala Hotel to fateh Muhammad School and from Lasi Goth Graveyard to Naddi & from Ajmeri Building to Rupali Centre, from Dost Muhammad Khan Wazir Goth to Faqeer Goth and from Sikh Goth to Noor Khan Goth, PS-99, District East, Karachi	LG (Roads)	Karachi (E)	97.00
2246	Improvement / Rehabilitation of roads in different areas of PS-99, District East Karachi	LG (Roads)	Karachi (E)	97.23
2247	Construction of Roads, Underpasses and Drainage at Taluka Daharki, District Ghotki	LG (Roads)	Ghotki	150.00
2248	Construction of road from Sehwan Daul Carriage Way to Kila Rest House road Mile 0/0-1/2 (2.012 Km)	LG (Roads)	Jamshoro	48.45
2249	Construction of roads at Taluka Matli District Badin (1) Village Sanpo Shah to main Tando Gh. Ali road (1.5 Km) (2) Village Soomar Chandio to vikio Jatvi UC Budho Qambrani (1 Km) (3) Village Ramzan Chandio to Jamarao Mori Dumbalo (1 Km) (4) Village M. Azeem Khoso to main T. Gh. Ali Road	LG (Roads)	Badin	49.36
2250	Improvement of Road from Bhan-Johi road to village Makki to Village Mushtaq Jamali and Paver Block Streets and drains at various streets of town Committee Phulji Station	LG (Roads)	Dadu	99.17

ADP NO	Name of Scheme	Department / Sector	Location	Cost
2374	Construction / Improvement of road from Kamber Wagan road @ point Ghat Shakh upto Asian Road connected with Wagan Warah road mile 0/0-3/7 (6.2 Kms)	LG (Roads)	Kamber	50.00
2407	Construction & Rehabilitation of Parks in 8/A, 8/B, 8/C UC-32 Bilal Colony, Korangi	LG (Community Services)	Karachi (Kor)	90.00
2408	Rehabilitation of Parks Behbood Ladies Park Shirin Jinnah Colony, Adjoining to Two Sword UC-30 & 31, DMC South	LG (Community Services)	Karachi (S)	33.33
2409	Establishment of Dispensaries & Parks and Grounds in Different UCs of NA-249	LG (Community Services)	Karachi (Kea)	195.36
2410	Construction of Multipurpose Sports Playground with Walking Track including Pavilion, Restrooms, Flood Lights, Standby Generator in Sachal Goth, UC-30	LG (Community Services)	Karachi (E)	99.85
2411	Construction of KDA Park including Walking Track, Rides, Boundary Fencing, Food Street, Grassy area & LED Park Lights, Beautification of Surrounding areas Adjacent to Kings Residency in Front of Corniche Comforts flats Block-13 Gulistan-e-Johar	LG (Community Services)	Karachi (E)	99.77
2412	Construction of Park and Playground in UC - 30 & 31	LG (Community Services)	Karachi (S)	100.00
2413	Rehabilitation of Grounds & Parks, Eid Gah Ground Ward-2, Railway Ground Ward-3, Qalandari Ground Ward-7, Park in Railway Colony Bulbul Barrick Ward-3 Park in Chandio village Adjourned to Dada Bhai village, Park in Kaleem Qazi Ground Ward-7	LG (Community Services)	Karachi (S)	132.48
2414	Rehabilitation of Public Parks and Public Grounds, UC-16,19,24 & UC-26, District West Karachi	LG (Community Services)	Karachi (W)	80.00
2415	Establishment of Public Grounds & Public Parks in UC-11, 12, 13, 17, 27 & 28	LG (Community Services)	Karachi (W)	64.44
2483	Construction of Civic Centre at Mula Fazal Auditorum Hall Chawkiwara Road Lyari	Mega Projects for Karachi	Karachi	434.63
2661	Construction of New Water Supply Scheme for various Villages in Taluka Hyderabad Rural. (SDG # 6)	Public Health Engineering	Hyderabad	371.46
2664	Installation of 10 Reverse Osmosis Plant (RO Plants) in UC Gabo Pat Keamari Town Karachi (SDG # 6).	Public Health Engineering	Karachi	97.88
2665	Laying of New Water Supply Line and Construction of Underground water Tank in UC Sahle Muhammad, UC Wali Muhammad UC Razzakabad and UC Chokundi (SDG # 6).	Public Health Engineering	Karachi	96.79
2666	Rural Water Supply Scheme Rehri Mian Goth Phase-II (SDG # 6).	Public Health Engineering	Karachi	99.72
2667	Construction of Water supply Scheme in UC Ghareebabad, Sahibdad Goth and UC Ghazi Dawood Brohi (SDG # 6).	Public Health Engineering	Karachi	99.88
2668	Water Supply Scheme for Jam Goth, Kotiraro, Ghulam Mohammad Goth, Hashim Goth (SDG # 6)	Public Health Engineering	Karachi	45.47
2677	Improvement of Water Supply Scheme in Town Committee Chhachhro & Town Committee Kheme-jo-Par (SDG # 6).	Public Health Engineering	Tharparkar	65.83
2680	Extension & Rehabilitation of Water Supply Scheme of Brohi Muhalla and Irrigation Muhalla of City Mirpur Bathoro (SDG#6)	Public Health Engineering	Sujawal	71.98
2687	Water Supply Scheme for village Ali Muhammad Katiyar (SDG # 6).	Public Health Engineering	Thatta	14.16
2688	Water Supply Scheme from Bawa Puran Das Branch in Fakir Jo Goth (Baba Sirichand Darbar )(SDG # 6).	Public Health Engineering	Thatta	48.59
2695	Water Supply Schemes in various Villages of Taluka Sehwan & Manjhand (SDG # 6).	Public Health Engineering	Jamshoro	116.37
2697	Construction of Water Supply Schemes in various Villages of Taluka Sehwan (SDG # 6).	Public Health Engineering	Jamshoro	85.90
2703	Water Supply Scheme of Village and Union Council Akbarpur. (SDG # 6).	Public Health Engineering	Sukkur	47.65
2704	Water Supply Scheme of Village and Union Council Khabri Bhatt (SDG # 6).	Public Health Engineering	Sukkur	49.73
2705	Water Supply Scheme of Village and Union Council Lal Jurio (SDG # 6).	Public Health Engineering	Sukkur	50.62

ADP NO	Name of Scheme	Department / Sector	Location	Cost
2706	Water Supply Tank Alongwith Distribution Network for Old Sukkur (SDG # 6).	Public Health Engineering	Sukkur	97.41
2707	Water Supply Scheme various Areas of Abad Lakha and Arain Sukkur (SDG # 6).	Public Health Engineering	Sukkur	53.99
2714	Construction of Water Supply Scheme Deh Gulanpur, Deh Kathgarh, Deh Line Purani and Deh Keenjhar (SDG#6)	Public Health Engineering	Kashmore	100.00
2717	Providing of Drinking Water through Tube Wells for K.N Shah City and adjoining villages Muhammd Murad Chandio & Fatihpur Taluka K.N Shah (SDG # 6).	Public Health Engineering	Dadu	100.00
2718	Water Supply Scheme Thariri Mohabat Town (SDG # 6).	Public Health Engineering	Dadu	54.54
2719	Construction of Water Supply Scheme in Village Ghaibi Dero, Sono Khan Chandio, Rabban Khan Chandio, Matara & Kajlo Khan Chandio, Taluka Kamber (SDG#6)	Public Health Engineering	Kamber	100.00
2720	Water Supply Schemes for Village Fateh Ali Lashari, Samano Chakrani, Ali Dino Burdi and Abdul Hakeem Chakrani, Village Mehar, Village Lique Rajper, Village Aleem Rajper, Village Wada Bhatti. (SDG # 6).	Public Health Engineering	Khairpur	81.47
2722	Installation of 02 Nos R.O Plant for Village Hashim Chawro UC Ratokat, Jaro Khan Jogi UC Kothi Kandhoro Taluka Larkano 09 Nos. of Colverts for Village Sabzal Mugheri, Taj Muhammad Mugheri (Bado Wah, Mahi Khan Talo Khan Jagirani (Bdo Wah) Kirir Khan Mugheri (Bado Wah), Syed Ameer Ali Shah (Sim Shaakh Khairpur) Ghulam Muhammad Mugheri Near Hassan (Mittho Dero) Sim Shaakh Kambir Khan Mugheri (Bado Wah), Qambeer Jagirani (Earther Wah Gerello), Hukumdad Brohi (Kothi Kalhoro) (SDG # 6).	Public Health Engineering	Larkano	35.00
2726	Construction of Water Supply Scheme for Old Nauabad City and adjoining areas (SDG # 6).	Public Health Engineering	Sanghar	22.59
2727	Construction of Water Supply Scheme for Lemo Khaskheli Deh Raharoo and adjoining Villages (SDG # 6).	Public Health Engineering	Sanghar	54.45
2728	Rural Water Supply Scheme Chak # 23, 24 Dewan Wali Ram. (SDG # 6).	Public Health Engineering	Sanghar	51.45
2770	Construction of New Drainage System & CC Blocks at UC Halepoto, UC Seri & UC Almani. (SDG # 6)	Public Health Engineering	Hyderabad	78.02
2771	Providing Sewerage System in various Ucs of Taluka Murad Memon (SDG # 6).	Public Health Engineering	Karachi	99.92
2772	Construction of RCC Nala from Mehmood Goth to Sea Side at Lath Basti UC Rehri, Taluka Ibrahim Hyderi. (SDG # 6).	Public Health Engineering	Karachi	99.79
2773	Construction of RCC Nala from Graveyard to Sea Side at Rehri Goth Taluka Ibrahim Hyderi (SDG # 6).	Public Health Engineering	Karachi	99.85
2774	Providing & Laying of Sewerage & Paver Blocks and internal roads at various villages (Pir Sarhandi, Jam Kando, Satal, Usman) of UC- 16 Kotraro, Bin Qasim (SDG # 6).	Public Health Engineering	Karachi	65.28
2775	Construction of Drainage Scheme Village Umer Bughio (SDG#6).	Public Health Engineering	Mirpurkhas	46.38
2783	Drainage Scheme along with CC Block for villages Nana Gandaro, Manik Behrani, Daragh Shah Mubeen, Abdul Majeed Sabughar, Daragh Shah Ladho via Kashighar Muhalla, Ghulam Thenga, Haji Khamiso Khaskheli, Christian Colony (SDG # 6).	Public Health Engineering	Thatta	70.00
2784	Construction of Open Surface Drain, CC Flooring and Paving Block for Different Wards of Thatta City (SDG#6)	Public Health Engineering	Thatta	174.28
2789	Construction of CC Block and Drainage Schemes at various locations of Taluka Sehwan (SDG # 6).	Public Health Engineering	Jamshoro	59.86
2790	Construction of Drainage Scheme Village Karampur and Adjoining Villages, Taluka Sehwan (SDG # 6).	Public Health Engineering	Jamshoro	98.72
2791	Construction of Drainage Scheme at Various Villages of Taluka Manjhand (SDG # 6).	Public Health Engineering	Jamshoro	49.83
2792	Extension & Rehabilitation of Drainage Scheme village Sari, UC Sari, Taluka Thano Bula Khan (SDG # 6).	Public Health Engineering	Jamshoro	51.04
2793	Construction of Disposal Work and Brick Masonry Nalla at Sandoz Road Taluka Kotri, District Jamshoro (SDG#6)	Public Health Engineering	Jamshoro	99.97

ADP NO	Name of Scheme	Department / Sector	Location	Cost
2794	Improvement and Extension of Urban Drainage Scheme Manjhad, District Jamshoro (SDG # 6).	Public Health Engineering	Jamshoro	97.62
2795	Construction of Drainage Scheme at Village Sain Dino Mallah Taluka Kotri (SDG # 6).	Public Health Engineering	Jamshoro	49.50
2796	Rural Drainage Scheme Bajara (SDG # 6).	Public Health Engineering	Jamshoro	65.23
2797	Construction of Drain Type 'A', 'B' & 'C' and CC Block at Taluka Sehwan.	Public Health Engineering	Jamshoro	166.56
2798	Construction of CC Block & Drains at various Villages of UC Talti, Bhambha & UC Shaikh (SDG # 6).	Public Health Engineering	Jamshoro	99.94
2799	Construction of CC Block & Drains at Various Streets of District Jamshoro (Revised on 15.03.22) (SDG # 6).	Public Health Engineering	Jamshoro	120.68
2803	Drainage Scheme of Belo City and C.C of Sujawal (SDG # 6)	Public Health Engineering	Sujawal	56.34
2804	CC at Bathoro City, Syedpur and Belo City and Drainage System of Daro (SDG # 6)	Public Health Engineering	Sujawal	43.47
2806	Improvement of Existing Drainage System in Bau Khan Pathan & Rural Drainage Scheme Paljani Station Taluka & District Matiari (SDG # 6).	Public Health Engineering	Matiari	99.50
2814	Construction of Drainage Scheme at Various Village of Union Council Akbarpur (SDG # 6).	Public Health Engineering	Sukkur	49.82
2815	Drainage Scheme Village Rajib Ali Dayo, Pir Hasil Shah Colony, Murad Shah Colony Lokoshed and Village Khari Mumbrani and; Rehabilitation of Drainage Scheme Mola Mohib Shah Muhallah, Bedal Becus Tunnel disposal, Al-Abbad disposal Rohri City (SDG # 6).	Public Health Engineering	Sukkur	96.17
2816	Construction of Drainage Scheme at Various Village of Khabri Bhatt (SDG # 6).	Public Health Engineering	Sukkur	47.42
2817	Construction of Drainage Scheme at various Village of Lal Jurio (SDG # 6).	Public Health Engineering	Sukkur	47.78
2818	Construction of Drainage Scheme at Bachal Shah Miani Sukkur (SDG # 6).	Public Health Engineering	Sukkur	133.30
2819	Construction of Drainage Scheme at Various Areas of Abad Lakha and Arain Sukkur (SDG # 6).	Public Health Engineering	Sukkur	48.26
2820	Construction of Drainage Scheme Allahabad Colony Sukkur (SDG # 6).	Public Health Engineering	Sukkur	90.79
2821	Construction of Drainage Scheme Lal Mashaikh Sukkur (SDG#6).	Public Health Engineering	Sukkur	41.42
2822	Construction of Drainage Scheme at Various areas of Newpind and Micro Tower Sukkur and Qureshi Goth (SDG#6).	Public Health Engineering	Sukkur	91.67
2823	Construction of Drainage Schemes on one side of Peer Wah Pano Akil town (SDG # 6).	Public Health Engineering	Sukkur	44.67
2824	Drainage Scheme for left over Area of City Pano Akil (SDG#6).	Public Health Engineering	Sukkur	44.05
2825	Rehabilitation of Drainage System of Bagarji Town & Village Gosarji/and Construction of Raods, Drains/Laying of Paver Block at Various Areas of UC Naseerabad and UC Jaffarabad Taluka New Sukkur (SDG # 6).	Public Health Engineering	Sukkur	99.92
2826	Drainage Scheme Village Piaro Labano, Village Lal Bux Mahtam, Village Ali Shaikh & Village Jatoi & Malik Taluka Rohri (SDG # 6)	Public Health Engineering	Sukkur	59.17
2828	Providing and Fixing Paving Blocks with Road Drainage in Various Streets of Khanpur Town and Various Villages of UC Mian Jo Goth (SDG # 6).	Public Health Engineering	Shikarpur	68.65
2829	Drainage Scheme Garhi Yaseen (SDG # 6).	Public Health Engineering	Shikarpur	94.39
2835	Construction of Sewerage System for Old Nauabad City and Adjoining Areas (SDG # 6).	Public Health Engineering	Sanghar	26.25

ADP NO	Name of Scheme	Department / Sector	Location	Cost
2836	Construction of Surface Drainage/CC Paver Streets for Kurkli, Jafar Leghari, Kandiyari Jam Nawaz Ali Taluka (SDG#6).	Public Health Engineering	Sanghar	123.85
2837	Improvement and Extension of Drainage Scheme (including C.C Paver) Village Mulla Makhan, Tando Adam (SDG # 6).	Public Health Engineering	Sanghar	44.32
2838	Rural Drainage Scheme Chak # 24, 39, 29 Dewan Wali Ram (SDG # 6).	Public Health Engineering	Sanghar	54.78
2839	Rural Drainage Scheme of Village, Ghundan preetamabad, Allahdad Leghari & sher Leghari (SDG # 6).	Public Health Engineering	Sanghar	118.29
2841	Improvement and Extension of Urban Drainage Scheme Sinjhor (SDG # 6).	Public Health Engineering	Sanghar	105.28
2843	Drainage Scheme of Radhan Town (SDG # 6).	Public Health Engineering	Dadu	99.53
2847	Construction of Paver Blocks & C.C Drains in Various Muhalla's City Shahdadkot (SDG # 6).	Public Health Engineering	Kamber	164.86
2848	Construction of C.C Drains and Paver Blocks in UC's (05 Nos.) of Taluka Shahdadkot (SDG # 6).	Public Health Engineering	Kamber	100.00
2849	Construction of C.C Drains and Paver Blocks for Muhallas of Shahdadkot City (SDG # 6).	Public Health Engineering	Kamber	100.00
2850	Paver Block and C.C Drains in Various Muhallas of Mirokhan City (SDG # 6).	Public Health Engineering	Kamber	52.18
2851	Paver Block and C.C Drain in Various villages of Taluka Mirokhan and Sujawal and Kamber (SDG # 6).	Public Health Engineering	Kamber	137.12
2852	Paver Block and C.C Drain in Various Muhallas of City Kamber. (SDG # 6).	Public Health Engineering	Kamber	90.99
2853	Construction and Renovation Road & Paver Block & CC Drain in Various location in City Kamber & Taluka Kamber (SDG # 6).	Public Health Engineering	Kamber	200.00
2854	Paver Block and C.C Drain in Various villages of Taluka Kamber & Warah (SDG # 6).	Public Health Engineering	Kamber	146.91
2855	Construction of Renovation Road & Paver Block & CC Drain in Various Location in City Warah & Taluka Warah (SDG#6).	Public Health Engineering	Kamber	96.42
2856	Construction of C.C Drain, CC Block & Paver Blocks at Various Villages of Taluka Warah (SDG # 6).	Public Health Engineering	Kamber	100.00
2857	Construction of C.C Drain, CC Block & Paver Blocks at Various Villages of Taluka Naseerabad (SDG # 6).	Public Health Engineering	Kamber	78.76
2858	Construction of Renovation Road & Paver Block & CC Drain in various location in City Nasirabad & Taluka Nasirabad (SDG#6)	Public Health Engineering	Kamber	96.43
2859	Construction of Renovation Road & Paver Block & CC Drain in Various Location in Town Ghaji Khuhawar (SDG # 6).	Public Health Engineering	Kamber	47.77
2861	Drainage System for left over areas of City Naudero (SDG#6).	Public Health Engineering	Larkano	124.85
2862	Construction of Paver Block And C.C Drain in Various Areas of City Ratodero (SDG # 6).	Public Health Engineering	Larkano	123.79
2863	Paver Block/ Drain for different Villages of UC's Bero Chandio, Maheto, Fatehpur, Rasheed Wagan, Mithodero, vikya Sangi, Lund, Dhamrah, Ratokot, Kothi Kalhoro Taluka Larkana (SDG#6).	Public Health Engineering	Larkano	115.00
2864	Construction of Paver Block & CC Drain in Various locations of UC-01 to 05 Larkano City (SDG # 6).	Public Health Engineering	Larkano	150.00
2865	Construction of Paver Block and CC Drains of Various Locations of UC-06 to 10 City Larkano (SDG # 6).	Public Health Engineering	Larkano	150.00
2866	Construction of Paver Block and CC Drains of Various Locations of UC-11 to 15 City Larkano (SDG # 6).	Public Health Engineering	Larkano	150.00
2867	Construction of CC Drains & Paver Blocks in various streets of Union Committees No. 16 to 20 of City Larkano (SDG#6).	Public Health Engineering	Larkano	200.00

ADP NO	Name of Scheme	Department / Sector	Location	Cost
2868	Paver Block & CC Drains from Allah Park Tower to Shahdadkot Naka Bab-e-Zulfiqar via Rest House and Kamber Lashari Road (2.0 Kms) at Taluka Ratodero (SDG # 6).	Public Health Engineering	Larkano	66.51
2869	Paver Block & CC Drains from Allah Wali Masjid to Abdul Wahid Soomro Gate via New Eid Gah and Massan (1.50 kms) at Taluka Ratodero (SDG # 6).	Public Health Engineering	Larkano	45.73
2870	Paver Block & CC Drains from Allah park Tower to Wado Alam pak via VIP Bakery, Harijan Road and Amrofi Mashid at Taluka Ratodero (1.5 kms) (SDG # 6).	Public Health Engineering	Larkano	45.83
2871	Construction of Drains & Paver Block in Various Streets of Ward No.1,II,III,V&VII of Naudero, Taluka Ratodero(SDG#6).	Public Health Engineering	Larkano	49.41
2872	Construction of Paver Block & C.C Drains in Various Uc's of Taluka Ratodero (SDG # 6).	Public Health Engineering	Larkano	144.97
2873	Construction of Paver Block & CC Drain of Akil Circle ( UC's Akil, Aghani & Phull) (2.50 KMs), Taluka Larkano (SDG # 6).	Public Health Engineering	Larkano	45.37
2874	Construction of Paver/CC Block & CC Drain from Railway Station Badeh to Govt. Hospital Badeh, and Construction of CC Block Paver Block & CC Drain Channa Bridge Dokri to Dokri Bus Stand Via Village Babal Jarwar and various streets of City Badeh and City Dokri (SDG # 6).	Public Health Engineering	Larkano	76.12
2875	Construction of Paver/CC Block & CC Drain in diferent Villages of District Larkano (SDG # 6).	Public Health Engineering	Larkano	94.62
2876	Construction of Drainage Scheme at Mohallah Jam Hassan Khan Dahar & CC Paver in various Streets Ubauro City (SDG # 6).	Public Health Engineering	Ghotki	106.54
2877	Drainage Scheme Village Pir Muhammad Bhutto, UC Ranwafi, Taluka Ubauro (SDG # 6).	Public Health Engineering	Ghotki	72.97
2878	Draiange Scheme Village Mari, UC Kamoon Shaheed Taluka Ubauro (SDG # 6).	Public Health Engineering	Ghotki	48.13
2883	Drainage Scheme for Various Wards of Nawabshah City (SDG#6)	Public Health Engineering	S.B.A	118.84
2884	Drainage Scheme in Various Streets of Town Committee Bucheri (SDG # 6).	Public Health Engineering	S.B.A	29.52
2889	Construction of Surface Drains, C.C Topping, C.C Paver Block, Culverts & Bricks Pavement and Sewer Line at Town Committee Mehrabpur Taluka Mehrabpur (SDG#6).	Public Health Engineering	N. Feroze	48.20
2890	Paver Block and Drains Town Committees Naushehro Feroze and Mithiani (SDG#6).	Public Health Engineering	N. Feroze	86.30
2891	Drainage Scheme i/c CC Topping and Paver Block of Village Saleemabad UC Ghulam Shah (SDG # 6).	Public Health Engineering	N. Feroze	49.89
2893	Providing & Fixing Paver Block including Drain Nalla Bhiria Road (SDG # 6).	Public Health Engineering	N. Feroze	46.63
2894	Construction of Surface Drains, CC Toping, CC Paver Blocks, Culverts, Birck Pavement and Pipe Line at Municipal Committee Moro Taluka Moro (SDG # 6).	Public Health Engineering	N. Feroze	142.26
2895	Construction of Surface Drains, CC Toping, CC Paver Blocks, Culverts, Birck Pavement and Pipe Line at Town Committee Padidan, Taluka Naushehro Feroze (SDG # 6).	Public Health Engineering	N. Feroze	44.26
2898	Drainage Scheme for Khandhkot Ward No. 1 to 16 (SDG#6).	Public Health Engineering	Kashmore	104.75
2910	Construction of Surface Drain & C.C Paver of Village Neer Waro Bhanbhan Kashif Raza (SDG # 6).	Public Health Engineering	Khairpur	27.87
2911	Paver Block & Sarface Drains of Town Razi Dero & Muhalla Makhdoom Pir Soomar sawae Town Committe Agra Taluka Gambat (SDG # 6).	Public Health Engineering	Khairpur	49.91
2914	Drainage and Paver Schemes in Various Villages of Khairpur and Kotdiji (SDG # 6)	Public Health Engineering	Khairpur	94.02
2949	Construction of Surface Drains, CC Block and Paver Block at different Mohallas of Town Committee Hingorja, UC Sami, Village Niwaro UC Meerak, Village Razal Memon, UC Madd, Village Haji Abdul Rahim Bhutto UC Rasolabad, Abbasi Mohalla and Mir Mohalla Committee Sobo Dero (SDG # 6)	Public Health Engineering	Khairpur	62.79
3057	Reconditioning of Road from Village Khairo Dhero to Village Allah Bux Hakro via Lashari Bridge including Paver Block and CC Drain, Taluka Ratodero.	Rural Developme nt	Larkano	110.00

ADP NO	Name of Scheme	Department / Sector	Location	Cost
3199	Construction of Football Stadium in Manghopir	Sports & Youth Affairs	Karachi (W)	44.00
3202	Rehabilitation, Upgradation and Renovation of Different Grounds / Sports Facilities UC-1 to UC-19 of District South	Sports & Youth Affairs	Karachi (S)	100.00
3358	Reconditioning of road from Jacobabad Dodapur G. Khairo road Landhi Bus Stand to village Kallar Kot via village Sher Muhamamd Mugheri, Bhai Khan Mugheri, village Quba Khoso, village Ali Hassan Zawrani., village Muhammad Ramzan Mugheri, village Khandoo Wahi, village Atta Muhammad Khoso (7.60 Kms)	Works & Services	Jacobabad	66.08
3359	Renovation of road from 45-RD via link A.D Mazari upto village Qabil Khan Mazari and Construction of road from Baqa Muhammad Khan Jakhriani via various village upto village Nisar Ahmed Khan Jakhriani (12.50 Kms)	Works & Services	Kashmore	129.91
3360	Reconditioning of road from Guddu Kashmore road Bypass upto Guddu Barrage and Construction of road from Food Godam via various villages and road from Colony No. 1 upto B.S Feeder	Works & Services	Kashmore	97.12
3362	Reconditioning of road from Son Wah to Chakar Khan Bagdar via Qaim Khan Wadhya (18.00 Kms)	Works & Services	Shikarpur	175.85
3363	Reconditioning of road from village Samandar Gopang to village Shahbaz Seelro (8.60 Kms)	Works & Services	Shikarpur	76.25
3364	Rehabilitation of Station road Madeji City Portion upto Rice Canal (Carpeting & Paver Block) (5.00 Kms)	Works & Services	Shikarpur	76.29
3365	Widening / Reconditioning of road from Dakhan to Bado (7.50 Kms)	Works & Services	Shikarpur	108.92
3366	Improvement of road from Old Indus Highways City Portion Larkano to N.I.P Side of Rice Canal via Hasnain Medical Center i/c Paver Link in Ghulam Akbar Jalbani Street upto SZABIST College and approaches to various streets Sachal Colony Larkana (4.40 Kms)	Works & Services	Larkano	119.99
3367	W/R of road from Sanhra Machi to Police Picket Post village Bosan, including approach to village Imam Bux Langah - Wassayo Bhutto road (6.00 Kms)	Works & Services	Larkano	101.98
3368	Reconditioning of link road from Naudero-Sukkur road @ Point Jat Bhutta Stop to Mubarak Jeho i/c M. Structure (4.80 Kms)	Works & Services	Larkano	80.71
3369	Reconditioning of road from GGPS Dhamrah to village Vikya Sanghi, Pandhi Golo, Besham-Ji-Wandh upto Larkano Mirokhan road. Reconditioning / Construction of road from village Razi Khan Jagirani, village Khan Muhammad Jhinjhin, village Hazori Sanghi upto village Mehrab Jhinjhin. Reconditioning of road from Indus Highway to village Shah Baig Jamali, village Lal Dino Bhutto upto Larkano Rasheed Waggan road (i/c M. Structure) (15.10 Kms)	Works & Services	Larkano	153.25
3370	Reconditioning of road from Moen-Jo-Daro Airport road Bagi Bridge to village Ghulam Hussain Butt via Karani road (i/c M. Structure)	Works & Services	Larkano	80.41
3371	Reconditioning of road form Airport road to village Mad Bahu via village Sijawal Tunio, village Haroon Tunio to Habib Petrol Pump Larkano Khairpur road i/c approaches to various villages and Reconditioning of road from village Hyder Brohi to village Gul Muhammad Jatoi (i/c M. Structure) 7.50+1.30 = 8.80 Kms	Works & Services	Larkano	87.81
3372	Reconditioning / Construction of link road of village Masoodero and village Muhammad Sharif Jalbani @ village Mir Muhammad Jalbani (3.40 Kms)	Works & Services	Larkano	60.19
3373	Reconditioning of road from Garhi Khuda Bux Bhutto Saidudero road to Dhamrah Mahota via village Kubro, village Sanwan Khan Gopang (Gulsher Gopang) & Wandh Khuda Bux Bhutto (5.00 Kms)	Works & Services	Larkano	79.62
3374	Reconditioning of road from Rahoja Bridge to village Shahni via village Khakhrani & village Bhoonbhatpur (4.00 Kms)	Works & Services	Larkano	65.99
3375	Improvement of road from Shahdadkot Motorway Bypass (M-8) road @ Point Police Chowki to village Meenhoon Khan Leghari (Old Railway Track) via Juneja and Brohi (11.00 Kms)	Works & Services	Kamber	109.94
3376	Reconditioning of road from Thouf Chosul - Bhand Chowk road Mahmoodabad Police Chowki to Miro Khan (7.00 Kms)	Works & Services	Kamber	76.93
3377	Improvement of road from Motorway (M-8) road to Qubo Saeed Khan and Paver Block in Qubo Saeed Khan	Works & Services	Kamber	54.85
3378	Improvement / Construction of various roads of Taluka Sijawal	Works & Services	Kamber	81.79
3379	Improvement / Construction of various roads of Taluka Qubo Saeed Khan	Works & Services	Kamber	81.86
3380	Reconditioning of road from Behram to Kamber Miro Khan road via Butthi Mubarak Kalhoro, Tharo Wadho, Lal Bux Leghari (8.00 Kms)	Works & Services	Kamber	93.42
3381	Reconditioning / Construction of road from Raharki Seedpur road at village Lal Bux Mirani i/c link road Mohammadpur road mile 0/0-6/2 (8.50 Kms)	Works & Services	Ghotki	127.74
3382	W/R of road from Reti to Daharki Taluka Ubauro (4.00 Kms)	Works & Services	Ghotki	69.55
3383	W/R of road from Old Keenjhur to Yaro Lund via Bari Adda, Taluka Daharki (11.00 Kms)	Works & Services	Ghotki	187.01
3384	Reconditioning of road from Gulo Pitafi Chowki to Meer Mor approach village Gulo Pitafi, Taluka Mirpur Mathelo (10.00 Kms)	Works & Services	Ghotki	107.74
3385	Reconditioning of road from Lohi Pull to village Roshan Shar, Taluka Daharki (8.50 Kms)	Works & Services	Ghotki	91.19
3386	Reconditioning / Construction of road from Kori Khooh to village Dino Mako via village Kamal Khan Mahar, village Esso Soomro, village Sardar Muhammad Bux Khan Mahar, Deh Khansar (9.00 Kms)	Works & Services	Ghotki	98.12
3387	Reconditioning of road from Adilpur to Qazi Badal (14.00 Kms)	Works & Services	Ghotki	195.75

ADP NO	Name of Scheme	Department / Sector	Location	Cost
3388	Rehabilitation / Widening and Reconditioning of road from Dhandi to Sultanpur via Bhatti Chowk (8.00 Kms)	Works & Services	Sukkur	99.81
3389	Rehabilitation / Widening and Reconditioning of road Rohri Interchange M-5 to Salehpat City Dual Carriageway (Due to Heavy Traffic existing 24' proposed 50') (0.80 Km)	Works & Services	Sukkur	97.85
3390	Rehabilitation / Construction of road from Dodanka to Arore Bachal Shah road @ Thariri village (6.50 Kms)	Works & Services	Sukkur	96.68
3391	Rehabilitation / Reconditioning of road from Hakra Panhwr Chowki to Bhira (10.00 Kms)	Works & Services	Sukkur	96.21
3392	Rehabilitation / Reconditioning of road from Ghulam Bund to Dhandi via Faqirabad (11.00 Kms)	Works & Services	Sukkur	98.67
3393	Reconditioning of road from Mohalla Ali Cheechro road to Mahesro Wah via Moli Dino, Motu Mirbahar, Mehar Mirbahar, Jado Indhar, Ahsan Khokhar and Muhammad Sachal Mallah, Gul Hassan Gamb enclosed various links (6.00 Kms)	Works & Services	Sukkur	94.65
3394	Reconditioning of road from Haleji Dhandhi Road to Wagah Chowki, Qasi Wah road via Qadu Indhar, Shahmir Indhar, Fateh Mohammad Bado Shar, Arib Wagho and Haleji link, Allah Yar Indhar, Jalal Goth Parallel to Thath Minor and enclosed various links (7.00 Kms)	Works & Services	Sukkur	93.29
3395	Reconditioning / Construction of road from Rojho Mahesro Main Chowk road to village Jalal Indhar via Adam Gopan, Allah Diyayo Malano, Wali Mohammad Arain enclosed various links (8.75 Kms)	Works & Services	Sukkur	97.00
3396	Reconditioning / Construction of road from Khanpur Thikratho road to Ibrahim Mahtam via Khameso Bhatti, Ali Madad Mahtam, Ucheer enclosed various links and Kabil Mahtam (9.00 Kms)	Works & Services	Sukkur	96.13
3397	A) Rehabilitation of road Salehpat Sikandarabad to village Wadero Allah Jurio Bhanbhro, Dinal Mallah and Ali Dost Bhanbhro (4.00 Kms) B) Rehabilitation of road Salehpat Sikandarabad to Arore Bachal Shah road via Channel RD-186 Bridge Nara Canal (4.00 Kms)	Works & Services	Sukkur	87.51
3398	Rehabilitation of road from NHA to Piryalo via Phul Wahan Razi Goth, Khedo Goth upto village Khorkhani (8.00 Kms)	Works & Services	Khairpur	105.04
3399	Reconditioning of various roads at village Seeri Piyaro Khan Nazar Muhammad Gaho, Imam Bux Palh, Sahib Khan Chakrani, Shadi Shaheed road Rattal Bhambhro and Babar Wada Jhando road to Ahdai Rajpar (15.20 Kms)	Works & Services	Khairpur	139.71
3400	Reconditioning of road from Mehran N/Highway to Deparja Nawab Ali Shah Bhambhan via Khairiri road (14.00 Kms)	Works & Services	Khairpur	134.81
3401	Reconditioning of road from Jalal Jee Stop Mehran N/Highway to village Pholirhi via Bhango Behan, UC Bhango (11.60 Kms)	Works & Services	Khairpur	107.43
3402	Reconditioning of road from Sutyaro to Kharirah and Pir Bux Jalalani, UC Kharirah	Works & Services	Khairpur	69.09
3403	Rehabilitation / Construction of road from Odha More to Ali Murad Jamali via Amanullah Odho, Paraocha Ulro, G. Nibo Ulro, Muhammad Hayat Ulro, Shaman Ulra, Mehmood Odho mile 0/0-7/4, UC Ulra, Taluka Kingri (12.06 Kms)	Works & Services	Khairpur	132.90
3404	Construction, Widening / Reconditioning of road from Asian road to Ahmedpur Bus Stop via Pir Badal / Tapali Sarak, Khawaja Pull road mile 0/0-7/6 (12.47 Kms)	Works & Services	Khairpur	185.85
3405	Rehabilitation / Construction of road from Daim Haji to Bolani Sahita via Pir Bux Khaskheli Rais Bangul Chang, AR Bhayo K.B Mari, UC Rasoolabad, Taluka Sobhodero (8.00 Kms)	Works & Services	Khairpur	88.04
3406	Rehabilitation of road from Sobhodero to Sagyoon City road mile 0/0-7/4, Taluka Sobhodero, District Khairpur (0/0-0/4 Paver Block 35+30/2) (12.00 Kms)	Works & Services	Khairpur	164.52
3407	Improvement of road from Fakirabad to Jan Muhammad Gopang to Old N.H Way road (5.80 Kms) Rehabilitation of road from Jhanda Shakh to Fakirabad upto GIMS road (8.00 Kms)	Works & Services	Khairpur	149.71
3408	Reconditioning of road from Kumb to Jagir Ali Akbar road (6.80 Kms)	Works & Services	Khairpur	85.85
3409	Widening / Reconditioning of road from Khahira to Zafarabad (12.00 Kms)	Works & Services	Khairpur	196.36
3410	Widening / Reconditioning of road from Thari to Tarko (8.00 Kms)	Works & Services	Khairpur	117.76
3411	Widening / Reconditioning of road from Mehar Vessar to Bozdar Wada (12.00 Kms)	Works & Services	Khairpur	169.88
3412	Widening / Reconditioning of road from Karoondi Town Committee Karoondi to Baseero Union Council Karam Khan Rajper road mile (13.00 Kms)	Works & Services	Khairpur	222.44
3413	Reconditioning of road from Pacca Chang to Karoondi via Hussain Shah & via Sijawal Khaskheli (5.20 Kms)	Works & Services	Khairpur	48.97
3414	Reconditioning of the road from Bab-e-Ahmed Shah Gate, National Highway Ranipur to Sobhodero City (11.26 Kms)	Works & Services	Khairpur	171.42
3415	Reconditioning of road from Ranipur Nangrija road, Jhanda Mashaikh to village Goth Rajper new Railway Phattak via village Ghous Bux Jamro, village Mureed Haji, village Kamaluddin Jamro and village Qadir Bux Jamro road (13.00 Kms)	Works & Services	Khairpur	107.84
3416	Reconditioning of road from N/Highway to village Wali Muhammad Kalhoro via village Wada Bhellar, village Mehar Hussain Mangrijo, village Khaki, village Sando Machi, village Ameer Bux, village Buet Panhyar, village Khalifo Juman, village Setharja Lower and village Wali Muhammad Gadehi (8.00 Kms)	Works & Services	Khairpur	74.32
3417	Reconditioning of road from Tando Masti Khan Road to Rafique Mahesar (Asphalt Work) 0/0-7/4 (12.06 Kms)	Works & Services	Khairpur	164.26

ADP NO	Name of Scheme	Department / Sector	Location	Cost
3418	Widening / Reconditioning of road from Khuhra City to Larkana Road via Kamaldero, Pir Essa Road (Asphalt Work) link with Syed Sabit Ali Shah to Shar (12.87 Kms)	Works & Services	Khairpur	151.83
3419	Reconditioning of road from Rafique Mahesar to Noraja via Khaat Nareja (Asphalt Work) road mile 0/0-7/0 (11.26 Kms)	Works & Services	Khairpur	97.73
3420	W/R of road from Khairpur Economic Zone upto Jeha Masjid road (13.30 Kms)	Works & Services	Khairpur	201.89
3421	W&R / Construction of road from Old National Highways Bhurghari Regulator to Hussainabad upto village Makol Pahore parallel to Mirwah Canal (Right side bank) (Phase-I) (2.50 Kms)	Works & Services	Khairpur	105.67
3422	W/R of road from Mori to Ahmedpur Pir Goth road via Raja Ulro Kot Mir Muhammad road (12.12 Kms)	Works & Services	Khairpur	217.09
3423	Reconditioning of road from Machar Minor to Sami to Merak via Niwaro, Taluka Sobhodero road (6.00 Kms)	Works & Services	Khairpur	63.04
3424	Reconditioning of road from NHA Halani to Khanwahan (9.50 Kms)	Works & Services	N. Feroze	129.99
3425	Reconditioning of road from Halani to Tando Gul Shah (i/c various approaches) (13.00 Kms)	Works & Services	N. Feroze	130.67
3426	Reconditioning of road from Bharya City Bypass to Tharushah (7.75 Kms)	Works & Services	N. Feroze	110.32
3427	Construction/Reconditioning of road from Mohabat Dero Jatoti Road to Pir Qadir Bux Shah via Allahdad Tanwari (i/c various approaches) (8.50 Kms)	Works & Services	N. Feroze	79.29
3428	Widening / Reconditioning of road from Haji Ali Nawaz Deepar to Achhi Masjid approach link village Budak (10.00 Kms)	Works & Services	N. Feroze	169.35
3429	Reconditioning of road from Kandiaro Bus Stop to Saeed Khan Lakho via Siddique Lakho (10.00 Kms)	Works & Services	N. Feroze	90.12
3430	Reconditioning / Construction of road from Mango Road to Jalbani Minor via Belawah, Taluka Bhiria	Works & Services	N. Feroze	147.23
3431	Reconditioning / Construction of road from village Abdul Raheem Keerio to Chaheen Suleman via Panwari, Taluka Bhiria (11.50 Kms)	Works & Services	N. Feroze	114.51
3432	Reconditioning of road from Railway Phatak Mehrabpur to Pir Wassan connect to Mehran Highway @ Pir Wassan, Taluka Mehrabpur = (13.50 Kms)	Works & Services	N. Feroze	128.26
3433	Reconditioning of road from Tharushah Mithani road to Fazul Mohammad Motomal via Moosa Siyal road (5.00 Kms)	Works & Services	N. Feroze	49.89
3434	Reconditioning of road from National Highway to Chuttal Rajper, Adh Khahi Mahi Waggan, Naik Muhammad Mooro, Tagar road, Khoro Shareef, Tharoshah to Bhorthi (14.50 Kms)	Works & Services	N. Feroze	119.88
3435	Reconditioning of road from Naushehro Feroze - Mithani road to village Niaz Ali Mashori, Pir Juman, Haji Sain Rakhio Chandio, Ameer Bux Mari, Moro road to Late Chandio (10.00 Kms)	Works & Services	N. Feroze	78.62
3436	Reconditioning of road from Naushehro Feroze - Padidan road to Dangeja, Dr. Kamil Rajpar, Nawab Khan Mari, Indus Highway to Khaliq Rajpar road (10.00 Kms)	Works & Services	N. Feroze	81.58
3437	W/R of road from Deparja to Chowdagi (with Asphalt) (11.50 Kms)	Works & Services	N. Feroze	204.42
3438	Reconditioning / Construction of Road from Qamar Din Chandio Morcho via Dewan Ja Karia upto Moro Bandhi road (10.00 Kms) (1-1/2" Carpet with Paver)	Works & Services	N. Feroze	81.88
3439	Reconditioning of road from Moro - Dadu road to village Jadal Shah 1-1/2" Carpet With Paver (6.00 Kms)	Works & Services	N. Feroze	65.64
3446	W/R / Construction of road from N.H.A Sarkari Khooh to connect Aumb Junejo road via Bachalpur, Muhammad Ismail Bhand road (16.00 Kms) (with 5cm thick Asphalt surface)	Works & Services	S.B.A	307.45
3447	W/R / Construction of road from N.H.A Nawab Wali Muhammad to connect Muhammad Ismail Bhand road via Jujhan Khan Muhammad Rind, Karam Bughio road (7.00 Kms) Actual Length 11.00 Kms (with 5cm thick Asphalt surface)	Works & Services	S.B.A	110.78
3448	W/R / Construction of road from 60th Mile - 3 Chak Suhallo road @ 18 Shak Stop to connect Ghazi Khan Bhurgari road @ Nim Stop via Sui Gas H.Q & link to village Masood Nabi Noor along Akdohi Minor mile 0/0-5/2+330 (8.50 Kms)	Works & Services	S.B.A	175.45
3449	Reconditioning / Construction of road from Daur Open Phattak @ Kothri Stop to Kari Mori via village Zawar Loung Khan Gorchani road mile 0/0- 3/6 (6.00 Kms)	Works & Services	S.B.A	81.19
3450	Reconditioning of road from Nawabshah - Sanghar road to village Ali Jan Brohi road (3.40 Kms)	Works & Services	S.B.A	45.52
3451	Widening / Reconditioning / Construction of road from Varr Stop to Connect Nawabshah - Ghupchani Shakal Jamali road via Khando Stop, Dost Pir, Hassan Jamali & Baksho Jamali (15.00 Kms) (with 5 cm Thick Asphalt Surface)	Works & Services	S.B.A	239.60
3452	Reconditioning / Construction of road from Pir Shah Mori to Commando Centre - Chattan Shah, Nasri and Jan Muhammad Lashari Road (14.00 Kms) (with 3.80 cm Thick Carpet with Paver Machine)	Works & Services	S.B.A	155.79
3453	Reconditioning / Construction of road from N.H Way Mir Khan Leghari Road to connect Sakrand - Khadhar road via Hamal Faqeer, Mehmood Leghari, Jan Muahmad Keerio, Abdul Wahid Soomro and Esso Keerio road (11.00 Kms) (with 3.80 cm Thick Carpet with Paver Machine)	Works & Services	S.B.A	118.78
3454	Reconditioning / Construction of road from Kazi Ahmed Pubjo road to connect Sher Purrian via Sun Sawari, Jevad Leghari, Wali Muhammad Merasi, Khushhal Dahri road (12.00 Kms)	Works & Services	S.B.A	128.53
3455	Reconditioning / Construction of road from Old National Highway to connect Al-Noor Sugar Mill road via Raj Muhammad Dahri, Khar Ashique Abad, Bahar Ji Koor and Bado Dahri road (11.80 Kms)	Works & Services	S.B.A	122.81

ADP NO	Name of Scheme	Department / Sector	Location	Cost
3456	Reconditioning of road from National Highway to Mir Khan Pakhrio via Hanif Chandio and Nagar Khan Chandio road (6.60 Kms) (with 3.80 cm Thick Carpet with Paver Machine)	Works & Services	S.B.A	65.73
3457	Reconditioning of road from Nawabshah - Kazi Ahmed road to connect Nawabshah - Sakrand road @ Landhi Stop Via Bildo Maggi, Khair Shah & Ghulam Qadir Jatoi (5.00 Kms) (With 2" Thick Asphalt)	Works & Services	S.B.A	66.18
3458	Reconditioning of road from Mehran Highway @ Bhooral Shah Stop to village Abdullah Bughio via Gabol Stop and village Jeeando Khan Gabol (6.03 Kms) (With 2" Thick Asphalt)	Works & Services	S.B.A	68.53
3459	Reconditioning of road from Daur - Kazi Ahmed road to connect Nawabshah - Naushahro Feroze road @ Basham Rind along Sim Nala road (5.00 Kms) (With 2" Thick Asphalt)	Works & Services	S.B.A	58.29
3460	Reconditioning of road from Workshop to Nawabshah road via Chak # 32, 62 Shafiabad, Chak # 74, Chak # 22 Alf road (20.00 Kms) (With Paver Carpet 1-1/2") (in portion)	Works & Services	Sanghar	198.70
3461	Reconditioning of road from Sinjhoro to Baig Stop via Jaffer Khan Leghari road mile 0/0 - 9/3 (15.00 Kms) (in portions) (With Paver Carpet 1-1/2")	Works & Services	Sanghar	50.27
3462	W/R / Construction of road from Perumal More to Tando Miitha Khan via Perumal road mile (16.40 Kms) (Asphalt Surface) (Phase-I)	Works & Services	Sanghar	498.31
3463	Improvement of road from Oderolal to Shahdadpur (From Oderolal to Mulla Mukhan road) (9.00 Kms) (with Asphalt Surface)	Works & Services	Sanghar	168.11
3464	Reconditioning of Circular road around Tando Adam (Northern Side) (Tando Adam Shahdadpur road to Tando Adam Berani road via Tando Adam Branch) road mile 3/2+330 - 5/5 = 3.70 Kms (2" Asphalt Surface) (18' Width)	Works & Services	Sanghar	80.31
3465	W/R of road from Shahdadpur City to UC Maldesi (18ft road) (with Asphalt Surface) (10.40 Kms)	Works & Services	Sanghar	198.16
3466	(A) Reconditioning of road from Head Jamrao road Gujri to Chak No.71 road mile 0/0 - 7/4 = (12.00 Kms) TST 12' Width (B) Reconditioning of road from Sanghar Nawabshah road Kundho to Chak No.70 Chak No. 66 via Chak No. 5 road mile 0/0 - 9/3 (15.00 Kms) (1-1/2" thick Carpet Paver) (12' Width) (C) Reconditioning of road from Sanghar Head Jamrao road to link road Chak No. 19 Chak No. 21 Dr. Muhammad Sharif Khaskheli road mile 0/0 - 3/6 = (6.00 Kms) TST 12' Width	Works & Services	Sanghar	260.26
3467	(A) Reconditioning of link road from Khipro Ghulam Nabi Shah road to village Molvi Abdul Rehman Dars to Ding Khahi Road via Dargah Abdullah Shah road mile 0/0 - 4/0 = (6.40 Kms) (With TST) (B) Reconditioning / Construction of link road from Aqil Hingoro road to village Haji Usman Chaniho to Hassan Ali Chaniho via village Drabhi to village Khamiso Khan Dars road mile 0/0 - 4/0 (6.40 Kms) (TST 12ft Width)	Works & Services	Sanghar	102.59
3468	(A) Reconditioning of road from Khipro to Khahi via village Ismail Chanhio road mile 0/0 - 8/2 = (13.20 Kms) (TST 12' Width) (B) Reconditioning / Construction of road from Khipro Khahi road to Khipro Ghulam Nabi Shah Road via village Haroon Samejo road mile 0/0 - 3/2 (5.20 Kms) (TST 12' Width) (C) Reconditioning of road from Khahi to Dolatabad road mile 0/0 - 3/6 (6.00 Kms)	Works & Services	Sanghar	142.92
3469	(A) Reconditioning of link road from Khipro Khahi road Khipro Phullahaiyoon road via Dargah Manthar Faqir road mile 0/0 - 3/1 = (5.00 Kms) (TST 12' Width) (B) Reconditioning / Construction of link road from Nangna road to Miandad Bhanbhro road via Dargha Ubhando Faqeer road 0/0 - 3/1 (5.00 Kms) (TST 12' Width)	Works & Services	Sanghar	73.30
3470	Improvement / Widening & Reconditioning of road from Bhudho Chandio to Mulla Makhan (with Asphalt) (9.00 Kms)	Works & Services	Sanghar	170.72
3471	Improvement / Widening & Reconditioning of road from Tando Adam Landhi road to Shahdadpur Sanghar road via Tayyab Thahim and Yar Muhammad Thahim road mile 0/0 - 1/6 = 2.80 Kms (2" Asphalt Surface 12' to 18' width)	Works & Services	Sanghar	50.46
3472	Repairing of Circular Road from Tando Adam Oderolal road to Tando Adam Shahdadpur road via Tando Adam Bhit Shah road 0/0 - 3/2+330 = 5.30 Kms (2" Asphalt Surface)	Works & Services	Sanghar	89.41
3473	W/R of Sarhari to Gupchani road mile 0/0-4/4 (7.20 Kms) (18ft) ( 1-1/2" Thick Carpet)	Works & Services	Sanghar	109.83
3474	W/R of Golo Pir Mori road to village Sultan Mallano road mile 0/0-1/7 (3.00 Kms) (12 to 18 Width) ( 1-1/2" Thick Asphalt Surface)	Works & Services	Sanghar	64.17
3475	W/R of Shahdadpur Gird Station road to village Budho Chandio road mile 0/0-4/3 (7.00 Kms) (18ft) (1-1/2" Thick Asphalt)	Works & Services	Sanghar	152.76
3476	Reconditioning of road from Chowdagi to Sarhari road mile 0/0-5/6 (9.20 Kms) (1-1/2" Thick Asphalt Surface 18' Width)	Works & Services	Sanghar	126.59
3477	Reconditioning / Construction of road from Nawabshah - Sanghar road to village Rasool Bux Dahri via Qubba Shahdad Road mile 0/0-5/0 = 8.00 Kms (1-1/2" Thick Carpet)	Works & Services	Sanghar	81.59
3478	Widening / Reconditioning of Sinjhoro Khadro road mile 0/0-5/0 @ Dhanda Mori (8.00 Kms) ( 1.5 inches Thick Asphalt 12' to 18' Width)	Works & Services	Sanghar	112.62
3479	Widening / Reconditioning of Sinjhoro Khadro road mile 5/0-10/0 = 8.00 Kms ( 1-1/2" Thick Asphalt Surface 12' to 18' Width)	Works & Services	Sanghar	111.88
3480	Improvement of road from Mirpurkhas - Khan Patoyoon road to connect various villages (12.40 Kms)	Works & Services	Mirpurkhas	99.84
3481	Reconditioning of road from Sindhri Khipro road to Shakir Shaheed road (with Asphalt) (4.40 Kms)	Works & Services	Mirpurkhas	49.63

ADP NO	Name of Scheme	Department / Sector	Location	Cost
3482	Reconditioning road from Mirpurkhas - Umerkot road @ 78 Mori to Jhillori road (with Asphalt) mile 0/0-6/2 (10.00 Kms)	Works & Services	Mirpurkhas	105.80
3483	Widening / Reconditioning of road from Muhammad Hashim Bhurgri to connect Kot Ghulam Muhammad (with Asphalt ) (7.00 Kms)	Works & Services	Mirpurkhas	123.33
3484	Widening / Reconditioning of road of Dengan Bhurgari to Jhuluri (9.00 Kms)	Works & Services	Mirpurkhas	149.64
3485	Improvement of road from Soofi Fakir to Dhoronaro Road 8.00 Kms	Works & Services	Umerkot	99.27
3486	Improvement of road from Shadi Palli Pithoro road 8.00 Kms	Works & Services	Umerkot	99.20
3487	Construction / Improvement of road from Umerkot to Kunri via Diggu / Gapno Phase-II (18.40 Kms)	Works & Services	Umerkot	185.95
3488	Improvement of road from Umerkot - Bodar to Point Bund Stop to More Jhango via Monium Palli, Hashim Palli and Karo Palli (6.50 Kms)	Works & Services	Umerkot	55.16
3489	W/R of Dhoronaro to Nohyoon road via Sadher (14.40 Kms)	Works & Services	Umerkot	285.70
3490	W/R of road Chhore Bypass from Foji Chowk to Railway Phatak (3.63 Kms)	Works & Services	Umerkot	99.43
3491	Reconditioning of road from Chhore - Umerkot road to Ahori Farm, Morand Pattu, Muhammad Hassan Mari, Mahar Ali Mari to connect Umerkot Dhoronaro road (14.60 Kms)	Works & Services	Umerkot	150.64
3492	Reconditioning of road from Dharnio More to Talhi Station (12.60 Kms)	Works & Services	Umerkot	148.80
3493	Reconditioning of road from Nabisar road to Nohto (10.00 Kms)	Works & Services	Umerkot	97.60
3494	Reconditioning of road from Kunri to Nabisar road (Phase-II) (8.25 Kms)	Works & Services	Umerkot	114.84
3495	W/R of road from Faqeer Nazar Pump to Bostan (4.22 Kms)	Works & Services	Umerkot	88.54
3496	Reconditioning of road from Samaro Kunri road @ Toban Shakh to Manjhakar (6.40 Kms)	Works & Services	Umerkot	54.17
3497	Repair and Reconditioning of road from Baloch Chowk (Badin-Mithi Road) to Kaloi Town (3.50 Kms)	Works & Services	Tharparkar	52.06
3498	Reconditioning of link road from village Bego Kaka Chowk road to Sarhari Road via village Bhale Dino Kaka road mile 0/0-7/0 (11.20 Kms)	Works & Services	Matitari	179.62
3499	Reconditioning of link road from Jamal Hajano road to village Maari Muhammad Khan road (7.20 Kms) (with Asphalt)	Works & Services	Matitari	83.69
3500	Reconditioning of link road from Allah Bux Mirjat Stop to village Haji Pir Muhammad Baloch via village Haji Ismail Baloch & link to village Haji Sher Muhammad Baloch & village Amitan Baloch (8.00 Kms)	Works & Services	Matitari	74.14
3501	Reconditioning of link road from N.H.Way Saeedabad road to village Zair Pir Road via Burira Chowk Road (with Asphalt) (6.40 Kms)	Works & Services	Matitari	77.10
3502	Reconditioning of link road from Hala New to village Banoth road including approach to link road village Vee mile 0/0-8/0 (with Asphalt)	Works & Services	Matitari	140.74
3503	Reconditioning of different link roads of Taluka Matitari (4 Units)	Works & Services	Matitari	114.84
3504	Reconditioning / Construction of different link roads of Taluka Matitari (2 Units)	Works & Services	Matitari	146.80
3506	Reconditioning of link road Chamber road Bukera road, Mirwah road, Nasarpur road i/c approaches Shafi Pitafi, Nagori Plot mile 0/0-2/4+330 (4.20 Kms)	Works & Services	T.A. Yar	100.00
3507	W/R road Missan Wadi to T.D.R Mirwah road via Qazi Noor Muhammad Leghari, Ghulam Ali Leghari, Saleh Faqeer Mir Jat i/c approach Bypass road Missan Nandhi mile 0/0-3/7 (6.24 Kms)	Works & Services	T.A. Yar	100.00
3508	Reconditioning of road Mashak Hoti Timore road i/c Lashari village mile 0/0-7/4 (12.00 Kms)	Works & Services	T.A. Yar	100.00
3509	Reconditioning of road from Mall Khan Thebo to Old Mirabad via Muhabbat Shah i/c link Soomar Khaskheli mile 0/0-7/4 (12.00 kms)	Works & Services	T.A. Yar	100.00
3510	Reconditioning of link road from Tando Adam - Mirpurkhas road to Yousuf Narejo via Murad Balouch Siddique Baloch, Piyaro Khaskheli, Saleh Khaskheli, Chacho Mall mile 0/0-7/4 (12.00 Kms)	Works & Services	T.A. Yar	100.00
3511	Reconditioning Tando Adam road to village Suleman Palli, village Mitho Mirjat, village Ibrahim Shah, village Madan Mirjat, village Ghulam Nabi Shah, village Khair Shah via Pannah Shah road approach Barecha mile 0/0 - 7/4 (12.00 Kms)	Works & Services	T.A. Yar	100.00
3512	Reconditioning of link road from village Shah Nawaz Muhajir to Tando Adam road and in village Allah Rakhio Pathan i/c village Allahyar Lund, Tayab Thebo, Ghulam Qadir Thebo, village Ibrahim Thebo and village Ali Sher Muhajir mile 0/0 - 7/4 (12.00 Kms) (with 1-1/2" Thick Carpet with Paver Machine)	Works & Services	T.A. Yar	100.00
3513	Reconditioning of link road from Hyderabad - Mirpurkhas road to Tando Allahyar Mirwah road via Haji Muhammad Ali Halepoto, Haji Hashim Kakepoto, Pir Ghulam Muhammad Qureshi, Mubarak Jarwar i/c Shadman Jarwar mile 0/0- 7/4 (12.00 Kms)	Works & Services	T.A. Yar	100.00
3514	Reconditioning of link road from Haji Wali Muhammad Dars near Haji Karim Dars to Piyaro Lund road via Ali Khan Jarwar, Mevo Khaskheli, Khuda Bux Mari, Daim Khaskheli, Bashir Babar mile 0/0-7/4 (12.00 Kms)	Works & Services	T.A. Yar	100.00
3515	Reconditioning of link road from Tando Allahyar Mirwah road to Wangi Mori Saindad Deeshak road via Jarar Thebo, Hanif Leghari, i/c Juman Otho mile 0/0-7/4 (12.00 Kms)	Works & Services	T.A. Yar	100.00

ADP NO	Name of Scheme	Department / Sector	Location	Cost
3516	Reconditioning of link road from Mian Chamber road to Mira Khori Minor via Saeed Khan Laghari, Haji Muhammad Khan Lund to Dad Jarwar to Zahoor Minor Mureed Mori mile 0/0-7/4 (12.00 Kms)	Works & Services	T.A. Yar	100.00
3517	Reconditioning of link road from Chamber road Azizullah Memon Otaque to Sahib Khan Jarwar road via Kouro Daidano, Saleh Solangi, Obhriyo Dars, Mitho Khaskheli mile 0/0-7/4 (12.00 Kms)	Works & Services	T.A. Yar	100.00
3518	Widening / Reconditioning of Asphalt Concrete road from Tando Fazal to Seri road mile 0/0-5/4 (8.80 Kms), Taluka Rural Hyderabad	Works & Services	Hyderabad	240.12
3519	Reconditioning of Asphalt Concrete road from Hyderabad - Mirpurkhas road at point Rahuki Bus Stop to Hyderabad - Shaikh Bhirkio road via Bhindo Sharif road & Reconditioning of Asphalt Concrete road from Mirpurkhas - Hyderabad road to village Wali Muhammad Khaskeli (6.30 Kms)	Works & Services	Hyderabad	64.42
3520	Reconditioning of Asphalt Concrete road from Tando Fazal Chowk to village Baksho Leghari (6.00 Kms)	Works & Services	Hyderabad	64.74
3521	Widening / Reconditioning of road from Ansari Sugar Mill (Hyderabad - Badin road) to Pir Ghulam Rasool (9.00 Kms)	Works & Services	T.M. Khan	139.77
3522	W/R of road from Tando Muhammad Khan - Shaikh Bhirkio road @ point 1/0 mile via Baqar Nizamani (9.25 Kms)	Works & Services	T.M. Khan	140.00
3523	Reconditioning of road from Bulri Shah Karim to Khiryari (4.30 Kms)	Works & Services	T.M. Khan	77.91
3524	Reconditioning of road from Ghoro Mori to Panjtana (6.20 Kms)	Works & Services	T.M. Khan	51.98
3525	Reconditioning of road from TMK - Sujawal road to Syed Qadir Dino Shah via Syed Rafiq Shah Farm (5.90 Kms)	Works & Services	T.M. Khan	90.52
3526	Reconditioning of road from Sujawal road @ mile 23/3 to Bulla Khan Jat mile 0/0-3/6 (6.00 Kms)	Works & Services	T.M. Khan	70.81
3527	Widening & Reconditioning of road from Dumbalo to Chhato Mori mile 0/0-3/0 (4.83 Kms)	Works & Services	Badin	121.90
3528	Improvement of road from Dumbalo to Kapri Mori mile 0/0-7/0 (11.263 Kms)	Works & Services	Badin	151.87
3529	Improvement of road from Matli Tando Ghulam Ali at mile 3/7 Saleh Soomro Bagh to Haroo Talpur (9.65 Kms)	Works & Services	Badin	99.78
3530	Improvement of road from Chhato Mori to Rajo Khanani Degri road via Ghulam Muhammad Arain mile 0/0-7/0 (11.26 Kms)	Works & Services	Badin	124.66
3531	Improvement of Road from Golarchi Sim Nala Chak No. Oil Field Road Garhari (9.50 Kms)	Works & Services	Badin	96.22
3532	Improvement of road from Bhugra Memon to Dargah Shaikh Kariyo via Model village Golo Mandhro and Roopa Mari (7.50 Kms) (Phase-I)	Works & Services	Badin	104.62
3533	Improvement of road from Kario Ghanwar i/p T.M.Khan Sim Nala to 70 Mori (9.40 Kms)	Works & Services	Badin	96.48
3534	Improvement of road from Shadi Large to Signal Chak 20.00 Kms and Qabili Chak Taluka Tando Bago (8.80 Kms)	Works & Services	Badin	96.41
3535	Improvement of road from Ali Bandar road to village Pagaro Ghulam Rasool Chandio via General Sir Anjam (8.80 Kms)	Works & Services	Badin	96.55
3536	Improvement of road from Matli Tando Ghulam Ali at mile 6/4 Shesh mile to Akram Wah mile (11.26 Kms)	Works & Services	Badin	99.67
3537	(A) Improvement of road from Matli Tando Ghulam Ali at mile 2/1 Jara Water Stop to Mara Wah mile 0/0-4/3 (7.00 Kms) (B) Improvement of road from Hyderabad - Badin at mile 25/0 Baran Mori to Shanani Mori mile 0/0-1/3 (2.21 Kms)	Works & Services	Badin	124.24
3538	Improvement / Construction of Road from Nawab Saifuddin Leghari to Peeral Mori via Tharoo Dull mile 0/0- 3/1 (5.028 Kms)	Works & Services	Badin	114.71
3539	Improvement of road from Rajo Khanani Talhar road to Mehro Bhurgari i/c link to Dewani Faqeer (10.00 Kms)	Works & Services	Badin	99.75
3540	Improvement of road from Saeedpur to Dabahro (11.66 Kms)	Works & Services	Badin	99.59
3541	Improvement of road from Dabahro to Ghulam Shah i/c link to Khadaro (12.06 Kms)	Works & Services	Badin	99.81
3542	Improvement of road from Tando Bago Talhar road to Shah Turail road i/c Mirzo Dalwani (12.06 Kms)	Works & Services	Badin	99.95
3543	Improvement / Construction of road from Tando Ghulam Ali road to Arab Khaskheli i/c link to Jani Jalalani & Umer Jaskani Mile 0/0 - 6/0 (9.66 Kms)	Works & Services	Badin	96.10
3544	Improvement of road from Khorwah to Mirpur Bathoro road (7.00 Kms) (12ft to 18ft) (With 2" Asphalt Concrete)	Works & Services	Badin	135.22
3545	Improvement / Construction of road from Khorwah - Mirpur Bathoro road at point 4.00 Kms (Ghungro Sim Nala) to village Haseeb Lashari & Qaim Khan Rind (5.00 Kms) (12ft) (With 1-1/2" Thick Premixed Carpet)	Works & Services	Badin	77.44
3546	Improvement / Construction of road from Badin - Sujawal road at Buxal Brohi to Chak No. 22 via village Ramzan Lund, Allah Bachayo Mallah, Parsoo Kolhi, Ali Hassan Nohrio, Muhammad Khan Brohi, Hassan Chandio (16.00 Kms) (12ft) (With 1-1/2" Premixed Carpet)	Works & Services	Badin	255.87
3547	Widening / Reconditioning of link road from Chach jahan Khan - Mian Usman Quba road @ 5.00 Kms to village Haji Ali Muhammad Jat Warri (7.30 Kms)	Works & Services	Sujawal	165.36
3548	Reconditioning of link road from Chuhar Jamali Chahch Jahan Khan road village Ladiyoon to Kothi (8.60 Kms)	Works & Services	Sujawal	99.99
3549	Reconditioning of link road from Chachjahan Khan - Mian Usman Quba road @ 1.42 Km to village Jaffar Boohar via Moosa Pathan (7.00 Kms)	Works & Services	Sujawal	73.95

ADP NO	Name of Scheme	Department / Sector	Location	Cost
3550	Reconditioning of link road from Bathoro Sujawal road Dari Mori to Village Jarr i/c Links (7.00 Kms)	Works & Services	Sujawal	70.00
3551	Rehabilitation of road from Amra Stop Sujawal Bathoro to village Shah Nawaz Khan Leghari (7.00 Kms)	Works & Services	Sujawal	76.45
3552	Maintenance & Rehabilitation of Inter-City Road / Streets of Taluka Mirpur Bathoro (7.00 Kms)	Works & Services	Sujawal	69.93
3553	Improvement / Construction of road from Makli - Thatta Bypass road mile 3/1 (R/S) along Sim Drain to village Allah Jurio Gandhro (Charan Memon) road mile 0/0-5/3 (8.60 Kms)	Works & Services	Sujawal	100.08
3554	Rehabilitation / Construction of Road from Ghoro-Sakro road mile 7/2 (Lait Stop) to Coastal Highway via village Mathino Rind and Moosa Khaskheli road (10.00 Kms)	Works & Services	Thatta	99.90
3555	Rehabilitation / Construction of road from Shahpur to Dhandhari via Udasi road (6.20 Kms)	Works & Services	Thatta	68.57
3556	Improvement of Road from Thatta - Hyderabad National Highway to village Raju Nizamani (5.00 Kms)	Works & Services	Thatta	50.42
3557	Widening / Reconditioning of road from 105 Mori via Maher Mitho Shaikh to connect Ghoro Keti Bunder road (20.30 Kms)	Works & Services	Thatta	449.89
3558	Reconditioning of road from Baghan -Keti Bunder road to Sadar Bridge (4.50 Kms)	Works & Services	Thatta	49.98
3559	Improvement of road from DC Office Gopang Centre to Muslim Town road via Garibabad, Sikanderabad, Brohi Chowk, Khosa Chowk upto Indus Highway i/c various streets (7.5 Kms)	Works & Services	Jamshoro	99.98
3560	Improvement / Construction of roads in District Jamshoro	Works & Services	Jamshoro	112.65
3561	Improvement of road from Main Road Khuda-ke-Basti road to Garaho Goth via Main Bazar Bihar Colony & various streets (5.00 Kms) i/c M/S	Works & Services	Jamshoro	50.16
3562	Improvement of roads of Taluka Thano Bula Khan as under: (I) Road From Sarri To Mole Via Baradani Khaskheli Mile 0/0-15/5 (II) Road From Thano Ahmed Khan To Guru Balpuri, Ashram Via Dau Dam i/c Causeway Of Nai Mithree Mile 0/0-7/2 (11.00 Kms)	Works & Services	Jamshoro	301.40
3563	Rehabilitation of road Indus Highway (Old alignment-Sendoz Road) Dual Carriageway (2.00 Kms)	Works & Services	Jamshoro	72.06
3564	Improvement of road from Unerpur village to Zardari Mori via Chara via Budhapur Back to Zardari Mori i/c M/S (7.24 Kms)	Works & Services	Jamshoro	50.61
3565	Improvement / Construction of roads of Taluka Manjhand: (i) Indus Highway to village Tangyani via Shah Awais village Golara, village Qaim Khan Khoso & Mureedani i/c M/S mile 0/0-11/4 (18.507 Kms) (ii) Indus Highway to Qubi via Faqeer Bux Fanani Khoso, i/c M/S mile 0/0-4/6 (7.64 Kms)	Works & Services	Jamshoro	173.61
3566	Improvement / Reconditioning of link road i/c Solar Lights from Indus Highway near Kotri Phattak to Babbar Stop i/c M/S @ mile 0/0-2/0 (3.22 Kms)	Works & Services	Jamshoro	99.78
3567	Improvement of road from Khuhara Rice Mill to Taluka Hospital via Tower Chowk Mehar City i/c Drain (3.00 Kms)	Works & Services	Dadu	97.88
3568	Rehabilitation of road from Indus Highway to Bughia Service Goli Marr road i/c Drain & Meer Hassan Chowk to K.N Shah Bypass along Paving Blocks Both Side of road (1.66 Kms)	Works & Services	Dadu	99.53
3569	Improvement of road from Sita K.N Shah Road to K.N Shah Sindhi Butira road via Raman Khoso & Eisa Machi & Mallah Muhalla at Sita road to Gabari village, Rahib Rind village, along approach to Sukhpur Shaikh (12.87 Kms)	Works & Services	Dadu	99.29
3570	Improvement of road from Kakar Piaro road to Muhab Ali Junejo via Andryan Taga & Danger village road ( 10.66 Kms)	Works & Services	Dadu	99.28
3571	Construction / Improvement of road from Sita Piaro road to Hussain Arain via Ameer Bux Khoso village i/c Phatak to Gorar Street & Bundo Chowk to Prechared Canal & Memon Muhalla School to Prechared Canal (4.80 Kms)	Works & Services	Dadu	98.14
3572	Improvement of road from Mehar Gahi road to village Mangwani via Raza Mohammad Rind connecting village Khondi & village Qazi Arif mile 0/0-7/4 in portions connecting villages mile 0/0-2/4 i/c Masonary Structure	Works & Services	Dadu	98.31
3573	Improvement of road from Indus Highway to village Poracho connecting village Mubarak Khoso mile 0/0-2/2 connecting mile 0/0-3/0 i/c Masonary Structure	Works & Services	Dadu	47.31
3574	Construction / Improvement of road from Burira to Meer Muhammad village via Rahoja & Bego Dero village mile 0/0-6/3 (10.26 Kms)	Works & Services	Dadu	99.99
3575	W/R of road from Indus Highway to Choukhandi via Ali Bux Junejo village Towards Boriri village i/c Paver Block & Drain (4.83 Kms)	Works & Services	Dadu	99.84
3576	Improvement of Road from Indus Highway Baridarro to Bothro i/c Construction of road village Jani Chandio Kamalpur UC Bothro (17.70 Kms)	Works & Services	Dadu	99.01
3577	Improvement of road from Indus Highway to village Rais Ali Bux via Khondi (10.00 Kms)	Works & Services	Dadu	97.81
3578	Improvement of road from Shah Panjo Phattak Kisho Chandio road to Mehar Aghamani road link to Bali Shah Masonary Structure (10.00 Kms)	Works & Services	Dadu	98.15
3579	W/R of Road from Phulji Dawach Road to L.S Bund and Improvement of road from Phulji Dawach road to village Piaro Arain via village Pir Tarho via village Qazi Pir Muhammad via village Sher Muhammad Dawach and village Lashkari Brohi and Construction of Paving Block / Drainage of above mentioned villages (7.86 Kms)	Works & Services	Dadu	99.86
3580	Improvement of road from Johi-Wahi Pandi road to Rasool Bux Jamali via Pario Jamali, Noor Muhammad Jamali, M. Ali Jamali, Fazal Jamali (9.60 Kms)	Works & Services	Dadu	95.66
3581	Improvement of road from Thariri Jado Shaheed - Phulji village road to village Bahadur Naich i/c road to village Bachal Jamali, Naban Darogho, Kharwani Jamali and Ustad Meeral Jamali (6.60 Kms)	Works & Services	Dadu	49.08

ADP NO	Name of Scheme	Department / Sector	Location	Cost
3582	Improvement of road from Wahi Pandhi road to Haleli (8.20 Kms)	Works & Services	Dadu	95.69
3583	Widening / Reconditioning of road from Walwani Chodagi to Tharri Jado Shaheed via Phulji village (8.50 Kms)	Works & Services	Dadu	98.99
3584	Improvement of road from Bhan Johi road to village Chapper Jamali via Dingree (6.80 Kms)	Works & Services	Dadu	47.47
3621	Widening of Railway Underpasses in Larkana City (03 Nos.)	Works & Services	Larkano	100.00
3824	Construction / Reconditioning of road from Mouladad road to village Sharbat Mundrani via Ali Hassan Jakhriani, Abdul Rasheed, Mir Khalid Nawaz, Ali Hassan, Sohrab Khan Jan Jakhriani (11.00 Kms)	Works & Services	Jacobabad	116.93
3825	Construction / Reconditioning of road from Thul Bahoo Khoso road village to Sardar Khan Nindvani via village Haji Faiz M. Khoso, village Hafiz Ali M. Khoso, village Haji Jaffar Sundrani, village Mandov Marheta, village Arsalah Jakhriani, village Raza M. Tanvri, village Usman Marheta, village Jan M. Kandran, UC Tajo Khoso, UC Maloi, Taluka Thull	Works & Services	Jacobabad	99.86
3826	Construction / Reconditioning of road from village Abdul Ghani Panhwar via Abdul Hayee Sadhayo / Irshad Sarki to Muhammad Amin Brohi (7.00 Kms)	Works & Services	Jacobabad	68.15
3827	Construction / Reconditioning of road from Miranpur Buriro to village Muhammad Hayat Brohi via Miskan Brohi, Sharbat Brohi, Gul Hassan Brohi, Ferozabad Bulledi (12.00 Kms)	Works & Services	Jacobabad	138.05
3828	Reconditioning of road from Thull Bahoo road to Allahabad (Manjhipur) via M. Ayuob Khoso, Abdul Qadir Brohi, Muhammad Yousif Khoso, Idressabad, M. Pannah Khoso, Payaro Khoso (8.00 Kms)	Works & Services	Jacobabad	70.68
3829	Construction / Reconditioning of road Nasir Muhammad Brohi (Jam Khan Khoso) to village Dr. Abdul Jabbar Khan Khoso via Zulfiqar Goloo / Lutufabad / Anisabad / Zarak Brohi / Juman Shah / Nizam Mastoi / Abdul Ghani Khoso and village Ghunai (5.00 Kms)	Works & Services	Jacobabad	58.78
3830	Construction of road Paver / Tuff Tile at various streets of Jacobabad City Taluka Jacobabad	Works & Services	Jacobabad	120.00
3831	Construction of road from Shahghazi road village Babu Bhangar (6.25 Kms)	Works & Services	Jacobabad	70.00
3832	Construction / Reconditioning of road from Thul road Laahi Charhi to via village Nasir Muhammad Brohi / village Jaam Khan Khoso / Village Shahnawaz Diyo / Budho Diyo / Village Ghous Bux Mastoi and Meral Purano at Jacobabad (3.00 Kms)	Works & Services	Jacobabad	60.47
3833	Construction of road UC Bahadurpur village Shahzaman Khoso / Village Shah Murad Brohi / Village Muhammad Brohi / Village Muhammad Khan Khoso / Village Gulab Banglani / Village New Karachi / Village Shoukat Banglani	Works & Services	Jacobabad	48.73
3834	Construction / Reconditioning of road from Mirpur Buriro upto Sanhri Sarak via village Shabir Buriro / Muhammad Ismail Buriro / Punhal Channa / Allah Wadhayo Channo / Galib Channo & village Sohrab Channo, Taluka Thull (9.00 Kms)	Works & Services	Jacobabad	99.98
3835	Construction of road from Azizabad upto Darghaai Jakhriani via Manjhi Minor / village Warayo Noonari / Razi Jakhriani / Dosoo Marheta / Rahim Jakhriani & village Beero Jakhriani, Taluka Thull (8.00 Kms)	Works & Services	Jacobabad	99.90
3836	Construction of Road from Thull Jongal road Moni Stop upto Khan Muhammad Pahore via village Mangho Khan / Rano Pahore / Sameja village and village Shaikh Muhammad Pahore, Taluka Thull (6.75 Kms)	Works & Services	Jacobabad	79.96
3837	Construction of link road from Railway Phatak to G. Khairo Bypass via Seer with (Ring Band G. Khairo) Mile 0/0-3/1 (5.00 Kms)	Works & Services	Jacobabad	128.94
3838	Construction / Reconditioning of road from Mouladad road to village Ghaibi Khan Mundrani via village Noor Muhammad Jiskani, Pathar Mor, Bhooro Jakhriani, Janhwar Gulwani, Meva Gulwani, Dip village Pinya Sarghani, Sobha Jikhriani (10.50 Kms)	Works & Services	Jacobabad	115.39
3839	Construction / Reconditioning of road from Noor Wah Bridge to Thull Jacobabad road via village Mehran Brohi, Nepar Gorshani, M. Ayoub Unar \ Syed Zahir Shah, Habibullah Kehar, Raja Khan Khoso, Ashiq Ali Pathan, Zalfiqar Gorshani, Naseer Khan Khoso (10.00 Kms)	Works & Services	Jacobabad	98.72
3840	Construction of link road from Muhammadpur Bosan road to Ratodero Sher Muhamamd Thahim road via Liaqat Sarghani, Zia Rehman Jakhriani, Ali Hassan Marri, Bhooro Sarghani, Dodo Rozrani (5.75 Kms)	Works & Services	Jacobabad	74.77
3841	Conduction of road Ahmeden Khan Bangwar link road via Gul Hassan Bangwar upto village Elsi Golo and Construction of road village Mir Ali Muhammad Khan Khoso upto Rasaldar and from Rasaldar road Kaji Laro upto Dothi and link to village Mir Raheem Bux Khoso (9.40 Kms)	Works & Services	Kashmore	118.56
3842	Reconstruction of road from Badani road along Chachar Minor via Raees Sijawal and Reconstruction of road from Indus Highway upto City Badani	Works & Services	Kashmore	86.83
3843	Reconditioning of road from Chachar Pull upto Chowk Sardar Deen Muhammad Khan Kosh and Reconstruction of road along Adio Wah (14.00 Kms)	Works & Services	Kashmore	124.22
3844	Construction of road from Indus Highway to Garhi Tegho and Construction of road village Muqadam Ali Hassan Salzoi Construction of road from Sardar Khan Muhammadani upto village Muqadam Sahto Khan Sabzoi (5.50 Kms)	Works & Services	Kashmore	78.02
3845	Reconstruction of road from Kandhkot via Kher Shah upto Shahi Wah (13.25 Kms)	Works & Services	Kashmore	99.85
3846	Reconstruction of road from Indus Highway upto village Gul Sher Jakhriani	Works & Services	Kashmore	84.03
3847	Construction / Reconditioning of road from Kashmore Minor along Lachhi Wah and various villages upto Sui Line Purani road (8.00 Kms)	Works & Services	Kashmore	89.29

ADP NO	Name of Scheme	Department / Sector	Location	Cost
3848	Reconditioning of road from BS Feeder to Dur Muhammad Nahar via Badani City Internal Road via Jam Mehar Samejo via K.S Ali Bilawal Domki, Gandher via K.K Band	Works & Services	Kashmore	99.93
3849	Construction / Reconditioning of link road from Karampur-Magsi road Mandhani point to connect Muhammad Zaman Serki via Noonari Goth & Shabbirabad (8.50 Kms)	Works & Services	Kashmore	98.96
3850	Reconditioning of road from Lashkar Khan Suhriyani road to Ahmadan Khan Bhangwar / Mushtaq Khan Bhangwar (11.00 Kms)	Works & Services	Kashmore	96.68
3851	Construction of link road from Mehboob Shah road Nalka More Point upto Faiz Wah Jaffarabad road viz Muhammad Ali Khoso, Hussain Bux Brohi, Shah Ali Brohi, Shah Ali Rind, Khairjan Khan Brohi and Khuda Bux Marhito alongwith Inspection Path of Ahmed Raj Wah (12.50 Kms)	Works & Services	Kashmore	150.06
3852	Construction / Reconditioning of link road from village Kajlo Khan Jafferi upto village Pahlwan Bapar via Dost Ali Jafferi, Hanif Jafferi and Raza Muhammad village (5.00 Kms)	Works & Services	Kashmore	59.15
3853	Construction / Reconditioning of road from Mandhani Chowk to connect Jamal Pull road (8.75 Kms)	Works & Services	Kashmore	93.67
3854	Construction / Reconditioning of road from Indus Highway Ali Gohar Brohi Petrol Pump to village Phero Arija, Mehmood Dero, Eidan Khan Brohi, Ghulam Ali Khauhawar, Khedkar, Noor Mohammad Korkani, SACHE Dino Kalhoro, Mubarak Chandio, Lund, Kadero Mugheri, Sayed Sardar Shah, Tharo Khan Jagirani, Loung Mugheri approaches	Works & Services	Larkano	153.25
3855	Construction of road from @ village Muhammad Essa Hullio to village Karani mile 0/0-11/0 (17.70 Kms)	Works & Services	Larkano	179.83
3856	Construction of road from @ village Wadha to village Karani mile 0/0-10/0 (16.09 Kms)	Works & Services	Larkano	164.50
3857	Construction of road from New Bypass Larkana Miro Khan to Kamber, Mirokhan road (3.00 Kms)	Works & Services	Kamber	179.15
3858	Construction & Improvement of various road of Taluka Shahdaktot	Works & Services	Kamber	99.98
3859	Reconditioning Of Road From Waggan Warah Road At Point Lalu Raunk To Ghabidero Road @ Point Thori Bijar (7.00 Kms)	Works & Services	Kamber	109.96
3860	Construction / Reconditioning of various roads in Taluka Nasirabad (8.50 Kms)	Works & Services	Kamber	109.16
3861	Reconditioning of various roads in Taluka Warah (19.95 Kms)	Works & Services	Kamber	216.78
3863	Construction of road from Nara Bagh link road to village Dilshad Gadani (2.50 Kms)	Works & Services	Ghotki	31.50
3864	Construction of road from Landiyoon Mahar Nonhdhi to village Kanbir Mahar (4.00 Kms)	Works & Services	Ghotki	51.38
3865	Reconditioning of road from Mohdpur to Chak Shahbazpur Taluka Ubauro (12.00 Kms)	Works & Services	Ghotki	126.73
3866	Reconditioning of road from Rati to Barota (8.20 Kms)	Works & Services	Ghotki	106.43
3867	Reconditioning of road from Daharki to Barota (9.00 Kms)	Works & Services	Ghotki	108.28
3868	Widening / Reconditioning of road from Daharki to Reti upto Narley Minor (6.00 Kms)	Works & Services	Ghotki	100.00
3869	Construction of road from National Highway Mirpur Minor Inspection Path to village Noor Muhammad Chijjan, village Bangul Sial, Taluka Mirpur Mathelo (4.00 Kms)	Works & Services	Ghotki	50.59
3870	Construction of road from FFC Maso Wah Bridge to Allah Diwayo Lashari approach to Sultan Lashari, Abdullah Malano, Allah Ditto Jalbani & Bagh Ali, Taluka Mirpur Mathelo (4.20 Kms)	Works & Services	Ghotki	65.33
3871	Construction / Reconditioning of New Metal road from village Pathan Goth to Hekal Patt via Alam Toba Jeewan Garh road Gul Bahar Mangi (17.00 Kms)	Works & Services	Ghotki	250.01
3872	Construction of road from Sardargarh Dahar Wah to Izzat Wari via Phullo Malik (10.00 Kms)	Works & Services	Ghotki	159.92
3873	Construction of road from Baghsar road to village Jan Muhammad Mahar (8.00 Kms)	Works & Services	Ghotki	122.78
3874	Construction of road from Murad Ghoti link road to Bakro Wah, Deh Hussain Beli (2.00 Kms)	Works & Services	Ghotki	25.14
3875	Construction of road from Izzat Wari to village Kaman Mahar via Raza Muhammad Mahar and village Aleem Malik ( 8.00 Kms)	Works & Services	Ghotki	111.69
3876	Construction of Khadheri Bridge Piling and Construction of road from Khadheri Bridge to Sangi Band alongwith connected roads of various areas (7.60 Kms)	Works & Services	Sukkur	175.04
3877	Construction of Bridge Piling at village Lal Muhammad Mahar and connected road of various areas (6.00 Kms)	Works & Services	Sukkur	95.54
3878	Construction of road from National Highway to Hussain Kalwar via Mehsro Wah (7.10 Kms)	Works & Services	Sukkur	76.99
3879	Construction of road Widening 40ft and Reconditioning alongwith Drainage from both sides from Baiji Chowk NHA to Dua Chowk via Eid Gah Chowk and Shahi Bazar Pano Akil (4.00 Kms)	Works & Services	Sukkur	98.50
3880	(A) New Construction of link road Baga Khan Shambani to village Gaji Bux Shambani (5.50 Kms) (B) New Construction of link road village Ghulam Sarwar Shambani to Safar Shambani, Ghulam Shambani and Ali Gohar Shambani via Channel RD-186 (4.00 Kms)	Works & Services	Sukkur	107.62

ADP NO	Name of Scheme	Department / Sector	Location	Cost
3881	Construction of new road from Bhango Shakh to village Noor Muhammad Minhas via enroot villages Meelad Phull, Rahim Bux, Koro Khaskheli, Hakeem Lakhmir Rajpar, Sono Majeedano, Rahmatullah Khan, Sikandar Khaskheli, Haji Kamal Khand @ village Noor Muhammad Minhas	Works & Services	Khairpur	129.47
3882	Construction of new road from Hindyari to Village Aliabad via Earoot village Abbasabad, Usman Dasti, Mithal Dasti @ Hindyari Bachrah road (6.00 Kms)	Works & Services	Khairpur	76.99
3883	Construction Of Road From Jhanda Shakh / Jhango Road To Village Arbab Ali Wassan, UC Ali Muhammad Machi Road (5.00 Kms)	Works & Services	Khairpur	53.00
3884	Construction of road from Village Piyaro Khan Rajper via Abro, Bhatti via Banyo Rajper Zigzag to Kot Shoukat Ali Rajper to Bilal Majeedano via Khaleefo Hisamuddin via Ali Murad Rajper (8.00 Kms)	Works & Services	Khairpur	110.00
3885	Construction / Reconditioning Of Road From Mehran Highway At Mungla Naako To Connect Malhar Mangrio Road Via Village Shaman Lashari And Village Muhammad Bux Mojai (9.00 Km)	Works & Services	Khairpur	99.48
3886	Construction Of Road From Roshan Ali Mari Along Faiz Ganj Wah Upto Juman Khaskheli Road (3.60 Kms)	Works & Services	Khairpur	51.91
3887	Construction & Reconditioning of Road from Ripri Khuhra Road to Village Khemtia via Village Ali Bux Sarohi & Village Ali Gohar Awan 0/0-7/0 (11.00 Kms)	Works & Services	Khairpur	99.76
3889	Construction / Reconditioning of Road Village Sultan Ahmed Siyal to Village Ali Muhammad Mubejo via Village Lahano Khan Siyal via Tatri Minor UC Bhanbhri and UC Dangeja (8.50 Kms)	Works & Services	N. Feroze	97.22
3890	Construction of Moro Mithani Road at point Manaheen to Village Gh.Hyder Kario via Seth Allah Warayo Behan via Muhammad Ismail Jesar via Koji Jesar via Golo Potho via Qadir Bux Lund via Dhani Bux Kario UC Manaheen and UC Daris Taluka Moro (14.50 Kms)	Works & Services	N. Feroze	164.26
3891	Construction of road village Tagar to Village Baloo Chandio via Umer Saihito via Sain Bux Chandio via Qasim Chandio, UC Detha (4.50 Kms)	Works & Services	N. Feroze	50.86
3892	Construction / Reconditioning of road from National Highway to Hashim Lanjar along Sehra Minor and protective bund crossing Trimor Sehra Branch Gumoo Mori (11.00 Kms)	Works & Services	N. Feroze	125.31
3893	Construction / Reconditioning of road from National Highway near Jam Noorullah to village Yaral Ghanghro (Malokani Ghanghra) along Gul Minor (6.80 Kms)	Works & Services	N. Feroze	65.92
3894	Construction of Road Ranjhan Khan Panhwar to Haji Saeed Khan Panhwar, Aftal Bohio to Raham Ali Khoso Nim Wara Khoso, Naushehro Feroze road to Bagan Kalhoro (10.50 Kms)	Works & Services	N. Feroze	122.70
3895	(A) Construction of road from Haleem Bhangwar village Simnala road to connect Jheemal Minor via Tarighat More to connect Mir Qurban Ali Bhangwar road (4.50 Kms) (B) Reconditioning of road from Nawabshah-Daur road @ 7/5 mile to Katchi Chowdagi to Sain Dad Zardari via Trimore road (6.00 Kms)	Works & Services	S.B.A	176.95
3896	Construction / Reconstruction of road from 60th Mile -3 Chak Suhallo road @ 18 Shak Stop to Bachi Kalhori via Khudadad Brohi road along Sim Nala / Drain (7.00 Kms)	Works & Services	S.B.A	98.85
3897	Construction / Reconditioning of road from 60th Mile, 3 chak Suhallo road @ Tariqabad Mour to connect Sultan Dahri Mori road @ village Mahram Shah road (5.80 Kms)	Works & Services	S.B.A	80.36
3898	Construction of road from Darya Khan Kaloi road at mile 1/3 to village Hashim Kaloi via Abdullah Kaloi, village Ashiq Hussain Zardari, Alan Manjotho, village Naseer Manjthio, Pyaro Magis to connect Nabi Dad Brohi road (4.20 Kms)	Works & Services	S.B.A	55.39
3899	Construction / Reconditioning of Road from Malwah Minor to Abdul Hameed Dahri, Muhammad Otho, Yar Muhammad Dahri, Qutibi & Sobho Dahri Road (6.20 Kms) (with 3.80 cm Thick Carpet with Paver Machine)	Works & Services	S.B.A	86.90
3901	Reconditioning of Road from Bandhi Moro road to village Abdul Rauf Dahri, Manahro, Chariro and Sawri, Kazi Ahmed (9.00 Kms)	Works & Services	S.B.A	115.80
3902	Construction of Road from Sanghar Chotiaryoon Road to Link Road Kot Nawab Road to Gulzar Shar Road mile 0/0-5/5=9.00 KM (1-1/2" Thick Paver Carpet 12' Width)	Works & Services	Sanghar	99.92
3903	Construction of Road from Mirpurkhas Road to Loharao via Gullan Khan Banbhro, Khuda Bux Chandio, Raja Bisharat Road mile 0/0-3/1 = 5.00 KM (With 1-1/2" Thick Carpet 12' Width)	Works & Services	Sanghar	55.72
3904	Construction of Road from Toori Mori Road to village Mangal Khan Bugti via Ali Nawaz Shar, Akbar Chandio Samaro Minor Village Kondho Chandio Road mile 0/0-3/1=5.00 KMs (With 1-1/2" Thick Paver Carpet 12' Width)	Works & Services	Sanghar	65.70
3905	Construction of Road from Baan Mori to Naukot from link road to Tamachi Wassan via Sain Habibullah Shah, Nobat Shar Road 0/0-3/3+330=5.50 KMs (With 1-1/2" Thick Paver Carpet 12' Width).	Works & Services	Sanghar	67.92
3906	Construction of Road from Dhani Parto Rajpar to Qadir Bux Lohar Jhando Khan Kumbhar Allah Wassayo Bhatti Photo Khan Mari Stop to Samoon Depar Hadi Bux Depar Road mile 0/0-3/2=5.20 KMs (With 1-1/2" thick Paver Carpet 12' Width)	Works & Services	Sanghar	64.72
3907	Construction of Road from Sanghar to Chotiaryoon road to Village Khamiso Laghari via Shah Baig Bakadar Bughti Qalandar Bux Lashari Naseer Laghari road mile 0/0-3/3+330 =5.50 KM (1-1/2" Thick Paver Carpat 12' Width)	Works & Services	Sanghar	68.02
3908	(A) Construction of link road from Tayab Dars road to village Haji Noor Hassan Dars Moorhadi road 0/0-3/1=5.00 KMs (TST 12' Width) (B) Construction Of Link Road From Jamal Shah Road To Village Garhar Mori Via Dost Muhammad Moor Road 0/0-3/1 =5.00 Kms (With TST 12' Width)	Works & Services	Sanghar	97.02
3909	Construction of New road from Mazar Khaskheli Road to Mushtaq Ahmed Bajwa via Hakim Magis, Umardin Rajpoot, Ghulam Qadir Arain, Sidiq Jat, Shafiq Bajwa, Khadim Jat road mile 0/0 - 4/6 = 7.60 Kms (TST 12' Width)	Works & Services	Sanghar	70.38

ADP NO	Name of Scheme	Department / Sector	Location	Cost
3910	Construction of road from Muhammad Hassan Makrani to village Haji Afzal Mehar Taluka Shujabad (5.60 KMS)	Works & Services	Mirpurkhas	79.56
3911	Construction / Reconditioning of Asphalt road Mirpurkhas District Mirpurkhas length 16.42 Kms	Works & Services	Mirpurkhas	199.49
3912	Construction of road from Siloor Mori to Adam Mori via Village Soomar Junejo, Taluka Jhudo (16.00 Kms)	Works & Services	Mirpurkhas	198.29
3913	Construction of road from Sattar Hotel to Jhulluri village Ch: Barkat Kolhi Colony, Sher Shah Mamora Khan Meo & Jhulluri (8.00 Kms)	Works & Services	Mirpurkhas	95.10
3914	Construction of road from Mirwah Digri Road Bandhi Shakh Stop to Village Mehran Khan Laghari U.C Kangoro, Taluka Digri (8.00 Kms)	Works & Services	Mirpurkhas	98.06
3915	Reconditioning / Construction of road Tedi More to Village Haji Niaz Muhammad Kapri Taluka Jhuddo (6.00 Kms)	Works & Services	Mirpurkhas	50.23
3916	Construction of road from Mirpurkhas-Sindhri to Patoyoon road to link various villages Union Council Old Mirpur & Ahmed Bux Narejo (8.30 Kms)	Works & Services	Mirpurkhas	99.79
3917	Construction of road from Mirpurkhas - Khan Patoyoon road to connect various villages (8.30 Kms)	Works & Services	Mirpurkhas	99.95
3918	Construction of road from Mirpurkhas - Tando Adam road to connect various villages (8.70 Kms)	Works & Services	Mirpurkhas	99.83
3919	Improvement of Road from Mirpurkhas Khipro road to Maghan More via Jhurbi (with Aphalt) mile 0/0-11/0 (17.671 Kms)	Works & Services	Mirpurkhas	283.84
3920	Construction of road Dengan Rasti to Pir Bux Dhonkai to LBOD Mori Ramzan Khoso to LBOD Mori Ubedullah Bhurgari (8.5 Kms)	Works & Services	Mirpurkhas	93.67
3921	Construction of road Alim Bhurgari to Noor Ahmed Bhurgari UC Ahmed Khan Bhurgari (8.00 Kms)	Works & Services	Mirpurkhas	79.56
3922	Construction of road Molvi Ibrahim Nohani Haji Siddique Khaskheli Molvi Abdul Hai Nohani (5.00 Kms)	Works & Services	Mirpurkhas	47.63
3923	Construction of road from Rano Solangi to village Qamar Din Shar via Kaloo Khan Lashari (5.00 km)	Works & Services	Umerkot	74.89
3924	Construction of road from Araro Bhurgari to Punhoon Khaskhally via Asif Brohi (5.63 km)	Works & Services	Umerkot	99.02
3925	Construction of road from Mureed Khaskhally to Sonharo Dal via Hassan Shah Baghban (4.00 km)	Works & Services	Umerkot	62.21
3926	Construction of road from Hadakar Kunbhar Bhada to Jarkhari via Okraro (4.00 km)	Works & Services	Umerkot	97.80
3927	Construction of road from Dhalo jo Tar to Jetrar road (7.00 Kms)	Works & Services	Umerkot	154.06
3928	Construction of road from Tar Ahmed to Samoon Rind via Umaid Ali Rind Faqir Tar (7.00 Kms)	Works & Services	Tharparkar	112.00
3929	Construction of road from Sakriyo Road to Piyaro Dal via Risham jo Tar Datar Dino Thebu (7.00 Kms)	Works & Services	Tharparkar	112.00
3930	Construction of road from Sohilo Sahu Sand Road to Danbhario via Sahu Sand (7.00 Kms)	Works & Services	Tharparkar	112.00
3931	Construction of road from Khenser to Graveyard Khansar (3.75 Kms)	Works & Services	Tharparkar	55.97
3932	Construction of Road Talo Jaam to Pabuhar via Balhiari, Jetrica, Edri, Malkar (11.00 Kms)	Works & Services	Tharparkar	216.67
3933	Construction of Road from Sarah to Jahirmiryo (5.00 Kms)	Works & Services	Tharparkar	110.10
3934	Construction of Road from Lakhmiar to Nikno Bheel via Sange Jo Tar, Nau Tar, Chando Kolhi (10.00 Kms)	Works & Services	Tharparkar	173.03
3935	Construction of road from Ramlani to Allah Rakhe jo Par Waya Menhlani, Chaudio & Gaje Jo Par (11.00 Kms)	Works & Services	Tharparkar	175.00
3936	Construction of road from Shivo Charan to Tharo Rind & Karimdad Jo Tar (6.00 Kms)	Works & Services	Tharparkar	92.96
3937	Construction of road from Jete Jo Tar to Khyaro Nohri (6.00 Kms)	Works & Services	Tharparkar	93.00
3938	Construction of Road from Tugosar to Rinpario via Jethyar 5.50 Kms	Works & Services	Tharparkar	99.95
3939	Construction of Road from Soondar to Bhaki via Manserio, Gunga Veri, Soomrat 6.00 Kms.	Works & Services	Tharparkar	99.94
3940	Construction of Road from Sakrio to Umar Unar via Rawatsar 6.00 Kms.	Works & Services	Tharparkar	99.97
3941	Construction of Road from Sakrio to Kharuruo via Bisarnio 5.75 Kms	Works & Services	Tharparkar	99.95
3942	Construction of Road from Naryasar to Burtala via Ranpur 5.25 Kms	Works & Services	Tharparkar	99.89
3943	Construction of road from Chibhryal to Gangan 4.00 KM and Construction of road from Veenjhnayari to Batangari 5.00 Kms	Works & Services	Tharparkar	148.33
3944	Construction of road from Meenhoon Lanjo to Mohantar 4.00 Kms and Momin Mangrio to Megh Khawria (5.00 Kms)	Works & Services	Tharparkar	147.49
3945	Construction of Road from Bitri Road to Khadhari (near Villages Roojhan, Charakhara, Thouharchaho, Sabankhoi Kehari) mile 0/0-4/2 (6.00 Kms)	Works & Services	Tharparkar	99.83
3946	Construction of Road from Diplo Badin Road to Hathni (Near Villages Darr & Wango Rahiman) Mile 0/0 - 4/3 (7.00 Kms)	Works & Services	Tharparkar	99.84
3947	Construction of Road from Abdullah je Wandh to Kathurio Saman & Kathurio Samejo via Karam Ali Saman, Bajhliar Katho Bheel, Katho Saman (6.50 Kms)	Works & Services	Tharparkar	99.86
3948	Construction of Road from Chhaho Rahiman to Turkini via Pireho, Phulano, Phulani (6.00 Kms)	Works & Services	Tharparkar	99.81

ADP NO	Name of Scheme	Department / Sector	Location	Cost
3949	Construction of Road from Village Kharo Bajir to Connect village Alamsar (6.80 Kms)	Works & Services	Tharparkar	99.88
3950	Construction of road from Mithi Islamkot bypass to village Beperboh Taluka Mithi (4.00 Kms)	Works & Services	Tharparkar	94.87
3951	Construction of road from Airport road @ Point Dhorio to Shivo Jo Tar (4.00 Kms)	Works & Services	Tharparkar	89.25
3952	Construction of Road from Valasai Colony Kaloi Town to Mithi Badin Road (4.50 Kms)	Works & Services	Tharparkar	100.00
3953	Construction & Reconditioning of different link roads of U.C K.K Nizamani Taluka Hala (3 Units)	Works & Services	Matari	86.29
3954	Construction & Reconditioning of different link roads of Taluka Matari (3 Units)	Works & Services	Matari	91.85
3955	Construction & Reconditioning of Different link roads of Taluka Saeedabad (5 Units)	Works & Services	Matari	70.04
3956	Construction & Reconditioning of different link roads of Taluka Saeedabad (7 Units)	Works & Services	Matari	119.39
3957	Construction & Reconditioning of different link roads of Taluka Hala (4 Units)	Works & Services	Matari	115.00
3958	Construction & Reconstruction of different link roads of Taluka Matari (3 Units)	Works & Services	Matari	161.04
3959	Construction / Reconditioning of link road from Tando Allahyar Tando Adam road to village Ibrahim Aqlani via village Bahar Mirjat, village Doulat Mirjat Deputy Abdul Haque village Kolhi Kot Aslam Nizamani village Sando Mirjat village Ahmed Mirjat road mile 0/0-7/4 (12.00 kms)	Works & Services	T.A. Yar	100.00
3960	Construction / Reconditioning from Bukera Road to Bheel Colony Sufaida Colony, Sameja Street Akram Colony, Nagori Plot to Bypass Bukera road via Soomra Colony and Chamber Road and Hyderabad road, Islamabad Colony and Madina Colony, Malak Street mile 0/0 - 5/4 (8.84 Kms) (with 1-1/2" Thick Carpet i/c Drain Nala, Paver Block)	Works & Services	T.A. Yar	100.00
3961	Reconstruction / Widening of Road from Warrer Mori Stop to Nago Shah Chowk to Seri Zaur via Main Road Lakhat (6.50 Kms)	Works & Services	T.M. Khan	99.86
3962	Reconstruction / Widening of Road from Village Nazarpur to Village Jeendo Mir Bahar to Village Khair Muhammad Khoso to Village Hajana to Village Nizam Samoon via Village Sharif Shah (7.00 Kms)	Works & Services	T.M. Khan	99.96
3963	Reconditioning / Widening of Road from Jarri Mori to Dando to Village Nazar Khoso via Haji Khan Stop (7.10 Kms)	Works & Services	T.M. Khan	99.99
3964	Reconditioning / Widening of Road from Digh Mori Soomerki Shakh to Village Jan Muhammad Wassan to Peeru Wassan to Village Bashir Brohi via Nawab Pakko (6.00 Kms)	Works & Services	T.M. Khan	99.73
3965	Reconditioning / Widening of Road from Abdul Majeed Nizamani Otaq to Village Muhammad Ali Chang (6.00 Kms)	Works & Services	T.M. Khan	100.00
3966	Construction / Reconditioning of road from Jahan Khan Mori to Haji Yaqoob Khaskheli via Dargah Lal Mehmoodani road mile 0/0-5/0 (8.00 Kms)	Works & Services	T.M. Khan	81.83
3967	Construction / Reconditioning of road from Haji Khan Stop to village Rahim Khaskheli mile 0/0-6/2 (10.00 Kms)	Works & Services	T.M. Khan	98.32
3968	Construction / Reconditioning of road from Kario Ghanwar road to village Haji Bachal Leghari alongwith Jarki Shakh mile 0/0-7/4 (12.00 Kms)	Works & Services	T.M. Khan	123.39
3969	Construction of road from Tando Muhammad Khan Badin road @ mile 42/2 to village Suwali Dangno along Dokia Wah mile 0/0-6/2 (10.00 Kms)	Works & Services	T.M. Khan	124.88
3970	Construction of road from Tando Bago Jhudho road 16.1 Sim Nala to Noor Muhammad Dal village i/c link to village Ghulam Muhammad Dal village Umed Ali Jamali from Tando Bago Dei road 6.08 Kms	Works & Services	Badin	99.88
3971	Construction of road from Pangrio Wango road to village Ibrahim Khaskheli via Choudhry Waseem i/c to link Salar Nahrio / Ahmedani village link to Bachal Khaskheli from Sono Jamali road 6.00 Kms	Works & Services	Badin	99.53
3972	Construction of road from Lutaf Ali Khoso to Gul Muhammad Soomro, Fazal Muhammad Lund contact Khoski Attarli Chak road 5.83 Kms	Works & Services	Badin	99.87
3973	Construction of road from Malkani City via Mehrab Regulator to Mehrab Shahar i/c link road to Babar Kaloi from Malkani Roopo Rebari road (3.42 Kms)	Works & Services	Badin	100.00
3974	Construction of road from Badin Nindo road to Talho Khan Bhurgri, Otiya Rai Singh, Saeed Khan Bhurgri, Haji Abdul Karim Bhurgri i/c Mir Muhammad Rind, Zubair Rind, via Karo Wah connect Tando Bago Nindo road 6.15 Kms	Works & Services	Badin	99.86
3975	Reconditioning / Construction of Various village roads of Taluka Shah Bander (5.90 Kms)	Works & Services	Sujawal	69.99
3976	Construction / Reconditioning of various village roads of District Sujawal (5.10 Kms)	Works & Services	Sujawal	67.41
3977	Construction of road from Allah Dino Mandhro road @ 11.60 KMs to Baharo Zangejo Village (5.00 KMs)	Works & Services	Sujawal	79.48
3978	Construction of Link road from Chachjahan Khan Mian Usman Quaba road @ 1.87 KM to Qadria Minor via Village Gul Muhammad Jat and Malook Kalmatfi (6.00 Kms)	Works & Services	Sujawal	80.21
3979	Reconditioning / Construction of Various Villages road Village Abdul Khaliq Leghari, Village Allah Dino Soomro and Village Muhammad Khan Dibh (6.00 Kms)	Works & Services	Sujawal	65.14
3980	Construction / Rehabilitation of various Roads of UC-19, UC-20 & UC 22, Taluka Mirpur Sakro (12.80 Kms)	Works & Services	Thatta	135.00
3981	Construction / Rehabilitation of various roads of UC-26 & UC-27, Taluka Mirpur Sakro (10.80 Kms)	Works & Services	Thatta	114.39
3982	Construction / Rehabilitation of various Roads of UC-11, UC-12, Taluka Thatta	Works & Services	Thatta	89.83

ADP NO	Name of Scheme	Department / Sector	Location	Cost
3983	Construction of various Metaled Roads in Taluka Sehwan & Manjhand District Jamshoro	Works & Services	Jamshoro	172.29
3984	Construction of road from Guru Balpuri Toung Road Mile 3/2 Village Allah Bux Lalani to village Chibhar Nout Deh Bhal (6.00 Kms)	Works & Services	Jamshoro	85.46
3985	Construction of road from Bhand Mari to Rais Ali Ahmed Chandio village via Maroof Ja Bhan, Gullan Ja Bhan mile 0/5-3/5 i/c Masonary Structure	Works & Services	Dadu	54.26
3986	Construction of road from Mitho Babar to Ibrahim Channa Village Bridge along Johi Barrage Path 0/0-5/1 (8.30 Kms)	Works & Services	Dadu	99.82
3987	Constrcution / Improvement of road from Drigh Bala to Kando Babbar village Gahno Gopang, Village Chiddi to Sher Mohmmad Talpur, Jam Babbar, Bahawal Babbar via Fato Brohi upto Wahi Pandhi road (10.40 Kms )	Works & Services	Dadu	99.37
3988	Construction of road from Golo Faqeer to Shahik Rodnan, Bahlil Shah, Sawro & Sijawal Alkhani (10.00 Kms)	Works & Services	Dadu	99.97
3989	Construction of road from Pat Gul Muhammad to Tore via Allah Bux Arain , Meero Pat, Lalher, Dital Leghari & Taj Muhammad Doltani (9.65 Kms)	Works & Services	Dadu	99.96
3999	Construction / Reconditioning from Mujahid Colony 1&2 Street Bukera road and Deh Naiki Disposal via Mangcha Mori to Ibrahim Colony 1, 2, 3,4 Street and Chamber road street Menghwar, Bheel, Khaskheli, Kamboh, Kabootra and Mandir street 0/0-5/1 (8.24 Kms) (with 2" Thick Carpet i/c Drain Nala Paver Blocks)	Works & Services	T.A. Yar	98.27
4012	Construction of road from Dokri Badah road @ village Dara Railway Phatak to Badah Nasirabad road (Bypass) Badah mile 0/0-2/2 (3.62 Kms)	Works & Services	Larkano	100.00
4013	Construction of road from village Chibhar Nout to Dargah Mallo Pir Deh Bhal (3.00 Kms)	Works & Services	Jamshoro	50.00


# Annexure (E)

## PROGRESS SUMMARY OF PSDP FY 2022-23 SCHEMES


### EXECUTED BY GOVERNMENT OF SINDH

Name of the Department	No. of Schemes	Estimated Cost	Expenditure up to 30 June 2022	Throw-forward as on 01-07-22	Allocation 2022-23	Revised Allocation 2022-23	Funds Authorized by Federal Govt.	Funds Received by GoS
CLIMATE CHANGE DIVISION (Ongoing 1)	1	2811.050	2438.980	372.070	260.060	260.060	50.000	0.000
FINANCE DIVISION PROVINCES & SPECIAL AREAS (Ongoing 2 + New 5)	7	53713.123	1454.578	52911.097	4143.776	4143.776	500.000	0.000
WATER RESOURCES DIVISION (WATER) (Ongoing 03 + New 03)	6	42513.621	28845.419	13668.202	1489.535	1379.535	1379.535	0.000
<b>GRAND TOTAL</b>	<b>14</b>	<b>99,037.79</b>	<b>32,738.98</b>	<b>66,951.37</b>	<b>5,893.37</b>	<b>5,783.37</b>	<b>1,929.54</b>	<b>0.000</b>


### Cost & Expenditure Analysis of PSDP Schemes in FY 2022-23

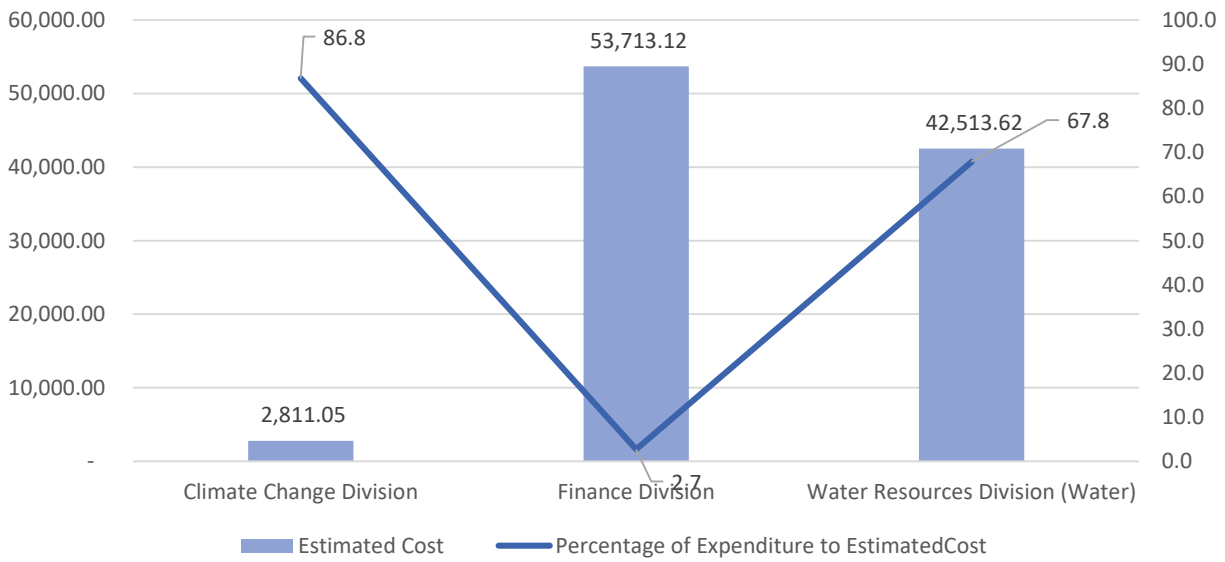

### PSDP RELEASE POSITION FY 2022-23

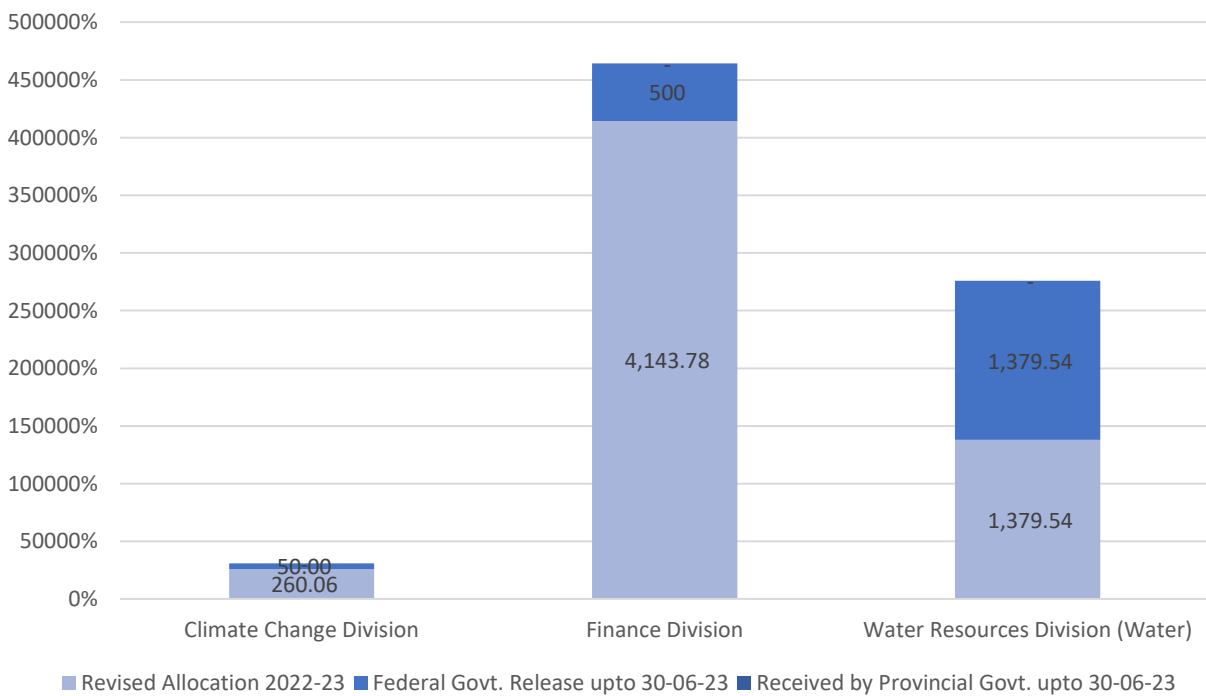

### Summary of Total Schmes of PSDP FY 2022-23

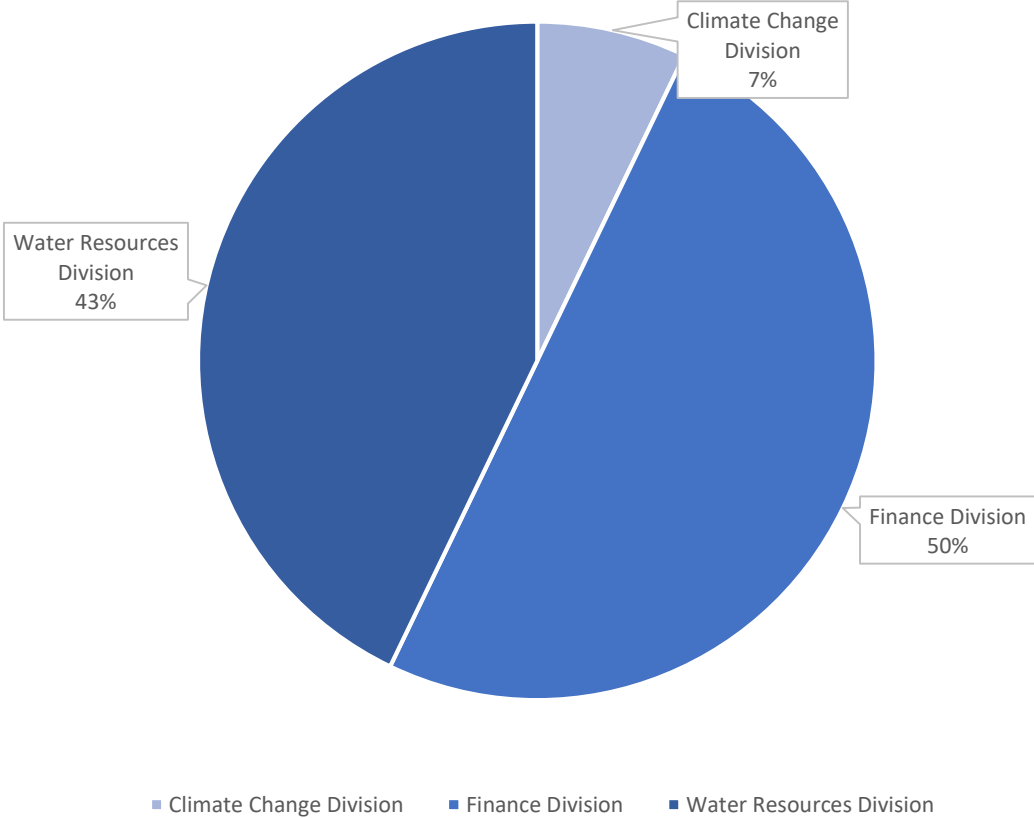

# Annexure (F)

## MEC Offices & Team Members

### SECRETARIAT HEAD OFFICE

<b>Ghulam Sarwar Chachar</b>	Director General (MEC)
<b>Gulan Khan Khaskheli</b>	Director (Coordination)
<b>Ghulam Hussain Bughio</b>	Director (A&A)
<b>M. Javed Khan</b>	Assistant Director
<b>Hafeez-ur-Rehman Janwari</b>	Assistant Director (HR)
<b>Sallah Saleh Thebo</b>	Admin & Accounts Officer
<b>Illahi Bux Chand</b>	Private Secretary
<b>Noor Muhammad</b>	Superintendent
<b>Abdul Rauf Shaikh</b>	Assistant
<b>Nabi Bux</b>	Assistant
<b>Ali Muhammad Jogi</b>	Assistant
<b>Syed Muhammad Fazal</b>	Sr. Clerk

### MIS DIRECTORATE

<b>Sarfraz Ahmed Khan</b>	Assistant Director / Director (MIS)
<b>Mohsin Ali Awan</b>	Assistant Director (Coord)
<b>Tufail Ahmed Shaikh</b>	Assistant Director (Content Management)
<b>Ashraf Baloch</b>	Sr. Programmer
<b>Bilal Bin Ismail</b>	Programmer (OS)
<b>Teerath Kumar</b>	Network Admin
<b>Avinash Sharma</b>	System Support Engineer
<b>Muhammad Faaz</b>	Hardware Technician
<b>Junaid Ahmed Shaikh</b>	Data Processing Officer
<b>Muhammad Panjal</b>	Data Processing Officer
<b>Suhail Ahmed Memon</b>	Data Processing Officer

## SECTOR MONITORING & PROCUREMENT OFFICE KARACHI

<b>Mr. Fateh uddin Junejo</b>	Sector Monitoring & Evaluation Officer (SMEO)- Infrastructure
<b>Dr. Javed Khawaja</b>	Sector Monitoring & Evaluation Officer (SMEO)- Social Sector
<b>Mr. Saeed Ahmed Nizamani</b>	Procurement Specialist
<b>Mr. Naveed Saleh Memon</b>	Sr. System Analyst
<b>Mr. Shabir Ahmed Pandhiani</b>	Compliance In charge
<b>Mr. Shuja Ahmed Lanjar</b>	Programmer
<b>Mr. Thakur Das</b>	In Charge Pendency
<b>Mr. Muhammad Faisal Tunio</b>	Data Processing Supervisor
<b>Mr. Muhkum din Shaikh</b>	Sub Engineer
<b>Mr. Arif Raza</b>	Key Punch Operator
<b>Muhammad Saleh Lund</b>	Steno-Typist

## REGIONAL MONITORING OFFICE KARACHI

<b>Mr. Aurangzeb Vistro</b>	Regional Monitoring Evaluation Officer (RMEO)- Karachi
<b>Mr. Muhammad Salman Shaikh</b>	Monitoring & Evaluation Officer (MEO)
<b>Mr. Ghulamullah Mahar</b>	Monitoring & Evaluation Officer (MEO)
<b>Mr. Imran Khan Memon</b>	Monitoring & Evaluation Officer (MEO)
<b>Mr. Ahmed Hussain Mahar</b>	Monitoring & Evaluation Officer (MEO)
<b>Ms. Rabia Muhammad Ali</b>	Monitoring & Evaluation Officer (MEO)
<b>Mr. Shafique Ahmed Samtio</b>	Sub Engineer
<b>Mr. Hizbullah Dars</b>	Data Processing Officer
<b>Mr. Muhammad Moosa</b>	Steno Typist

## REGIONAL MONITORING OFFICE LARKANA

<b>Aziz-ur-Rehman</b>	Regional Monitoring & Evaluation Officer (RMEO)
<b>Kashif Anwar</b>	MEO (Water Supply & Drainage)
<b>Rasheed Ahmed Jumani</b>	MEO (Agriculture)
<b>Shah Faisal</b>	MEO (Live Stock & Fisheries)
<b>Shams Uddin Mahesar</b>	MEO (Live Stock & Fisheries)
<b>Umair Aslam</b>	MEO (Roads)
<b>Ghulam Murtaza Khan</b>	System Support Engineer
<b>Waseem Ahmed Soomro</b>	Data Processing Officer
<b>Mohsin Ali Khokhar</b>	Office Assistant
<b>Khalid Hussain</b>	I.T Assistant

## REGIONAL MONITORING OFFICE HYDERABAD

<b>Mr. Tufail Ahmed Abro</b>	Sector Monitoring & Evaluation Officer (SMEO)
<b>Mr. Muhammad Azeem Jarwar</b>	Regional Monitoring Officer
<b>Mr. Syed Shafqat Shah</b>	MEO (Health)
<b>Mr. Rameez Bajkani</b>	MEO (Road)
<b>Mr. Jahanzeb Mallah</b>	MEO (Education)
<b>Mr. Abdul Qayoom Paliyo</b>	MEO (Water & Drainage)
<b>Mr. Bilal Ahmed</b>	MEO (Education)

## REGIONAL MONITORING OFFICE SUKKUR

<b>Shahzeb AhmedShaikh</b>	Regional Monitoring Evaluation Officer (RMEO)
<b>Muhammad Naeem Korejo</b>	MEO (Agriculture)
<b>Muhammad Aamir Arain</b>	MEO (Health)
<b>Dr. Shazia Mahar</b>	MEO (Livestock & Fisheries)
<b>Mohsan Ali Memon</b>	MEO (Social Sector)
<b>Muhammad Hanif Abro</b>	MEO (Buildings)
<b>Muhammad Hanif Hingoro</b>	MEO (Education)
<b>Jahangir Khan Chandio</b>	MEO (Livestock & Fisheries)
<b>Nisar Ahmed Khatii</b>	MEO (Irrigation)
<b>Ameef Kumar</b>	Data Processing Officer

# Annexure (G)

## MEC Team Members Pictures



Director Coordination Office Karachi



Director Admin & Accounts Office Karachi



SMEO Infra Office



SMEO Social Office



Procurement & System Analyst Office Karachi



MIS Directorate Office Karachi



Regional Office Karachi



Regional Office Larkana



Regional Office Sukkur



Regional Office Hyderabad





**MONITORING & EVALUATION CELL**  
**PLANNING & DEVELOPMENT DEPARTMENT**  
**GOVT OF SINDH**

**DIRECTOR GENERAL (MEC)**

**3RD FLOOR, TUGHULUQ HOUSE,  
SINDH SECRETARIAT, KARACHI**

**WWW.MECSINDH.GOV.PK**

**MIS DIRECTORATE**

**9th Floor, Vital Foak Tower, Shahrah-e-Faisal, Karachi**

**KARACHI REGIONAL OFFICE**

**Barrack# 92, Sindh Secretariate,  
Oppsite Sindh Assembly  
+92 21 99204634**

**SUKKUR REGIONAL OFFICE**

**Bungalow#: A-128, Sindhi,  
Society, Sukkur  
+92 71 9310737**

**HYDERABAD REGIONAL OFFICE**

**Block-F, Adj. DG Agriculture Ext. Office,  
Shahbaz Building, Thandi Sarak, Hyd.  
+92 22 9201337**

**LARKANA REGIONAL OFFICE**

**Bunglow #: 20, Street #3,  
Shahbaz Colony, Larkana  
+92 74 4752101**
